



OCMS

Ministry of Statistics & Programme Implementation

Government of India
Ministry of Statistics and Programme Implementation



474th *Flash Report on Central Sector Infrastructure Projects*

(Rs. 150 crore & above) April 2025

CONTENTS

Synopsis	1-2
List of Tables	3-235
Table:-1. Overview of Ongoing Projects: Sector-wise Distribution.....	3-4
Table:-2. Overview of Ongoing Projects: State-wise Distribution.....	5-6
Table:-3. Project List: Completed during April 2025.....	7-10
Table:-4. Project List: Added during April 2025.....	11-13
Table:-5. Project List: Ongoing Projects of North-East Region.....	14-38
Table:-6. Project List: Ongoing Projects as of 30th April 2025.....	39-264

SYNOPSIS

Flash Report - Central Sector Infrastructure Projects Costing Rs. 150 crore & above

Total Ongoing Projects (1670, ₹27,93,673.76 crore)


Mega*
(602 projects,
₹ 23,02,729.03
crore)

Major*
(1068 projects,
₹ 4,90,944.73...


Completed®
projects during
April 2025
(34 projects,
₹ 18457.95
crore)

**Newly Added/
elevated\$**
Projects during
April 2025
(26 projects,
₹ 33679.69
crore)


Note: @ Indicated legend is in format (Project Count, Cumulative Expenditure)
other Indicated legends are in format (Project count, Original Cost)
* Mega Project if having original cost ≥ 1000 crore
* Major Project if original cost < 1000 crore
\$ reported Anticipated cost more than 150 crore
reported Anticipated cost less than 150 crore
1 frozen project has been dropped from OCMS

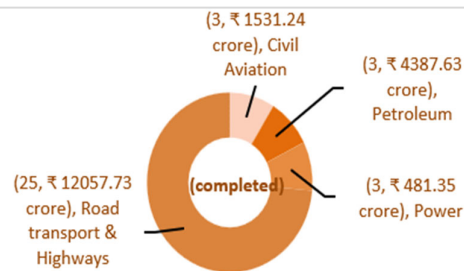

Note: all indicated legends are in format (Project count, Cumulative expenditure)

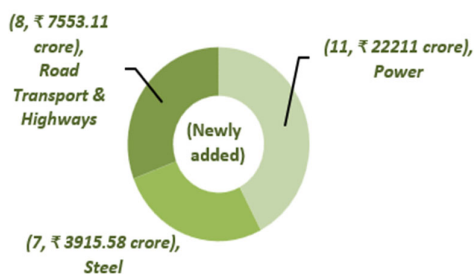




Note: all indicated legends are in format (Project count, Original Cost)

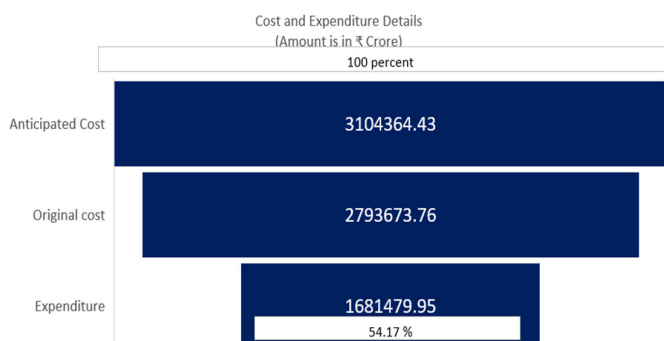


Total North East Region Ongoing Projects (210, ₹ 2,07,023.8 crore)

Mega*
(25 projects,
Rs. 1,29,703.85
crore)

Major*
(185 projects,
Rs. 77,319.95
crore)

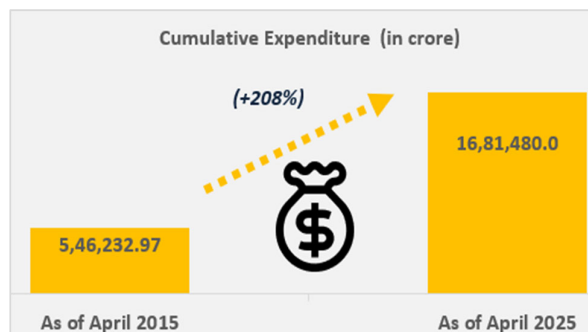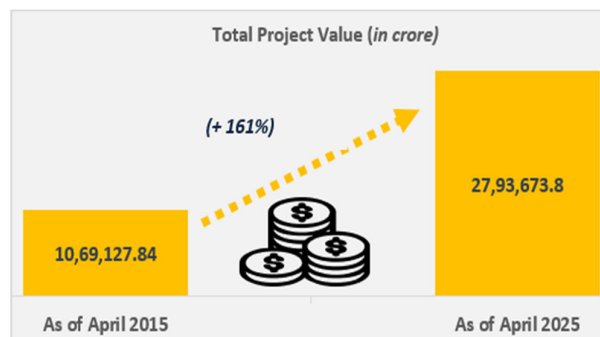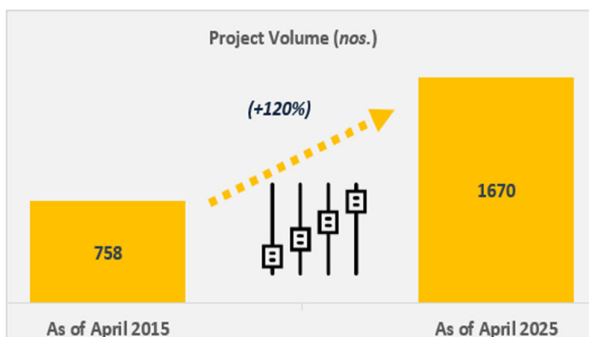


Sectoral Comparison : Major Sectors (as per count)
 [Outer Ring: Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

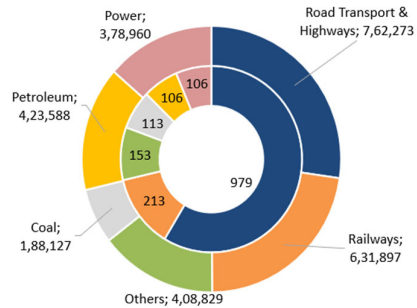


*Others include Water Resources, Civil Aviation, Urban Development, Department of Higher Education, Steel, Health & Family welfare, Mines, Telecommunications, Home Affairs, Finance, DPIIT, Shipping & Ports, and Social Justice

State Comparison : Major States (as per count)
 [Outer Ring:Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

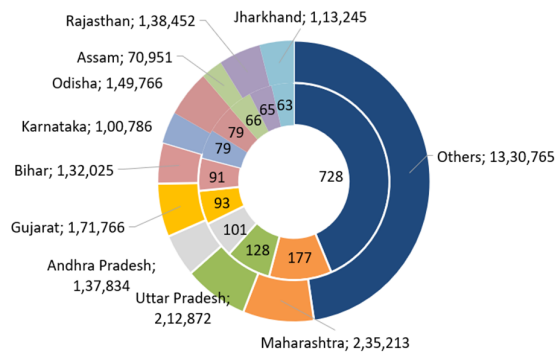

*Others include Tamilnadu, Madhya Pradesh, Delhi, Chhattisgarh, Haryana, Jammu & Kashmir, West Bengal, Kerala, Arunachal Pradesh, Punjab, Telangana, Uttarakhand, Himachal Pradesh, Manipur, Sikkim, Nagaland, Mizoram, Meghalaya, Tripura, Goa, A&N Island, Ladakh and Multistate

Sectoral Distribution of total 673 projects with reported Physical Progress between 80-100%

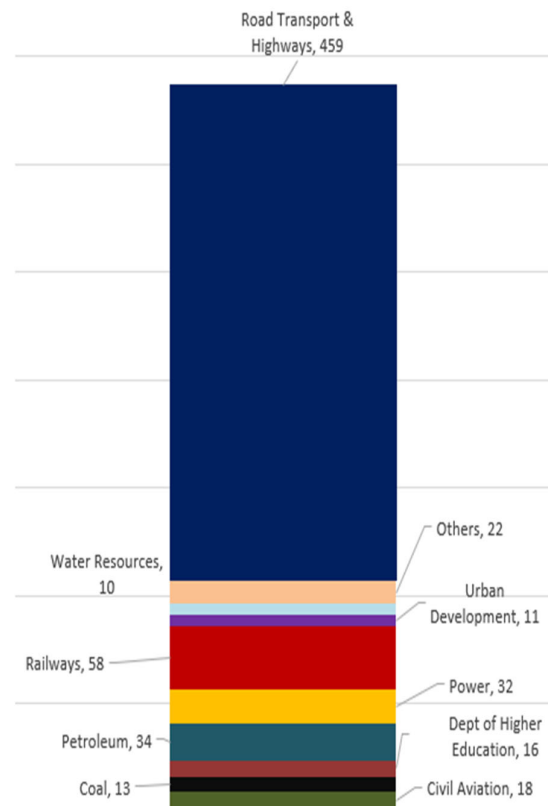

Note: This report is as of April 2025, based on the (non-exhaustive) list of projects and information as reported by Line Ministries/ implementing agencies on the OCMS (www.cspm.gov.in) portal latest by 8th May 2025.

A decorative frame resembling a scroll or a stylized 'C' shape, with a light gray fill and a dark gray outline. It has rounded ends and a small circular detail at the top left and bottom left.

LIST OF TABLES

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	CIVIL AVIATION	38	26,718.18 (27,771.19) {30,473.90}	17,430.52
2	COAL	113	188,127.06 (192,671.10) {197,500.35}	66,702.32
3	DEPARTMENT OF HIGHER EDUCATION	20	9,680.92 (10,152.14) {10,206.43}	7,219.42
4	DPIIT	2	24,857.00 (31,457.00) {32,085.00}	9,939.78
5	FINANCE	2	577.27 (577.27) {569.04}	399.67
6	HEALTH AND FAMILY WELFARE	8	7,301.27 (7,358.40) {7,356.19}	4,704.48
7	HOME AFFAIRS	5	2,025.73 (2,949.25) {2,949.25}	2,466.60
8	MINES	8	7,559.78 (9,356.73) {9,845.57}	5,983.20
9	PETROLEUM	106	423,588.30 (474,888.00) {485,041.21}	2,38,890.69
10	POWER	106	378,959.85 (397,275.55) {464,282.09}	2,29,667.95
11	RAILWAYS	213	631,896.84 (620,968.20) {658,071.79}	4,50,664.81
12	ROAD TRANSPORT AND HIGHWAYS	979	762,272.76 (793,364.28) {805,114.24}	4,01,122.11
13	SHIPPING AND PORTS	1	5,369.18 (5,061.15) {5,061.15}	3,414.95
14	SOCIAL JUSTICE	1	170.99 (170.99) {170.99}	73.80
15	STEEL	20	16,297.20 (20,228.73) {20,228.73}	7,561.30
16	TELECOMMUNICATIONS	6	26,961.69 (26,949.89) {26,949.89}	9,434.73

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
17	URBAN DEVELOPMENT	27	265,881.46 (272,720.33) {286,578.30}	1,98,371.86
18	WATER RESOURCES	15	15,428.28 (15,429.03) {61,880.31}	27,431.76
	Total	1670	2,793,673.76 (2,909,349.23) {3,104,364.43}	16,81,479.95

*Either Revised or Original Cost

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	ANDAMAN AND NICOBAR ISLANDS	10	2,956.02 (3,029.18) {3,010.04}	1,808.58
2	ANDHRA PRADESH	101	137,833.86 (138,333.19) {186,185.06}	98,734.38
3	ARUNACHAL PRADESH	15	45,355.10 (45,418.63) {65,231.68}	29,936.93
4	ASSAM	66	70,951.17 (71,435.04) {78,927.98}	48,896.87
5	BIHAR	91	132,025.16 (143,881.81) {156,093.17}	98,897.94
6	CHHATTISGARH	50	75,244.87 (79,134.30) {79,609.36}	34,568.92
7	DELHI	21	90,609.18 (96,063.03) {94,869.54}	75,889.17
8	GOA	3	1,201.05 (1,201.05) {1,287.55}	479.89
9	GUJARAT	93	171,766.13 (178,643.20) {180,047.13}	88,746.28
10	HARYANA	27	64,666.15 (75,462.06) {75,513.65}	38,801.14
11	HIMACHAL PRADESH	29	38,377.91 (39,407.59) {47,304.24}	31,113.84
12	JAMMU AND KASHMIR	54	110,434.59 (111,493.16) {124,794.68}	78,431.58
13	JHARKHAND	63	113,244.62 (117,005.23) {116,157.04}	64,585.11
14	KARNATAKA	79	100,786.16 (102,083.89) {101,111.19}	48,636.34
15	KERALA	32	64,106.75 (69,889.93) {70,321.90}	35,689.51
16	LADAKH	6	2,474.97 (2,474.97) {2,634.64}	1,335.62
17	MADHYA PRADESH	59	113,890.17 (113,291.57) {119,877.89}	40,597.62

Table:-2. Overview of Ongoing Projects: State-wise Distribution

18	MAHARASHTRA	177	235,212.75 (238,989.52) {263,997.81}	1,36,456.61
19	MANIPUR	32	25,355.56 (23,343.00) {33,267.37}	19,554.67
20	MEGHALAYA	15	6,583.27 (6,574.29) {6,528.65}	3,555.45
21	MIZORAM	17	14,519.38 (13,013.38) {18,688.72}	16,133.12
22	MULTI STATE	51	333,913.59 (338,914.31) {352,924.44}	2,43,139.16
23	NAGALAND	30	15,476.91 (16,825.59) {16,524.56}	9,021.07
24	ODISHA	79	149,765.57 (151,845.86) {154,533.92}	64,807.08
25	PUNJAB	38	37,743.85 (38,226.32) {38,643.81}	14,813.37
26	RAJASTHAN	65	138,451.86 (166,631.81) {167,672.73}	91,740.84
27	SIKKIM	21	20,872.24 (25,371.63) {26,215.20}	18,481.26
28	TAMIL NADU	63	92,087.08 (98,096.10) {103,639.15}	27,057.19
29	TELANGANA	52	29,124.48 (29,461.83) {31,449.35}	14,352.84
30	TRIPURA	14	7,910.17 (7,947.06) {8,032.54}	1,230.63
31	UTTAR PRADESH	128	212,871.97 (218,361.06) {224,779.80}	1,10,082.09
32	UTTARAKHAND	31	58,781.06 (63,618.31) {62,977.39}	46,271.73
33	WEST BENGAL	58	79,080.16 (83,881.33) {91,512.25}	47,633.12
	Total	1670	2,793,673.76 (2,909,349.23) {3,104,364.43}	16,81,479.95

***Either Revised or Original Cost**

Table:-3. Project List: Completed during April 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
CIVIL AVIATION					
	1	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI (AAI) (N04000075) (TAMIL NADU)	951.28	10/2021	1,084.94
	2	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD (AAI) (N04000086) (TELANGANA)	353.61	05/2022	303.22
	3	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT (AAI) (N04000089) (ANDHRA PRADESH)	177.10	02/2020	143.08
PETROLEUM					
	4	REVAMPING OF FACILITIES AT VIZAG TERMINAL (IOCL) (N16000343) (ANDHRA PRADESH)	355.00	04/2022	249.00
	5	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV (ONGC) (N16000358) (MAHARASHTRA)	3,228.80	03/2022	3,867.19
	6	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT (HPCL) (N16000413) (CHHATTISGARH)	456.00	03/2024	271.44
POWER					
	7	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C (PGCIL) (N18000338) (MULTI STATE)	186.19	03/2025	91.53
	8	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME XXVII (PGCIL) (N18000354) (CHHATTISGARH)	271.69	09/2024	192.03

Table:-3. Project List: Completed during April 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	9	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME-XXVIII AND XXIX (PGCIL) (N18000355) (CHHATTISGARH)	260.30	03/2025	197.79
ROAD TRANSPORT AND HIGHWAYS					
	10	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO (NHAI) (N24001728) (UTTAR PRADESH)	1,138.81	07/2025	528.10
	11	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN (NHAI) (N24001783) (HARYANA)	2,252.75	09/2021	1,223.07
	12	SANCHORE - SANTALPUR FROM KM 4.888 - KM 35.000 OF NH-754K (AJ-RGBS-PACKAGE-1) (NHAI) (N24001791) (GUJARAT)	606.51	06/2023	453.89
	13	4 LANING OF BATHALAPALLI TO MUDIGUBBA SECTION (DESIGN CHAINAGE KM. 96.300 TO 129.300) INCLUDING BATH (MoRTH) (N24001931) (ANDHRA PRADESH)	536.00	02/2025	334.06
	14	NH167B FROM KM 99.103 CS PURAM TO KM 143.320 MALAKONDA TO 2LPS (MoRTH) (N24001949) (ANDHRA PRADESH)	277.30	03/2024	206.25
	15	NH167B FROM KM.143.320 MALAKONDA TO 189.050 SINGARAYAKONDA ON NH 16 TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001950) (ANDHRA PRADESH)	369.81	02/2025	303.78
	16	2 LANE WITH PAVED SHOULDER CONFIGURATION FROM SEETHARAMAPURAM TO DUTTALURU SECTION OF NH-167 BG FROM (MoRTH) (N24002141) (ANDHRA PRADESH)	364.07	07/2025	227.21

Table:-3. Project List: Completed during April 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	17	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451) (ASSAM)	215.27	07/2024	105.40
	18	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 (NHAI) (N24001675) (KARNATAKA)	1,732.73	05/2025	754.79
	19	AURAD - BIDAR KM 0.00 TO KM 45.878 (NHAI) (N24001683) (KARNATAKA)	912.37	04/2023	255.94
	20	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 (NHAI) (N24001686) (KARNATAKA)	1,065.06	03/2023	736.55
	21	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN (NHAI) (N24001691) (KARNATAKA)	1,225.24	10/2021	1,043.00
	22	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY (NHAI) (N24000552) (KARNATAKA)	701.40	03/2019	923.99
	23	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO (NHAI) (N24000796) (UTTAR PRADESH)	1,117.84	12/2021	1,960.91
	24	SHAHPUR PATGAON SECTION I (MoRTH) (N24001027) (MAHARASHTRA)	150.79	12/2019	81.14
	25	JINTUR TO PARBHANI (MoRTH) (N24001039) (MAHARASHTRA)	356.66	N.A.	209.48

Table:-3. Project List: Completed during April 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	26	HIMAYATNAGAR TO PHULSAWANGI (MoRTH) (N24001081) (MAHARASHTRA)	294.87	12/2019	183.17
	27	SELDOH TO PANVAR (MoRTH) (N24001097) (MAHARASHTRA)	404.33	05/2020	140.65
	28	SATARA MURVAD PILLOV PANDHARPUR (MoRTH) (N24001095) (MAHARASHTRA)	388.44	N.A.	240.05
	29	KOLHA TO NASRATPUR (MoRTH) (N24001111) (MAHARASHTRA)	281.78	04/2019	77.83
	30	KUMBHARI PHTA TO DEULGAON RAJA (MoRTH) (N24001127) (MAHARASHTRA)	406.51	06/2019	340.26
	31	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859) (MIZORAM)	642.96	06/2023	686.42
	32	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES (MoRTH) (N24000941) (PUNJAB)	293.64	08/2020	295.46
	33	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948) (ARUNACHAL PRADESH)	568.92	12/2019	508.65
	34	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277) (MIZORAM)	275.02	10/2022	237.68
		Total	22,819.05		18,457.95

Table:-4. Project List: Added during April 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
POWER	1	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-4: 3.5 GW): PART A (PGCIL) (N18000407) (UTTAR PRADESH)	12-2024	5,846.00 (N.A.) {5,846.00}	12/2026 (N.A.) {12/2026}
	2	TRANSMISSION SYSTEM UNDER ISTS FOR EVACUATION OF POWER FROM KUDANKULAM UNIT - 3 & 4 (2X1000 MW) (PGCIL) (N18000408) (TAMIL NADU)	1-2025	548.00 (N.A.) {548.00}	7/2028 (N.A.) {7/2028}
	3	SYSTEM STRENGTHENING AT KOPPAL-II AND GADAG-II FOR INTEGRATION OF RE GENERATION PROJECTS (PGCIL) (N18000409) (KARNATAKA)	1-2025	1,354.00 (N.A.) {1,354.00}	1/2027 (N.A.) {1/2027}
	4	AUGMENTATION OF TRANSFORMATION CAPACITY AT BIDAR PS (PGCIL) (N18000410) (KARNATAKA)	2-2025	288.00 (N.A.) {288.00}	2/2027 (N.A.) {2/2027}
	5	AUGMENTATION OF TRANSFORMATION CAPACITY AT KPS2 & KPS2 (PGCIL) (N18000411) (GUJARAT)	3-2025	466.00 (N.A.) {466.00}	3/2027 (N.A.) {3/2027}
	6	AUGMENTATION OF BANASKANTHA (RAGHANESDA) PS (GIS) (PGCIL) (N18000412) (GUJARAT)	3-2025	172.00 (N.A.) {172.00}	3/2027 (N.A.) {3/2027}
	7	TRANSMISSION SYSTEM FOR INTEGRATION OF KURNOOL-IV REZ ? PHASE-I (FOR 4.5 GW) (PGCIL) (N18000413) (ANDHRA PRADESH)	3-2025	5,000.00 (N.A.) {5,000.00}	3/2027 (N.A.) {3/2027}
	8	RAJASTHAN REZ PH-V (PART-1: 4 GW) [SIROHI/NAGAUR] COMPLEX (PGCIL) (N18000414) (RAJASTHAN)	3-2025	5,028.00 (N.A.) {5,028.00}	3/2027 (N.A.) {3/2027}
	9	AUGMENTATION AT FATEHGARH-II PS, FATEHGARH-IV PS (SECTION-II) AND BARMER-I (PGCIL) (N18000415) (RAJASTHAN)	3-2025	404.00 (N.A.) {404.00}	12/2026 (N.A.) {12/2026}

Table:-4. Project List: Added during April 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
ROAD TRANSPORT AND HIGHWAYS	10	TRANSMISSION SYSTEM STRENGTHENING AT KURNOOL- III PS FOR INTEGRATION OF ADDITIONAL RE GENERATION PRO (PGCIL) (N18000416) (ANDHRA PRADESH)	3-2025	2,886.00 (N.A.) {2,886.00}	3/2027 (N.A.) {3/2027}
	11	TRANSMISSION SCHEME FOR EVACUATION OF POWER FROM RATLE HEP (850 MW) & KIRU (624 MW): PART B (PGCIL) (N18000417) (JAMMU AND KASHMIR)	3-2025	219.00 (N.A.) {219.00}	3/2027 (N.A.) {3/2027}
	12	BILASIPURA- GUWAHATI ROAD PKG-2 (NHIDCL) (N24002229) (ASSAM)	11-2023	1,338.61 (N.A.) {1,338.61}	6/2027 (N.A.) {6/2027}
	13	BADARPUR ? CHURAIBARI PKG-6 (NHIDCL) (N24002230) (ASSAM)	3-2024	870.00 (N.A.) {870.00}	3/2027 (N.A.) {3/2027}
	14	KARIMGANI - SUTARKANDI SECTION ON SILCHAR-CHURAIBARI PKG-7 (NHIDCL) (N24002231) (ASSAM)	2-2024	791.79 (N.A.) {791.79}	2/2027 (N.A.) {2/2027}
	15	IMPHAL-KOHIMA ROAD PKG-5A (NHIDCL) (N24002232) (MANIPUR)	9-2020	228.97 (N.A.) {228.97}	8/2026 (N.A.) {8/2026}
	16	DAINADUBI-DARUGIRI PKG-1B (NHIDCL) (N24002233) (MEGHALAYA)	3-2023	705.83 (N.A.) {705.83}	3/2027 (N.A.) {3/2027}
	17	WIDENING TO 4L FROM KM.108.50 TO 139.00 OF NH-135A PKG- II (JAUNPUR TO AKBARPUR SECTION) ON HAM IN TH (MoRTH) (N24002234) (UTTAR PRADESH)	3-2023	1,511.57 (N.A.) {1,511.57}	3/2027 (N.A.) {3/2027}
	18	CONSTRUCTION OF RAEBARELI RING ROAD (PHASE-2) WITH FOUR LANE CONFIGURATION FOR RAEBARELI CITY IN THE (MoRTH) (N24002235) (UTTAR PRADESH)	3-2022	1,273.72 (N.A.) {1,273.72}	5/2027 (N.A.) {5/2027}

Table:-4. Project List: Added during April 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	19	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM - VIJAYAWADA (NHAI) (N24002236) (TELANGANA)	3-2023	832.62 (N.A.) {832.62}	3/2025 (N.A.) {3/2027}
STEEL	20	REPLACEMENT OF HOT LEVELLER-1 OF PLATE MILL AT BHILAI STEEL PLANT (SAIL) (N12000137) (CHHATTISGARH)	7-2024	198.62 (N.A.) {198.62}	7/2026 (N.A.) {7/2026}
	21	INSTALLATION OF NEW BAR MILL AT DURGAPUR STEEL PLANT (SAIL) (N12000138) (WEST BENGAL)	9-2024	2,115.44 (N.A.) {2,115.44}	6/2027 (N.A.) {6/2027}
	22	UP-GRADATION OF BLAST FURNACE NO. 3 AT DURGAPUR STEEL PLANT (SAIL) (N12000139) (WEST BENGAL)	9-2024	758.09 (N.A.) {758.09}	6/2026 (N.A.) {6/2026}
	23	REVAMPING OF AIR POLLUTION CONTROL SYSTEMS OF SP-1 AT DURGAPUR STEEL PLANT (SAIL) (N12000140) (WEST BENGAL)	11-2024	196.40 (N.A.) {196.40}	5/2026 (N.A.) {5/2026}
	24	THIRD LADLE FURNACE IN SECONDARY REFINERY UNIT AT IISCO STEEL PLANT (SAIL) (N12000141) (WEST BENGAL)	11-2024	227.96 (N.A.) {227.96}	7/2026 (N.A.) {7/2026}
	25	REPLACEMENT OF EXISTING GRINDERS IN CRM-I & II AT BOKARO STEEL PLANT (SAIL) (N12000142) (JHARKHAND)	1-2025	211.94 (N.A.) {211.94}	1/2027 (N.A.) {1/2027}
	26	SECONDARY EMISSION CONTROL IN CONVERTERS OF SMS-II AT BOKARO STEEL PLANT (SAIL) (N12000143) (JHARKHAND)	1-2025	207.13 (N.A.) {207.13}	10/2026 (N.A.) {10/2026}
Grand Total				33,679.69 (-) {33,679.69}	

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ARUNACHAL PRADESH	CIVIL AVIATION	1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (5/2025) {5/2025}	645.63 (N.A.) {732.00}	690.39	99.5
	POWER	2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	24,022.52	96.2
		3	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	3,222.41	14.7
	ROAD TRANSPORT AND HIGHWAYS	4	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (3/2024) {3/2025}	180.57 (244.10) {180.57}	160.46	96.62
		5	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (6/2025) {12/2025}	1,718.59 (1,718.59) {1,718.59}	728.21	73.2
		6	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (5/2023) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59
		7	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA- HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (2/2025) {2/2025}	301.06 (N.A.) {301.06}	191.34	81.06
		8	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	389.68	95.28

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		9	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	179.53	41.94
		10	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (8/2024) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		11	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8-2020	4/2022 (2/2024) {9/2024}	294.04 (N.A.) {294.04}	147.13	100
		12	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (2/2024) {4/2025}	184.88 (N.A.) {184.88}	99.32	97.42
		13	HUNLI TO HAYULIANG PKG-1 (NHIDCL) (N24002222)	2-2024	2/2028 (N.A.) {2/2028}	1,262.43 (N.A.) {1,262.43}	0.00	0.75
		14	HUNLI TO ITHUN BRIDGE SECTION (NHIDCL) (N24002223)	2-2024	1/2027 (N.A.) {1/2027}	275.50 (N.A.) {275.50}	0.00	1.2
		15	PANGO TO JORGING ROAD PKG-1 (NHIDCL) (N24002224)	1-2024	7/2027 (N.A.) {7/2027}	898.19 (N.A.) {898.19}	7.08	1.97
ASSAM	CIVIL AVIATION	16	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (8/2025) {8/2025}	1,142.00 (N.A.) {2,333.00}	1,850.93	86.95
	COAL	17	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290)	7-2022	11/2030 (N.A.) {11/2030}	159.77 (N.A.) {159.77}	81.45	0

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		18	TIRAP OCP (CIL) (N06000291)	11-2022	11/2027 (N.A.) {11/2027}	289.46 (N.A.) {289.46}	105.59	0
	HEALTH AND FAMILY WELFARE	19	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (4/2023) {11/2024}	875.00 (873.92) {860.00}	787.90	99.4
	PETROLEUM	20	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	99.52	20.1
		21	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	97.22	90
		22	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	250.17	55.2
		23	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	169.95	44.1
		24	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (12/2024) {6/2025}	543.91 (726.93) {726.93}	491.56	93.89
		25	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	15,412.49	73.06
		26	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	9,247.50	84.53

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		27	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (5/2026) {5/2026}	412.00 (595.20) {595.20}	399.81	82.5
		28	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (9/2026) {9/2026}	277.00 (N.A.) {277.00}	175.69	66.02
		29	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (4/2025) {7/2025}	860.00 (N.A.) {860.00}	535.46	96
		30	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (3/2024) {6/2025}	430.76 (N.A.) {430.76}	308.90	83.56
		31	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	80.34	31.4
		32	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (7/2027) {7/2027}	156.36 (156.36) {156.36}	38.92	28.5
		33	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (7/2027) {7/2027}	384.04 (N.A.) {384.04}	87.82	30.7
	RAILWAYS	34	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2026 (N.A.) {3/2027}	4,059.65 (N.A.) {4,983.94}	3,626.20	92.31
	ROAD TRANSPORT AND HIGHWAYS	35	BILASIPURA- GUWAHATI ROAD PKG-1 (NHIDCL) (N24002225)	2-2024	8/2027 (N.A.) {8/2027}	1,081.15 (N.A.) {1,081.15}	0.00	1.16

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		36	SILCHAR-JIRIBAM PKG-1 (NHIDCL) (N24002226)	1-2024	1/2028 (N.A.) {1/2028}	957.95 (N.A.) {957.95}	0.00	0
		37	BILASIPURA- GUWAHATI ROAD PKG-2 (NHIDCL) (N24002229)	11-2023	6/2027 (N.A.) {6/2027}	1,338.61 (N.A.) {1,338.61}	0.50	0
		38	BADARPUR ? CHURAIBARI PKG-6 (NHIDCL) (N24002230)	3-2024	3/2027 (N.A.) {3/2027}	870.00 (N.A.) {870.00}	0.00	0
		39	KARIMGANI - SUTARKANDI SECTION ON SILCHAR-CHURAIBARI PKG-7 (NHIDCL) (N24002231)	2-2024	2/2027 (N.A.) {2/2027}	791.79 (N.A.) {791.79}	0.00	0
		40	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.87	100
		41	SILCHAR VAIRENGTE SAIRANG ROAD PKG- 1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	520.82	36.05
		42	SILCHAR VAIRENGTE SAIRANG ROAD PKG- 2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	983.58	63.52
		43	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	283.15	51.88
		44	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	380.59	61.1

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		45	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	522.78	44.9
		46	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	303.94	24.5
		47	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	422.31	24.26
		48	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	236.11	72.87
		49	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	129.18	14.06
		50	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3-2023	12/2025 (N.A.) {12/2026}	643.42 (N.A.) {643.42}	69.47	8.89
		51	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	279.86	41.57
		52	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	153.60	36.55
		53	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.76	100

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		54	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	147.96	75.89
		55	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,382.39	60.8
		56	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (5/2025) {12/2025}	261.13 (N.A.) {261.13}	68.75	57.42
		57	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (4/2025) {12/2025}	217.50 (N.A.) {217.50}	88.99	68.03
		58	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (1,019.17) {925.47}	192.50	30.65
		59	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	328.49	65.84
		60	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {5/2025}	625.64 (N.A.) {625.64}	550.60	100
		61	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {5/2025}	204.10 (N.A.) {204.10}	142.31	95.01
		62	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {6/2025}	909.02 (N.A.) {909.02}	509.89	97.63

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		63	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (9/2024) {6/2024}	175.00 (N.A.) {175.00}	200.80	100
		64	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	567.75	76.4
		65	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {5/2025}	457.72 (N.A.) {457.72}	365.99	100
		66	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	110.75	35.63
		67	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {7/2025}	458.59 (N.A.) {458.59}	196.51	61.42
		68	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	102.23	31.23
		69	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	391.08	62.21
		70	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	365.69	62.61

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		71	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	417.14	60.47
		72	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	293.45	91.18
		73	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	276.61	92.13
		74	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	217.06	97.76
		75	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (1/2025) {6/2025}	216.49 (241.52) {216.49}	111.59	82.79
		76	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {5/2025}	437.39 (N.A.) {437.39}	547.95	96.13
		77	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	490.44	75.52
		78	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1-1991	6/2019 (6/2019) {6/2025}	520.01 (N.A.) {520.01}	305.76	97.7

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		79	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (7/2021) {12/2025}	289.99 (N.A.) {289.99}	233.23	88.03
		80	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {5/2025}	294.17 (N.A.) {294.17}	381.37	97.63
		81	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {5/2025}	252.00 (N.A.) {330.30}	219.65	87.19
MANIPUR	CIVIL AVIATION	82	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (3/2026) {3/2026}	499.00 (N.A.) {499.00}	154.47	39.4
	RAILWAYS	83	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	12/2026 (3/2028) {3/2028}	14,322.79 (12,274.06) {22,234.60}	15,265.40	68.7
	ROAD TRANSPORT AND HIGHWAYS	84	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (1/2025) {9/2025}	292.24 (N.A.) {292.24}	130.66	89.72
		85	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (1/2025) {10/2025}	365.53 (N.A.) {365.53}	156.31	77.36
		86	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3-2020	6/2022 (1/2025) {5/2025}	167.95 (204.12) {167.95}	88.05	69.89
		87	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7-2020	8/2022 (2/2025) {5/2025}	177.76 (N.A.) {177.76}	89.67	80.53

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		88	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (6/2025) {10/2025}	379.39 (N.A.) {379.39}	214.93	67.72
		89	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (1/2025) {9/2025}	315.56 (N.A.) {315.56}	121.49	79.4
		90	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (2/2025) {3/2026}	410.68 (N.A.) {410.68}	147.81	67.64
		91	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (9/2025) {12/2025}	504.76 (N.A.) {504.76}	183.15	74.23
		92	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (2/2025) {3/2025}	152.11 (N.A.) {152.11}	73.48	100
		93	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (7/2025) {12/2025}	579.63 (N.A.) {579.63}	172.65	69.38
		94	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (1/2025) {1/2026}	477.86 (N.A.) {477.86}	243.46	83.92
		95	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (11/2024) {12/2025}	311.18 (N.A.) {311.18}	186.15	81.65
		96	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (10/2024) {2/2025}	467.41 (N.A.) {467.41}	264.83	100

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		97	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (3/2025) {7/2025}	226.32 (N.A.) {226.32}	104.95	74.48
		98	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (10/2024) {2/2025}	188.36 (N.A.) {188.36}	126.71	100
		99	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3-2021	12/2022 (3/2025) {3/2026}	195.14 (N.A.) {195.14}	61.81	50.79
		100	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (9/2024) {11/2025}	234.08 (N.A.) {234.08}	139.45	91.85
		101	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (5/2025) {10/2025}	211.70 (N.A.) {211.70}	83.79	68.65
		102	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (3/2025) {10/2025}	467.00 (N.A.) {467.00}	193.81	77.74
		103	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (1/2025) {1/2025}	185.80 (N.A.) {185.80}	117.78	100
		104	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (8/2024) {12/2025}	483.87 (N.A.) {483.87}	278.89	92.8
		105	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (2/2025) {3/2025}	198.77 (N.A.) {198.77}	127.86	100
		106	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (3/2025) {5/2025}	673.27 (N.A.) {673.27}	377.12	78.46

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		107	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (3/2025) {5/2025}	310.76 (N.A.) {310.76}	129.15	96.77
		108	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (12/2025) {3/2026}	760.16 (N.A.) {760.16}	148.98	58.19
		109	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (3/2026) {3/2026}	578.98 (N.A.) {578.98}	145.62	69.25
		110	MARREM KHULLEN TO JESSAMI SECTION IMPHAL- UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	11.64	9.21
		111	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	13.14	14.91
		112	IMPHAL-KOHIMA ROAD PKG-5A (NHIDCL) (N24002232)	9-2020	8/2026 (N.A.) {8/2026}	228.97 (N.A.) {228.97}	0.00	4.6
		113	JESSAMI TO LAYNEN BRIDGE UKHRUL - JESSAMI PKG-7 (NHIDCL) (N24002227)	3-2023	6/2026 (N.A.) {6/2026}	164.89 (N.A.) {164.89}	1.46	3.28
MEGHALAYA	DEPARTMENT OF HIGHER EDUCATION	114	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (7/2025) {7/2025}	484.32 (429.70) {429.70}	295.55	83
	ROAD TRANSPORT AND HIGHWAYS	115	DAINADUBI-DARUGIRI PKG-1B (NHIDCL) (N24002233)	3-2023	3/2027 (N.A.) {3/2027}	705.83 (N.A.) {705.83}	0.31	0

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		116	RANIKOR-MAHESKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10-2020	4/2022 (6/2024) {2/2025}	157.86 (146.92) {157.86}	152.95	100
		117	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (12/2024) {12/2025}	359.86 (N.A.) {359.86}	232.55	89
		118	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	210.58	28
		119	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	281.90	23
		120	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	297.79	24
		121	RANIKOR-MAHESKHOLA- BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3-2021	12/2022 (6/2024) {2/2025}	260.21 (N.A.) {260.21}	239.35	100
		122	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	206.15	26
		123	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	100.93	23.1

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		124	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM ((NHIDCL) (N24001313)	11-2020	12/2023 (10/2025) {10/2025}	351.12 (N.A.) {351.12}	295.87	61.5
		125	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	425.76	31
		126	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (3/2025) {3/2025}	302.88 (N.A.) {302.88}	140.20	95
		127	RANIKOR- MAHESKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11-2021	6/2024 (12/2024) {5/2025}	283.50 (N.A.) {283.50}	256.07	96.93
		128	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (3/2025) {6/2025}	553.51 (610.09) {553.51}	419.49	84.94
MIZORAM	RAILWAYS	129	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2025 (N.A.) {7/2025}	6,527.45 (5,021.45) {8,213.72}	7,948.91	96
	ROAD TRANSPORT AND HIGHWAYS	130	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (N.A.) {6/2025}	519.09 (N.A.) {785.65}	667.78	96.6
		131	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (N.A.) {5/2024}	640.07 (N.A.) {1,286.35}	1,192.26	98.9

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		132	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (N.A.) {6/2025}	473.18 (N.A.) {688.25}	539.93	94.38
		133	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (N.A.) {6/2025}	537.82 (N.A.) {789.05}	768.85	96.82
		134	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (N.A.) {5/2025}	518.53 (N.A.) {906.76}	847.17	97.2
		135	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (N.A.) {5/2025}	404.29 (N.A.) {750.32}	654.75	97.71
		136	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (N.A.) {5/2025}	428.11 (N.A.) {746.39}	606.93	97.9
		137	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (N.A.) {6/2024}	206.88 (N.A.) {219.33}	265.18	100
		138	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (N.A.) {6/2025}	292.24 (N.A.) {331.17}	291.20	93.2
		139	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9-2021	5/2023 (N.A.) {5/2024}	492.94 (N.A.) {492.94}	354.89	90.5

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		140	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWLRANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {12/2025}	523.78 (N.A.) {523.78}	643.63	78
		141	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (4/2024) {4/2024}	233.25 (N.A.) {233.25}	172.09	100
		142	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (N.A.) {3/2026}	698.44 (N.A.) {698.45}	499.26	59.4
		143	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (N.A.) {3/2026}	740.58 (N.A.) {740.58}	362.71	57.4
		144	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	250.46	65.1
		145	ZORINPUI- HMAWNGBU-LONGMASU (NH-502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	67.12	1.12
NAGALAND	PETROLEUM	146	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	4.54	17.5
	RAILWAYS	147	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2026 (N.A.) {12/2029}	6,663.20 (6,663.20) {6,663.20}	4,611.24	71
	ROAD TRANSPORT AND HIGHWAYS	148	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3-2022	12/2024 (N.A.) {1/2025}	605.36 (N.A.) {605.36}	273.21	100

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		149	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3-2020	6/2022 (9/2022) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.4
		150	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7-2021	3/2023 (9/2025) {9/2025}	258.52 (N.A.) {258.52}	83.96	77.9
		151	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	92.24	49.95
		152	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	39.97	22.28
		153	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	159.36	59.2
		154	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (6/2025) {6/2025}	192.93 (N.A.) {192.93}	103.62	88.6
		155	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {12/2025}	177.77 (199.02) {199.02}	43.33	61.13
		156	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	62.08	66.76
		157	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (6/2026) {6/2026}	252.19 (N.A.) {252.19}	11.97	14.5

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		158	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3-2021	7/2024 (6/2025) {6/2025}	297.24 (N.A.) {297.24}	137.57	76.2
		159	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (3/2025) {3/2025}	226.44 (N.A.) {226.44}	140.24	100
		160	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3-2016	9/2019 (11/2022) {5/2025}	373.07 (534.41) {534.41}	382.50	99.81
		161	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (9/2025) {9/2025}	429.52 (794.74) {794.74}	321.40	90.84
		162	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (2/2023) {4/2025}	387.00 (688.12) {688.12}	389.81	100
		163	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (8/2024) {4/2025}	500.09 (698.81) {698.81}	393.53	100
		164	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU- MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (8/2022) {8/2025}	215.79 (N.A.) {215.79}	127.85	77.1
		165	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU- MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (6/2023) {9/2025}	323.98 (N.A.) {323.98}	112.43	52.47

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		166	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	114.35	63.2
		167	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3-2020	6/2022 (10/2022) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
		168	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (11/2025) {11/2025}	330.80 (N.A.) {330.80}	168.02	91.97
		169	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (11/2026) {11/2026}	232.29 (350.88) {232.29}	69.98	14.42
		170	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (9/2024) {6/2026}	277.44 (N.A.) {277.44}	168.88	66.12
		171	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (6/2025) {6/2025}	159.85 (342.29) {159.85}	101.93	29.36
		172	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (4/2023) {8/2025}	202.36 (N.A.) {202.36}	75.17	30.8
		173	UPGRADATION OF EXISTING ROAD TO 2- LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9-2020	4/2022 (5/2024) {12/2025}	315.63 (N.A.) {315.63}	116.70	74.23

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
SIKKIM		174	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEM YONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3-2017	11/2020 (2/2023) {2/2023}	217.35 (N.A.) {217.35}	214.18	100
		175	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3-2019	12/2022 (1/2023) {1/2023}	237.51 (N.A.) {237.51}	215.47	100
	CIVIL AVIATION	176	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	24.98	9.9
	DEPARTMENT OF HIGHER EDUCATION	177	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8-2020	1/2025 (N.A.) {1/2025}	314.06 (N.A.) {303.55}	157.24	76
	POWER	178	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	4,249.86	67.08
		179	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,439.46	87.07
	RAILWAYS	180	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	5/2015 (12/2027) {12/2027}	7,876.92 (11,963.43) {11,963.43}	8,569.25	76.5
	ROAD TRANSPORT AND HIGHWAYS	181	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {4/2025}	311.00 (N.A.) {273.78}	257.86	94.94
		182	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (8/2024) {4/2025}	345.38 (395.59) {395.59}	362.61	90.82

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		183	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {6/2025}	402.94 (N.A.) {402.94}	247.12	76.54
		184	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (11/2024) {7/2025}	295.97 (N.A.) {295.97}	248.39	95.22
		185	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3-2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	100
		186	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (5/2022) {12/2023}	375.80 (N.A.) {375.80}	288.56	96.55
		187	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11-2017	10/2020 (8/2023) {4/2024}	290.05 (N.A.) {290.05}	218.36	100
		188	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (1/2026) {1/2026}	385.15 (N.A.) {385.15}	170.32	81.11
		189	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1-2021	9/2023 (4/2025) {12/2025}	332.20 (348.92) {348.92}	149.38	41.04
		190	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (4/2025) {12/2025}	410.60 (379.30) {379.30}	234.27	73.22

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		191	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (10/2024) {12/2025}	230.45 (244.91) {244.91}	206.95	82.32
		192	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (7/2025) {3/2026}	493.42 (478.79) {478.79}	302.83	55.21
		193	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (6/2025) {12/2026}	816.79 (786.60) {786.60}	326.82	50.6
		194	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (10/2023) {12/2025}	292.80 (N.A.) {292.80}	202.92	60.8
		195	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (10/2023) {12/2025}	183.31 (439.56) {439.56}	355.31	51.85
		196	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (8/2024) {12/2025}	262.84 (414.20) {414.20}	221.86	47.56
TRIPURA	PETROLEUM	197	GRASS ROOT RAIL FED DEPOT AT SEKEREKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (9/2025) {9/2025}	656.00 (N.A.) {656.00}	395.18	81.15
	ROAD TRANSPORT AND HIGHWAYS	198	KHOWAI ?TELIAMURA-AMARPUR-HARINA-SABROOM SECTION PKG-4 (NHIDCL) (N24002228)	1-2024	12/2026 (N.A.) {12/2026}	726.90 (N.A.) {726.90}	0.00	2.25

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		199	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	63.55	18.6
		200	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH- 8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	18.44	7.96
		201	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	7.56	16.61
		202	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	46.60	31.45
		203	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	11.96	27.5
		204	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	0.00	0
		205	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {4/2025}	201.99 (N.A.) {287.47}	148.22	100
		206	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (10/2023) {11/2024}	159.13 (171.50) {171.50}	84.33	100
		207	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (N.A.) {12/2025}	354.79 (N.A.) {354.79}	34.08	0

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		208	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (5/2025) {5/2025}	456.88 (N.A.) {456.88}	122.23	49.17
		209	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {11/2025}	195.95 (N.A.) {195.95}	38.10	38.44
		210	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (2/2024) {12/2024}	277.50 (302.02) {302.02}	260.38	99.94
			Total			207,023.80 (50,458.42) {253,416.70}	1,46,810.00	

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ANDAMAN AND NICOBAR ISLANDS	CIVIL AVIATION	1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR (AAI) (N04000073)	10-2013	9/2018 (6/2023) {6/2023}	417.23 (707.73) {707.73}	698.80	100.00
	RAILWAYS	2	LUDHIANA KILA RAIPUR (19 KMS) WITH FREIGHT LINE AT GILL STATION ON LDH-JHL SECTION (NR) (N22000584)	3-2019	3/2025 (12/2025) {12/2025}	235.72 (N.A.) {235.72}	54.28	55.00
	ROAD TRANSPORT AND HIGHWAYS	3	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N (NHIDCL) (N24000745)	3-2017	12/2019 (3/2023) {5/2025}	409.85 (N.A.) {409.85}	214.23	95.10
		4	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O (NHIDCL) (N24000749)	3-2018	9/2020 (11/2022) {5/2025}	234.27 (N.A.) {234.27}	126.50	82.93
		5	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 (MoRTH) (N24000820)	11-2017	11/2019 (N.A.) {11/2019}	237.80 (N.A.) {238.00}	222.13	98.23
		6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000821)	11-2017	11/2019 (N.A.) {11/2019}	257.34 (N.A.) {238.00}	214.90	100.00
		7	AJANTHA TO BULDHANA (MoRTH) (N24001008)	2-2017	7/2019 (N.A.) {12/2023}	401.00 (401.00) {401.00}	260.08	97.00
		8	MAJOR BRIDGE OVER MIDDLE STRAIT CREEK (NHIDCL) (N24002207)	12-2024	2/2026 (N.A.) {2/2026}	371.80 (207.99) {207.99}	0.00	2.11

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ANDHRA PRADESH		9	PACKAGE-3A (NHIDCL) (N24002208)	2-2018	9/2025 (3/2024) {9/2025}	207.54 (154.01) {154.01}	16.21	35.50
		10	PACKAGE-3B (NHIDCL) (N24002209)	2-2018	11/2025 (N.A.) {11/2025}	183.47 (N.A.) {183.47}	1.45	25.27
	CIVIL AVIATION	11	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT (AAI) (N04000091)	4-2020	3/2023 (8/2025) {8/2025}	611.80 (N.A.) {611.80}	433.85	73.00
		12	RAJAHMUNDRY AIRPORT: CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUD (AAI) (N04000103)	12-2022	8/2025 (N.A.) {8/2025}	347.15 (347.15) {347.15}	72.12	43.00
		13	KADAPPA AIRPORT- CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUDING MA (AAI) (N04000106)	3-2023	1/2026 (N.A.) {1/2026}	265.91 (N.A.) {265.91}	39.49	27.00
	DEPARTMENT OF HIGHER EDUCATION	14	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE (CPWD EDUCATION) (N42000005)	2-2019	6/2020 (N.A.) {6/2020}	655.34 (N.A.) {655.34}	366.21	95.00
		15	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC (CPWD EDUCATION) (N42000007)	9-2019	9/2022 (N.A.) {6/2024}	588.72 (656.39) {656.39}	630.55	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	16	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT (ONGC) (N16000247)	3-2016	6/2020 (3/2025) {6/2025}	34,012.00 (N.A.) {34,012.00}	33,149.29	96.40
		17	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY (HPCL) (N16000432)	9-2021	6/2024 (3/2026) {3/2026}	160.00 (220.00) {220.00}	50.04	56.00
		18	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS (IOCL) (N16000485)	3-2022	3/2030 (N.A.) {3/2030}	1,420.00 (N.A.) {1,420.00}	144.41	6.10
		19	MULTI-PRODUCT PIPELINE FROM KRISHNAPATNAM COASTAL INSTALLATION TO THE PROPOSED INSTALLATION AT HYDER (BPCL) (N16000499)	9-2019	3/2025 (N.A.) {10/2025}	1,932.00 (N.A.) {1,932.00}	1,491.64	85.30
		20	HP TRIJET UNIT IN VR (HPCL) (N16000535)	7-2024	7/2027 (N.A.) {7/2027}	193.00 (N.A.) {193.00}	0.38	19.00
		21	CONSTRUCTION OF AVIATION FUEL FARM FACILITIES AT BHOGAPURAM AIRPORT (HPCL) (N16000538)	8-2024	3/2026 (N.A.) {3/2026}	240.00 (N.A.) {240.00}	16.74	25.50
		22	VISAKHA RAIPUR PIPELINE PROJECT (HPCL) (N16000539)	9-2024	9/2027 (N.A.) {9/2027}	2,212.00 (N.A.) {2,212.00}	2.41	3.65
	POWER	23	TRANSMISSION SCHEME FOR SOLAR ENERGY ZONE IN ANANTHPURAM (2500MW) AND KURNOOL (1000MW) (PGCIL) (N18000380)	9-2023	3/2025 (N.A.) {9/2025}	1,249.00 (N.A.) {1,249.00}	418.81	53.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		24	AUGMENTATION OF 1500MVA 3RD 765/400KV TRANSFORMATION CAPACITY AT KURNOOL NEW SUBSTATION (PGCIL) (N18000395)	5-2023	9/2025 (N.A.) {9/2025}	164.00 (N.A.) {164.00}	66.00	15.00
		25	TRANSMISSION SYSTEM FOR INTEGRATION OF KURNOOL-IV REZ ? PHASE-I (FOR 4.5 GW) (PGCIL) (N18000413)	3-2025	3/2027 (N.A.) {3/2027}	5,000.00 (N.A.) {5,000.00}	0.00	-
		26	TRANSMISSION SYSTEM STRENGTHENING AT KURNOOL- III PS FOR INTEGRATION OF ADDITIONAL RE GENERATION PRO (PGCIL) (N18000416)	3-2025	3/2027 (N.A.) {3/2027}	2,886.00 (N.A.) {2,886.00}	0.00	-
	RAILWAYS	27	KOTLPALLI-NARASAPUR (NL) (SCR) (SCR) (220100265)	12-2001	3/2028 (N.A.) {3/2027}	2,500.98 (N.A.) {2,500.98}	1,141.44	18.00
		28	NADIKUDE-SRI KALAHASTI (SCR) (N22000286)	4-2011	5/2027 (N.A.) {5/2027}	2,312.00 (N.A.) {3,122.35}	1,935.77	-
		29	GUNTUR-GUNTAKAL (SCR) (N22000368)	4-2016	12/2025 (N.A.) {12/2025}	3,733.37 (N.A.) {3,887.48}	3,478.23	-
		30	VIJAYAWADA-GUDUR (RVNL) (N22000369)	4-2015	11/2024 (N.A.) {12/2024}	6,654.00 (N.A.) {6,238.67}	5,883.89	-
		31	KOTTAVALSA - KORAPUT DOUBLING (ECOR) (N22000377)	4-2015	3/2022 (N.A.) {3/2022}	2,499.71 (N.A.) {2,499.71}	1,919.28	69.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		32	PENUKONDA-DHARMAVARAM, EXCL. DHARMAVARAM (41.5 KM) (SWR) (N22000555)	4-2019	3/2026 (N.A.) {12/2025}	294.67 (307.66) {307.66}	197.73	50.00
		33	MALUGUR-PALASAMUDRAM (17.98 KM) (PB#29/NR/2022-23) (SWR) (N22000556)	9-2022	12/2025 (N.A.) {12/2026}	323.14 (342.41) {342.41}	46.89	12.00
		34	DOUBLING BETWEEN GOOTY- PENDAKALLU (29.225) (SCR) (N22000585)	3-2023	3/2027 (N.A.) {3/2027}	351.83 (N.A.) {351.83}	0.00	-
		35	VIJAYAWADA KAZIPET BYPASS LINE (SCR) (N22000586)	4-2016	12/2025 (N.A.) {12/2025}	647.37 (N.A.) {226.72}	235.48	-
		36	RENIGUNTA WADI GOOTY - BYPASS (SCR) (N22000587)	4-2016	12/2025 (N.A.) {12/2025}	302.00 (N.A.) {302.00}	209.83	50.00
	ROAD TRANSPORT AND HIGHWAYS	37	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES (MoRTH) (N24000301)	3-2015	10/2015 (5/2021) {5/2021}	271.45 (N.A.) {271.45}	238.23	100.00
		38	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 (NHAI) (N24000811)	3-2018	12/2020 (12/2022) {12/2024}	314.43 (N.A.) {348.72}	85.61	68.10

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		39	REHABILITATION AND UPGRADATION OF EXISTING NH- 167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 (MoRTH) (N24000931)	11-2016	5/2017 (N.A.) {11/2024}	290.15 (N.A.) {236.16}	205.02	90.00
		40	REHABILITATION AND UPGRADATION OF NEW NH- 544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG (MoRTH) (N24000937)	3-2018	8/2018 (N.A.) {11/2024}	289.67 (290.00) {285.29}	254.19	98.50
		41	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH- 214(NH216)(KAKINAD (MoRTH) (N24000964)	8-2016	1/2017 (N.A.) {5/2025}	350.61 (N.A.) {411.18}	407.92	98.00
		42	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 (MoRTH) (N24000969)	1-2017	9/2017 (N.A.) {6/2025}	263.45 (N.A.) {263.45}	208.15	85.00
		43	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) (NHAI) (N24001301)	11-2019	1/2024 (N.A.) {7/2024}	1,601.10 (N.A.) {1,601.10}	1,386.24	88.50
		44	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU- GONDIGUDA SECT (MoRTH) (N24001386)	8-2020	3/2021 (N.A.) {6/2025}	222.61 (N.A.) {222.61}	120.46	95.00
		45	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI (NHAI) (N24001476)	9-2021	9/2022 (9/2024) {6/2025}	517.05 (N.A.) {655.06}	515.30	90.14

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		46	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP (NHAI) (N24001477)	9-2021	9/2022 (9/2024) {6/2025}	622.00 (N.A.) {817.91}	533.42	73.89
		47	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16 (NHAI) (N24001817)	2-2019	3/2023 (10/2024) {10/2024}	757.45 (N.A.) {757.45}	607.76	99.41
		48	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG- IV) (NHAI) (N24001818)	2-2021	1/2025 (N.A.) {1/2025}	818.73 (N.A.) {1,105.00}	556.95	24.23
		49	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) (NHAI) (N24001819)	3-2021	1/2025 (N.A.) {1/2025}	1,102.63 (N.A.) {1,303.00}	1,082.99	91.81
		50	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG- I) (NHAI) (N24001820)	2-2021	12/2024 (N.A.) {12/2024}	1,484.83 (N.A.) {1,768.00}	1,493.57	87.50
		51	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP (NHAI) (N24001821)	11-2020	10/2024 (N.A.) {10/2024}	1,137.74 (N.A.) {1,289.00}	1,256.44	94.60
		52	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE (NHAI) (N24001822)	12-2020	10/2024 (N.A.) {10/2024}	1,075.27 (N.A.) {1,307.00}	1,092.90	81.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		53	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A (NHA/) (N24001823)	1-2022	1/2025 (1/2023) {1/2025}	1,852.12 (N.A.) {1,787.00}	774.62	86.00
		54	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP (NHA/) (N24001824)	3-2020	1/2024 (12/2024) {12/2024}	1,863.09 (N.A.) {2,238.00}	1,227.61	98.76
		55	6L KANTAKAPALLE ? SABBAVARAM SECTION OF NH- 130CD ROAD FROM KM 445.100 TO KM 464.662 (PKG-4) (NHA/) (N24001836)	2-2021	10/2024 (N.A.) {3/2026}	824.29 (N.A.) {924.00}	424.23	70.20
		56	6L JAKKUVA ? KORLAM SECTION OF NH-130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) (NHA/) (N24001837)	2-2021	3/2024 (7/2024) {12/2025}	663.60 (N.A.) {768.00}	380.88	98.80
		57	6L ALURU - JAKKUVA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) (NHA/) (N24001838)	2-2021	3/2024 (N.A.) {9/2025}	922.50 (N.A.) {1,128.68}	473.80	82.92
		58	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA (NHA/) (N24001841)	12-2022	9/2025 (N.A.) {2/2026}	912.94 (N.A.) {912.94}	238.71	54.23
		59	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 (NHA/) (N24001842)	12-2022	11/2025 (N.A.) {11/2025}	750.81 (N.A.) {750.81}	145.15	45.65

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		60	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH (NHAI) (N24001843)	12-2022	11/2025 (N.A.) {11/2025}	992.89 (N.A.) {992.89}	163.14	42.06
		61	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. (NHAI) (N24001844)	12-2022	10/2025 (N.A.) {10/2025}	1,058.90 (N.A.) {1,058.90}	249.94	42.47
		62	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 (NHAI) (N24001845)	2-2023	10/2025 (N.A.) {10/2025}	1,253.24 (N.A.) {1,253.24}	156.15	16.50
		63	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. (NHAI) (N24001846)	2-2023	10/2025 (N.A.) {10/2025}	1,200.42 (N.A.) {1,200.42}	57.99	5.20
		64	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA (NHAI) (N24001847)	1-2023	11/2025 (N.A.) {11/2025}	956.14 (N.A.) {956.14}	176.30	35.54
		65	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTALA 196.000 KM. PACK (NHAI) (N24001848)	2-2023	10/2025 (N.A.) {10/2025}	909.02 (N.A.) {909.02}	128.01	13.20
		66	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 (NHAI) (N24001849)	5-2022	7/2025 (N.A.) {9/2025}	1,063.72 (N.A.) {1,063.72}	458.56	72.29

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		67	CONSTRUCTION OF 4-LANE HIGHWAY FROM SAMARLAKOTA TO ACHAMPETA JUNCTION (FROM KM. 0.000 TO KM. 12.250 (NHAI) (N24001856)	5-2023	8/2025 (N.A.) {8/2025}	648.75 (N.A.) {648.75}	223.27	54.13
		68	2L+PS FROM KM. 0+000 TO KM. 32+000 (MUDIGUBBA TO PUTTAPARTHI) OF NH-342 (MoRTH) (N24001932)	3-2022	9/2024 (N.A.) {6/2025}	401.72 (N.A.) {401.72}	139.07	80.00
		69	NH440 RAYACHOTY TOVEMPALLI 2LPS (MoRTH) (N24001934)	12-2021	5/2024 (N.A.) {7/2025}	439.82 (N.A.) {439.82}	119.72	27.00
		70	4 LANE WITH PAVED SHOULDER FROM KM 0.000 TO KM 51.119 OF TADIPATRI TO MUDDANUR OF NH67 (MoRTH) (N24001935)	3-2022	8/2025 (N.A.) {8/2025}	724.17 (N.A.) {724.17}	229.73	97.00
		71	NH165 FROM KM 0.000 TO KM 64.020 PAMARRU TO AKIVEEDU SECTION TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001939)	3-2020	9/2023 (N.A.) {12/2025}	529.24 (N.A.) {529.24}	224.81	52.00
		72	2LPS FROM KM36.400 TO KM. 107.224 OF NH167BG FROM DUTTALUR TO KAVALI SECTION (MoRTH) (N24001942)	3-2021	7/2024 (N.A.) {3/2025}	423.67 (N.A.) {423.67}	145.72	61.00
		73	NH167AD FROM MACHERLA TO DACHEPALLI FROM KM.0.000 TO 43.659 TO 2LPS (MoRTH) (N24001951)	1-2022	1/2025 (N.A.) {1/2025}	403.22 (N.A.) {403.22}	201.69	97.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		74	NH 167 B KADAPA NELLORE BORDER TO CSPURAM I.E. FROM KM 58.635 TO KM 99.409 (MoRTH) (N24001952)	3-2022	8/2025 (N.A.) {8/2025}	285.50 (N.A.) {285.50}	204.29	95.00
		75	NH-30-BHADRACHALAM TO KONTA SECTION 2LPS (MoRTH) (N24001953)	12-2021	9/2024 (N.A.) {3/2025}	388.71 (N.A.) {388.71}	159.29	80.00
		76	WIDENING TO 2LPS OF RAMPACHODAVARAM - KOYYURU SECTION OF NH516E FROM KM.43.700 TO KM 113.820 (MoRTH) (N24001954)	3-2022	1/2025 (N.A.) {1/2025}	568.12 (N.A.) {568.12}	215.09	91.50
		77	GUDIWADA TOWN 2 LANE ROB AND ROAD IMPROVEMENT OF NH165 IN REPLACEMENT OF LC NO 3ESPL3 AT KM 231.700 (MoRTH) (N24001955)	3-2022	5/2025 (N.A.) {5/2025}	317.22 (N.A.) {317.22}	84.57	80.00
		78	2LPS FROM GONDIGUDA TO ARAKU BHALLAGUDA KM 27.480 TO KM 51.772 SECTION OF NH 516E (MoRTH) (N24001956)	8-2020	9/2023 (N.A.) {12/2024}	296.66 (N.A.) {296.66}	190.30	87.00
		79	2LPS OF KOYYURU TO CHAPRATHIPALEM SECTION OF NH 516E (MoRTH) (N24001957)	8-2020	7/2024 (N.A.) {6/2025}	349.29 (N.A.) {349.29}	114.53	76.00
		80	2LPS OF CHAPRATHIPALEM TO LAMBASINGI SECTION OF NH 516E (MoRTH) (N24001958)	8-2020	10/2024 (N.A.) {6/2025}	311.22 (N.A.) {311.22}	85.45	72.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		81	4 LANE FROM KM 56.400 TO KM 120.300 FROM B.KOTHAPALLI JUNCTION TO GORANTLA OF NH 716G (MoRTH) (N24001959)	3-2022	9/2025 (N.A.) {9/2025}	839.98 (N.A.) {839.98}	146.12	67.00
		82	4L GREENFIELD ROAD CONNECTING NORTH AND SOUTH INDUSTRIAL CLUSTER OF KHANDALERU CREEK NEAR KRISHNAPAT (NHAI) (N24001979)	8-2022	9/2025 (N.A.) {9/2025}	609.43 (N.A.) {609.43}	25.24	48.80
		83	4 LANING OF NH 544D FROM EXISTING KM 346.300 OF NH 44 (DESIGN CHAINAGE KM 0.000) TO KM 39.380 (DESIG (NHAI) (N24001980)	10-2022	7/2025 (N.A.) {7/2025}	907.76 (N.A.) {907.76}	387.99	81.07
		84	CONSTRUCTION OF SIX LANING OF NAIDUPETA JUNCTION - TURPUKANUPUR SECTION FROM KM.57+046 TO KM.91+927 (NHAI) (N24001981)	7-2022	10/2025 (N.A.) {10/2025}	1,398.84 (N.A.) {1,398.84}	58.68	13.52
		85	4L PS FROM KURNOOL (EXISTING KM. 5.400 OF NH-40/DESIGN KM.0.000) TO MANDLEM (EXISTING KM.38.000/DESIG (NHAI) (N24001982)	3-2023	10/2025 (N.A.) {10/2025}	827.39 (N.A.) {827.39}	332.64	99.15
		86	4 LANING FROM EXISTING KM 39.380 (DESIGN CH. 37.000) TO KM 74.450 (DESIGN CH. 69.000) OF MUCHUKOTA ? (NHAI) (N24001983)	10-2022	8/2025 (N.A.) {8/2025}	972.63 (N.A.) {1,055.23}	309.39	50.90
		87	4L PS FROM MANDLEM (EXISTING KM. 38.000/DESIGN KM.30.600) TO ATMAKUR (EXISTING KM.73.000/DESIGN KM 6 (NHAI) (N24001984)	3-2023	10/2025 (N.A.) {10/2025}	887.28 (N.A.) {887.28}	263.47	78.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		88	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-II) FROM KM.96.000 TO KM 127.000 (BAIREDDYPALLE TO BANGAR (NHAI) (N24001985)	3-2021	6/2025 (N.A.) {6/2025}	1,942.94 (2,171.00) {2,171.00}	1,569.61	60.50
		89	4L OF PILERU TO KALUR SECTION FROM KM 55.900 TO KM 92.800 AND KM 94.500 TO KM 95.717 (NHAI) (N24001986)	10-2023	4/2025 (N.A.) {4/2025}	1,047.32 (N.A.) {1,047.32}	301.20	82.50
		90	CONSTRUCTION OF 1 NOS ROB, 2 NOS VUPS, SERVICE ROADS, PROVISION OF LIGHTING AND CONSTRUCTION OF OTHE (NHAI) (N24001987)	6-2023	12/2024 (N.A.) {12/2024}	152.05 (N.A.) {152.05}	133.08	76.62
		91	6L OF CHITTOOR TO THATCHUR FROM KUMARAJAPET TO VEERA KAVERI RAJA PURAM FROM KM 43.800 TO KM 61.380 O (NHAI) (N24001988)	2-2021	10/2025 (N.A.) {10/2025}	591.99 (703.00) {703.00}	496.65	60.16
		92	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED HIGHWAY FROM CHILLAKURU CROSS ROAD TO TURPUKANUPUR KM 0+000 (NHAI) (N24002033)	7-2022	12/2025 (N.A.) {12/2025}	909.47 (N.A.) {909.47}	97.03	26.90
		93	COMPLETION OF BALANCE WORKS PENDING IN BIT AND PIECES (INCOMPLETE STRETCH AT 7 LOCATIONS) AND LISTED (NHAI) (N24002103)	9-2022	1/2025 (N.A.) {4/2025}	166.52 (N.A.) {166.52}	52.79	93.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		94	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NARAYANMPET (CH. 203+500) TO CHANDRASEKHARPURAM (CH. 22 (NHA) (N24002122)	2-2024	2/2026 (N.A.) {2/2026}	813.66 (N.A.) {813.66}	91.47	21.19
		95	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM CHANDRASEKHARAPURAM (CH. 228+000) TO POLAVARAM (CH. 260 (NHA) (N24002123)	2-2024	2/2026 (N.A.) {2/2026}	1,292.65 (N.A.) {1,292.65}	135.06	13.10
		96	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM POLAVARAM (CH. 260+000) TO MARRIPUDI (CH. 285+500) OF [(NHA) (N24002124)	2-2024	2/2026 (N.A.) {2/2026}	747.29 (N.A.) {747.29}	118.30	28.10
		97	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MARRIPUDI (CH. 285+500) TO SOMAVARAPPADU (CH. 314+600) (NHA) (N24002125)	2-2024	2/2026 (N.A.) {2/2026}	976.40 (N.A.) {976.40}	197.02	37.90
		98	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM SOMAVARAPPADU (CH.314.600) TO MUPPAVARAM (CH.343+240) O (NHA) (N24002126)	2-2024	2/2026 (N.A.) {2/2026}	1,103.89 (N.A.) {1,103.89}	133.52	12.04
		99	4-LANE WITH PAVED SHOULDERS FROM KM 32/0 TO KM 79/650 (DESIGN CHAINAGE KM 32+000 TO KM 78+760) PUTTA (MoRTH) (N24002139)	3-2023	12/2025 (N.A.) {11/2025}	1,318.57 (N.A.) {1,318.57}	201.00	56.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		100	SOMAYAJULAPALLI ? DHONE SECTION OF NH ? 340B FROM KM.0/0 TO 56/200 [DESIGN CH. KM 0/00 TO KM 53/33] (MoRTH) (N24002140)	4-2023	12/2025 (N.A.) {12/2025}	629.73 (N.A.) {629.73}	103.00	62.00
		101	2-LANE WITH PAVED SHOULDER CONFIGURATION OF LAMBASINGI TO PADERU SECTION (KM 205+000 TO KM 253+974) (MoRTH) (N24002142)	8-2023	11/2025 (N.A.) {11/2025}	361.24 (N.A.) {361.24}	7.00	26.00
		102	BYPASS ROAD TO ADONI TOWN CONNECTING NH-167 (HAGARI - JADCHARLA ROAD) FROM KM.62/700 TO 71/400 IN KU (MoRTH) (N24002143)	8-2023	2/2026 (N.A.) {2/2026}	361.24 (N.A.) {361.24}	109.65	56.00
		103	VODAREVU-CHILAKALURIPET SECTION (DESIGN CHAINAGE 0+00 TO 47+000) OF NH-167A (PACKAGE-I) (MoRTH) (N24002144)	8-2023	2/2026 (N.A.) {2/2026}	1,064.24 (N.A.) {1,064.24}	80.00	60.00
		104	TADIPATRI BYPASS (KM 0+000 TO KM 6+285) OF 4-LANE ON NH- 67 IN ANANTAPURAMU (MoRTH) (N24002145)	11-2023	3/2026 (N.A.) {3/2026}	159.66 (N.A.) {159.66}	11.95	63.50
		105	KURNOOL/KADAPA BORDER- JAMMALAMADUGU SECTION OF NH-167K I.E. DESIGN CH. KM 248+010 TO KM 269+900 (MoRTH) (N24002146)	11-2023	11/2025 (N.A.) {11/2025}	292.63 (N.A.) {292.63}	61.36	20.00
		106	DORNALA TO KUNTA JUNCTION FROM DESIGN CHAINAGE KM 244+000 TO 267+990 SECTION OF NH-765 (PACKAGE-2) (MoRTH) (N24002147)	12-2022	1/2024 (N.A.) {3/2026}	244.83 (N.A.) {244.83}	104.32	74.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		107	PADERU BYPASS (KM 0+000 TO KM 13+000) OF 2- LANE WITH PAVED SHOULDER ON NH-516E (MoRTH) (N24002148)	3-2023	3/2024 (N.A.) {2/2026}	244.43 (N.A.) {244.43}	22.77	-
		108	DAVUALAPALLY TO MALLAPALEM SECTION {DESIGN CH. KM 133+922 TO KM 154+216 (EXISTING CH. KM 133+922 TO (MoRTH) (N24002149)	1-2024	2/2024 (N.A.) {2/2026}	393.61 (N.A.) {393.61}	40.00	24.00
		109	DEVELOPMENT OF SIX LANE ACCESS CONTROLLED GREEN FIELD HIGHWAY FROM KAVULAKUNTALA (KM.196+000) TO NARA (NHAI) (N24002215)	2-2023	2/2027 (N.A.) {2/2027}	1,092.18 (N.A.) {1,092.18}	0.14	-
		110	ACCESS CONTROLLED HIGHWAY OF 4 LANE WITH PAVED SHOULDERS FROM TN/AP BORDER (DESIGN CHAINAGE KM 61+51 (NHAI) (N24002217)	12-2024	12/2026 (N.A.) {12/2026}	1,346.82 (N.A.) {1,346.82}	0.00	5.64
	<u>WATER RESOURCES</u>	111	POLAVARAM IRRIGATION PROJECT (PPA) (N30000002)	2-2009	3/2020 (3/2027) {12/2027}	10,151.04 (N.A.) {55,548.87}	23,775.68	75.68
<u>ARUNACHAL PRADESH</u>	<u>CIVIL AVIATION</u>	112	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (5/2025) {5/2025}	645.63 (N.A.) {732.00}	690.39	99.50
	<u>POWER</u>	113	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	24,022.52	96.20

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	114	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	3,222.41	14.70
		115	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (3/2024) {3/2025}	180.57 (244.10) {180.57}	160.46	96.62
		116	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (6/2025) {12/2025}	1,718.59 (1,718.59) {1,718.59}	728.21	73.20
		117	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (5/2023) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59
		118	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (2/2025) {2/2025}	301.06 (N.A.) {301.06}	191.34	81.06
		119	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	389.68	95.28
		120	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH- 415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	179.53	41.94

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		121	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (8/2024) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		122	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8-2020	4/2022 (2/2024) {9/2024}	294.04 (N.A.) {294.04}	147.13	100.00
		123	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (2/2024) {4/2025}	184.88 (N.A.) {184.88}	99.32	97.42
		124	HUNLI TO HAYULIANG PKG-1 (NHIDCL) (N24002222)	2-2024	2/2028 (N.A.) {2/2028}	1,262.43 (N.A.) {1,262.43}	0.00	0.75
		125	HUNLI TO ITHUN BRIDGE SECTION (NHIDCL) (N24002223)	2-2024	1/2027 (N.A.) {1/2027}	275.50 (N.A.) {275.50}	0.00	1.20
		126	PANGO TO JORGING ROAD PKG- 1 (NHIDCL) (N24002224)	1-2024	7/2027 (N.A.) {7/2027}	898.19 (N.A.) {898.19}	7.08	1.97
ASSAM	CIVIL AVIATION	127	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (8/2025) {8/2025}	1,142.00 (N.A.) {2,333.00}	1,850.93	86.95
	COAL	128	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290)	7-2022	11/2030 (N.A.) {11/2030}	159.77 (N.A.) {159.77}	81.45	-
		129	TIRAP OCP (CIL) (N06000291)	11-2022	11/2027 (N.A.) {11/2027}	289.46 (N.A.) {289.46}	105.59	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	HEALTH AND FAMILY WELFARE	130	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (4/2023) {11/2024}	875.00 (873.92) {860.00}	787.90	99.40
	PETROLEUM	131	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (12/2024) {6/2025}	543.91 (726.93) {726.93}	491.56	93.89
		132	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINERY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	15,412.49	73.06
		133	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	9,247.50	84.53
		134	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (5/2026) {5/2026}	412.00 (595.20) {595.20}	399.81	82.50
		135	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (9/2026) {9/2026}	277.00 (N.A.) {277.00}	175.69	66.02
		136	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (4/2025) {7/2025}	860.00 (N.A.) {860.00}	535.46	96.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		137	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (3/2024) {6/2025}	430.76 (N.A.) {430.76}	308.90	83.56
		138	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	80.34	31.40
		139	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (7/2027) {7/2027}	156.36 (156.36) {156.36}	38.92	28.50
		140	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (7/2027) {7/2027}	384.04 (N.A.) {384.04}	87.82	30.70
		141	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	97.22	90.00
		142	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	250.17	55.20
		143	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	169.95	44.10
		144	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	99.52	20.10

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	145	BONGAIGAON-GOALPARA- GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2026 (N.A.) {3/2027}	4,059.65 (N.A.) {4,983.94}	3,626.20	92.31
	ROAD TRANSPORT AND HIGHWAYS	146	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {5/2025}	437.39 (N.A.) {437.39}	547.95	96.13
		147	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	490.44	75.52
		148	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1-1991	6/2019 (6/2019) {6/2025}	520.01 (N.A.) {520.01}	305.76	97.70
		149	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (7/2021) {12/2025}	289.99 (N.A.) {289.99}	233.23	88.03
		150	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {5/2025}	294.17 (N.A.) {294.17}	381.37	97.63
		151	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {5/2025}	252.00 (N.A.) {330.30}	219.65	87.19

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		152	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	217.06	97.76
		153	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (1/2025) {6/2025}	216.49 (241.52) {216.49}	111.59	82.79
		154	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,382.39	60.80
		155	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (5/2025) {12/2025}	261.13 (N.A.) {261.13}	68.75	57.42
		156	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (4/2025) {12/2025}	217.50 (N.A.) {217.50}	88.99	68.03
		157	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.76	100.00
		158	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	147.96	75.89
		159	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (1,019.17) {925.47}	192.50	30.65

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		160	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	328.49	65.84
		161	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {5/2025}	625.64 (N.A.) {625.64}	550.60	100.00
		162	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {5/2025}	204.10 (N.A.) {204.10}	142.31	95.01
		163	FOUR LANING OF SRIRAMPUR- DHUBRI PKG-2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {6/2025}	909.02 (N.A.) {909.02}	509.89	97.63
		164	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (9/2024) {6/2024}	175.00 (N.A.) {175.00}	200.80	100.00
		165	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	567.75	76.40
		166	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {5/2025}	457.72 (N.A.) {457.72}	365.99	100.00
		167	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	110.75	35.63

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		168	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {7/2025}	458.59 (N.A.) {458.59}	196.51	61.42
		169	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	102.23	31.23
		170	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH- 137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	391.08	62.21
		171	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH- 137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	365.69	62.61
		172	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH- 137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	417.14	60.47
		173	WIDENING/IMPROVEMENT TO 4- LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	293.45	91.18
		174	WIDENING/IMPROVEMENT TO 4- LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	276.61	92.13

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		175	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	522.78	44.90
		176	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	303.94	24.50
		177	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	422.31	24.26
		178	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	236.11	72.87
		179	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	129.18	14.06
		180	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3-2023	12/2025 (N.A.) {12/2026}	643.42 (N.A.) {643.42}	69.47	8.89
		181	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.87	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		182	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	520.82	36.05
		183	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	983.58	63.52
		184	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	283.15	51.88
		185	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	380.59	61.10
		186	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	279.86	41.57
		187	WIDENING/IMPROVEMENT TO 4- LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	153.60	36.55
		188	BILASIPURA- GUWAHATI ROAD PKG-1 (NHIDCL) (N24002225)	2-2024	8/2027 (N.A.) {8/2027}	1,081.15 (N.A.) {1,081.15}	0.00	1.16
		189	SILCHAR-JIRIBAM PKG-1 (NHIDCL) (N24002226)	1-2024	1/2028 (N.A.) {1/2028}	957.95 (N.A.) {957.95}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		190	BILASIPURA- GUWAHATI ROAD PKG-2 (NHIDCL) (N24002229)	11-2023	6/2027 (N.A.) {6/2027}	1,338.61 (N.A.) {1,338.61}	0.50	-
		191	BADARPUR ? CHURABARI PKG-6 (NHIDCL) (N24002230)	3-2024	3/2027 (N.A.) {3/2027}	870.00 (N.A.) {870.00}	0.00	-
		192	KARIMGANI - SUTARKANDI SECTION ON SILCHAR- CHURABARI PKG-7 (NHIDCL) (N24002231)	2-2024	2/2027 (N.A.) {2/2027}	791.79 (N.A.) {791.79}	0.00	-
BIHAR	CIVIL AVIATION	193	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II (AAI) (N04000082)	5-2018	10/2022 (6/2025) {6/2025}	1,216.90 (N.A.) {1,216.90}	987.35	89.06
		194	DARBHANGA:DEVELOPMENT OF NEW CIVIL ENCLAVE AT DARBHANGA, BIHAR. SH- CONSTRUCTION OF NEW TERMINAL BUI (AAI) (N04000112)	7-2024	7/2026 (N.A.) {7/2026}	911.66 (N.A.) {911.66}	112.84	15.00
	DEPARTMENT OF HIGHER EDUCATION	195	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA (CPWD EDUCATION) (N28000100)	2-2016	6/2017 (N.A.) {1/2024}	496.18 (496.00) {460.00}	390.15	100.00
		196	PERMANENT CAMPUS FOR IIM BODH GAYA (CPWD EDUCATION) (N42000009)	9-2018	9/2020 (N.A.) {9/2020}	375.00 (N.A.) {375.00}	342.18	99.50
	PETROLEUM	197	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA (IOCL) (N16000386)	1-2020	4/2023 (8/2026) {8/2026}	14,810.00 (18,113.00) {18,113.00}	10,668.28	85.10

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		198	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA (IOCL) (N16000423)	6-2019	12/2029 (3/2030) {3/2030}	163.00 (N.A.) {163.00}	96.78	40.10
		199	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI (IOCL) (N16000453)	1-2022	4/2025 (N.A.) {5/2026}	389.00 (N.A.) {389.00}	37.55	30.90
		200	CITY GAS DISTRIBUTION PROJECTS AT GOPALGANJ SIWAN WEST CHAMPARAN EAST CHAMPARAN AND DEORIA DISTRICTS (BPCL) (N16000523)	12-2022	6/2030 (N.A.) {6/2030}	3,919.00 (N.A.) {3,919.00}	376.96	13.00
		201	CITY GAS DISTRIBUTION PROJECTS AT DARBHANGA, MADHUBANI, SUPAUL, SITAMARHI AND SHEOHAR DISTRICTS (BPCL) (N16000524)	12-2022	3/2030 (N.A.) {3/2030}	3,638.00 (N.A.) {3,638.00}	376.61	19.00
	POWER	202	BARH STPP(3X660MW) NTPC (NTPC) (180100242)	2-2005	10/2011 (7/2023) {3/2025}	8,692.97 (21,312.11) {21,312.11}	22,290.14	95.00
		203	BUXAR THERMAL POWER PLANT (1320 MW) (SJVN) (N18000194)	3-2019	1/2024 (N.A.) {9/2025}	10,439.09 (N.A.) {14,390.09}	11,451.47	89.95
	RAILWAYS	204	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) (ECR) (220100257)	4-1997	12/2024 (N.A.) {3/2027}	614.45 (614.45) {614.45}	474.57	52.00
		205	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR (ECR) (220100303)	4-2003	12/2014 (N.A.) {12/2026}	2,066.78 (2,087.36) {2,087.36}	2,294.71	73.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		206	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR (NFR) (N22000087)	9-2006	12/2024 (N.A.) {9/2025}	2,650.00 (2,132.03) {4,412.25}	3,787.25	90.00
		207	SAKRI-HASANPUR ROAD (NL) (ECR) (N22000171)	4-1999	(N.A.) {3/2027}	325.00 (735.20) {735.20}	602.01	78.00
		208	ARARIA-SUPAUL (NL) (ECR) (N22000177)	4-2008	3/2024 (N.A.) {5/2025}	1,605.17 (1,605.17) {1,605.17}	1,654.14	65.00
		209	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC (ECR) (N22000181)	4-2009	3/2022 (N.A.) {3/2026}	819.00 (548.00) {783.83}	544.31	75.00
		210	SAMASTIPUR-DARBANGHA (ECR) (N22000329)	5-2015	3/2025 (N.A.) {10/2025}	519.33 (519.33) {519.33}	626.71	80.00
		211	KIUL - GAYA DOUBLING PROJECT (ECR) (N22000349)	12-2015	9/2024 (N.A.) {2/2025}	2,462.11 (1,200.20) {1,771.07}	1,833.59	99.00
		212	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE (ECR) (N22000350)	12-2015	12/2024 (N.A.) {12/2025}	2,373.64 (1,491.47) {1,600.00}	1,763.21	77.00
		213	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM (ECR) (N22000472)	4-2016	12/2024 (N.A.) {6/2025}	1,215.54 (1,215.54) {1,215.54}	1,556.04	90.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		214	MUZAFFARPUR SAGALI DOUBLING 100.60 KM (ECR) (N22000473)	4-2016	6/2024 (N.A.) {5/2025}	1,586.22 (1,185.73) {1,300.00}	1,470.35	96.00
		215	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, (ECR) (N22000476)	4-1991	3/2023 (N.A.) {5/2025}	1,473.30 (803.09) {2,722.16}	2,764.98	90.00
		216	DARBHANGA - BYPASS LINE CONNECTING SHISHO HALT AND KAKARGHATI EXCL DARBHANGA YARD (7.64 KM) (ECR) (N22000523)	6-2019	6/2025 (N.A.) {10/2024}	983.62 (253.23) {415.00}	417.57	100.00
		217	BARAUNI- BACHWARA 3RD AND 4TH LINE (ECR) (N22000524)	7-2022	7/2027 (N.A.) {12/2025}	486.00 (N.A.) {486.00}	123.91	33.00
		218	JHAJHA - BATIA (UMBRELLA WORK PB#23/2018-19/NR) (ECR) (N22000526)	2-2019	6/2028 (N.A.) {12/2026}	496.47 (N.A.) {496.47}	22.53	-
		219	SONENAGAR BYE PASS LINE FROM CHIRALAPOTHU TO BAGHA BISHUNPUR (ECR) (N22000528)	10-2022	10/2027 (N.A.) {12/2026}	234.00 (223.69) {223.69}	22.57	-
		220	KATIHAR-KUMEDPUR AND KATIHAR-MUKURIA (64.5 KM) (UMBRELLA WORK PB#57/2019- 20/NR) (NFR) (N22000570)	8-2022	8/2027 (N.A.) {8/2026}	745.00 (N.A.) {942.64}	280.10	25.00
		221	PATNA-MUZAFFARPUR (NHA) (N24000165)	8-2010	2/2013 (N.A.) {12/2024}	671.30 (N.A.) {671.30}	1,830.13	97.78
	ROAD TRANSPORT AND HIGHWAYS							

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		222	4-LANNING OF CHAPRA- HAJIPUR (NHAI) (N24000187)	1-2011	7/2013 (6/2025) {6/2025}	575.00 (N.A.) {575.00}	573.48	89.81
		223	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR (MoRTH) (N24000382)	1-2014	10/2019 (6/2025) {6/2025}	675.00 (N.A.) {780.77}	764.69	96.13
		224	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 (NHAI) (N24000480)	12-2015	4/2019 (3/2025) {7/2025}	1,041.10 (567.00) {639.58}	553.73	97.58
		225	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 (NHAI) (N24000507)	12-2015	12/2019 (N.A.) {12/2024}	1,167.45 (N.A.) {1,182.94}	735.99	96.00
		226	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 (MoRTH) (N24000531)	2-2016	11/2018 (N.A.) {5/2025}	319.68 (N.A.) {503.28}	453.00	98.80
		227	CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-I-KM 40.00 TO KM 65.400 AND K (MoRTH) (N24000576)	2-2016	5/2016 (N.A.) {5/2025}	178.85 (N.A.) {278.54}	232.61	98.35
		228	PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-III-KM 156.5 (MoRTH) (N24000578)	2-2016	5/2016 (N.A.) {5/2025}	553.30 (N.A.) {706.39}	712.38	98.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		229	FOUR LANING OF GAYA-HISUA- RAJGIRI-NALANDA- BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR (MoRTH) (N24000579)	1-2014	10/2016 (6/2025) {6/2025}	1,408.85 (N.A.) {2,138.16}	1,738.55	96.95
		230	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT- SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN (NHAI) (N24000665)	3-2017	3/2020 (12/2025) {12/2025}	672.89 (736.01) {830.31}	678.03	85.27
		231	SIX LANNING OF AUNTA- SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 (NHAI) (N24000696)	8-2017	2/2022 (10/2024) {5/2025}	950.64 (1,161.00) {1,168.33}	1,126.75	97.05
		232	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 (NHAI) (N24000714)	12-2017	10/2024 (4/2025) {12/2026}	2,598.00 (N.A.) {1,978.01}	1,381.14	76.76
		233	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I (NHAI) (N24000723)	1-2018	12/2021 (12/2024) {8/2025}	573.70 (644.50) {726.99}	492.33	81.84
		234	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER (NHAI) (N24000813)	3-2018	11/2021 (12/2024) {5/2025}	496.20 (470.18) {470.18}	399.41	98.25
		235	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND (MoRTH) (N24000943)	9-2018	6/2024 (5/2026) {5/2026}	1,478.40 (N.A.) {1,478.40}	941.27	69.88

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		236	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 (MoRTH) (N24001201)	2-2019	9/2024 (N.A.) {9/2026}	2,926.42 (N.A.) {2,926.42}	1,300.42	56.27
		237	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT (NHAI) (N24001303)	10-2013	12/2020 (12/2024) {12/2024}	649.90 (N.A.) {750.00}	711.53	98.30
		238	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE (NHAI) (N24001304)	10-2013	11/2020 (12/2024) {12/2024}	446.97 (598.48) {740.50}	638.80	96.30
		239	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA (NHAI) (N24001305)	10-2013	11/2020 (12/2024) {12/2024}	464.09 (605.53) {765.12}	698.25	97.30
		240	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N (NHAI) (N24001371)	10-2019	8/2023 (12/2025) {12/2025}	1,101.99 (N.A.) {1,101.99}	854.90	75.92
		241	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH-119D (PKG-III) (NHAI) (N24001697)	2-2023	2/2025 (N.A.) {12/2025}	1,358.00 (N.A.) {1,358.00}	183.47	13.51
		242	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH (NHAI) (N24001698)	8-2022	8/2024 (9/2025) {9/2025}	1,198.02 (N.A.) {1,198.02}	14.85	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		243	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT- GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH-3 (NHAI) (N24001699)	3-2022	12/2024 (N.A.) {12/2025}	312.58 (N.A.) {312.58}	189.18	78.29
		244	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO (NHAI) (N24001700)	12-2021	3/2024 (12/2024) {12/2024}	552.55 (553.00) {553.00}	414.79	74.39
		245	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU (NHAI) (N24001701)	4-2022	4/2024 (9/2025) {9/2025}	1,769.50 (N.A.) {1,769.50}	3.12	-
		246	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT- GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH: (NHAI) (N24001702)	12-2021	9/2024 (N.A.) {5/2025}	184.90 (185.00) {185.00}	163.01	97.42
		247	6 L OF AURANGABAD TO BIHAR- JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N (NHAI) (N24001703)	2-2022	5/2025 (N.A.) {5/2025}	786.81 (787.00) {787.00}	0.00	3.04
		248	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI (NHAI) (N24001704)	3-2021	3/2024 (9/2025) {9/2025}	1,020.84 (N.A.) {1,020.84}	120.84	-
		249	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C (NHAI) (N24001705)	3-2022	3/2024 (12/2025) {12/2025}	1,485.66 (N.A.) {1,485.66}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		250	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20 (NHAI) (N24001708)	9-2020	6/2024 (N.A.) {12/2024}	2,156.22 (N.A.) {2,156.22}	2,134.67	98.23
		251	BAKHTIYARPUR RAJAULI PKG-II FROM KM 54.405 TO KM 101.630 NH20 (NHAI) (N24001709)	9-2020	4/2023 (12/2024) {12/2024}	897.45 (N.A.) {1,090.00}	1,037.63	97.85
		252	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G (NHAI) (N24001711)	9-2020	3/2023 (12/2024) {12/2024}	939.43 (N.A.) {939.43}	370.62	100.00
		253	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO (NHAI) (N24001712)	8-2020	7/2023 (5/2025) {5/2025}	690.00 (N.A.) {690.00}	770.73	98.80
		254	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI?MOTIHARI- RAXAUL SECTION OF NH-28A FRO (NHAI) (N24001715)	12-2018	10/2020 (N.A.) {1/2024}	333.60 (466.59) {461.41}	460.38	100.00
		255	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH 122B FROM KM 29.730 TO KM 72.348 IN STATE OF BIH (MoRTH) (N24001870)	2-2022	11/2024 (N.A.) {11/2025}	624.43 (N.A.) {624.43}	280.98	82.00
		256	WIDENING AND STRENGTHENING FROM KM 70.15 TO KM 121.025 OF NH-80 (MoRTH) (N24001875)	3-2021	1/2025 (N.A.) {6/2025}	477.54 (N.A.) {477.54}	334.36	89.73

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		257	WIDENING and STRENGTHENING FROM KM132.895 TO KM 190.15 NH-80 (MoRTH) (N24001876)	3-2021	3/2024 (N.A.) {9/2025}	566.15 (N.A.) {566.15}	239.20	56.12
		258	CONSTRUCTION OF NEW 4- LANE BRIDGE (PARALLEL TO EXISTING VIKRAMASHILA SETU)FROM KM 8+920 TO KM 13+375 (MoRTH) (N24001877)	7-2020	5/2027 (N.A.) {5/2027}	1,110.23 (N.A.) {1,110.23}	425.49	40.12
		259	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH-319A FROM KM 0 TO KM 45 IN STATE OF BIHAR UNDER (MoRTH) (N24001878)	2-2022	12/2024 (N.A.) {7/2025}	427.29 (N.A.) {427.29}	197.04	78.00
		260	CONSTRUCTION OF PROPOSED 4 _LANE REVELGUNJ BYPASS NH- 19 IN THE STATE OF BIHAR ON EPC MODE CONNECTING (MoRTH) (N24001879)	3-2022	7/2025 (N.A.) {7/2025}	295.24 (N.A.) {295.24}	77.05	53.46
		261	CONSTRUCTION OF 6- LANE BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD (NH- (NHAI) (N24002062)	3-2023	9/2027 (N.A.) {9/2027}	3,012.27 (N.A.) {3,012.27}	215.85	8.10
		262	BALANCE WORK - WB-10 (GANDAK BRIDGE) KM 402.00 TO KM 440.00 (DEVANPUR - KOTWA) (NHAI) (N24002063)	12-2021	1/2024 (N.A.) {6/2025}	210.05 (N.A.) {210.05}	104.35	69.00
		263	PERMANENT RECTIFICATION OF 3 NOS. OF BLACK SPOTS IN PROJECT HIGHWAY NH-27 OF U.P BORDER - DEWAPUR - (NHAI) (N24002064)	12-2022	12/2025 (N.A.) {12/2025}	381.80 (N.A.) {381.80}	115.30	43.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		264	4L GREENFIELD ALIGNMENT OF AMAS TO SHIVRAMPUR FROM 0.000 KM. TO 55.002 KM. OF NH 119 D (PKG-I) (NHAI) (N24002065)	2-2022	3/2025 (N.A.) {3/2025}	1,390.92 (N.A.) {1,390.92}	150.71	20.76
		265	4L GREENFIELD ALIGNMENT OF SHIVRAMPUR TO RAMNAGAR FROM KM. 55.002 TO KM. 109.300 OF NH 119 D (PKG-I) (NHAI) (N24002066)	2-2022	7/2025 (N.A.) {7/2025}	1,494.31 (N.A.) {1,494.31}	38.28	4.59
		266	IMPROVEMENT OF 2 LANE WITH PAVED SHOULDER OF STRETCH FROM BIKRAMGANJ DAWATH MELAYABAGH NAWANAGR -DUM (MoRTH) (N24002133)	3-2021	3/2025 (N.A.) {6/2025}	178.63 (N.A.) {178.63}	116.16	90.61
		267	CONSTRUCTION OF 4 LANE ROB AND ITS APPROACHES AT THE LEVEL OF CROSSING (L C NO. 29-B) OF KM 29 (EKAN (MoRTH) (N24002193)	3-2023	7/2026 (N.A.) {7/2026}	201.08 (N.A.) {201.08}	23.73	24.00
		268	CONSTRUCTION OF 6-LANE ELEVATED / EXTRA DOSE CABLE BRIDGE ON RIVER GANGA PARALLEL TO AND WESTERN SID (MoRTH) (N24002194)	1-2024	11/2027 (N.A.) {11/2027}	3,064.45 (N.A.) {3,064.45}	78.87	2.40
		269	ESTIMATE FOR IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM RAMNAGAR TO ROSEDA FROM (KM 3.500 TO 4 (MoRTH) (N24002195)	1-2022	4/2026 (N.A.) {4/2026}	495.16 (N.A.) {495.16}	129.17	9.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		270	CONSTRUCTION OF BHABHUA BYPASS FROM CH. 10+800(DESIGN CH. 10+800) TO CH. 19+860 (DESIGN CH. 18+150) (MoRTH) (N24002196)	2-2022	3/2026 (N.A.) {7/2026}	179.86 (N.A.) {179.86}	25.07	0.03
		271	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM JUNCTION OF NH-22 NEAR HAJIPUR TO JUNCTION OF NH-12 (MoRTH) (N24002197)	2-2024	2/2026 (N.A.) {2/2026}	226.15 (N.A.) {226.15}	9.77	13.00
		272	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF BH/WBBORDER-AMDABAD- MANIHARI SECTION FROM DESIGN KM (MoRTH) (N24002198)	1-2022	3/2026 (N.A.) {3/2026}	353.27 (N.A.) {353.27}	25.33	-
		273	PERMANENT RECTIFICATION OF 4 NOS. OF BLACKSPOTS ON NH 27 OF KOTWA MEHSI MUZAFFARPUR SECTION FROM (NHAI) (N24002220)	12-2022	11/2026 (N.A.) {11/2026}	410.75 (N.A.) {410.75}	34.83	21.04
		274	4L OF GREENFIELD ALIGNMENT FROM KM. 47.000 TO KM. 89.210 OF BALBHADARPUR TO BELA NAWDA SECTION OF NH (NHAI) (N24002221)	2-2022	3/2026 (N.A.) {3/2026}	2,185.75 (N.A.) {2,185.75}	513.47	10.57
	URBAN DEVELOPMENT	275	PATNA METRO RAIL CORPORATION LIMITED (PATNA METRO RAI) (N28000148)	2-2019	6/2024 (N.A.) {9/2024}	13,365.77 (N.A.) {13,925.50}	3,158.18	44.03
	WATER RESOURCES	276	SEWER NETWORK SPS AND STP BEGUSARAI (BUIDCO) (N30000026)	3-2018	7/2021 (12/2019) {4/2025}	230.06 (N.A.) {230.06}	261.47	97.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		277	I AND D AND STP WORKS FOR BHAGALPUR (BUIDCO) (N30000027)	10-2017	9/2020 (11/2020) {4/2025}	254.13 (413.29) {413.29}	123.10	90.00
		278	SEWER NETWORKS SPS AND STP HAJIPUR (BUIDCO) (N30000035)	3-2018	8/2021 (3/2018) {6/2025}	305.19 (N.A.) {305.19}	346.46	95.00
		279	SEWER NETWORKS, SPS AND STP, MUNGER (BUIDCO) (N30000036)	3-2018	10/2021 (3/2018) {6/2024}	294.02 (350.79) {522.85}	428.70	100.00
		280	SAIDPUR SEWER NETWORK PATNA (BUIDCO) (N30000039)	4-2015	1/2021 (N.A.) {6/2022}	268.63 (N.A.) {493.85}	491.13	100.00
		281	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK (BUIDCO) (N30000044)	3-2017	5/2021 (3/2017) {2/2023}	277.42 (253.98) {277.42}	355.31	100.00
		282	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA (BUIDCO) (N30000050)	8-2017	6/2022 (N.A.) {12/2025}	578.89 (453.83) {578.89}	164.87	52.00
		283	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA (BUIDCO) (N30000051)	8-2017	6/2022 (N.A.) {12/2025}	824.00 (734.09) {824.00}	384.17	55.00
CHHATTISGARH	COAL	284	GEVRA EXPANSION OCP (SECL) (35-70) MTY (SECL) (060100093)	6-2010	3/2023 (3/2026) {3/2026}	11,816.40 (N.A.) {11,816.40}	6,584.29	77.20

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		285	PELMA OCP(15.00MTY) (SECL) (N06000045)	10-2022	3/2023 (N.A.) {3/2033}	1,624.59 (N.A.) {1,725.04}	15.52	17.00
		286	CHHAL OC SEAM -III (6.00 MTY) (SECL) (N06000104)	12-2013	3/2022 (6/2025) {6/2025}	610.63 (N.A.) {610.63}	576.41	85.00
		287	AMERA OC RCE (SECL) (N06000123)	2-2015	3/2018 (3/2026) {3/2026}	335.97 (N.A.) {335.97}	86.98	42.00
		288	AMGAON OPENCAST PROJECT RCE (SECL) (N06000135)	7-2015	3/2020 (3/2026) {3/2026}	316.10 (N.A.) {316.10}	188.33	71.00
		289	MAHAMAYA OPENCAST PROJECT (SECL) (N06000164)	5-2018	3/2026 (N.A.) {3/2026}	410.26 (N.A.) {410.26}	180.18	38.00
		290	JHIRIA WEST OPENCAST PROJECT (SECL) (N06000166)	1-2024	3/2029 (N.A.) {3/2029}	366.94 (N.A.) {366.94}	33.37	41.00
		291	BAROUD OC EXPANSION (3-10 MTY) (SECL) (N06000197)	8-2020	3/2029 (N.A.) {3/2029}	2,309.80 (N.A.) {2,309.80}	904.69	41.00
		292	JAMPALI OCP RCE (SECL) (N06000198)	5-2020	3/2024 (3/2025) {6/2025}	278.64 (N.A.) {278.64}	208.65	82.00
		293	PORDA CHIMTAPANI OCP (10 MTY) (SECL) (N06000199)	12-2020	3/2029 (N.A.) {3/2029}	2,310.12 (N.A.) {2,310.12}	46.52	10.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		294	DIPKA OC EXPANSION 40 MTY (SECL) (N06000200)	12-2020	3/2029 (N.A.) {3/2029}	5,241.40 (N.A.) {5,241.40}	2,800.26	37.30
		295	JAGANNATHPUR OC RCE (3.0 MTY) (SECL) (N06000232)	7-2016	3/2020 (3/2026) {3/2026}	459.49 (N.A.) {459.49}	263.63	92.00
		296	KATKONA RO UG PROJECT (1.74 MTY) (SECL) (N06000274)	1-2023	3/2029 (N.A.) {3/2029}	329.22 (N.A.) {329.22}	60.38	2.00
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	297	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. (CPWD EDUCATION) (N28000141)	3-2020	7/2022 (2/2024) {3/2024}	808.62 (879.22) {808.62}	640.70	100.00
	<u>POWER</u>	298	WESTERN REGION EXPANSION SCHEME XXV (PGCIL) (N18000350)	2-2023	11/2023 (N.A.) {6/2025}	385.84 (N.A.) {385.84}	258.71	91.00
		299	LARA SUPER THERMAL POWER PROJECT, STAGE-II (2X800 MW) (NTPC) (N18000381)	8-2023	6/2028 (N.A.) {6/2028}	15,530.00 (N.A.) {15,530.00}	1,636.45	6.50
	<u>RAILWAYS</u>	300	KIRANDUL - JAGDALPUR DOUBLING (ECOR) (N22000318)	12-2012	3/2020 (N.A.) {3/2024}	1,588.70 (N.A.) {1,553.11}	1,515.71	94.50
		301	JHARSUGUDA-BILASPUR 4TH LINE (SECR) (N22000484)	4-2015	10/2024 (12/2023) {12/2025}	2,140.34 (2,135.34) {2,135.34}	2,264.16	88.00
		302	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I (IRCON) (N22000489)	4-2013	9/2018 (N.A.) {3/2026}	3,055.00 (N.A.) {3,438.39}	3,112.73	92.60

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		303	Gauge conversion of Raipur(Kendri)- Dhamtari and Abhanpur-Rajim branch (67.20 km) (SECR) (N22000572)	7-2011	10/2024 (N.A.) {6/2025}	1,171.30 (N.A.) {1,171.30}	573.10	82.00
		304	NIPANIA-BHATAPRA (14.4 KM) 4TH LINE (PB#72/NR/2022-23) (SECR) (N22000573)	9-2022	12/2026 (N.A.) {12/2026}	170.49 (N.A.) {170.49}	0.13	2.00
		305	4TH LINE - BHATAPARA- HATHBAND (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000574)	12-2022	12/2026 (N.A.) {12/2026}	177.03 (N.A.) {177.03}	6.23	2.00
		306	4TH LINE - BHILAI-BHILAI NAGAR (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000575)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {177.34}	1.72	2.00
		307	4TH LINE - DADHAPARA-BELHA (9.2 KM) (PB#72/NR/2022-23) (SECR) (N22000576)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {169.06}	15.05	30.00
		308	4TH LINE - RAJNANDGAON- DONGARHGARH (31.2 KM) (PB#72/NR/2022-23) (SECR) (N22000577)	9-2022	9/2026 (N.A.) {9/2026}	328.34 (N.A.) {328.34}	13.35	20.00
		309	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (N22000579)	9-2022	9/2026 (N.A.) {9/2026}	167.64 (N.A.) {167.64}	0.00	-
		310	DOUBLING OF BORIDAND - AMBIKAPUR (SURAJPUR) (SECR) (N22000580)	6-2022	6/2030 (N.A.) {3/2027}	1,376.20 (1,242.94) {1,242.94}	158.88	12.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		311	DALLIRAJHARA - ROWGHAT (95 KM) {PART OF DALLIRAJHARA-JAGDALPUR (235 KM)} (RVNL) (N22000602)	3-2008	6/2025 (N.A.) {6/2025}	1,627.56 (N.A.) {1,627.56}	1,349.09	-
		312	CHIRIMIRI-NAGPUR HALT (SECR) (N22000616)	10-2018	6/2030 (N.A.) {6/2030}	241.00 (N.A.) {241.00}	0.00	-
	ROAD TRANSPORT AND HIGHWAYS	313	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 (MoRTH) (N24001217)	1-2016	8/2016 (N.A.) {6/2025}	497.14 (572.66) {572.66}	385.27	60.41
		314	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION (MoRTH) (N24001221)	1-2016	10/2016 (N.A.) {3/2025}	624.98 (N.A.) {731.50}	620.67	100.00
		315	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI (MoRTH) (N24001222)	3-2016	7/2016 (N.A.) {12/2025}	452.94 (N.A.) {435.61}	322.59	69.99
		316	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. (MoRTH) (N24001227)	3-2018	1/2019 (N.A.) {5/2025}	349.03 (N.A.) {349.03}	316.52	97.90
		317	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A (MoRTH) (N24001228)	11-2017	5/2019 (N.A.) {5/2025}	188.80 (N.A.) {188.80}	136.81	97.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		318	DEVELOPMENT OF SIX LANE SARGI-BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA (NHAI) (N24001588)	12-2021	1/2025 (N.A.) {9/2025}	1,470.73 (N.A.) {1,470.73}	646.79	76.62
		319	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA (NHAI) (N24001593)	11-2021	9/2024 (N.A.) {6/2025}	1,368.19 (N.A.) {1,368.19}	896.51	96.12
		320	4 LANE OF BILASPUR TO URG PROJECT (KM 0.00 TO KM 70.2) OF NH-130A (NHAI) (N24001611)	4-2020	3/2024 (N.A.) {9/2025}	1,855.59 (2,523.86) {2,523.86}	683.34	91.78
		321	UP GRADATION OF NH 930 SHERPAR TO KOHKA FROM KM 67.880 TO KM 114.860 TO TWO LANE WITH PAVED SHOULDER (MoRTH) (N24001917)	3-2020	5/2024 (N.A.) {6/2025}	278.97 (N.A.) {278.97}	206.61	87.05
		322	UP GRADATION OF NH 130C ABHANPUR TO PAUND FROM NK KM 0.000 TO KM. 40.380 TO TWO LANE WITH PAVED SHOU (MoRTH) (N24001919)	12-2020	9/2023 (2/2025) {6/2025}	193.16 (N.A.) {193.16}	103.83	80.71
		323	UPGRADATION OF NH 130A MUNGELI TO PONDII FROM NH KM. 51.600 TO KM. 77.870 KM. 80.970 TO 96.970 TO 2 (MoRTH) (N24001920)	3-2021	9/2024 (N.A.) {5/2025}	218.57 (N.A.) {218.57}	136.26	88.71
		324	DEVELOPMENT OF SIX LANE BASANWAHI-MARANGPURI OF NH 130 CD FROM KM.99+500 TO 124+661 UNDER RAIPUR VIS (NHAI) (N24002017)	3-2022	10/2025 (N.A.) {9/2026}	1,307.16 (N.A.) {1,307.16}	199.96	30.33

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		325	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 1 SECTION OF NH 53 FROM CH 0.000 TO CH 44.50 (NHAI) (N24002045)	6-2022	7/2025 (N.A.) {7/2025}	1,828.00 (N.A.) {1,828.00}	499.83	39.85
		326	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 2 SECTION OF NH 53 FROM CH 44+500 TO CH.92+230 I (NHAI) (N24002046)	6-2022	5/2025 (N.A.) {5/2025}	1,958.94 (1,959.00) {1,958.94}	659.49	35.58
	<u>STEEL</u>	327	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 (NMDC) (N12000124)	11-2015	6/2023 (7/2024) {12/2025}	2,907.00 (5,427.06) {5,427.06}	2,865.64	75.20
		328	SCREENING PLANT-III AT KIRANDUL (NMDC) (N12000127)	3-2021	8/2024 (N.A.) {1/2026}	2,092.97 (2,718.84) {2,718.84}	1,472.86	70.31
		329	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (NMDC) (N12000130)	7-2021	11/2024 (N.A.) {12/2025}	282.44 (349.75) {349.75}	218.55	78.00
		330	REPLACEMENT OF CONVERTER VESSELS, TRUNNION RINGS, SUPPORT SYSTEM AND INSTALLATION OF SECONDARY EMISS (SAIL) (N12000131)	10-2023	6/2026 (N.A.) {6/2026}	471.83 (N.A.) {471.83}	77.95	17.50
		331	REBUILDING OF COKE OVEN BATTERY NO.7 AND 8 OF BHILAI STEEL PLANT (SAIL) (N12000134)	11-2023	10/2025 (N.A.) {10/2025}	884.10 (N.A.) {884.10}	352.17	66.00
		332	REPLACEMENT OF HOT LEVELLER-1 OF PLATE MILL AT BHILAI STEEL PLANT (SAIL) (N12000137)	7-2024	7/2026 (N.A.) {7/2026}	198.62 (N.A.) {198.62}	0.00	4.55

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>URBAN DEVELOPMENT</u>	333	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV- 112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI (CPWD) (N28000149)	5-2019	9/2020 (10/2024) {10/2024}	299.97 (299.97) {299.97}	272.05	90.00
<u>DELHI</u>	<u>CIVIL AVIATION</u>	334	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR (AAI) (N04000076)	11-2016	4/2020 (4/2024) {4/2024}	303.80 (374.98) {351.21}	344.49	100.00
	<u>DPIIT</u>	335	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE (IICC FOR DPIIT) (N40000002)	11-2017	12/2019 (N.A.) {12/2019}	4,773.00 (N.A.) {5,401.00}	4,969.89	99.74
	<u>FINANCE</u>	336	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA (NPCC) (N07000001)	7-2018	4/2022 (N.A.) {4/2022}	228.50 (N.A.) {220.27}	176.28	85.00
	<u>HOME AFFAIRS</u>	337	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI (CPWD FOR MHA) (N28000071)	10-2013	10/2019 (N.A.) {9/2024}	1,219.21 (2,091.53) {2,091.53}	1,947.12	100.00
		338	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI (CPWD FOR MHA) (N45000002)	6-2019	7/2022 (N.A.) {9/2025}	277.35 (N.A.) {277.35}	107.00	63.00
	<u>RAILWAYS</u>	339	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE (NR) (N22000281)	4-2012	3/2023 (N.A.) {6/2026}	586.36 (N.A.) {699.00}	169.99	45.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	340	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR (NHA/) (N24001771)	6-2020	12/2024 (N.A.) {12/2024}	1,479.22 (N.A.) {1,479.22}	1,491.26	99.00
		341	6L ACCESS CONTROLLED HIGHWAY FROM DND MAHARANI BAGH JN. WITH JAIPUR PUSHTA ROAD OF NH 148NA FROM (NHA/) (N24001773)	5-2020	7/2024 (N.A.) {9/2025}	1,467.44 (N.A.) {1,942.89}	1,015.86	90.07
		342	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-)0.70 (NHA/) (N24001777)	7-2020	10/2023 (N.A.) {6/2025}	2,171.80 (N.A.) {2,171.80}	958.13	99.99
		343	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) (NHA/) (N24001779)	3-2018	9/2022 (N.A.) {6/2025}	2,507.00 (N.A.) {3,030.73}	1,155.70	94.27
		344	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O (NHA/) (N24001781)	1-2018	10/2021 (N.A.) {5/2025}	2,067.67 (N.A.) {2,160.00}	1,496.49	99.30
		345	DEVELOPMENT OF 6L UER II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM (NHA/) (N24001825)	7-2020	10/2023 (N.A.) {6/2025}	1,894.96 (N.A.) {1,894.96}	741.88	93.81
	TELECOMMUNI CATIONS	346	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT (CPWD FOR TELECO) (N28000115)	10-2014	3/2018 (N.A.) {10/2025}	248.20 (N.A.) {248.20}	236.27	98.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	URBAN DEVELOPMENT	347	DELHI MRTS PHASE-III (DMRC) (N28000056)	9-2011	3/2016 (8/2021) {8/2021}	38,585.00 (43,095.35) {40,180.91}	40,602.26	100.00
		348	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR (NBCC) (N28000105)	7-2016	(N.A.) {10/2024}	2,694.00 (N.A.) {2,694.00}	2,247.61	98.00
		349	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I (CPWD) (N28000128)	10-2016	7/2021 (N.A.) {6/2024}	1,180.00 (N.A.) {1,100.80}	36.69	2.00
		350	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I (CPWD) (N28000129)	10-2016	3/2022 (N.A.) {6/2024}	1,128.00 (N.A.) {1,128.00}	709.96	64.00
		351	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS (DMRC) (N28000135)	7-2019	3/2025 (N.A.) {3/2026}	24,948.65 (N.A.) {24,948.65}	15,744.30	64.58
		352	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI (CPWD) (N28000153)	1-2022	11/2024 (5/2025) {5/2025}	646.52 (N.A.) {646.52}	473.63	91.00
		353	REDEVELOPMENT OF GPRA AT NETAJI NAGAR NEW DELHI PACKAGE 2 (NBCC) (N28000156)	10-2016	3/2024 (6/2025) {3/2025}	1,536.72 (N.A.) {1,536.72}	481.85	-
	WATER RESOURCES	354	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD ? 10MG/L (DJB) (N30000014)	3-2017	12/2022 (N.A.) {3/2025}	665.78 (N.A.) {665.78}	782.51	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
GOA	CIVIL AVIATION	355	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. (AAI) (N04000095)	11-2017	9/2021 (6/2025) {6/2025}	255.69 (N.A.) {255.69}	119.89	84.00
	DEPARTMENT OF HIGHER EDUCATION	356	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. (CPWD EDUCATION) (N42000002)	5-2019	8/2021 (N.A.) {12/2024}	303.90 (N.A.) {390.40}	360.00	99.30
	ROAD TRANSPORT AND HIGHWAYS	357	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM. 508.000 TO KM. 513.150 INCLUDING APPROACHES ON N (MoRTH) (N24002181)	4-2023	4/2026 (N.A.) {4/2026}	641.46 (N.A.) {641.46}	0.00	-
GUJARAT	CIVIL AVIATION	358	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT (AAI) (N04000088)	1-2018	8/2022 (12/2024) {12/2024}	1,405.00 (N.A.) {1,405.00}	1,304.38	100.00
		359	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. (AAI) (N04000093)	8-2018	2/2021 (3/2025) {3/2025}	353.25 (N.A.) {353.25}	348.77	100.00
		360	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1. (AAI) (N04000099)	6-2022	12/2025 (N.A.) {12/2025}	1,305.00 (1,143.95) {1,143.95}	560.95	55.00
	PETROLEUM	361	REDEVELOPMENT OF SANTHAL FIELD (ONGC) (N16000279)	2-2017	3/2026 (N.A.) {3/2026}	1,162.56 (N.A.) {1,162.56}	1,156.20	93.60

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		362	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY (IOCL) (N16000382)	11-2019	5/2023 (3/2024) {5/2025}	5,251.00 (5,894.00) {5,894.00}	4,571.49	99.50
		363	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY (IOCL) (N16000409)	9-2020	8/2024 (12/2025) {12/2025}	18,936.00 (N.A.) {18,936.00}	10,618.86	81.10
		364	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM (IOCL) (N16000411)	10-2020	8/2023 (6/2025) {6/2025}	1,614.00 (N.A.) {1,614.00}	1,087.52	94.77
		365	REDEVELOPMENT OF LINCH FIELD (ONGC) (N16000428)	4-2021	3/2025 (N.A.) {7/2025}	631.03 (860.04) {860.04}	385.12	65.90
		366	REDEVELOPMENT OF SOBHASAN COMPLEX (ONGC) (N16000431)	8-2021	2/2026 (N.A.) {2/2026}	885.63 (1,286.67) {1,286.67}	547.42	69.40
		367	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD (ONGC) (N16000444)	1-2022	11/2024 (N.A.) {11/2025}	621.40 (N.A.) {621.40}	137.69	21.40
		368	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT (IOCL) (N16000454)	1-2022	9/2024 (N.A.) {5/2025}	328.00 (N.A.) {328.00}	74.19	44.50
		369	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT (ONGC) (N16000477)	5-2022	2/2025 (N.A.) {9/2025}	249.43 (N.A.) {249.43}	208.81	92.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		370	KALOL REDEVELOPMENT PROJECT (ONGC) (N16000481)	8-2022	3/2027 (N.A.) {3/2027}	1,487.41 (N.A.) {1,487.41}	926.54	60.00
		371	OLD PIPE LINE REPLACEMENT (OPRP) GROUP-A (ONGC) (N16000483)	7-2021	7/2025 (N.A.) {7/2025}	173.03 (N.A.) {169.84}	140.40	84.00
		372	REVAMPING OF SV STATIONS, GAS TERMINAL AND KRIBHCO TERMINAL (ONGC) (N16000514)	11-2022	8/2026 (N.A.) {8/2026}	837.34 (N.A.) {837.34}	163.26	42.10
	POWER	373	GUJARAT 200 MW (GUVNL TENDER) (NTPC) (N18000295)	1-2021	7/2022 (N.A.) {3/2026}	842.27 (N.A.) {842.27}	769.66	30.00
		374	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) (NTPC) (N18000296)	5-2021	9/2022 (N.A.) {4/2025}	674.92 (N.A.) {674.92}	572.53	91.00
		375	Bagodara Solar Power Project (SJVN) (N18000297)	5-2021	10/2022 (N.A.) {12/2025}	339.35 (N.A.) {339.35}	317.31	51.22
		376	DAYAPAR WIND ENERGY PROJECT 150MW (NTPC) (N18000319)	11-2021	5/2023 (N.A.) {5/2025}	937.80 (N.A.) {937.80}	798.89	98.00
		377	DAYAPAR WIND ENERGY PROJECT 200MW (NTPC) (N18000345)	7-2022	3/2025 (N.A.) {3/2026}	1,316.02 (N.A.) {1,316.02}	324.35	23.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		378	KHAVDA 1255MW SOLAR PROJECT (KHAVDA SOLAR PARK) (NTPC) (N18000346)	9-2022	9/2024 (N.A.) {6/2025}	7,179.54 (N.A.) {7,179.54}	4,714.20	61.00
		379	BHUJ SOLAR 300MW (TRANCHE- IV WIND SOLAR HYBRID) (NTPC) (N18000349)	11-2022	3/2024 (N.A.) {1/2026}	1,442.60 (N.A.) {1,442.60}	793.54	2.00
		380	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK (PGCIL) (N18000357)	3-2023	12/2024 (N.A.) {5/2025}	922.30 (N.A.) {922.30}	672.67	88.70
		381	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT (PGCIL) (N18000358)	3-2023	3/2025 (N.A.) {6/2025}	815.12 (N.A.) {815.12}	10.99	88.00
		382	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK (PGCIL) (N18000359)	3-2023	12/2024 (N.A.) {5/2025}	966.79 (N.A.) {966.79}	646.22	93.00
		383	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000360)	3-2023	3/2025 (N.A.) {9/2025}	1,167.55 (N.A.) {1,167.55}	712.14	83.70
		384	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000361)	3-2023	3/2025 (N.A.) {6/2025}	2,820.99 (N.A.) {2,820.99}	2,304.46	68.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		385	KHAVDA 1200MW (4X300MW) IN KHAVDA RE PARK (NTPC) (N18000365)	6-2023	12/2024 (N.A.) {2/2026}	6,283.81 (N.A.) {6,283.81}	1,731.91	16.00
		386	DAYAPAR WIND- III (HYBRID TRANCHE-V) (NTPC) (N18000366)	5-2023	1/2025 (N.A.) {12/2025}	1,095.01 (N.A.) {1,095.01}	345.08	-
		387	TS FOR EVACUATION OF POWER FROM POTENTIAL RE ZONE IN KHAVDA AREA OF GUJARAT UNDER PH-IV PART E3 (PGCIL) (N18000383)	7-2023	7/2025 (N.A.) {8/2025}	334.00 (N.A.) {334.00}	0.00	15.00
		388	TS FOR EVACUATION OF ADDITIONAL 7GW RE POWER FROM KHAVDA RE PARK UNDER PHASE-III PART B [VATAMAN TRA (PGCIL) (N18000384)	12-2023	12/2025 (N.A.) {6/2026}	3,752.00 (N.A.) {3,752.00}	797.02	12.00
		389	TS FOR EVACUATION OF POWER FROM 7GW REZ IN KHAVDA AREA UNDER PHASE-IV PART E2 (PGCIL) (N18000390)	5-2024	5/2026 (N.A.) {5/2026}	679.00 (N.A.) {679.00}	0.00	12.00
		390	AUGMENTATION OF TRANSFORMATION CAPACITY AT JAM KHAMBHALIYA PS [GIS] [SPV NAME POWERGRID JAM KHAMBHAL (PGCIL) (N18000398)	10-2024	7/2026 (N.A.) {7/2026}	329.00 (N.A.) {329.00}	0.00	1.00
		391	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000400)	10-2024	10/2026 (N.A.) {10/2026}	4,766.00 (N.A.) {4,766.00}	155.00	2.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		392	PROVISION OF DYNAMIC REACTIVE COMPENSATION AT KHAVDA POOLING STATION 1 [KPS1] AND KHAVDA POOLING STA (PGCIL) (N18000402)	11-2024	11/2026 (N.A.) {11/2026}	501.00 (N.A.) {501.00}	0.00	1.00
		393	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000405)	11-2024	5/2029 (N.A.) {5/2029}	24,819.00 (N.A.) {24,819.00}	1,340.00	1.00
		394	600 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000406)	4-2022	3/2026 (N.A.) {3/2026}	4,100.45 (N.A.) {4,100.45}	0.71	9.00
		395	AUGMENTATION OF TRANSFORMATION CAPACITY AT KPS2 & KPS2 (PGCIL) (N18000411)	3-2025	3/2027 (N.A.) {3/2027}	466.00 (N.A.) {466.00}	0.00	-
		396	AUGMENTATION OF BANASKANTHA (RAGHANESDA) PS (GIS) (PGCIL) (N18000412)	3-2025	3/2027 (N.A.) {3/2027}	172.00 (N.A.) {172.00}	0.00	-
	RAILWAYS	397	MIYAGAM-KARJAN-DABHOI- SAMLAYA (GC) (WR) (N22000142)	4-2011	3/2021 (10/2026) {10/2026}	844.10 (844.10) {844.10}	597.62	41.00
		398	ANAND GODHRA DOUBLING PROJECT 79 KMS (WR) (N22000504)	4-2017	12/2024 (2/2025) {2/2025}	692.26 (692.26) {692.26}	676.64	97.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		399	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS (WR) (N22000505)	4-2018	3/2024 (10/2024) {10/2024}	537.31 (537.31) {688.74}	844.55	100.00
		400	4TH LINE BETWEEN BAREJADI NANDEJ (GERATPUR)- SANAND (38.20 KM) (AHMEDABAD BYPASS). (WR) (N22000532)	2-2023	3/2027 (2/2027) {2/2027}	961.67 (961.67) {961.67}	108.78	16.00
		401	QUADRUPLING BETWEEN GANDHIDHAM - ADIPUR WITH Y CONNECTION AT ADIPUR FOR PROVIDING DIRECT ENTRY TOWAR (WR) (N22000533)	2-2023	12/2025 (12/2025) {12/2025}	152.44 (152.44) {152.44}	62.26	32.00
		402	RAJKOT-KANALUS (111.20 KM) (WR) (N22000535)	10-2021	10/2026 (3/2026) {3/2026}	1,080.58 (1,080.58) {1,080.58}	1,337.86	65.00
		403	HIMMATNAGAR-KHEDBRAHMA (54.83 KM) (WR) (N22000537)	6-2022	2/2030 (6/2025) {6/2025}	354.99 (482.42) {482.42}	834.53	84.00
		404	PETLAD-BHADRAN (22.5 KM) (WR) (N22000538)	5-2022	5/2030 (12/2025) {12/2025}	202.50 (307.12) {307.12}	80.49	8.00
		405	NADIAD-PETLAD (37.26 KM) (WR) (N22000539)	5-2022	6/2030 (N.A.) {12/2025}	335.34 (461.91) {461.91}	73.29	7.00
		406	SAMLAYA-TIMBA ROAD (53.53 KM) (WR) (N22000540)	2-2023	3/2030 (7/2026) {7/2026}	670.00 (670.17) {670.17}	89.31	12.00
		407	SAMNI-JAMBUSAR (24.08 KM) (WR) (N22000541)	5-2022	3/2030 (12/2025) {12/2025}	216.72 (349.93) {349.93}	86.23	25.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		408	VIJAPUR-AMBLIYASAN (41.53 KM) (WR) (N22000547)	5-2022	3/2030 (7/2025) {7/2025}	309.81 (415.38) {415.38}	565.62	85.00
		409	ADRAJ MOTI-VIAJAPUR (39.75 KM) (WR) (N22000548)	5-2022	5/2030 (7/2025) {5/2030}	296.54 (N.A.) {296.54}	20.09	65.00
		410	NEW BG LINE BETWEEN NALIYA-JAKHAU PORT (WR) (N22000550)	2-2023	1/2028 (9/2026) {9/2026}	410.46 (410.46) {410.46}	33.63	2.00
		411	NEW BG LINE INTERSECTION (5 NOS) BETWEEN GERATPUR-SANAND AND BOTAD-AHMEDABAD (16.51 KM) (PB29/NR/20) (WR) (N22000551)	10-2022	10/2027 (2/2027) {10/2027}	437.21 (N.A.) {437.21}	23.75	-
		412	TARANGA HILL ABU ROAD VIA AMBAJI NEW LINE (NWR) (N22000592)	7-2022	7/2030 (N.A.) {12/2026}	2,798.16 (N.A.) {2,798.16}	1,020.70	11.00
		413	JUNAGARH -VISAVADAR (42.28) KM (RVNL) (N22000600)	6-2022	9/2028 (N.A.) {12/2026}	493.00 (N.A.) {492.83}	0.00	-
		414	MODASA- SHAMLAJI NEW LINE (MM OF AHMEDABAD-HIMMATNAGAR-UDAIPUR (299.2 KM)) (WR) (N22000622)	9-2012	3/2027 (2/2026) {2/2026}	261.68 (261.68) {261.68}	649.60	55.00
	ROAD TRANSPORT AND HIGHWAYS	415	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. (NHAI) (N24000567)	5-2016	8/2019 (N.A.) {6/2024}	998.18 (N.A.) {998.18}	802.89	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		416	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST (NHAI) (N24000569)	5-2016	9/2019 (5/2024) {5/2025}	723.64 (N.A.) {723.64}	562.31	97.00
		417	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU (NHAI) (N24000570)	5-2016	8/2019 (N.A.) {3/2025}	763.08 (N.A.) {763.08}	520.19	99.54
		418	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 (NHAI) (N24000592)	7-2016	7/2020 (N.A.) {5/2025}	829.97 (N.A.) {829.97}	486.93	96.63
		419	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP- V(PKG VI)REG. (NHAI) (N24000649)	1-2017	12/2020 (10/2025) {10/2025}	1,251.11 (1,527.75) {1,527.75}	684.97	89.22
		420	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR (NHAI) (N24000834)	3-2018	10/2021 (5/2025) {7/2025}	1,161.39 (1,738.03) {1,404.00}	679.63	83.00
		421	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA (MoRTH) (N24000925)	10-2018	11/2020 (9/2024) {9/2024}	400.76 (394.44) {394.44}	287.04	87.00
		422	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT (MoRTH) (N24001427)	6-2020	4/2023 (9/2024) {9/2024}	166.21 (N.A.) {166.21}	97.12	93.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		423	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 (NHA) (N24001443)	5-2020	3/2024 (6/2025) {6/2025}	690.30 (929.95) {929.95}	828.47	93.27
		424	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION (NHA) (N24001444)	5-2020	1/2024 (6/2025) {6/2025}	882.00 (1,229.37) {1,229.37}	979.04	86.22
		425	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB (NHA) (N24001445)	5-2020	7/2023 (5/2025) {5/2025}	691.52 (903.85) {903.85}	872.33	98.75
		426	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG (NHA) (N24001446)	5-2020	12/2023 (5/2025) {5/2025}	894.00 (1,210.06) {1,210.06}	1,130.52	96.11
		427	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 (NHA) (N24001515)	9-2020	2/2024 (N.A.) {3/2026}	1,542.02 (N.A.) {1,542.02}	969.46	68.35
		428	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 (NHA) (N24001516)	9-2020	2/2024 (4/2025) {8/2025}	1,185.69 (N.A.) {1,185.69}	979.62	93.52
		429	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 (NHA) (N24001518)	11-2019	9/2023 (N.A.) {4/2025}	1,669.56 (N.A.) {1,669.56}	1,066.35	96.90

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		430	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 (NHAI) (N24001519)	9-2020	11/2023 (N.A.) {4/2025}	1,198.55 (N.A.) {1,198.55}	911.04	95.78
		431	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 (NHAI) (N24001520)	11-2019	5/2024 (N.A.) {6/2025}	1,604.06 (N.A.) {1,604.06}	1,241.40	95.73
		432	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT (NHAI) (N24001785)	3-2022	6/2025 (N.A.) {6/2025}	1,373.06 (1,085.00) {1,373.06}	594.59	83.06
		433	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU (NHAI) (N24001786)	3-2021	3/2024 (N.A.) {3/2026}	1,259.00 (2,652.24) {1,910.00}	278.29	34.08
		434	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU (NHAI) (N24001788)	7-2020	12/2023 (N.A.) {5/2025}	2,271.86 (3,372.97) {3,916.00}	1,101.59	98.10
		435	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA (NHAI) (N24001789)	7-2020	8/2023 (N.A.) {4/2025}	1,710.30 (2,665.08) {1,927.00}	891.83	90.56
		436	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH- 754K (AJ-RGBS-PACKAGE-3) (NHAI) (N24001790)	2-2020	8/2023 (12/2024) {12/2024}	752.30 (N.A.) {766.20}	452.13	98.14

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		437	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II) (NHAI) (N24001792)	3-2021	9/2022 (N.A.) {1/2025}	536.03 (N.A.) {536.03}	480.77	100.00
		438	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) (NHAI) (N24001793)	3-2021	9/2022 (N.A.) {5/2025}	485.75 (N.A.) {485.75}	393.88	99.36
		439	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH- 754K (AJ-RGBS-PACKAGE-4) (NHAI) (N24001794)	2-2020	3/2023 (12/2024) {12/2024}	778.15 (N.A.) {785.67}	547.22	99.70
		440	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE (NHAI) (N24001827)	3-2022	3/2023 (N.A.) {3/2025}	162.73 (N.A.) {162.73}	131.79	100.00
		441	UPGRADATION AND STRENGTHENING TO 2 LANE PS FROM KM 95/500 TO KM 129/775 OF NH 168 G IDAR BHILODA SA (MoRTH) (N24002014)	9-2022	12/2023 (12/2025) {12/2025}	237.28 (N.A.) {237.28}	0.34	-
		442	UPGRADATION TO 4L PS DIVIDED CARRIAGEWAY FROM PATAN (NEAR RAJPUR) TO GOJARIYA FROM KM 52.000 TO KM 1 (NHAI) (N24002034)	12-2021	3/2025 (N.A.) {3/2025}	1,181.34 (1,181.00) {1,181.34}	515.21	74.72
		443	WIDENING TO 6L OF EXISTING 4L JETPUR - GONDAL - RAJKOT SECTION FROM KM. 117.600 TO KM. 185.00 ON NH- (NHAI) (N24002035)	9-2023	9/2025 (N.A.) {9/2025}	2,070.44 (N.A.) {2,070.44}	740.96	20.77

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		444	UPGRADATION OF DHORAJI JAMKANDORNA KALAVAD SECTION OF NH 927D FROM DESIGN CHAINAGE KM 00 TO KM 58.11 (MoRTH) (N24002117)	10-2022	2/2024 (2/2026) {2/2026}	246.60 (291.00) {291.00}	27.57	15.00
		445	UPGRADATION TO TWO LANE WITH PAVED SHULDER CONFIGURATION FROM KM 00 TO 47 OF NH 351 MAHUA TO BADHA (MoRTH) (N24002118)	12-2022	2/2024 (8/2025) {8/2025}	173.06 (N.A.) {219.00}	0.15	-
		446	WORK OF DEVELOPMENT AND CONSTRUCTION OF ELEVATED CORRIDOR FROM KM 38/660 TO KM 42/690 (ISCON JUNCTION (MoRTH) (N24002182)	3-2023	3/2026 (N.A.) {3/2026}	530.20 (N.A.) {530.20}	0.00	-
		447	WIDENING 2 LANE TO 4-LANE FROM KM 92/320 TO KM 115/320 (VAV CHOKDI-SATLASANA TO TO VRUNDAVAN CHOKDI, (MoRTH) (N24002183)	3-2022	3/2026 (N.A.) {3/2026}	151.13 (N.A.) {171.00}	0.00	-
	URBAN DEVELOPMENT	448	AHMEDABAD METRO RAIL PROJECT PHASE 1 (AMR) (N28000122)	11-2014	12/2018 (N.A.) {8/2025}	10,773.00 (N.A.) {12,924.55}	12,462.07	99.88
		449	AHMEDABAD METRO RAIL PROJECT PHASE II (AMR) (N28000137)	3-2019	3/2024 (N.A.) {12/2025}	5,384.17 (N.A.) {5,384.17}	3,999.66	85.10
		450	SURAT METRO RAIL PROJECT (AMR) (N28000138)	3-2019	3/2024 (N.A.) {6/2026}	12,020.32 (N.A.) {12,020.32}	6,685.69	64.30

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
HARYANA	HEALTH AND FAMILY WELFARE	451	ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT MANETHI, HARYANA. (HITES) (N21000032)	3-2019	3/2023 (3/2026) {3/2026}	1,294.34 (1,294.34) {1,294.34}	244.20	19.00
	HOME AFFAIRS	452	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" (CPWD FOR MHA) (N28000147)	1-2020	10/2023 (3/2025) {6/2025}	166.98 (170.23) {170.23}	132.08	96.00
	PETROLEUM	453	R and D CAMPUS II AT FARIDABAD (IOCL) (N16000375)	6-2019	12/2022 (7/2025) {3/2026}	2,281.94 (3,219.94) {3,219.94}	1,697.83	62.60
		454	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA (IOCL) (N16000412)	2-2021	9/2024 (12/2025) {12/2025}	34,627.00 (38,231.00) {38,231.00}	19,698.88	85.20
		455	POLY BUTADIENE RUBBER PLANT AT PANIPAT (IOCL) (N16000458)	3-2022	3/2025 (6/2026) {6/2026}	1,459.00 (2,948.62) {2,948.62}	904.44	63.90
	RAILWAYS	456	DOUBLING BETWEEN BHIWANI- DOBH BAHALI (NWR) (N22000604)	2-2023	2/2028 (N.A.) {12/2025}	471.06 (N.A.) {471.06}	97.11	41.00
		457	DOUBLING BETWEEN REWARI- KATHUWAS (27.73 KM) (NWR) (N22000606)	2-2023	6/2027 (N.A.) {12/2025}	352.41 (N.A.) {352.41}	158.65	31.00
	ROAD TRANSPORT AND HIGHWAYS	458	CONSTRUCTION OF 4-LANE NH- 344P-PACKAGE-4 (FROM KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA (NHAI) (N24001532)	11-2021	11/2023 (1/2024) {8/2024}	694.00 (1,918.00) {1,500.00}	1,682.82	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		459	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR- KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP (NHAI) (N24001533)	11-2020	12/2023 (N.A.) {5/2025}	1,690.23 (N.A.) {2,010.17}	1,451.11	98.50
		460	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR- KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP (NHAI) (N24001534)	12-2020	1/2024 (4/2024) {5/2025}	1,334.04 (N.A.) {1,334.00}	1,044.27	99.00
		461	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 (NHAI) (N24001535)	7-2020	7/2022 (5/2024) {8/2025}	899.00 (1,882.46) {1,882.46}	1,123.98	97.10
		462	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI (NHAI) (N24001536)	7-2020	7/2022 (N.A.) {6/2025}	817.00 (1,605.00) {1,605.00}	1,026.56	99.90
		463	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F (NHAI) (N24001633)	12-2020	12/2023 (3/2024) {3/2025}	1,430.88 (1,813.91) {1,813.91}	1,122.45	99.90
		464	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO (NHAI) (N24001634)	1-2021	12/2023 (3/2024) {4/2025}	1,306.95 (1,564.14) {1,564.14}	942.66	99.97

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		465	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O (NHAI) (N24001635)	3-2022	2/2025 (N.A.) {2/2025}	1,269.50 (N.A.) {1,269.50}	233.00	51.00
		466	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K (NHAI) (N24001673)	3-2020	3/2023 (11/2024) {6/2025}	510.97 (N.A.) {510.97}	529.00	95.50
		467	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH-352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU (NHAI) (N24001774)	12-2020	11/2023 (N.A.) {6/2024}	1,524.03 (N.A.) {1,524.03}	1,092.97	64.79
		468	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH-11 AS A FEEDER ROUTE IN THE STATE (NHAI) (N24001775)	2-2020	1/2023 (12/2024) {12/2024}	808.31 (N.A.) {958.00}	915.12	100.00
		469	UPGRADATION OF EXISTING 4 LANE ISMAILABAD-AMBALA SECTION (KM. 0+000 TO KM 42+500) (PART OF AMBALA-KO (NHAI) (N24002037)	1-2023	12/2025 (N.A.) {3/2026}	609.32 (609.00) {609.00}	180.20	43.80
		470	CONSTRUCTION OF 6-LANE GREENFIELD KARNAL RING ROAD STARTING FROM NH-44 NEAR VILLAGE SHAMGARH (DESIGN (NHAI) (N24002038)	11-2022	8/2025 (N.A.) {8/2025}	1,691.45 (1,998.00) {1,998.00}	649.71	58.76
		471	CONSTRUCTION OF 6-LANE GREENFIELD AMBALA RING ROAD STARTING FROM JUNCTION WITH SHAMLI- AMBALA SECTION (NHAI) (N24002039)	2-2023	10/2025 (N.A.) {10/2025}	1,088.64 (1,178.00) {1,178.00}	391.51	45.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		472	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM RANIPUR BARS (SAHARANPUR DISTRICT) TO ADHOYA (NHAI) (N24002040)	4-2022	5/2025 (N.A.) {5/2028}	1,554.21 (N.A.) {1,554.21}	517.05	54.00
		473	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM ADHOYA MUSALMANA (AMBALA DISTRICT) TO SADOPUR (NHAI) (N24002041)	4-2022	5/2025 (N.A.) {5/2025}	1,491.71 (N.A.) {1,491.71}	706.26	49.70
		474	CONSTRUCTION OF 4-LANING OF BHIWANI HANSI ROAD SECTION OF NH 148B (DESIGN LENGTH 42.934 KM) UNDER BH (NHAI) (N24002042)	11-2022	12/2025 (N.A.) {12/2025}	1,322.13 (N.A.) {1,322.13}	354.52	73.13
		475	CONSTRUCTION OF 4-LANE GREENFIELD JALBEHRA - SHAHBAD SECTION OF NH ? 152G FROM KM 0+000 TO KM 22+850 (NHAI) (N24002043)	3-2022	6/2025 (N.A.) {6/2025}	927.22 (1,173.66) {1,173.66}	458.86	78.65
		476	4L AMBALA - KALAAMB FROM KM. -0.800 TO KM. 33.015 OF OLD NH-72 (NHAI) (N24002044)	6-2023	6/2025 (N.A.) {6/2025}	629.16 (N.A.) {629.16}	216.00	88.00
		477	CONSTRUCTION OF GREENFIELD CONNECTIVITY TO JEWAR INTERNATIONAL AIRPORT FROM DND FARIDABAD BALLABHGAR (NHAI) (N24002048)	7-2022	6/2025 (N.A.) {3/2026}	2,414.67 (2,898.00) {2,898.00}	1,229.90	45.56
HIMACHAL PRADESH	DEPARTMENT OF HIGHER EDUCATION	478	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR (CPWD EDUCATION) (N42000008)	9-2018	6/2022 (12/2024) {8/2025}	392.51 (N.A.) {446.43}	316.16	91.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		479	CONSTRUCTION OF PERMANENT CAMPUSES OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND DHARAMSHAL (CPWD) (N42000011)	3-2021	11/2024 (7/2025) {7/2025}	512.37 (300.45) {300.45}	144.32	70.00
	POWER	480	PARBATI HEP (4X200 MW) (NHPC) II (NHPC) (180100210)	9-2002	9/2009 (4/2025) {4/2025}	3,919.59 (N.A.) {13,045.00}	12,832.59	100.00
		481	LUHRI HYDROELECTRIC PROJECT (STAGE1) (SJVN) (N18000279)	11-2020	1/2026 (N.A.) {12/2028}	1,810.56 (N.A.) {3,371.61}	1,704.72	51.32
		482	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) (SJVN) (N18000291)	10-2020	11/2025 (N.A.) {3/2027}	687.97 (N.A.) {1,511.87}	851.02	66.20
		483	SUNNI DAM HYDRO ELECTRIC PROJECT (SJVN) (N18000344)	1-2023	4/2028 (N.A.) {12/2028}	2,614.51 (N.A.) {4,540.71}	935.08	28.58
	RAILWAYS	484	BHANUPALI-BILASPUR BERI NL (RVNL) (N22000273)	4-2008	12/2026 (N.A.) {3/2025}	13,370.29 (N.A.) {6,753.42}	5,369.57	-
	ROAD TRANSPORT AND HIGHWAYS	485	FOUR LANNING OF NERCHOWK- PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH (NHAI) (N24000613)	9-2016	7/2020 (N.A.) {3/2025}	1,273.71 (N.A.) {1,478.61}	1,439.49	96.68
		486	FOUR LANING OF SOLAN- KAITHLIGHAT SECTION OF NH- 22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M (NHAI) (N24000852)	3-2018	5/2021 (12/2024) {12/2024}	478.74 (N.A.) {1,514.46}	1,349.59	83.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		487	REHABILITATION AND UPGRADATION TO 2-LANE/2- LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA (MoRTH) (N24001381)	8-2020	4/2021 (N.A.) {4/2021}	272.98 (N.A.) {272.98}	140.69	-
		488	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA- ASHYARI SECTION (KM 25.000 TO KM 50. (MoRTH) (N24001382)	8-2020	3/2021 (N.A.) {3/2021}	242.80 (N.A.) {242.80}	96.76	90.94
		489	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 (MoRTH) (N24001383)	8-2020	4/2021 (N.A.) {4/2021}	349.20 (N.A.) {349.20}	239.34	100.00
		490	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI- SHRI KYARI SECTION (KM 50.000 TO K (MoRTH) (N24001422)	2-2021	9/2021 (N.A.) {9/2021}	345.89 (N.A.) {345.89}	152.01	90.02
		491	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR- KARNOHAL SECTION (KM 141.000 TO K (MoRTH) (N24001447)	8-2020	12/2024 (N.A.) {12/2024}	371.93 (N.A.) {371.93}	154.04	80.00
		492	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF KALWAHAN-MANDI SECTION (KM 208.950 TO KM 2 (MoRTH) (N24001470)	8-2020	4/2025 (N.A.) {4/2025}	314.32 (N.A.) {314.32}	49.26	44.00
		493	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF (NHAI) (N24001808)	3-2021	12/2024 (12/2024) {12/2024}	1,322.95 (1,442.47) {1,442.47}	887.60	96.61

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		494	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU (NHAI) (N24001809)	5-2022	3/2024 (12/2024) {12/2024}	469.95 (N.A.) {280.00}	302.91	97.90
		495	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP (NHAI) (N24001810)	2-2022	6/2024 (N.A.) {6/2024}	190.60 (N.A.) {163.00}	103.48	100.00
		496	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH- 20 (NEW NH-154) (PACKAGE-IB) (NHAI) (N24001811)	4-2021	6/2024 (N.A.) {5/2025}	583.93 (770.00) {770.00}	171.98	99.96
		497	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) (NHAI) (N24001812)	3-2021	5/2024 (N.A.) {12/2025}	1,002.11 (1,361.79) {1,361.76}	189.98	45.67
		498	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A (NHAI) (N24001813)	7-2021	9/2024 (N.A.) {9/2024}	1,692.05 (N.A.) {1,692.05}	942.14	21.60
		499	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS-5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001915)	3-2021	6/2026 (N.A.) {6/2026}	230.54 (N.A.) {230.54}	20.16	20.16
		500	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS 5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001916)	3-2021	5/2026 (N.A.) {5/2026}	314.67 (N.A.) {314.67}	76.05	44.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		501	PKG NAME: 4L OF KATHLIGHAT TO SHAKRAL VILLAGE FROM KM 128.835 TO KM 146.300 OF NH- 5 (SHIMLA BYPASS) (NHAI) (N24002049)	3-2022	4/2026 (N.A.) {4/2026}	1,703.48 (2,278.00) {2,278.00}	651.98	14.50
		502	REHABILITATION AND UPGRADATION TO 4L CONFIGURATION and STRENGTHENING OF SIHUNI TO RAJOL FROM KM 51.0 (NHAI) (N24002050)	2-2022	9/2025 (N.A.) {9/2025}	696.65 (698.46) {698.46}	367.52	61.78
		503	CONSTRUCTION OF NEW 2 LANE WITH PAVED SHOULDER OF HAMIRPUR BYPASS (PACKAGE IVA) OF NH-88 (NEW NH-103) (NHAI) (N24002051)	7-2022	10/2025 (N.A.) {10/2025}	739.39 (N.A.) {739.39}	328.46	78.00
		504	REHABILITATION AND UP-GRADATION OF EXISTING ROAD TO 2L PS FROM END OF HAMIRPUR BYPASS (NEAR CHILBAHA) (NHAI) (N24002052)	2-2022	4/2025 (N.A.) {4/2025}	1,146.19 (N.A.) {1,146.19}	918.75	65.30
		505	REHABILITATION AND UP-GRADATION TO 4L CONFIGURATION AND STRENGTHENING OF THANPURI TO PAROR SECTION F (NHAI) (N24002192)	6-2022	12/2025 (N.A.) {12/2025}	815.69 (815.69) {815.69}	378.19	28.90
	URBAN DEVELOPMENT	506	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D) (CPWD) (N28000154)	4-2022	11/2024 (N.A.) {11/2024}	512.34 (N.A.) {512.34}	0.00	-
JAMMU AND KASHMIR	CIVIL AVIATION	507	JAMMU - CONSTRUCTION OF NEW CIVIL ENCLAVE (AAI) (N04000107)	7-2022	6/2026 (N.A.) {6/2026}	861.37 (N.A.) {861.37}	133.82	29.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	508	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) (CPWD EDUCATION) (N28000130)	3-2019	7/2022 (1/2025) {1/2025}	424.93 (N.A.) {500.91}	448.15	96.00
		509	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) (CPWD EDUCATION) (N28000131)	1-2018	4/2023 (4/2025) {4/2025}	676.00 (1,144.68) {1,144.68}	54.75	100.00
	<u>HEALTH AND FAMILY WELFARE</u>	510	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR (CPWD FOR HEALTH) (N21000029)	3-2019	9/2023 (5/2025) {5/2025}	1,404.00 (1,642.00) {1,642.00}	1,461.68	99.90
		511	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR (CPWD FOR HEALTH) (N28000150)	3-2019	9/2025 (1/2025) {11/2025}	1,828.00 (1,577.00) {1,577.00}	976.64	64.00
	<u>PETROLEUM</u>	512	SETTING UP A COMMON USER PETROLEUM TERMINAL AT JAMMU FOR RE-SITEMENT OF EXISTING DEPOTS OF PSU OMCS (BPCL) (N16000500)	4-2021	3/2025 (N.A.) {3/2025}	676.89 (N.A.) {676.89}	478.41	74.00
		513	CGD PROJECT AT JAMMU DISTRICTS (IOCL) (N16000527)	3-2022	3/2032 (9/2034) {9/2034}	538.00 (N.A.) {538.00}	3.87	0.60
	<u>POWER</u>	514	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) (CVPPPL) (N18000172)	10-2014	4/2020 (7/2025) {9/2026}	8,112.12 (N.A.) {12,727.76}	6,321.40	67.90
		515	KIRU HYDRO ELECTRIC PROJECT (CVPPPL) (N18000278)	3-2019	8/2024 (N.A.) {9/2026}	4,287.59 (N.A.) {5,409.00}	2,503.38	59.14

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		516	RATLE HE PROJECT (NHPC) (N18000324)	2-2021	2/2026 (N.A.) {11/2028}	5,281.94 (N.A.) {5,281.94}	932.07	22.10
		517	KWAR HE PROJECT (CVPPPL) (N18000363)	5-2022	11/2026 (N.A.) {12/2027}	4,526.12 (N.A.) {4,526.12}	1,083.48	20.80
		518	TRANSMISSION SCHEME FOR EVACUATION OF POWER FROM RATLE HEP (850 MW) & KIRU (624 MW): PART B (PGCIL) (N18000417)	3-2025	3/2027 (N.A.) {3/2027}	219.00 (N.A.) {219.00}	0.00	-
	<u>RAILWAYS</u>	519	UDHAMPUR-SRINAGAR- BARAMULLA (NL),NR (NR) (220100133)	3-1995	8/2024 (12/2024) {12/2024}	37,012.00 (37,012.26) {43,780.00}	42,328.83	100.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	520	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A (NHAI) (N24000488)	12-2015	12/2018 (5/2025) {5/2025}	2,136.97 (2,644.00) {2,644.00}	2,386.51	99.50
		521	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE (NHAI) (N24000717)	12-2017	7/2021 (5/2025) {5/2025}	1,471.75 (1,471.75) {1,903.98}	1,715.72	98.64
		522	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU- AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA (NHIDCL) (N24000868)	3-2018	7/2021 (8/2023) {10/2025}	253.44 (N.A.) {253.44}	187.74	82.10
		523	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z- MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D (NHIDCL) (N24001256)	8-2020	9/2026 (N.A.) {9/2026}	6,808.69 (N.A.) {6,808.69}	3,013.84	49.92

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		524	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL (NHIDCL) (N24001264)	7-2020	4/2022 (10/2024) {10/2026}	228.39 (N.A.) {228.39}	67.60	87.60
		525	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K (NHIDCL) (N24001266)	7-2020	4/2022 (11/2023) {6/2025}	210.79 (N.A.) {210.79}	71.00	90.14
		526	KHELLANI-KHANABAL PKG-1 (NHIDCL) (N24001323)	3-2021	9/2022 (10/2024) {10/2024}	486.45 (N.A.) {486.45}	126.73	96.58
		527	KHELLANI-KHANABAL PKG-3 (NHIDCL) (N24001341)	3-2021	12/2022 (10/2024) {5/2025}	398.51 (N.A.) {398.51}	80.64	95.52
		528	KHELLANI-KHANABAL PKG-2 (NHIDCL) (N24001394)	7-2021	2/2023 (6/2025) {6/2026}	512.43 (N.A.) {512.43}	71.65	51.21
		529	KHELLANI-KHANABAL PKG-4 (NHIDCL) (N24001395)	7-2021	8/2023 (12/2025) {6/2026}	859.67 (N.A.) {859.67}	190.91	44.02
		530	KHELLANI-KHANABAL PKG-5 (NHIDCL) (N24001396)	7-2021	2/2023 (3/2025) {8/2025}	497.09 (N.A.) {497.09}	172.85	87.14
		531	GOHA-KHELLANI PKG-3 (NHIDCL) (N24001397)	2-2021	3/2023 (2/2025) {3/2025}	431.28 (N.A.) {431.28}	365.12	100.00
		532	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA (NHAI) (N24001472)	9-2021	12/2023 (6/2024) {6/2024}	811.19 (N.A.) {811.19}	848.57	99.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		533	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY (NHAI) (N24001511)	3-2021	2/2024 (4/2025) {10/2025}	2,919.96 (N.A.) {2,919.96}	2,293.76	67.50
		534	FOUR LANING OF JAMMU- AKHNOOR PKG-1 (NHIDCL) (N24001543)	7-2022	1/2025 (N.A.) {10/2025}	245.34 (N.A.) {245.34}	57.03	38.48
		535	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG- XVI) EXISTING JAKH (VIJAYPUR)- KUNJWANI SECTION OF NH-4 (NHAI) (N24001550)	9-2021	9/2024 (9/2025) {9/2025}	1,821.72 (1,917.32) {1,917.32}	1,005.24	81.20
		536	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG- XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5 (NHAI) (N24001551)	10-2021	9/2024 (7/2025) {7/2025}	3,044.02 (3,044.02) {3,044.02}	1,585.04	70.15
		537	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG- XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B (NHAI) (N24001552)	10-2021	9/2024 (9/2025) {9/2025}	2,714.95 (2,714.95) {2,714.95}	1,641.42	83.50
		538	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH- (NHAI) (N24001619)	8-2022	6/2024 (6/2025) {6/2025}	200.05 (200.05) {208.92}	153.05	58.60
		539	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SLIP ZONES AT KM 130.550 TO KM.130.750; KM. (NHAI) (N24001620)	9-2021	10/2023 (12/2025) {12/2025}	442.14 (N.A.) {442.14}	328.36	19.88

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		540	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL. (NHAI) (N24001621)	7-2021	8/2024 (6/2025) {6/2025}	614.48 (N.A.) {614.48}	185.83	7.00
		541	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX (NHAI) (N24001622)	7-2021	6/2024 (6/2025) {6/2025}	1,401.87 (N.A.) {1,401.87}	686.33	-
		542	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM. 187.00 TO KM. 189.350 (NHAI) (N24001623)	1-2020	1/2024 (4/2025) {4/2025}	336.01 (N.A.) {336.01}	222.92	34.00
		543	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI (NHAI) (N24001624)	7-2019	10/2020 (4/2023) {9/2024}	157.05 (N.A.) {157.05}	139.54	100.00
		544	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K (NHAI) (N24001627)	7-2021	2/2025 (5/2026) {5/2026}	1,912.17 (N.A.) {1,912.17}	129.05	-
		545	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B (NHIDCL) (N24001833)	7-2022	3/2025 (N.A.) {8/2025}	198.28 (N.A.) {198.28}	85.39	71.09
		546	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 102 TO KM 13 (BRO) (N24001897)	3-2021	7/2024 (3/2025) {3/2024}	642.24 (N.A.) {642.24}	345.14	95.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		547	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 30.000 TO K (BRO) (N24001898)	7-2020	11/2024 (N.A.) {11/2024}	272.49 (N.A.) {272.49}	133.66	88.00
		548	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 134.95 TO KM (BRO) (N24001899)	2-2021	7/2024 (N.A.) {3/2025}	395.25 (N.A.) {395.25}	140.42	64.00
		549	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 49.150 TO KM (BRO) (N24001900)	3-2020	8/2024 (N.A.) {3/2025}	796.97 (N.A.) {796.97}	323.85	79.00
		550	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 64.535 TO K (BRO) (N24001901)	3-2020	9/2023 (N.A.) {3/2025}	152.93 (N.A.) {152.93}	90.30	78.27
		551	CONSTRUCTION OF TWIN TUBE TUNNELS ON JAMMU KASHMIR RING ROAD (NH-244A) BETWEEN DESIGN CH. 50+600 TO (NHAI) (N24001926)	3-2023	6/2025 (N.A.) {6/2025}	939.86 (N.A.) {939.86}	475.07	63.93
		552	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER FROM (DESIGN CH. 14+200 TO 24+400), (DESIGN CH. 35+300 TO (BRO) (N24001998)	6-2022	8/2025 (N.A.) {8/2025}	832.46 (N.A.) {823.46}	227.50	46.00
		553	2L NH-1 FROM KM 8.660 TO KM 33.775 (SUMBAL TO WAYUL) TO 4L DUAL CARRIAGEWAY NH STANDARD AS PART OF S (NHAI) (N24002059)	9-2022	6/2026 (6/2026) {12/2026}	1,183.60 (N.A.) {1,183.60}	185.45	11.75

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		554	DELHI AMRITSAR KATRA EXPRESSWAY (PHASE-II PKG XVIII) DEVELOPMENT AND UPGRADATION OF FOUR LANE ACCESS (NHA) (N24002060)	3-2023	11/2025 (N.A.) {11/2025}	1,107.00 (N.A.) {975.38}	291.41	36.79
		555	4/6L ACCESS CONTROL EXPRESSWAY FROM DESIGN CHAINAGE KM 515.000 TO 528.300 (KUNJWANI TO SIDHRA SECTIO (NHA) (N24002061)	8-2022	6/2025 (N.A.) {8/2025}	2,474.47 (N.A.) {2,894.74}	923.45	36.20
		556	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM 162.800 TO KM (BRO) (N24002119)	10-2022	1/2026 (N.A.) {1/2026}	562.45 (N.A.) {562.45}	99.06	25.00
		557	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER (PATTAN BYPASS) GREENFIELD BYPASS FROM EXISTING CH. KM 24 (BRO) (N24002179)	3-2023	7/2026 (N.A.) {7/2026}	980.21 (N.A.) {980.21}	300.02	8.00
		558	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 166.100 TO KM (BRO) (N24002180)	9-2021	7/2026 (N.A.) {7/2026}	734.64 (N.A.) {734.64}	19.60	8.00
		559	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDERS (BARAMULLA BYPASS) GREENFIELD BYPASS FROM EXISTING CH. K (BRO) (N24002185)	3-2023	9/2026 (N.A.) {9/2026}	992.43 (N.A.) {992.43}	338.33	-
		560	WIDENING AND STRENGTHENING OF RAFIABAD- KUPWARA-CHOWKIBAL- TANGDHAR-CHAMKOT (NH-701) ROAD FROM DESIGN (BRO) (N24002210)	3-2024	5/2027 (N.A.) {5/2027}	1,404.94 (N.A.) {1,404.94}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
JHARKHAND	COAL	561	RAJRAPPA RCE OCP (3.0 MTY) (CCL) (N06000087)	12-2009	3/2016 (N.A.) {3/2027}	510.85 (N.A.) {510.85}	488.57	75.00
		562	MURAI DIH UG TURN-KEY PROJECT (BCCL) (N06000096)	2-2011	4/2014 (N.A.) {1/2026}	339.88 (N.A.) {339.88}	190.48	70.00
		563	MOONIDIH XV SEAM UG (BCCL) (N06000098)	8-2011	3/2019 (N.A.) {5/2026}	1,230.27 (N.A.) {1,230.27}	603.82	81.00
		564	CHITRA EAST (RCE) OCP (ECL) (N06000169)	8-2018	3/2026 (3/2026) {3/2026}	513.98 (N.A.) {513.98}	227.24	51.00
		565	TETARIAKHAR EXPANSION OCP (CCL) (N06000186)	11-2019	3/2023 (N.A.) {3/2027}	243.52 (N.A.) {243.52}	44.64	24.00
		566	PACHWARA SOUTH COAL BLOCK (NLC) (N06000193)	7-2013	9/2028 (N.A.) {9/2028}	2,242.92 (2,242.90) {2,242.90}	583.81	54.00
		567	PATHERDIH 2.5 NLW COAL WASHERY (BCCL) (N06000194)	10-2015	4/2018 (N.A.) {3/2026}	334.27 (N.A.) {334.27}	135.25	45.00
		568	REVISED PROJECT REPORT MAGADH EXPANSION OCP (CCL) (N06000216)	8-2020	3/2028 (N.A.) {3/2028}	7,254.37 (N.A.) {7,254.37}	1,495.43	29.00
		569	EXPANSION PROJECT AMRAPALI OCP (CCL) (N06000217)	8-2020	3/2028 (N.A.) {3/2028}	5,136.15 (N.A.) {5,136.15}	1,063.25	41.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		570	UCE OF EPR OF NORTH URIMARI OCP (CCL) (N06000218)	7-2021	3/2029 (N.A.) {3/2029}	778.80 (N.A.) {778.80}	694.11	75.00
		571	KOTRE BASANTPUR PACHMO OCP (CCL) (N06000237)	8-2020	3/2032 (N.A.) {3/2032}	625.40 (625.40) {625.40}	441.24	41.00
		572	CHANDRAGUPT OCP (CCL) (N06000238)	8-2020	3/2032 (N.A.) {3/2032}	973.50 (N.A.) {973.50}	339.32	12.40
		573	SIRKA OCP (CCL) (N06000239)	5-2020	3/2028 (N.A.) {3/2028}	222.82 (N.A.) {222.82}	139.31	60.00
		574	JHARKHAND LAIYO OCP (CCL) (N06000240)	8-2020	3/2031 (N.A.) {3/2031}	764.57 (N.A.) {764.57}	145.80	28.00
		575	EPR TAPIN SOUTH OCP (CCL) (N06000241)	11-2020	3/2028 (N.A.) {3/2028}	230.41 (N.A.) {230.41}	20.77	18.30
		576	EPR PUNDI OCP (CCL) (N06000242)	11-2020	3/2027 (N.A.) {3/2027}	713.35 (N.A.) {713.35}	236.57	21.00
		577	EPR ROHINI KARKATA OCP (CCL) (N06000243)	1-2021	3/2028 (N.A.) {3/2028}	1,020.42 (N.A.) {1,020.42}	83.44	11.70
		578	EXPANSION OF KONAR OCP (CCL) (N06000245)	1-2022	3/2032 (N.A.) {3/2032}	799.34 (N.A.) {799.34}	416.73	32.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		579	EXPANSION OF KARO OCP (CCL) (N06000246)	1-2022	3/2029 (N.A.) {3/2029}	908.47 (N.A.) {908.47}	217.68	20.00
		580	EXPANSION OF ASHOK OCP (CCL) (N06000247)	5-2021	3/2028 (N.A.) {3/2028}	2,898.28 (N.A.) {2,898.28}	176.50	20.00
		581	AMALGAMATED NTST KUJAMA OCP 8.5 MTY (BCCL) (N06000273)	1-2023	3/2030 (N.A.) {3/2030}	4,011.85 (N.A.) {4,011.85}	397.65	25.00
		582	HURA C OC (ECL) (N06000275)	8-2022	3/2029 (N.A.) {3/2029}	859.41 (N.A.) {859.41}	442.98	62.00
		583	CHUPERBHITA- SIMLONG OCP (ECL) (N06000280)	12-2023	3/2037 (3/2037) {3/2037}	979.08 (N.A.) {979.08}	0.00	-
		584	BLOCK-E OCP (15 MTY) (BCCL) (N06000287)	3-2024	3/2029 (N.A.) {3/2029}	5,850.83 (N.A.) {5,850.83}	5.85	2.00
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	585	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD (CPWD EDUCATION) (N28000067)	9-2012	3/2016 (N.A.) {3/2016}	171.86 (N.A.) {171.86}	174.48	99.00
	<u>PETROLEUM</u>	586	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) (ONGC) (N16000445)	11-2019	1/2024 (3/2025) {6/2025}	431.00 (N.A.) {431.00}	186.95	57.90
		587	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI (IOCL) (N16000480)	3-2023	2/2026 (N.A.) {2/2026}	202.07 (N.A.) {202.07}	48.39	42.06

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		588	CGD PROJECT IN BIHAR JHARKHAND (HPCL) (N16000497)	6-2022	6/2030 (N.A.) {6/2030}	1,377.00 (N.A.) {1,377.00}	274.32	22.00
	POWER	589	NORTH KARANPURA STPP (3X660 MW) (NTPC) (N18000177)	2-2014	6/2019 (10/2022) {3/2025}	16,242.90 (N.A.) {16,242.90}	16,745.68	98.00
		590	PATRATU STPP-I (3X800MW) (NTPC) (N18000275)	11-2017	3/2023 (N.A.) {3/2026}	17,112.00 (N.A.) {17,112.00}	16,305.18	81.00
		591	BADAM COAL MINING PROJECT (NTPC) (N18000367)	2-2019	10/2024 (4/2027) {4/2027}	501.79 (784.39) {501.79}	302.22	59.79
		592	KERANDARI COAL MINING PROJECT (NTPC) (N18000370)	9-2015	11/2019 (3/2025) {3/2025}	1,553.00 (2,896.64) {2,896.64}	2,014.94	64.00
	RAILWAYS	593	KODERMA-TILAIYA (NL), ECR (ECR) (220100305)	4-2002	3/2023 (N.A.) {12/2025}	1,625.87 (1,625.87) {1,700.00}	2,000.95	80.00
		594	BONDAMUNDA RANCHI DOUBLING (SER) (N22000396)	3-2016	6/2024 (N.A.) {6/2026}	3,029.04 (3,029.04) {3,029.04}	2,349.31	83.00
		595	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) (SER) (N22000508)	4-2018	6/2026 (N.A.) {6/2026}	501.52 (N.A.) {472.50}	275.66	2.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		596	DOUBLING OF PRADHANKHUNTA JN - PATHERDIH BAZAR-BHOJUDIH (<i>ECR</i>) (N22000529)	11-2022	11/2027 (N.A.) {3/2026}	202.00 (349.22) {349.22}	57.76	2.00
		597	KHARAGPUR-ADITYAPUR - 3RD LINE (132 KM) (<i>RVNL</i>) (N22000595)	12-2015	3/2025 (N.A.) {3/2025}	3,249.98 (N.A.) {3,270.07}	2,899.45	-
		598	3RD LINE BETWEEN DHANBAD SONNAGAR (<i>RVNL</i>) (N22000599)	11-2016	3/2026 (N.A.) {3/2026}	8,975.00 (N.A.) {7,906.38}	4,705.38	-
		599	GARHWA ROAD - RAIL OVER RAIL (<i>ECR</i>) (N22000610)	3-2017	6/2024 (N.A.) {2/2026}	262.71 (N.A.) {262.71}	221.66	70.00
		600	GOMOH - FLYOVER FOR DOWN TRAINS (<i>ECR</i>) (N22000611)	1-2018	3/2023 (N.A.) {3/2026}	686.03 (N.A.) {487.73}	385.56	45.00
	ROAD TRANSPORT AND HIGHWAYS	601	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION (<i>NHAI</i>) (N24000726)	1-2018	11/2021 (6/2025) {6/2025}	1,155.16 (N.A.) {950.49}	657.82	70.00
		602	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I (<i>MoRTH</i>) (N24001216)	12-2016	9/2021 (N.A.) {12/2024}	196.00 (N.A.) {196.00}	164.21	90.10
		603	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 (<i>NHAI</i>) (N24001589)	9-2020	3/2024 (12/2024) {4/2025}	755.26 (N.A.) {1,039.00}	621.92	85.80

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		604	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH- 75 [REHLA / GARHWA BYPASS] (NHAI) (N24001590)	9-2020	10/2023 (12/2024) {1/2025}	748.99 (N.A.) {903.00}	831.75	100.00
		605	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM (NHAI) (N24001594)	2-2022	1/2025 (3/2025) {3/2025}	534.73 (N.A.) {534.73}	155.31	97.00
		606	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH (NHAI) (N24001595)	8-2020	3/2024 (6/2025) {6/2025}	1,034.00 (1,879.55) {1,879.55}	41.50	96.50
		607	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF (NHAI) (N24001596)	11-2021	7/2023 (6/2025) {6/2025}	1,302.72 (1,504.80) {1,504.80}	875.86	74.51
		608	FOUR LANING WITH PAVED SHOULDER OF SECTION FROM KM 53.600 (GOLA ON NH-320) TO KM 81.446 (ORMANJHI ON (NHAI) (N24001854)	6-2023	6/2025 (N.A.) {6/2025}	1,214.93 (1,324.95) {1,462.00}	998.69	70.00
		609	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM 0.00 TO 44.00 (KURU-GHAGHRA SECTION) OF NH-143A INCLU (MoRTH) (N24001922)	2-2020	8/2023 (N.A.) {12/2024}	153.01 (N.A.) {153.01}	83.63	96.23
		610	WIDENING AND STRENGTHENING OF EXISTING PAVEEMNT TO TWO LANE WITH PAVED SHOULDERS FROM KM 116.00 TO K (MoRTH) (N24001923)	1-2022	7/2024 (N.A.) {12/2024}	315.21 (N.A.) {315.21}	117.26	80.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		611	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDER/TWO LANE+ PAVED SHOULDER WITH SERVICE ROA (MoRTH) (N24001924)	3-2022	8/2025 (N.A.) {8/2025}	514.22 (N.A.) {514.22}	15.19	6.10
		612	WIDENING AND STRENGTHENING/RECONSTRUC TION TO TWO LANE WITH PAVED SHOULDER/ TWO LANE WITH PAVED SHOUL (MoRTH) (N24001925)	3-2022	8/2025 (N.A.) {8/2025}	423.18 (N.A.) {423.18}	0.11	-
		613	FOUR LANING OF KHAJURI TO WYNDHAMGANJ FROM KM 219.600 TO KM 260.483 ON NH-75 PKG SEC-V ON HAM (NHAI) (N24002053)	4-2022	9/2025 (N.A.) {9/2025}	1,232.00 (1,343.00) {1,400.00}	606.60	77.45
		614	FOUR LANING OF BHOGU TO SANKHA FROM KM 147.450 TO KM 196.870 ON NH-75 PKG SEC- III (NHAI) (N24002054)	10-2022	11/2025 (N.A.) {11/2025}	1,390.77 (1,391.00) {1,600.00}	296.46	65.95
		615	FOUR LANING OF BASUKINATH- DEOGHAR SECTION OF NH-114A FROM KM 85.081 TO KM 130.240 UNDER NHDP PHASE-I (NHAI) (N24002055)	3-2023	12/2025 (N.A.) {12/2025}	1,444.94 (N.A.) {1,444.94}	0.00	-
		616	BHARATMALA PARIYOJANA OF BOKARO JAINA MORE - GOLA SECTION OF NH-320 FROM KM. 21.110 TO KM. 53.600 IN (NHAI) (N24002056)	6-2020	6/2025 (N.A.) {6/2025}	964.64 (N.A.) {964.64}	432.70	52.91

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		617	FOUR LANING OF MEHGAMA HANSDIHA SECTION OF NH-33 FROM EXISTING KM 41.900 TO 93.000 IN THE STATE OF J (NHAI) (N24002057)	12-2022	5/2025 (N.A.) {5/2025}	1,443.77 (N.A.) {1,443.77}	0.00	-
	STEEL	618	NEW SINTER PLANT AT BOKARO STEEL PLANT (SAIL) (N12000095)	3-2015	10/2017 (11/2026) {11/2026}	1,034.01 (1,752.30) {1,752.30}	874.42	51.75
		619	REVAMPING OF OLD SUB SYSTEM OF BLAST FURNACE 3 AT BOKARO STEEL PLANT (SAIL) (N12000129)	9-2023	7/2025 (11/2025) {11/2025}	513.82 (N.A.) {513.82}	153.95	62.00
		620	REBUILDING OF COKE OVEN BATTERY NO.6 OF BOKARO STEEL PLANT (SAIL) (N12000133)	11-2023	11/2026 (N.A.) {11/2026}	627.31 (N.A.) {627.31}	80.19	31.00
		621	REPLACEMENT OF REMAINING 04 NOS. OF BATTERY CYCLONES WITH 04 NOS. OF ESPS IN SINTER PLANT-1 AT BSL (SAIL) (N12000135)	3-2024	6/2026 (N.A.) {6/2026}	260.37 (N.A.) {260.37}	39.21	10.00
		622	REPLACEMENT OF EXISTING GRINDERS IN CRM-I & II AT BOKARO STEEL PLANT (SAIL) (N12000142)	1-2025	1/2027 (N.A.) {1/2027}	211.94 (N.A.) {211.94}	0.00	-
		623	SECONDARY EMISSION CONTROL IN CONVERTERS OF SMS-II AT BOKARO STEEL PLANT (SAIL) (N12000143)	1-2025	10/2026 (N.A.) {10/2026}	207.13 (N.A.) {207.13}	0.00	

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
KARNATAKA	CIVIL AVIATION	624	BELAGAVI AIRPORT- EXPANSION OF TERMINAL BUILDING AND ASSOCIATED WORKS (AAI) (N04000105)	6-2023	2/2026 (N.A.) {2/2026}	322.45 (N.A.) {322.45}	88.75	38.00
		625	HUBBALI AIRPORT - CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS (AAI) (N04000108)	6-2023	2/2026 (N.A.) {2/2026}	320.47 (N.A.) {320.47}	49.67	27.00
	DEPARTMENT OF HIGHER EDUCATION	626	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) (CPWD EDUCATION) (N42000006)	7-2019	3/2022 (6/2025) {11/2025}	851.00 (930.36) {930.36}	918.06	98.75
		627	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL (CPWD) (N42000010)	8-2021	2/2024 (11/2024) {11/2024}	316.25 (N.A.) {316.25}	281.32	94.00
	PETROLEUM	628	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE (HPCL) (N16000369)	12-2018	12/2022 (8/2025) {8/2025}	854.00 (854.00) {854.00}	692.71	97.20
		629	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE (IOCL) (N16000437)	1-2022	7/2025 (12/2025) {12/2025}	463.00 (500.62) {500.62}	233.40	70.72
		630	POWER SYSTEM UPGRADATION PROJECT (MANGALORE REFIN) (N16000509)	10-2023	2/2026 (N.A.) {2/2026}	385.00 (N.A.) {385.00}	121.87	52.41

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		631	DEMO PLANT FOR PRODUCTION OF BIO-ATF (MANGALORE REFIN) (N16000536)	3-2024	3/2027 (N.A.) {3/2027}	364.00 (N.A.) {364.00}	9.92	5.20
	POWER	632	TS FOR INTRGRATION OF RE ZONE (PHASE II) IN KOPPAL II (PHASE A and B) AND GADAG II (PHASE A) IN KARN (PGCIL) (N18000385)	12-2023	12/2025 (N.A.) {12/2025}	2,889.00 (N.A.) {2,889.00}	602.00	24.90
		633	TS FOR SOLAR ENERGY ZONE IN BIDAR (2500MW), KARNATAKA [BIDAR TRANSMISSION LTD] (PGCIL) (N18000388)	2-2024	2/2026 (N.A.) {2/2026}	2,148.00 (N.A.) {2,148.00}	557.00	36.00
		634	SYSTEM STRENGTHENING AT KOPPAL-II AND GADAG-II FOR INTEGRATION OF RE GENERATION PROJECTS (PGCIL) (N18000409)	1-2025	1/2027 (N.A.) {1/2027}	1,354.00 (N.A.) {1,354.00}	0.00	-
		635	AUGMENTATION OF TRANSFORMATION CAPACITY AT BIDAR PS (PGCIL) (N18000410)	2-2025	2/2027 (N.A.) {2/2027}	288.00 (N.A.) {288.00}	0.00	-
	RAILWAYS	636	TUMKUR-CHITRADURGA- DAVENGERE NL (SWR) (N22000256)	4-2011	3/2019 (N.A.) {12/2027}	1,876.00 (N.A.) {1,801.01}	494.03	12.00
		637	BAGALKOT-KUDACHI NL (SWR) (N22000258)	4-2010	3/2027 (N.A.) {3/2027}	1,378.00 (1,378.00) {1,378.00}	627.04	34.00
		638	HOSPET-HUBLI-LONDA- VASCODAGAMA DL (RVNL) (N22000297)	4-2010	3/2027 (N.A.) {12/2026}	5,060.36 (N.A.) {3,692.60}	3,505.49	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		639	GADAG-WADI NL (SWR) (N22000299)	4-2013	3/2027 (N.A.) {12/2027}	2,841.84 (N.A.) {2,841.84}	1,300.11	28.00
		640	MARIKUPPAM - KUPPAM (SWR) (N22000308)	4-2012	3/2016 (N.A.) {12/2027}	279.54 (296.72) {296.72}	120.94	14.00
		641	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) (SWR) (N22000486)	3-1996	6/2025 (N.A.) {3/2026}	825.31 (825.31) {825.31}	682.36	66.00
		642	BAIYYAPPANAHALLI-HOSUR (48 KM) (NCRTC) (N22000542)	4-2019	3/2026 (N.A.) {3/2026}	375.67 (N.A.) {375.67}	0.00	-
		643	YESHVANTHPUR- CHANNASANDRA (21.7 KM) (NCRTC) (N22000543)	4-2019	3/2026 (N.A.) {3/2026}	169.65 (N.A.) {169.65}	71.75	-
		644	BELGAUM-DHARWAD VIA KITTUR (73.10 KM) (UMBRELLA WORK PB#22/2019-20/NR) (SWR) (N22000557)	9-2020	12/2027 (N.A.) {12/2027}	1,590.80 (927.42) {927.42}	0.72	-
		645	HASSAN (ALUR) - BELUR (32 KM) (UMBRELLA WORK PB#23/2018- 19/NR) (SWR) (N22000558)	6-2019	4/2028 (N.A.) {3/2028}	748.86 (748.85) {748.85}	0.88	1.00
		646	SHIMOGA-SHIKARIPURA- RANEBENNUR (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000559)	9-2019	12/2027 (N.A.) {12/2027}	1,453.73 (994.47) {994.47}	71.25	7.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		647	BANGALORE-WHITEFIELD- BANGALORE CITY- KRISHNARAJAPURAM QUADRUPLING (SWR) (N22000621)	3-2018	6/2025 (N.A.) {6/2025}	492.87 (N.A.) {492.87}	241.18	75.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	648	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP (MoRTH) (N24000334)	3-2015	11/2015 (8/2024) {8/2024}	165.67 (N.A.) {165.67}	126.47	99.00
		649	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION (NHAI) (N24000462)	7-2012	8/2016 (1/2020) {6/2025}	1,655.01 (1,990.99) {1,990.99}	1,818.12	97.80
		650	HOSPET-BELLARY-KARNATAKA AP BORDER (NHAI) (N24000603)	8-2016	3/2019 (5/2025) {5/2025}	1,167.42 (N.A.) {1,224.01}	1,028.39	86.35
		651	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH- 150A HOSMANE CROSS ? PA (MoRTH) (N24001156)	1-2017	9/2017 (5/2023) {5/2023}	166.67 (N.A.) {264.34}	192.08	100.00
		652	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH (MoRTH) (N24001157)	8-2016	2/2017 (7/2024) {7/2024}	175.50 (N.A.) {241.60}	178.73	90.10
		653	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 (MoRTH) (N24001158)	3-2018	6/2019 (12/2023) {12/2023}	159.97 (N.A.) {242.61}	113.15	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		654	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION (MoRTH) (N24001159)	1-2018	7/2018 (N.A.) {3/2022}	159.70 (N.A.) {159.70}	142.88	100.00
		655	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH- 234 BANAVARA-HULIYAR (MoRTH) (N24001160)	9-2017	10/2018 (4/2022) {4/2022}	191.60 (N.A.) {191.60}	112.01	100.00
		656	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- (MoRTH) (N24001161)	12-2017	1/2019 (4/2022) {4/2022}	297.30 (N.A.) {318.28}	277.27	100.00
		657	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN (MoRTH) (N24001162)	3-2018	10/2018 (11/2022) {11/2022}	325.86 (N.A.) {386.41}	356.76	100.00
		658	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN (MoRTH) (N24001164)	10-2016	3/2017 (7/2022) {7/2022}	396.96 (N.A.) {396.96}	329.58	100.00
		659	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT (MoRTH) (N24001165)	11-2016	3/2017 (10/2021) {10/2021}	314.90 (N.A.) {314.90}	233.95	100.00
		660	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH- 218 (218-KNT-2014-15-775) (MoRTH) (N24001166)	3-2015	1/2016 (N.A.) {7/2024}	159.12 (N.A.) {159.12}	127.72	98.06

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		661	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT (MoRTH) (N24001168)	5-2018	5/2018 (12/2023) {12/2023}	171.60 (N.A.) {171.60}	129.72	100.00
		662	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U (MoRTH) (N24001172)	1-2017	8/2017 (N.A.) {6/2022}	291.49 (N.A.) {291.49}	238.77	100.00
		663	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI ? JADERCELA SECTION (MoRTH) (N24001173)	2-2017	5/2019 (N.A.) {10/2025}	157.32 (188.00) {187.61}	43.16	60.00
		664	WIDENING TO 2-LANE WIH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT (MoRTH) (N24001387)	1-2017	9/2017 (5/2023) {5/2023}	264.34 (N.A.) {264.34}	201.07	100.00
		665	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA (MoRTH) (N24001388)	3-2019	12/2019 (11/2024) {11/2024}	423.15 (N.A.) {423.15}	268.97	82.00
		666	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN (NHAI) (N24001425)	3-2021	11/2021 (11/2025) {11/2025}	1,100.88 (1,687.31) {1,687.31}	1,098.32	78.80
		667	4L OF ADDAHOLE TO BANTWAL CROSS SECTION (NHAI) (N24001426)	3-2021	10/2021 (5/2025) {5/2025}	317.90 (572.01) {572.01}	369.95	97.42

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		668	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) (NHA) (N24001598)	1-2022	4/2025 (4/2025) {4/2025}	1,388.70 (1,388.70) {1,388.70}	438.61	62.50
		669	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. (NHA) (N24001599)	3-2018	12/2022 (12/2022) {11/2025}	440.16 (N.A.) {440.16}	350.41	68.79
		670	BANGALORE/TN BORDER TO HOSKOTE (NHA) (N24001674)	2-2023	2/2025 (9/2025) {9/2025}	1,240.60 (1,240.60) {1,240.60}	935.35	80.20
		671	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 (NHA) (N24001676)	12-2022	6/2025 (3/2026) {6/2025}	2,718.46 (N.A.) {2,718.46}	438.90	52.20
		672	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12 (NHA) (N24001677)	11-2022	5/2024 (5/2024) {5/2024}	226.76 (226.76) {226.76}	86.76	68.70
		673	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 (NHA) (N24001679)	10-2022	4/2025 (4/2025) {4/2025}	1,479.30 (1,479.30) {1,479.30}	580.74	78.20
		674	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE (NHA) (N24001680)	3-2021	10/2024 (1/2026) {1/2026}	1,409.68 (1,808.12) {1,808.12}	999.67	58.70

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		675	TUMKUR - NELAMANGALA(6L) (NHAI) (N24001681)	8-2022	8/2025 (3/2026) {3/2026}	2,032.15 (2,032.15) {2,032.15}	182.43	51.58
		676	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA (NHAI) (N24001682)	11-2021	3/2024 (3/2024) {12/2026}	294.62 (309.90) {309.90}	55.68	15.06
		677	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION (NHAI) (N24001684)	9-2020	1/2023 (9/2020) {5/2025}	688.00 (602.09) {688.00}	514.23	80.02
		678	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 (NHAI) (N24001687)	10-2021	10/2023 (12/2025) {12/2025}	1,331.77 (2,082.98) {2,082.98}	470.87	76.06
		679	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM. 54.370 TO KM. 101.400 (BI (MoRTH) (N24001936)	3-2021	3/2023 (7/2024) {7/2024}	344.79 (N.A.) {344.79}	10.00	90.00
		680	BALANCE WORK OF REHABILITATION AND UPGRADING TO 2LANE/2LANE WITH PAVED SHOULDER CONFIGURATION AND ST (MoRTH) (N24001937)	2-2023	2/2024 (2/2025) {2/2025}	398.48 (N.A.) {398.48}	5.00	50.00
		681	CONSTRUCTION OF ELEVATED CORRIDOR FROM KM. 135.650 TO 136.300 ON 63, FROM KM. 249 TO KM. 250.050 ON (MoRTH) (N24001938)	6-2021	6/2024 (6/2025) {6/2025}	298.00 (N.A.) {298.00}	10.70	52.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		682	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24001940)	1-2023	1/2026 (9/2025) {9/2025}	166.58 (N.A.) {166.58}	3.54	-
		683	WIDENING TO 4 LANE FROM KM. 133.00 TO 158.04 (DESIGN CHAINAGE KM. 130.88 TO 155.145) (SHIRUR CROSS T (MoRTH) (N24001941)	1-2023	1/2025 (1/2025) {1/2025}	350.69 (N.A.) {350.69}	10.00	56.00
		684	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM. 33.13 TO KM. 40.23 AND KM. 52.00 TO KM. 71.00 (EX (MoRTH) (N24001943)	9-2022	3/2024 (1/2025) {1/2025}	172.98 (N.A.) {172.98}	6.48	65.00
		685	WIDENING TO INTERMEDIATE/TWO LANE TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHANGES KM 112.750 TO (MoRTH) (N24001944)	1-2023	6/2024 (7/2024) {7/2024}	255.88 (N.A.) {255.88}	60.99	78.00
		686	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 116.800 TO 149.070(DESIGN CHANGES) ON HOSADURGA HOL (MoRTH) (N24001945)	8-2022	2/2024 (12/2024) {12/2024}	170.34 (N.A.) {170.34}	4.25	72.00
		687	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM 24.400 TO 27.270, 40.500 TO 41.900, 84.300 TO 88.20 (MoRTH) (N24001946)	11-2022	11/2024 (11/2024) {11/2024}	218.93 (N.A.) {218.93}	10.00	95.00
		688	WIDENING TO EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FROM DESIGN KM 153.00 (MoRTH) (N24001947)	2-2023	2/2025 (2/2025) {2/2025}	177.94 (N.A.) {177.94}	6.66	47.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		689	WIDENING TO 4 LANE FROM KM 51.60 TO 76.20 (HEBRI TO PARKALA) AND FROM KM 85.20 TO 88.90 (KARAVALI JU) (MoRTH) (N24001948)	10-2022	10/2024 (12/2024) {12/2024}	355.72 (N.A.) {355.72}	11.32	60.00
		690	FOUR LANING OF LEFT OVER WORKS OF HOSPET BELLARY KARNATAKA/ AP BORDER FROM KM.280.080 TO KM. 375.450 (NHAI) (N24001989)	3-2023	5/2025 (N.A.) {5/2025}	830.28 (N.A.) {830.28}	634.76	73.64
		691	DEVELOPMENT OF 6 LANE ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KM. 97.000 TO KM. 162.500 MARADGI S (NHAI) (N24001993)	12-2022	10/2025 (N.A.) {10/2025}	1,589.00 (N.A.) {1,589.00}	724.33	60.70
		692	4/6L OF BANGALORE - PUNE SECTION OF BYPASS CONNECTING DHARWAD - HUBLI FROM KM. 403.80 TO KM. 433.20 (NHAI) (N24001994)	5-2022	3/2023 (N.A.) {9/2025}	1,135.39 (N.A.) {1,135.39}	339.37	66.12
		693	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM 422.000 TO 523.600 (CHITR) (MoRTH) (N24002011)	12-2021	6/2024 (12/2024) {12/2024}	516.96 (N.A.) {516.96}	19.93	70.00
		694	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40.00 TO KM 75.00 (EXISTING CHAINAGES) OF MANGALOR (MoRTH) (N24002012)	3-2023	3/2025 (3/2025) {3/2025}	718.52 (N.A.) {718.52}	24.81	23.00
		695	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM KM.0 TO KM. 80 ON NH 548B (VIJAYAPURA-SANKESWAR SE) (MoRTH) (N24002013)	3-2021	2/2022 (10/2024) {10/2024}	766.64 (N.A.) {766.64}	13.55	75.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		696	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24002186)	3-2024	9/2025 (N.A.) {9/2025}	166.58 (N.A.) {166.58}	3.62	-
		697	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM 55.6 TO KM 90.7 (EXISTING CHAINAGES) OF NH-766C () (MoRTH) (N24002187)	2-2024	2/2026 (N.A.) {2/2026}	313.56 (N.A.) {313.56}	53.65	-
		698	WIDENING TO 2L+PS FROM KM 71.00 TO 104.00 (EXISTING CHAINAGES) (SARJAPUR TO PATTADKALLU) ON BHANAPUR (MoRTH) (N24002188)	3-2024	3/2026 (N.A.) {3/2026}	445.62 (N.A.) {445.62}	33.24	-
		699	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0.00 (DESIGN CHAINAGE 0.00) TO KM 23.338 (DESIGN C) (MoRTH) (N24002189)	9-2024	3/2026 (N.A.) {3/2026}	196.05 (N.A.) {196.05}	2.34	-
	<u>STEEL</u>	700	SCREENING PLANT-II, DONIMALAI (NMDC) (N12000136)	9-2023	8/2026 (N.A.) {8/2026}	1,043.63 (N.A.) {1,043.63}	176.30	11.27
	<u>URBAN DEVELOPMENT</u>	701	BANGALORE METRO RAIL PROJECT PHASE-2 (BMRCL) (N28000058)	2-2014	2/2021 (N.A.) {3/2025}	26,405.14 (N.A.) {26,405.14}	20,936.29	89.00
		702	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B (BMRCL) (N28000151)	6-2021	6/2026 (N.A.) {6/2026}	14,788.10 (N.A.) {14,788.10}	2,424.04	30.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
KERALA	CIVIL AVIATION	703	CALICUT AIRPORT - DEVELOPMENT OF ADDITIONAL RESA ON EITHER END ON RUNWAY 10-28 AT CALICUT AIRPORT (AAI) (N04000111)	6-2023	9/2025 (N.A.) {9/2025}	484.57 (N.A.) {323.98}	54.09	16.50
	DEPARTMENT OF HIGHER EDUCATION	704	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA (CPWD EDUCATION) (N28000140)	7-2019	3/2021 (N.A.) {11/2025}	753.63 (N.A.) {753.63}	411.86	67.00
	HEALTH AND FAMILY WELFARE	705	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST (CPWD FOR HEALTH) (N28000112)	9-2017	3/2020 (5/2024) {11/2024}	150.29 (N.A.) {162.00}	146.95	100.00
	PETROLEUM	706	REPLACEMENT AND EXTENSION OF JETTY PIPELINES AT KOCHI REFINERY (BPCL) (N16000508)	3-2023	3/2026 (N.A.) {3/2026}	621.87 (N.A.) {621.87}	166.60	78.30
		707	SETTING UP POLYPROPYLENE UNIT AT KOCHI REFINERY (BPCL) (N16000530)	12-2023	10/2027 (N.A.) {10/2027}	4,460.00 (N.A.) {4,460.00}	214.40	9.60
	RAILWAYS	708	TRIVANDRUM-KANYAKUMARI DOUBLING (SR) (N22000399)	2-2015	3/2024 (N.A.) {12/2027}	1,431.90 (N.A.) {3,785.45}	3,184.42	42.10
		709	ERNAKULAM-KUMBALAM - PATCH DOUBLING (7.71 KM) (SR) (N22000619)	12-2010	3/2028 (N.A.) {12/2026}	600.82 (N.A.) {595.39}	282.30	8.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		710	KUMBALAM-THURAVUR - PATCH DOUBLING (15.59 KM) (SR) (N22000620)	12-2011	3/2027 (N.A.) {12/2026}	812.85 (N.A.) {802.80}	268.32	7.00
	ROAD TRANSPORT AND HIGHWAYS	711	4-LANNING OF THALSERRY - MAHE BYPASS (NHAI) (N24000704)	9-2017	5/2020 (11/2023) {2/2024}	1,124.11 (1,573.18) {1,573.18}	1,525.92	100.00
		712	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH (NHAI) (N24000784)	2-2018	2/2023 (12/2024) {6/2025}	1,424.77 (2,065.95) {2,065.95}	901.96	93.63
		713	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK (MoRTH) (N24001369)	2-2017	8/2017 (3/2022) {8/2024}	294.28 (296.53) {296.53}	286.80	98.00
		714	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) (MoRTH) (N24001370)	2-2017	9/2017 (1/2023) {8/2024}	380.76 (372.87) {372.87}	347.04	100.00
		715	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE (NHAI) (N24001648)	8-2022	1/2026 (N.A.) {1/2026}	2,429.52 (N.A.) {2,429.52}	1,028.39	56.75
		716	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 (NHAI) (N24001649)	12-2021	2/2025 (2/2025) {1/2026}	3,273.61 (N.A.) {3,273.61}	740.30	58.51

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		717	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTAM SECTION OF NH-66(OLD NH-47) FROM KM. 517+250 TO KM.54 (NHA) (N24001650)	12-2021	1/2025 (4/2026) {4/2026}	3,635.64 (N.A.) {3,635.64}	324.02	38.75
		718	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O (NHA) (N24001651)	9-2021	9/2024 (3/2026) {9/2024}	2,878.97 (N.A.) {2,878.97}	516.63	41.78
		719	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR (NHA) (N24001652)	3-2020	6/2022 (2/2024) {6/2024}	210.37 (216.94) {216.94}	198.10	100.00
		720	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH ?66 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 ((NHA) (N24001653)	11-2021	4/2025 (N.A.) {4/2025}	3,565.82 (N.A.) {3,064.11}	1,997.30	60.14
		721	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 (NHA) (N24001654)	6-2021	3/2025 (2/2026) {2/2026}	2,641.37 (N.A.) {2,641.37}	607.07	76.02
		722	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX (NHA) (N24001655)	6-2021	2/2025 (N.A.) {11/2025}	3,606.00 (3,946.56) {3,946.56}	3,120.23	70.41
		723	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. (NHA) (N24001656)	6-2021	3/2025 (N.A.) {12/2025}	2,595.00 (N.A.) {4,009.57}	3,044.77	62.75

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		724	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC (NHAI) (N24001657)	6-2021	10/2024 (12/2025) {12/2025}	2,842.14 (N.A.) {2,842.14}	477.69	70.53
		725	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM (NHAI) (N24001658)	1-2021	7/2024 (3/2025) {3/2025}	4,265.42 (N.A.) {4,728.40}	3,474.21	99.10
		726	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH- 66(OLD NH-17) FROM DESIGN CH (NHAI) (N24001659)	2-2021	7/2024 (3/2025) {3/2025}	3,375.31 (3,824.07) {3,824.07}	2,351.43	98.30
		727	SIX LANING OF THALIPARAMBHA- MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH (NHAI) (N24001660)	8-2020	2/2024 (8/2025) {3/2026}	2,714.60 (3,557.65) {2,714.60}	1,898.58	71.15
		728	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 (NHAI) (N24001661)	10-2020	4/2024 (5/2025) {3/2026}	3,219.47 (3,898.46) {3,896.46}	2,295.20	56.58
		729	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH (NHAI) (N24001662)	5-2020	5/2024 (11/2021) {5/2025}	1,981.07 (2,651.79) {1,981.07}	1,540.36	93.85
		730	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ (NHAI) (N24001663)	6-2020	4/2024 (10/2021) {12/2025}	3,041.65 (3,867.66) {3,041.65}	2,387.89	80.60

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		731	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ (NHAI) (N24001664)	6-2020	4/2024 (10/2021) {11/2025}	1,746.45 (2,538.06) {1,746.45}	1,250.34	78.55
		732	WIDENING/DEVELOPMENT OF EXISTING NH-85 FROM KM 0.000 TO KM 124.636 SECTION TO 2L/@L+PS SECTION IN TH (NHAI) (N24002074)	8-2022	6/2025 (N.A.) {6/2025}	1,231.74 (N.A.) {1,231.74}	399.90	45.20
	URBAN DEVELOPMENT	733	KOCHI METRO RAIL PROJECT PHASE II FROM JLN STADIUM TO INFOPARK VIA KAKKANAD (KMRCL) (N28000158)	7-2018	11/2026 (N.A.) {11/2026}	1,957.05 (N.A.) {1,957.05}	244.80	7.40
		734	KOCHI METRO RAIL PROJECT PHASE IB SECTION FROM S N JUNCTION TO THRIPIUNITHURA (KMRCL) (N28000159)	6-2019	9/2023 (N.A.) {9/2023}	355.70 (448.00) {448.33}	1.64	100.00
LADAKH	CIVIL AVIATION	735	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT (AAI) (N04000078)	7-2018	9/2021 (10/2025) {10/2025}	480.33 (N.A.) {640.00}	407.93	63.20
		736	KARGIL-ZANSKR PACKAGE-1 (NHIDCL) (N24001343)	3-2021	1/2023 (12/2024) {11/2025}	384.23 (N.A.) {384.23}	162.54	60.40
	ROAD TRANSPORT AND HIGHWAYS	737	KARGIL-ZANSKR PACKAGE-2 (NHIDCL) (N24001344)	3-2021	1/2023 (2/2025) {11/2025}	404.89 (N.A.) {404.89}	244.21	64.36
		738	KARGIL-ZANSKR PACKAGE-3 (NHIDCL) (N24001345)	8-2020	1/2023 (8/2025) {8/2025}	381.01 (N.A.) {381.01}	230.28	74.11

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MADHYA PRADESH		739	KARGIL-ZANSKR PACKAGE-8 (NHIDCL) (N24001348)	3-2021	1/2023 (8/2025) {8/2025}	398.37 (N.A.) {398.37}	274.39	82.28
		740	CONSTRUCTION OF REALIGNMENT BETWEEN PANDRASS- PASHKYUN (TOTAL LENGTH 27.10 KM) ON ROAD ZOZILA-KARGIL (BRO) (N24001999)	11-2021	6/2025 (N.A.) {6/2025}	426.14 (N.A.) {426.14}	16.27	37.00
	CIVIL AVIATION	741	UPGRADATION OF JABALPUR AIRPORT (AAI) (N04000087)	6-2016	6/2021 (7/2024) {7/2024}	412.24 (N.A.) {412.24}	402.81	100.00
		742	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 (AAI) (N04000098)	10-2021	8/2023 (8/2024) {8/2024}	446.12 (455.00) {455.00}	451.41	100.00
	COAL	743	KANCHAN OC EXPANSION (SECL) (N06000125)	12-2014	3/2021 (3/2026) {3/2026}	371.04 (N.A.) {371.04}	136.72	47.00
		744	AMADAND OPENCAST EXPANSION PROJECT (SECL) (N06000148)	3-2016	3/2021 (3/2027) {3/2027}	869.44 (N.A.) {869.44}	271.74	73.00
		745	GANDHIGRAM UG MINE (WCL) (N06000183)	8-2019	3/2026 (N.A.) {3/2026}	414.16 (N.A.) {414.16}	11.75	28.00
		746	BLOCK-B EXPANSION OPENCAST PROJECT (NCL) (N06000184)	7-2019	3/2023 (N.A.) {3/2027}	998.71 (N.A.) {998.71}	431.21	29.48
		747	NIGAHI EXPANSION OCP (15 TO 25 MTPA) (NCL) (N06000196)	11-2020	3/2025 (N.A.) {3/2028}	1,729.68 (N.A.) {1,729.68}	760.98	44.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		748	RAMPUR BATURA OC (4.0 MTY) (SECL) (N06000233)	7-2019	3/2026 (N.A.) {3/2026}	1,248.93 (N.A.) {1,248.93}	487.87	44.00
		749	TAWA III UG MINE (WCL) (N06000250)	12-2021	3/2027 (N.A.) {3/2027}	314.09 (N.A.) {324.25}	0.56	9.00
		750	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY) (WCL) (N06000257)	9-2022	3/2027 (N.A.) {3/2027}	399.20 (N.A.) {497.01}	64.13	42.00
		751	VISHNUPURI UG TO OC (WCL) (N06000260)	11-2022	3/2029 (N.A.) {3/2029}	220.62 (N.A.) {227.65}	0.00	7.00
		752	URDHAN OC (WCL) (N06000265)	1-2023	3/2031 (N.A.) {3/2031}	206.88 (N.A.) {228.42}	22.12	9.00
		753	SHARDA UG (WCL) (N06000266)	9-2023	3/2028 (N.A.) {3/2028}	166.25 (N.A.) {200.16}	1.69	11.00
	PETROLEUM	754	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF (BPCL) (N16000518)	5-2023	5/2028 (N.A.) {5/2028}	43,367.00 (N.A.) {43,367.00}	1,577.00	11.50
	POWER	755	SHAJAPUR 325MW SOLAR PV PROJECT (NTPC) (N18000348)	6-2022	3/2024 (N.A.) {6/2025}	1,530.49 (N.A.) {1,530.49}	1,207.64	70.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		756	TS FOR EVACUATION POWER RAJASTHAN REZ PH-IV (PART- 2:5.5GW) (JAISALMER/BARMER COMPLEX): PART-C (PGCIL) (N18000392)	8-2024	8/2026 (N.A.) {8/2026}	2,708.00 (N.A.) {2,708.00}	75.00	18.70
		757	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-2 5.5GW] [JAISALMER/BARME (PGCIL) (N18000399)	10-2024	10/2026 (N.A.) {10/2026}	3,674.00 (N.A.) {3,674.00}	81.00	7.00
	RAILWAYS	758	RAMGANJMUNDI-BHOPAL (NL),WCR (WCR) (220100314)	4-2001	12/2025 (12/2025) {6/2026}	3,032.00 (3,032.46) {5,125.16}	3,423.90	69.00
		759	RATLAM-MHOW-KHANDWA- AKOLA (GC) (WR) (N22000120)	4-2008	2/2027 (2/2027) {2/2027}	5,677.88 (5,677.80) {6,203.51}	4,271.40	80.00
		760	KATNI - SINGRAULI DOUBLING PROJECT (WCR) (N22000351)	12-2015	12/2026 (12/2027) {12/2027}	2,445.29 (2,445.30) {4,353.50}	3,092.70	90.00
		761	KATNI GRADE SEPARATOR/BYE PASS (WCR) (N22000416)	8-2016	9/2024 (6/2025) {9/2024}	1,247.64 (1,247.64) {2,300.00}	1,404.52	89.00
		762	ANUPPUR-KATNI (SECR) (N22000485)	4-2015	12/2021 (12/2023) {3/2025}	1,860.94 (1,680.00) {2,311.02}	1,913.51	100.00
		763	NIMACH BADI SADRI NEW LINE PROJECT (WR) (N22000503)	4-2017	3/2022 (N.A.) {3/2026}	495.18 (N.A.) {495.18}	276.02	20.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		764	NIMACH-RATLAM (133 KM) (WR) (N22000536)	10-2021	10/2027 (6/2025) {6/2025}	1,095.88 (1,095.88) {1,095.88}	1,038.90	72.00
		765	SATNA - REWA (50 KM) (WCR) (N22000554)	11-2015	3/2026 (N.A.) {3/2026}	500.00 (40.00) {500.00}	1.41	80.00
		766	INDORE BUDNI (INDORE JABALPUR) (RVNL) (N22000601)	9-2018	9/2030 (N.A.) {9/2030}	7,474.01 (N.A.) {7,393.75}	1,004.86	-
	ROAD TRANSPORT AND HIGHWAYS	767	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 (MoRTH) (N24000513)	3-2015	8/2017 (12/2023) {6/2025}	511.83 (N.A.) {511.83}	478.84	93.06
		768	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN (NHAI) (N24000709)	12-2017	2/2020 (12/2024) {12/2024}	950.27 (N.A.) {786.43}	643.90	99.50
		769	4LBERKHEDI TO GODPEHRA NH- 44 (NHAI) (N24001614)	2-2022	11/2024 (N.A.) {11/2024}	524.84 (N.A.) {524.84}	2,423.91	50.00
		770	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I) (NHAI) (N24001615)	3-2021	4/2024 (5/2024) {8/2024}	790.78 (N.A.) {790.78}	2,139.29	75.00
		771	2L PS OF SATNA - MAIHAR SECTION OF NH-135BG FROM KM 80.800 TO KM 120.125 (NHAI) (N24001616)	1-2021	10/2023 (N.A.) {2/2025}	428.04 (N.A.) {428.04}	351.97	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		772	KATNI BYPASS FROM KM. 359.50 TO KM. 378.50 (NHAI) (N24001618)	9-2019	9/2022 (N.A.) {2/2025}	194.40 (235.00) {235.00}	207.60	98.84
		773	4L OF CHANDESARA TO KHEDAKHAJURIYA FROM KM. 0.000 TO (-) 750 AND KM 0.000 TO KM 41.400 OF NH-752D (NHAI) (N24001759)	1-2020	6/2024 (6/2025) {6/2025}	909.84 (N.A.) {909.84}	502.49	99.00
		774	INDORE - HARD A (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] (NHAI) (N24001762)	10-2021	1/2024 (12/2024) {12/2024}	1,146.22 (N.A.) {1,146.22}	662.24	91.21
		775	ADDITIONAL WORKS (2VUPS, MR-10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE-DEWAS SECTION OF N (NHAI) (N24001765)	8-2022	7/2024 (N.A.) {12/2025}	207.77 (N.A.) {207.77}	65.02	49.28
		776	INDORE - HARD A (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] (NHAI) (N24001766)	1-2022	10/2024 (N.A.) {5/2025}	1,011.29 (N.A.) {1,011.29}	284.80	62.10
		777	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND (NHAI) (N24001767)	1-2021	4/2024 (N.A.) {4/2024}	1,001.69 (N.A.) {1,001.69}	517.00	82.09
		778	BALANCE WORK OF 4L OF INDORE-GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF (NHAI) (N24001768)	8-2019	4/2023 (N.A.) {11/2023}	323.51 (N.A.) {323.51}	51.96	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		779	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69 (NHA) (N24001770)	2-2022	3/2024 (3/2025) {5/2025}	417.51 (N.A.) {417.51}	288.41	95.37
		780	2- LANE WITH PAVED SHOULDERS OF HINOTIYA TO MEHULWA FROM DESIGN KM 27+000 90F EXISTING SH-19 KM 26+5 (NHA) (N24001921)	8-2021	9/2025 (N.A.) {9/2025}	581.65 (592.03) {581.65}	186.33	39.53
		781	CONSTRUCTION OF MIHONA BYPASS, LAHAR BYPASS, DABOH BYPASS and BHANDER BYPASS (TOTAL LENGTH 20.60 KM) (MoRTH) (N24001962)	3-2022	12/2024 (N.A.) {3/2025}	179.19 (N.A.) {179.19}	47.91	96.00
		782	UPGRADATION OF NASRULLAGANI-REHTI-BUDHNI SCCTION TO 2-LANE WITH PAVED SHOULDER FROM KM 0+150 TO KM (MoRTH) (N24001963)	12-2021	10/2024 (N.A.) {9/2025}	305.12 (N.A.) {305.12}	71.47	34.46
		783	UPGRADATION and WIDENING OF JHARKHEDA- BERSIA - DHOLKHEDI FROM DESIGN KM 0+000 TO KM 87+900 (DESIGN (MoRTH) (N24001964)	3-2022	5/2025 (N.A.) {5/2025}	365.21 (N.A.) {365.21}	112.27	64.00
		784	REHABILITATION AND UPGRADATION OF KURWAI?MUNGAOLI?CHANDERI ROAD SECTION OF NH-346, FROM DESIGN CHAIN (MoRTH) (N24001965)	3-2022	2/2025 (N.A.) {12/2025}	386.49 (N.A.) {386.49}	77.42	48.77
		785	BALANCE WORK FOR REHABILITATION AND UP- GRADATION OF SIDHI- SINGRAULI FROM KM 82.400 TO KM 187.993 SEC (MoRTH) (N24001966)	12-2020	4/2023 (N.A.) {6/2025}	529.44 (N.A.) {529.44}	378.40	62.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		786	4L GREENFIELD RUDHI TO DESHGAON (PKG V OF BETUL- KHANDWA/DESHGAON) - N/04015/06003/MP (NHAI) (N24001967)	11-2018	10/2025 (N.A.) {10/2025}	521.21 (N.A.) {521.21}	98.23	39.80
		787	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF JIRAPUR- SUSNER-MP-RJ B (MoRTH) (N24002018)	1-2022	3/2025 (N.A.) {3/2025}	239.72 (232.22) {232.22}	73.40	100.00
		788	UPGRADATION OF DINDORI- SAGARTOLA-KABICHABUTRA (MP-CG BORDER) SECTION OF NH -45 FROM KM 0+00(DESIGN) (MoRTH) (N24002019)	1-2022	9/2025 (N.A.) {9/2025}	329.14 (319.09) {319.09}	52.70	50.12
		789	CONSTRUCTION OF KAITHI- PADARIA KALA BYPASS, PATNA- TAMOLI BYPASS, JASO BYPASS , NAGOD BYPASS (TOTAL L (MoRTH) (N24002020)	3-2022	10/2025 (N.A.) {10/2025}	158.36 (158.00) {158.36}	22.68	30.00
		790	BALANCE WORK OF 4L OF NAURADEHI SANCTUARY DE- SCOPE STRETCH OF HIRAN RIVER TO SINDOOR RIVER FROM KM. (NHAI) (N24002067)	1-2021	7/2023 (N.A.) {4/2025}	178.18 (N.A.) {178.18}	161.64	93.10
		791	CONSTRUCTION OF 4-LANE FROM BARELA TO MANEGAON SECTION OF NH-30 FROM DESIGN CH. 2.900 TO DESIGN CH. (NHAI) (N24002068)	12-2022	3/2025 (N.A.) {12/2025}	652.33 (N.A.) {652.33}	334.34	71.32
		792	CONSTRUCTION OF ADDITIONAL 3 LANE WITH PAVED SHOULDER (DESIGN LENGTH 8.87 KM) AS REALIGNMENT OF BAKA (NHAI) (N24002069)	7-2022	12/2024 (N.A.) {12/2024}	209.29 (N.A.) {209.29}	140.22	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		793	INDORE - EDLABAD (PKG-II) [TEJAJINAGAR TO BALWARA] (NHAI) (N24002070)	1-2022	1/2025 (N.A.) {1/2025}	1,162.80 (N.A.) {1,162.80}	488.48	80.00
		794	CONSTRUCTION OF (I) 4-LANE HIGHWAY FROM VIDISHA TO HINOTIYA FROM KM. 0.000 TO KM. 27.000 (LENGTH=27 (NHAI) (N24002077)	9-2022	12/2025 (N.A.) {12/2025}	1,000.63 (N.A.) {1,000.63}	289.65	50.10
		795	FOUR LANING OF RAGHOGARH (DESIGN CH.29.300/EXISTING CH. 29.555) TO NANASA (DESIGN CH.92.971/EXISTING (NHAI) (N24002166)	3-2024	3/2026 (3/2026) {3/2026}	799.20 (N.A.) {799.20}	306.27	32.60
		796	BALANCE WORKS OF 4 LANE DIVIDED CARRIAGEWAY OF MISSING LINK SECTION OF NH- 39 (REWA BYPASS) FROM JUNC (NHAI) (N24002200)	4-2024	4/2026 (N.A.) {4/2026}	355.36 (N.A.) {355.36}	39.06	22.49
	<u>SOCIAL JUSTICE</u>	797	CENTRE FOR DISABILITY SPORTS (CPWD) (N38000001)	2-2019	3/2024 (N.A.) {3/2024}	170.99 (N.A.) {170.99}	73.80	74.00
	<u>URBAN DEVELOPMENT</u>	798	BHOPAL METRO RAIL (MPMRCL) (N28000124)	11-2018	2/2023 (6/2028) {6/2028}	6,941.40 (N.A.) {6,941.40}	2,937.30	39.76
		799	INDORE METRO RAIL (MPMRCL) (N28000125)	11-2018	2/2023 (12/2028) {12/2028}	7,500.80 (N.A.) {7,500.80}	3,677.77	52.18
<u>MAHARASHTRA</u>	<u>CIVIL AVIATION</u>	800	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT (AAI) (N04000079)	3-2017	4/2021 (12/2023) {12/2023}	475.39 (N.A.) {520.00}	532.88	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		801	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM (AAI) (N04000096)	6-2017	12/2020 (N.A.) {4/2024}	255.68 (N.A.) {270.00}	267.86	100.00
	COAL	802	AMALGAMATED YEKONA-I YEKONA-II (WCL) (N06000132)	8-2015	3/2025 (N.A.) {3/2025}	727.28 (N.A.) {727.28}	530.02	86.00
		803	UKNI DEEP OC (WCL) (N06000179)	1-2019	3/2021 (3/2025) {3/2025}	237.06 (N.A.) {318.14}	163.86	91.00
		804	GHONSA EXPANSION DEEP OC (WCL) (N06000205)	3-2021	3/2028 (N.A.) {3/2029}	184.71 (N.A.) {241.72}	9.25	6.00
		805	SASTI EXPANSION OC (WCL) (N06000206)	8-2020	3/2026 (N.A.) {3/2026}	319.04 (N.A.) {371.59}	68.64	24.00
		806	DHUPTALA OC(SASTI UG TO OC) (WCL) (N06000209)	10-2021	3/2028 (N.A.) {3/2028}	711.00 (N.A.) {720.87}	159.15	33.00
		807	ADASA UG TO OC (1.50 MTY) (WCL) (N06000219)	11-2018	3/2024 (3/2025) {3/2025}	316.00 (N.A.) {333.43}	208.20	78.00
		808	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) (WCL) (N06000222)	2-2020	3/2027 (N.A.) {3/2027}	822.88 (N.A.) {1,184.33}	578.89	48.00
		809	AMALGAMATED INDER- KAMPTEE DEEP OC (3.20 MTY) (WCL) (N06000226)	9-2018	3/2024 (3/2025) {3/2025}	235.90 (N.A.) {313.34}	116.46	87.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		810	SAONER UG MINE I EXPANSION (WCL) (N06000251)	1-2022	3/2028 (N.A.) {3/2028}	228.64 (N.A.) {253.51}	118.34	27.00
		811	SINGHORI DEEP OC (WCL) (N06000252)	5-2022	3/2029 (N.A.) {3/2029}	335.75 (N.A.) {421.84}	22.01	16.00
		812	MAKARDHOKDA I EXPANSION OC (WCL) (N06000253)	6-2022	3/2026 (N.A.) {3/2026}	361.87 (N.A.) {497.06}	33.90	12.00
		813	BHATADI EXPANSION OC (WCL) (N06000254)	5-2022	3/2028 (N.A.) {3/2028}	580.60 (N.A.) {729.86}	61.33	17.00
		814	NEW MAJARI UG TO OC (3.0 MTY) (WCL) (N06000255)	9-2022	3/2027 (N.A.) {3/2027}	402.27 (N.A.) {496.38}	47.99	27.00
		815	BHANEGAON OC (1.15MTY) (WCL) (N06000256)	9-2022	3/2028 (N.A.) {3/2028}	405.20 (N.A.) {494.60}	10.21	7.00
		816	GOKUL EXPANSION OC (WCL) (N06000264)	4-2021	3/2026 (N.A.) {3/2026}	309.58 (N.A.) {456.95}	3.65	7.00
		817	KOLGAON EXPANSION (DEEP) OC (WCL) (N06000267)	9-2023	3/2027 (N.A.) {3/2027}	198.71 (N.A.) {206.19}	0.55	5.00
		818	AMALGAMATED GAURI PAUNI EXPANSION OC (WCL) (N06000271)	3-2024	3/2030 (N.A.) {3/2030}	1,225.21 (N.A.) {1,428.25}	52.83	17.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		819	GAURI CENTRAL OCM (WCL) (N06000278)	6-2024	3/2030 (N.A.) {3/2030}	973.07 (N.A.) {1,015.07}	0.00	-
		820	BALLARPUR NORTHWEST OC MINE (WCL) (N06000282)	12-2022	3/2029 (N.A.) {3/2029}	360.18 (N.A.) {360.18}	0.00	-
		821	NORTHERN EXTENSION OF MUNGOLI NIRGUDA DEEP OC (WCL) (N06000283)	6-2024	3/2029 (N.A.) {3/2029}	1,024.91 (N.A.) {1,184.44}	0.00	-
		822	AMALGAMATED GONDEGAON - GHATROHAN EXPANSION OCM (WCL) (N06000284)	9-2024	3/2029 (N.A.) {3/2029}	668.54 (N.A.) {871.59}	0.00	-
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	823	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI (CPWD EDUCATION) (N28000117)	1-2018	7/2020 (11/2023) {2/2024}	223.37 (275.00) {230.00}	141.16	100.00
	<u>HEALTH AND FAMILY WELFARE</u>	824	500 BEDDED HOSPITAL INCLUDING 50 SUPERSPECIALITY BEDS FOR ESIC AT PUNE (CPWD) (N21000033)	7-2022	9/2025 (N.A.) {9/2025}	429.25 (N.A.) {429.25}	99.08	-
	<u>PETROLEUM</u>	825	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS (ONGC) (N16000213)	12-2015	4/2018 (12/2023) {6/2025}	3,190.69 (3,375.90) {3,375.90}	3,006.09	88.40
		826	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND (GAIL) (N16000430)	5-2019	4/2025 (10/2025) {10/2025}	8,797.00 (11,256.00) {11,256.00}	6,237.68	82.79

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		827	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL (BPCL) (N16000442)	4-2021	6/2024 (N.A.) {4/2025}	1,164.69 (N.A.) {1,164.69}	827.81	79.30
		828	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY (IOCL) (N16000446)	9-2021	10/2023 (5/2024) {5/2024}	378.00 (N.A.) {378.00}	120.07	39.08
		829	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI (BPCL) (N16000452)	5-2022	3/2024 (N.A.) {9/2024}	423.39 (N.A.) {423.39}	241.66	75.10
		830	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA) (IOCL) (N16000456)	9-2022	8/2025 (N.A.) {3/2026}	165.00 (N.A.) {165.00}	74.85	64.01
		831	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK (ONGC) (N16000470)	6-2022	10/2025 (N.A.) {2/2026}	4,144.41 (6,406.90) {6,406.90}	2,782.76	77.10
		832	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS (IOCL) (N16000487)	3-2022	3/2030 (N.A.) {9/2031}	865.00 (N.A.) {865.00}	54.99	2.80
		833	ANDHERI RESIDENTIAL TOWERS MUMBAI (IOCL) (N16000503)	6-2017	5/2025 (6/2026) {6/2026}	281.35 (389.67) {389.67}	216.88	49.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		834	CONSTRUCTION OF ADDITIONAL TANKAGES AND ALLIED FACILITIES AT JNPT TERMINAL (IOCL) (N16000504)	4-2022	10/2024 (8/2026) {8/2026}	341.43 (436.14) {436.14}	232.19	45.80
		835	INSTALLATION OF INDEPENDENT DE- AROMATIZED SOLVENTS PRODUCTION FACILITIES AT MUMBAI REFINERY (BPCL) (N16000507)	3-2023	7/2025 (N.A.) {7/2025}	405.00 (N.A.) {405.00}	174.12	75.70
		836	PART REPLACEMENT PIPELINE PROJECT (PRPP) (ONGC) (N16000515)	11-2022	5/2024 (12/2024) {3/2025}	1,219.48 (N.A.) {1,145.10}	678.96	84.00
		837	POL AND LOBS INSTALLATIONS WITH RECEIPT PIPELINES AT RASAYANI (BPCL) (N16000519)	5-2023	5/2026 (N.A.) {5/2026}	2,585.00 (N.A.) {2,585.00}	438.55	53.00
		838	MHN TCPP PGC BGC PROJECT (MTPBP) (ONGC) (N16000526)	2-2024	5/2026 (N.A.) {5/2026}	2,329.45 (N.A.) {2,354.23}	500.96	37.00
		839	PRP-VIII GROUP B (NH AND BS ASSET) (ONGC) (N16000533)	6-2024	5/2026 (N.A.) {2/2026}	2,379.84 (N.A.) {2,379.84}	473.40	47.90
		840	HP TDAE UNIT IN MUMBAI REFINERY (HPCL) (N16000534)	6-2024	4/2026 (N.A.) {4/2026}	240.00 (N.A.) {240.00}	24.24	25.70
		841	INTEGRATED DEVELOPMENT OF 4 CONTRACT AREAS UNDER DSF2 (ONGC) (N16000537)	5-2023	4/2027 (N.A.) {4/2027}	6,183.79 (N.A.) {6,183.79}	0.00	11.20

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		842	LUBE MODERNIZATION AND BOTTOM UPGRADATION PROJECT (HPCL) (N16000540)	12-2024	3/2028 (N.A.) {3/2028}	4,679.00 (N.A.) {4,679.00}	163.61	4.10
	POWER	843	BIKANER SOLAR POWER PROJECT (SJVN) (N18000335)	4-2022	5/2024 (N.A.) {9/2025}	5,491.89 (532.00) {5,491.89}	3,979.19	74.00
		844	TS FOR EVACUATION OF 7GW RE INJECTION AT KHAVDA PS UNDER PHASE-IV PART E4 (PGCIL) (N18000377)	11-2023	7/2025 (N.A.) {9/2025}	224.00 (N.A.) {224.00}	0.00	5.00
	RAILWAYS	845	AHMEDNAGAR-PARLI VAIJNATH(NL) CR (CR) (220100181)	2-1997	3/2026 (N.A.) {1/2026}	2,539.00 (N.A.) {4,957.27}	4,777.07	94.00
		846	MUMBAI URBAN TRANSPORT PROJECT PHASE-II (MRTP) (N22000092)	4-2008	3/2014 (N.A.) {3/2014}	8,087.11 (N.A.) {918.53}	7,110.54	77.30
		847	WARDHA-NANDED MAHARASHTRA (CR) (N22000231)	4-2008	3/2027 (N.A.) {1/2026}	3,445.48 (N.A.) {3,445.34}	3,107.47	47.00
		848	KALYAN-KASARA 3RD LINE (CR) (N22000233)	4-2011	12/2025 (N.A.) {12/2026}	792.89 (N.A.) {1,395.79}	868.61	50.00
		849	WARDHA-SEWAGRAM NGP 3RD LINE (CR) (N22000250)	4-2012	12/2025 (N.A.) {2/2026}	540.02 (N.A.) {540.02}	729.82	80.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		850	WARDHA-BALHARSHAH - 3RD LINE (132 KM) (CR) (N22000356)	2-2015	12/2025 (N.A.) {3/2026}	1,384.72 (N.A.) {1,384.72}	1,517.52	67.00
		851	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) (CR) (N22000358)	2-2015	3/2027 (N.A.) {3/2027}	2,449.91 (N.A.) {2,449.91}	1,704.81	50.00
		852	PUNE-MIRAJ-LONDA (467 KM) (CR) (N22000359)	2-2015	2/2025 (N.A.) {5/2025}	3,627.47 (3,627.00) {7,037.24}	4,584.11	84.00
		853	DAUND - MANMAD (236 KM) (CR) (N22000360)	2-2016	12/2025 (N.A.) {1/2026}	2,081.27 (N.A.) {2,081.27}	2,670.38	88.00
		854	MANMAD - JALGAON - 3RD LINE (160 KM) (CR) (N22000361)	2-2016	12/2024 (N.A.) {3/2026}	1,035.16 (N.A.) {1,558.75}	1,636.16	80.00
		855	WARDHA - NAGPUR - 4TH LINE (76 KM) (CR) (N22000362)	2-2016	12/2025 (N.A.) {2/2026}	638.00 (N.A.) {637.95}	941.27	80.00
		856	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) (SECR) (N22000420)	9-2016	12/2024 (N.A.) {12/2025}	3,544.92 (N.A.) {3,544.25}	3,023.12	95.00
		857	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (WR) (N22000434)	3-2010	10/2024 (N.A.) {3/2024}	311.00 (N.A.) {311.36}	0.00	-
		858	WADSA-GADHCHIROLI NEW LINE (52.36 KM) (SECR) (N22000480)	6-2018	3/2027 (N.A.) {12/2026}	1,886.05 (N.A.) {1,880.61}	740.67	25.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		859	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (N22000511)	8-2022	8/2027 (N.A.) {3/2029}	955.00 (N.A.) {2,089.25}	114.84	-
		860	SOLAPUR-TULJAPUR- OSMANABAD (UMBRELLA WORK) (CR) (N22000513)	1-2019	3/2028 (N.A.) {12/2027}	904.92 (N.A.) {2,933.01}	1,130.01	7.00
		861	DHULE (BORVIHIR)-NARDANA (UMBRELLA WORK) (CR) (N22000514)	1-2019	12/2026 (N.A.) {3/2028}	492.76 (N.A.) {1,158.99}	198.13	5.00
		862	KALYAN-MURBAD VIA ULHASNAGAR (UMBRELLA WORK) (CR) (N22000515)	2-2023	3/2027 (N.A.) {3/2027}	836.12 (N.A.) {836.12}	9.23	-
		863	BARAMATI - LONAND (CR) (N22000615)	2-1999	3/2027 (N.A.) {3/2027}	736.44 (N.A.) {1,843.90}	663.53	50.00
		864	MUMBAI URBAN TRANSPORT PROJECT IIIA (MRVC) (N22000627)	4-2019	12/2027 (N.A.) {12/2027}	33,690.00 (N.A.) {33,690.00}	812.06	-
		865	NAGPUR- NAGBHIR RAILWAY LINE GAUGE CONVERSION PROJECT (MRIDC) (N22000629)	10-2019	6/2024 (N.A.) {10/2025}	1,400.00 (N.A.) {2,383.00}	1,739.70	85.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	866	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM (MoRTH) (N24000332)	1-2015	(N.A.) { }	225.81 (N.A.) {225.81}	167.96	96.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		867	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN (NHAI) (N24000442)	12-2015	3/2019 (11/2023) {5/2025}	649.50 (N.A.) {649.50}	614.65	92.64
		868	NAGPUR RING ROAD PACKAGE- 2 (NHAI) (N24000560)	3-2016	7/2019 (3/2024) {5/2025}	591.66 (N.A.) {591.66}	632.40	98.73
		869	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000584)	3-2016	(N.A.) {12/2023}	1,142.62 (1,907.03) {1,142.62}	1,056.08	95.17
		870	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000585)	3-2016	(N.A.) { }	1,101.58 (N.A.) {1,101.58}	608.53	-
		871	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) (NHAI) (N24000656)	3-2017	3/2020 (7/2022) {12/2025}	744.64 (N.A.) {1,007.00}	467.65	94.65
		872	4-LANNING OF WARANGA- MAHAGAON SECTION(KM 253.7000 TO 320.580) (NHAI) (N24000659)	3-2017	3/2017 (5/2021) {10/2024}	1,059.73 (1,071.00) {1,071.00}	878.19	96.50
		873	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF (NHAI) (N24000851)	3-2018	7/2021 (N.A.) {6/2025}	1,162.92 (1,182.87) {1,182.87}	412.38	59.00
		874	SARSAM TO KOTHARI (MoRTH) (N24001002)	2-2016	7/2019 (N.A.) {12/2023}	545.64 (N.A.) {545.64}	232.64	93.68

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		875	AKOLA TO AKOT (MoRTH) (N24001003)	1-2017	6/2019 (N.A.) {12/2023}	313.95 (N.A.) {313.95}	270.26	99.00
		876	DIGRAS DARWAH KARANJA (MoRTH) (N24001013)	1-2017	6/2019 (N.A.) {12/2023}	391.06 (391.00) {391.06}	287.60	92.76
		877	DAHEGAON TO KUHI (MoRTH) (N24001017)	1-2017	6/2019 (N.A.) {12/2023}	228.89 (229.00) {228.89}	154.82	99.00
		878	BHANDARA TO GHOTITOK (MoRTH) (N24001018)	1-2017	6/2019 (N.A.) {6/2019}	392.83 (393.00) {392.83}	274.75	100.00
		879	AMDIT TO SAONER (MoRTH) (N24001021)	1-2017	6/2019 (N.A.) {12/2023}	396.91 (397.00) {396.91}	289.79	98.69
		880	WADI TO ASOLA (MoRTH) (N24001022)	1-2017	9/2019 (N.A.) {12/2023}	363.82 (364.00) {363.82}	154.65	93.15
		881	RALEGAON TO RAMTIRTH (MoRTH) (N24001046)	1-2017	7/2019 (N.A.) {8/2023}	210.81 (N.A.) {210.81}	210.81	96.50
		882	VITA TO NAGAJ (MoRTH) (N24001050)	3-2018	12/2019 (N.A.) {12/2023}	304.58 (305.00) {304.58}	154.68	68.39
		883	KARAD PATAN CHIPLUN GUHAGAR (MoRTH) (N24001057)	2-2017	6/2019 (N.A.) {10/2023}	407.19 (407.00) {407.19}	323.02	90.00
		884	KARWANDI TO RAJURI (MoRTH) (N24001058)	3-2018	12/2019 (N.A.) {3/2024}	276.95 (277.00) {276.95}	160.94	92.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		885	PALPHATA TO PHULAMBARI (MoRTH) (N24001060)	3-2018	12/2019 (N.A.) {12/2023}	227.19 (227.00) {227.19}	141.92	95.00
		886	NANDED TO JALKOT (MoRTH) (N24001069)	12-2017	9/2019 (N.A.) {9/2019}	456.93 (457.00) {456.93}	278.22	95.00
		887	PUNE TO MALE VILLAGE (MoRTH) (N24001078)	3-2018	12/2019 (N.A.) {12/2023}	228.31 (N.A.) {228.31}	100.97	93.83
		888	ARDHAPUR TO HIMAYATNAGAR (MoRTH) (N24001079)	12-2017	6/2020 (N.A.) {12/2023}	426.06 (426.00) {426.06}	271.40	96.25
		889	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER (MoRTH) (N24001080)	3-2018	12/2019 (N.A.) {10/2023}	256.15 (N.A.) {256.15}	126.62	98.00
		890	PUNE RAIGARH DISTRICT BORDER TO MANGAON (MoRTH) (N24001082)	3-2018	12/2019 (N.A.) {12/2023}	223.46 (N.A.) {223.46}	123.46	100.00
		891	KOLDE TO KHETIYA (MoRTH) (N24001090)	1-2017	7/2019 (N.A.) {12/2023}	509.18 (N.A.) {509.18}	283.13	94.81
		892	SATARA TO MHASWAD (MoRTH) (N24001092)	1-2017	7/2019 (N.A.) {12/2023}	653.46 (N.A.) {653.46}	369.62	77.00
		893	MHASWAD TO TEMBHURNI (MoRTH) (N24001099)	1-2017	7/2019 (N.A.) {12/2023}	488.60 (N.A.) {488.60}	279.42	76.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		894	KURUDWADI TO PANDHARPUR (MoRTH) (N24001101)	1-2017	7/2019 (N.A.) {11/2023}	307.63 (N.A.) {307.63}	232.57	96.27
		895	PANDHARPUR TO SANGOLA (MoRTH) (N24001102)	7-2017	7/2019 (N.A.) {12/2023}	218.38 (N.A.) {218.38}	182.63	99.78
		896	PEN TO KHOPOLI (MoRTH) (N24001106)	3-2018	3/2018 (N.A.) {1/2024}	301.39 (302.00) {301.39}	170.12	82.07
		897	PANCHARAL TO MANDANGHAR (MoRTH) (N24001107)	7-2018	5/2020 (N.A.) {5/2020}	381.08 (302.00) {381.08}	45.66	-
		898	NASRATPUR TO BARASGAON (MoRTH) (N24001112)	7-2016	9/2019 (N.A.) {9/2019}	406.54 (407.00) {406.54}	274.30	-
		899	INDAPUR TO VADPALE (MoRTH) (N24001114)	1-2017	12/2019 (N.A.) {3/2024}	1,202.52 (1,656.94) {1,202.52}	1,450.82	61.42
		900	PAITHAN TO SHIRUR (MoRTH) (N24001122)	3-2017	6/2019 (N.A.) {3/2024}	341.80 (N.A.) {341.80}	226.19	78.60
		901	SHIRUR TO KHARDA (MoRTH) (N24001123)	2-2017	6/2019 (N.A.) {12/2023}	381.77 (N.A.) {381.77}	199.48	83.93
		902	AURANGABAD TO SILLOD (MoRTH) (N24001124)	2-2017	6/2019 (N.A.) {12/2023}	456.32 (541.93) {456.32}	355.54	94.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		903	SILLOD TO FARDAPUR (MoRTH) (N24001125)	2-2017	6/2019 (N.A.) {12/2023}	337.46 (432.98) {337.46}	335.30	92.00
		904	BHOGAN KHURD TO KASHEDI (MoRTH) (N24001132)	9-2017	6/2021 (N.A.) {12/2023}	743.21 (743.00) {743.21}	911.64	88.69
		905	KANTE TO WAKED (MoRTH) (N24001134)	3-2016	11/2019 (N.A.) {12/2024}	1,230.02 (1,230.00) {1,230.02}	791.80	-
		906	PARLI PIMPLA DAHIGUDA (MoRTH) (N24001138)	2-2017	6/2019 (N.A.) {8/2023}	205.72 (206.00) {205.72}	85.71	100.00
		907	UPGRADATION OF ADHALGAON- JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH (MoRTH) (N24001448)	11-2021	2/2022 (N.A.) {2/2022}	223.35 (N.A.) {223.35}	209.36	87.88
		908	REPANPALLI TO SIRONCHA (MoRTH) (N24001468)	3-2022	6/2022 (N.A.) {6/2024}	282.07 (N.A.) {282.07}	34.65	-
		909	TUNNEL AT KAMBATAKI GHAT SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0 (NHAI) (N24001486)	2-2019	2/2022 (12/2024) {8/2025}	493.00 (N.A.) {493.00}	399.49	76.49
		910	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL-ALANDI SECTION (NHAI) (N24001488)	9-2021	9/2023 (12/2024) {5/2025}	618.45 (N.A.) {618.45}	639.23	96.20

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		911	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) (NHAI) (N24001493)	12-2022	12/2024 (N.A.) {11/2025}	1,749.86 (N.A.) {1,749.86}	1,838.16	65.41
		912	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 ((NHAI) (N24001495)	11-2022	11/2024 (N.A.) {9/2025}	930.00 (N.A.) {930.00}	618.34	75.90
		913	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH-965G (SAINT TUKARAM MARG) (NHAI) (N24001502)	9-2021	9/2023 (5/2025) {5/2025}	624.45 (580.15) {580.15}	420.42	2.00
		914	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH-965G (SAINT TUKARAM MARG) (NHAI) (N24001503)	9-2021	9/2023 (1/2025) {3/2025}	667.66 (666.21) {666.21}	610.63	3.00
		915	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) (NHAI) (N24001504)	5-2022	5/2024 (6/2025) {6/2025}	1,260.00 (N.A.) {1,260.00}	665.73	96.00
		916	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) (NHAI) (N24001505)	3-2022	3/2024 (6/2025) {6/2025}	1,549.02 (N.A.) {1,549.02}	699.00	78.13
		917	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) (NHAI) (N24001506)	2-2022	2/2024 (6/2025) {6/2025}	2,747.00 (N.A.) {2,747.00}	1,125.16	77.05

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		918	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) (NHAI) (N24001507)	11-2022	5/2024 (6/2025) {6/2025}	1,124.00 (N.A.) {1,124.00}	483.84	70.03
		919	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) (NHAI) (N24001508)	11-2022	10/2024 (6/2025) {6/2025}	1,450.00 (N.A.) {1,450.00}	718.65	82.05
		920	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XV) [KM. 20.200 TO KM. 43.000 OF SPUR] (AKLOLI - AMNE) (NHAI) (N24001521)	11-2022	10/2024 (4/2025) {4/2025}	990.00 (N.A.) {990.00}	406.91	70.25
		921	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) (NHAI) (N24001546)	1-2023	1/2025 (N.A.) {1/2025}	1,025.20 (N.A.) {1,025.20}	446.14	43.52
		922	BALANCE WORKS OF 4L PANVEL- INDAPUR SECTION OF NH-66 (OLD NH-17) FROM KM 42.300 (KASU) TO KM 84.600 ((NHAI) (N24001607)	10-2022	5/2024 (12/2025) {12/2025}	332.00 (N.A.) {332.00}	240.77	64.63
		923	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) (NHAI) (N24001608)	9-2021	7/2025 (N.A.) {7/2025}	2,208.68 (N.A.) {2,208.68}	565.20	73.73
		924	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH-66(OLD NH- 17) FROM KM 0.000 (PANVEL) TO (NHAI) (N24001609)	1-2023	12/2023 (6/2025) {6/2025}	151.26 (N.A.) {151.26}	153.74	86.38

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		925	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL ? ALANDI S (NHAI) (N24001610)	1-2022	5/2024 (3/2025) {5/2025}	1,833.73 (N.A.) {1,833.73}	539.18	95.64
		926	FOUR LANING OF AURANGABAD- PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA . (NHAI) (N24001795)	10-2022	7/2024 (6/2025) {12/2024}	490.40 (N.A.) {289.00}	275.78	91.00
		927	4L OF RAJURA-KORPANA- ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B (NHAI) (N24001796)	3-2022	10/2024 (4/2025) {4/2025}	1,013.33 (1,013.33) {1,111.33}	355.07	62.01
		928	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800 (NHAI) (N24001797)	10-2021	1/2024 (N.A.) {5/2025}	815.77 (N.A.) {815.77}	732.70	100.00
		929	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH-53 (NHAI) (N24001798)	2-2021	11/2023 (N.A.) {5/2025}	540.21 (N.A.) {540.21}	451.46	100.00
		930	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J (NHAI) (N24001799)	2-2021	10/2023 (N.A.) {9/2025}	1,166.96 (N.A.) {1,251.00}	1,078.48	80.97
		931	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794) (NHAI) (N24001804)	12-2019	9/2022 (6/2024) {11/2025}	1,654.07 (N.A.) {980.00}	835.19	95.75

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		932	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH-166 (PKG ? II) (NHA/) (N24001834)	5-2023	5/2025 (N.A.) {5/2025}	839.00 (N.A.) {839.00}	437.79	54.00
		933	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH-166 (PKG?III) (NHA/) (N24001835)	5-2023	5/2025 (N.A.) {5/2025}	986.00 (N.A.) {986.00}	474.23	52.10
		934	REHABILITATION AND UP- GRADATION TO 4 LANE ROAD WITH PAVED SHOULDER CONFIGURATION OF SECTION FROM UND (MoRTH) (N24001880)	3-2022	7/2025 (N.A.) {7/2025}	778.18 (N.A.) {778.18}	135.78	-
		935	CONSTRUCTION OF NEW FOUR LANE BYPASS TO PARBHANI CITY (PARWA TO ASOLA) KM 463/265 TO KM 481/180 (DES (MoRTH) (N24001882)	3-2022	10/2024 (N.A.) {10/2024}	496.64 (N.A.) {496.64}	0.00	8.00
		936	CONSTRUCTION OF 4 LANE FLYOVER AT NAGPUR RTO CHOWK TO NAGPUR UNIVERSITY CAMPUS FROM CH 2/250 TO 5/10 (MoRTH) (N24001883)	3-2021	3/2024 (N.A.) {4/2024}	478.83 (N.A.) {478.83}	233.48	65.00
		937	REHABILITATION AND UPGRADATION OF SATANA TO MANGRUL (CHANDWAD) SECTION OF NH752 G DESIGN CH: KM 64.0 (MoRTH) (N24001884)	3-2023	5/2025 (N.A.) {5/2025}	428.80 (N.A.) {428.80}	54.11	30.69
		938	REHABILITATION AND UP- GRADATION OF JINTUR- SHIRAD SHAHAPUR SECTION KM 258.300 TO KM 306.300 [DESIGN (MoRTH) (N24001885)	2-2023	12/2024 (N.A.) {12/2024}	414.81 (N.A.) {414.81}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		939	DEVELOPMENT/WIDENING OF TALEGAON ? CHAKAN ? SHIKRAPUR ? NHAVARA SECTION OF NH 548DG (NHAVARA TO CHOU (MoRTH) (N24001886)	10-2022	8/2024 (N.A.) {8/2024}	304.68 (N.A.) {304.68}	97.09	58.78
		940	REHABILITATION AND UPGRADATION OF BHOKARDAN TO KUMBHARI FATA DESIGN CH. (KM 13+500 TO 17+00) AND RAJ (MoRTH) (N24001887)	8-2022	6/2024 (N.A.) {6/2024}	291.37 (N.A.) {291.37}	102.94	78.44
		941	UP-GRADATION OF TIRORA- GONDIA, STATE HIGHWAY FROM EXISTING KM 163+213 (ON SH-335, TIRORA) TO KM 191+ (MoRTH) (N24001888)	8-2021	4/2023 (N.A.) {5/2024}	288.14 (N.A.) {288.14}	63.01	46.31
		942	2 LANE + PS PIMPLNER TO SATANA -[DESIGN CHAINAGE KM 21.427 TO 64.00] OF NH- 752G] (MoRTH) (N24001889)	9-2019	7/2021 (N.A.) {12/2023}	277.81 (N.A.) {277.81}	148.68	90.00
		943	REHABILITATION AND UPGRADATION OF PARLI TO SIRSALA SECTION OF NH-361F (KM 136+700 TO 115+000) (LENGT (MoRTH) (N24001890)	2-2023	12/2024 (N.A.) {12/2024}	261.82 (N.A.) {261.82}	70.59	46.00
		944	BALANCE WORK OF REHABILITATION AND UP- GRADATION TO NH-166F FROM MAHAD JUNCTION (AT KM 123/400 ON NH- (MoRTH) (N24001891)	7-2021	11/2023 (N.A.) {3/2024}	256.54 (N.A.) {256.54}	80.10	59.66
		945	REHABILITATION AND UPGRADATION OF SHIRAPUR JUNCTION TO SHIVAJI CHOWK (DESIGN CHAINAGE KM. 130+00 TO (MoRTH) (N24001892)	2-2023	12/2024 (N.A.) {12/2024}	245.61 (N.A.) {245.61}	43.39	32.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		946	2 LANE + PS ASTHAMODE - TIVATYAL [DESIGN CH. KM 24.300 - 62.00] [KM 134.98-172.95 OF NH-63] (MoRTH) (N24001894)	9-2019	7/2021 (N.A.) {12/2023}	228.82 (N.A.) {228.82}	144.54	95.44
		947	REHABILITATION AND UPGRADATION TO TWO LANES WITH PAVED SHOULDER CONFIGURATION FROM WATUR TO CHARTHANA (MoRTH) (N24001895)	11-2021	9/2023 (N.A.) {12/2023}	228.01 (N.A.) {228.01}	103.01	99.00
		948	UPGRADATION AND REHABILITATION OF SECTION OF NH 361 F FROM PARLI (00/000) TO GANGAKHED (30/400) TO (MoRTH) (N24001896)	11-2021	9/2023 (N.A.) {4/2024}	224.44 (N.A.) {224.44}	75.34	45.63
		949	REHABILITATION AND UP- GRADATION OF SABALKHED TO ASHTI SECTION FROM KM 37+900 TO KM 55+100 AND CHINCH (MoRTH) (N24001902)	12-2022	9/2024 (N.A.) {9/2024}	213.32 (N.A.) {213.32}	20.00	34.00
		950	REHABILITATION AND UP- GRADATION OF MUDKHED TO NANDED SECTION FROM KM. 372+000 TO KM 388+400 OF NH 16 (MoRTH) (N24001903)	8-2022	4/2025 (N.A.) {4/2025}	206.54 (N.A.) {206.54}	21.36	-
		951	KOPARGAON TO SAVALI VIHIR SECTION (MoRTH) (N24001904)	9-2022	7/2024 (N.A.) {7/2024}	195.38 (N.A.) {195.38}	29.59	19.76
		952	CONSTRUCTION OF MAJOR BRIDGE ACROSS MANJRA RIVER NEAR YESGI VILLAGE @ KM, 166/500 ON NH 63 TQ BILOLI (MoRTH) (N24001905)	10-2021	8/2023 (N.A.) {12/2023}	188.69 (N.A.) {188.69}	111.26	95.80

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		953	UP-GRADATION TO 4 LANING OF DAULTABAD T-POINT TO MALIWADA [FROM DESIGN KM.0.000 TO KM 4.000] AND UPG (MoRTH) (N24001906)	8-2022	3/2024 (N.A.) {3/2024}	185.59 (N.A.) {185.59}	63.56	48.00
		954	CONSTRUCTION OF SIX LANE FLYOVER AT KATRAJ JUNCTION AT KM, 3/880 OF NH 548-DD (VADGAON - KATRAJ - KO (MoRTH) (N24001907)	6-2021	2/2024 (N.A.) {3/2024}	169.15 (N.A.) {169.15}	36.94	35.96
		955	UPGRADATION OF EXHISTING 2 LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDERS RIGID PAVEMENT FROM DESI (MoRTH) (N24001908)	12-2021	5/2024 (N.A.) {5/2024}	167.97 (N.A.) {167.97}	35.28	36.76
		956	STRENGTHING AND WIDINING OF EXISTING CARRIAGEWAY TO 10 M IN KM, 156/160 TO 229/160 (TEMBHURNI - KUSL (MoRTH) (N24001909)	11-2021	6/2024 (N.A.) {6/2024}	157.72 (N.A.) {157.72}	55.38	90.41
		957	REHABILITATION AND UPGRADATION OF JAMKHEDE TO SAUTADA SECTION OF NH548 D (FROM KM 195.375 TO KM 208.7 (MoRTH) (N24001910)	9-2022	7/2024 (N.A.) {7/2024}	157.62 (N.A.) {157.62}	13.86	17.03
		958	PANGAON TO DHARMAPURI AND PARALI TO INJEGAON 2L+PS (MoRTH) (N24001911)	3-2018	7/2024 (N.A.) {12/2023}	152.03 (N.A.) {152.03}	81.35	97.57
		959	4L OF INDORA CHOWK TO PACHPAOLI AND AGRASEN CHOWK - ASHOKA CHOWK (NHAI) (N24002071)	3-2023	6/2026 (N.A.) {6/2026}	998.27 (N.A.) {998.27}	318.58	42.12

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		960	IMPROVEMENT OF EXISTING ALIGNMENT OF PANDHARPUR TOWN PART BYPASSED SECTION FROM WAKHARI TO LORD VITT (NHAI) (N24002072)	7-2022	10/2025 (N.A.) {10/2025}	150.21 (150.21) {150.21}	24.66	2.00
		961	STRENGTHENING OF 6-LANE PIMPALGAON-NASHIK-GONDE (KM. 380 - KM. 440) SECTION OF NH-3 IN MAHARASHTRA U (NHAI) (N24002137)	2-2024	3/2025 (N.A.) {3/2025}	175.00 (206.49) {206.49}	198.54	100.00
		962	REHABILITATION/UPGRADATION OF EXISTING HIGHWAY TO 2L+PS/4 LANE OF DHAWALI TO RAJOLI FROM DESIGN KM.1 (MoRTH) (N24002169)	3-2022	9/2025 (N.A.) {9/2025}	316.44 (N.A.) {316.44}	0.00	-
		963	REHABILITATION/ UPGRADATION OF EXISTING HIGHWAY TO FOUR LANE STANDARDS IN KURKHEDA TOWN FROM (KM.413 (MoRTH) (N24002170)	3-2022	5/2025 (N.A.) {5/2025}	163.86 (N.A.) {163.86}	0.00	-
		964	REHABILITATION AND UP- GRADATION FOR TALERE A?? GAGANBAWDAA?? KOLHAPUR ROAD (NH-166G) STRETCHES START (MoRTH) (N24002171)	2-2023	4/2025 (N.A.) {4/2025}	249.13 (N.A.) {249.13}	0.00	-
		965	UP-GRADATION TO 4 LANE CONFIGURATION FOR THE WORK OF PETH NAKA TO SANGLI ROAD, NH-166H, FROM KM 0+00 (MoRTH) (N24002172)	2-2023	12/2025 (N.A.) {12/2025}	856.82 (N.A.) {856.82}	0.00	-
		966	REHABILITATION AND UP- GRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF MAHUD SANGOLA ROAD NH (MoRTH) (N24002173)	2-2023	4/2025 (N.A.) {4/2025}	253.78 (N.A.) {253.78}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		967	UP-GRADATION TO FOUR LANE/ TWO LANE WITH PAVED SHOULDERS CONFIGURATION OF KALYAN - MURBAD - MALSHEJ (MoRTH) (N24002174)	2-2023	8/2026 (N.A.) {8/2026}	984.07 (N.A.) {984.07}	0.00	-
		968	CONSTRUCTION OF FOUR-LANE CONCRETE ROAD FROM POLICE HEADQUARTER GONDIA CITY TO RAWANWADI VILLAGE (BI (MoRTH) (N24002175)	2-2023	8/2025 (N.A.) {8/2025}	328.11 (N.A.) {328.11}	0.00	-
		969	REHABILITATION/UP GRADATION OF KARANJA ? KHERDA - MURTIZAPUR SECTION TO 4LANE+PAVED SHOULDER STAND A (MoRTH) (N24002176)	3-2023	2/2026 (N.A.) {2/2026}	594.44 (N.A.) {594.44}	0.00	-
		970	REHABILITATION / UPGRADATION TO 4 LANE WITH PAVED SHOULDER OF EXISTING SECTION IN SILLOD TOWN WITH D (MoRTH) (N24002177)	3-2023	7/2025 (N.A.) {7/2025}	153.79 (N.A.) {153.79}	0.00	-
		971	REHABILITATION, UPGRADATION AND WIDENING OF EXISTING HIGHWAY TO RIGID PAVEMENT 2 LANE WITH PAVED SHO (MoRTH) (N24002178)	2-2023	7/2026 (N.A.) {7/2026}	723.13 (N.A.) {723.13}	0.00	-
	URBAN DEVELOPMENT	972	MUMBAI METRO LINE 3 (COLABA- BANDRA-SEEPZ) (MMRCL) (N28000086)	7-2013	3/2020 (7/2025) {7/2025}	23,136.00 (N.A.) {37,276.00}	28,615.78	95.00
		973	PUNE METRO RAIL PROJECT (PHASE 1) (MMRC) (N28000121)	12-2016	11/2021 (9/2024) {9/2024}	11,420.00 (13,656.22) {13,656.22}	13,036.65	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		974	NAGPUR METRO RAIL PROJECT PHASE II (NMRCL) (N28000155)	12-2022	12/2027 (N.A.) {12/2027}	6,708.00 (N.A.) {6,708.00}	768.34	21.60
		975	PCMC NIGDI PROJECT EXTENSION OF CORRIDOR 1 OF PUNE METRO PHASE 1 (MMRC) (N28000157)	10-2023	1/2027 (N.A.) {1/2027}	910.18 (N.A.) {910.18}	81.34	14.97
		976	PUNE METRO PHASE-1 EXTENSION FROM SWARGATE TO KATRAJ (MMRC) (N28000160)	9-2024	3/2029 (N.A.) {3/2029}	2,954.53 (N.A.) {2,954.53}	15.14	2.00
MANIPUR	CIVIL AVIATION	977	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (3/2026) {3/2026}	499.00 (N.A.) {499.00}	154.47	39.40
	RAILWAYS	978	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	12/2026 (3/2028) {3/2028}	14,322.79 (12,274.06) {22,234.60}	15,265.40	68.70
	ROAD TRANSPORT AND HIGHWAYS	979	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (1/2025) {9/2025}	292.24 (N.A.) {292.24}	130.66	89.72
		980	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (1/2025) {10/2025}	365.53 (N.A.) {365.53}	156.31	77.36

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		981	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3-2020	6/2022 (1/2025) {5/2025}	167.95 (204.12) {167.95}	88.05	69.89
		982	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7-2020	8/2022 (2/2025) {5/2025}	177.76 (N.A.) {177.76}	89.67	80.53
		983	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (6/2025) {10/2025}	379.39 (N.A.) {379.39}	214.93	67.72
		984	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (3/2025) {7/2025}	226.32 (N.A.) {226.32}	104.95	74.48
		985	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (10/2024) {2/2025}	188.36 (N.A.) {188.36}	126.71	100.00
		986	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3-2021	12/2022 (3/2025) {3/2026}	195.14 (N.A.) {195.14}	61.81	50.79
		987	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (9/2024) {11/2025}	234.08 (N.A.) {234.08}	139.45	91.85
		988	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (5/2025) {10/2025}	211.70 (N.A.) {211.70}	83.79	68.65
		989	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (3/2025) {10/2025}	467.00 (N.A.) {467.00}	193.81	77.74

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		990	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (1/2025) {1/2025}	185.80 (N.A.) {185.80}	117.78	100.00
		991	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (8/2024) {12/2025}	483.87 (N.A.) {483.87}	278.89	92.80
		992	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (2/2025) {3/2025}	198.77 (N.A.) {198.77}	127.86	100.00
		993	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (3/2025) {5/2025}	673.27 (N.A.) {673.27}	377.12	78.46
		994	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (1/2025) {1/2026}	477.86 (N.A.) {477.86}	243.46	83.92
		995	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (11/2024) {12/2025}	311.18 (N.A.) {311.18}	186.15	81.65
		996	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (10/2024) {2/2025}	467.41 (N.A.) {467.41}	264.83	100.00
		997	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (7/2025) {12/2025}	579.63 (N.A.) {579.63}	172.65	69.38
		998	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (3/2025) {5/2025}	310.76 (N.A.) {310.76}	129.15	96.77

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		999	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (2/2025) {3/2026}	410.68 (N.A.) {410.68}	147.81	67.64
		1000	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (9/2025) {12/2025}	504.76 (N.A.) {504.76}	183.15	74.23
		1001	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (2/2025) {3/2025}	152.11 (N.A.) {152.11}	73.48	100.00
		1002	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (1/2025) {9/2025}	315.56 (N.A.) {315.56}	121.49	79.40
		1003	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (12/2025) {3/2026}	760.16 (N.A.) {760.16}	148.98	58.19
		1004	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (3/2026) {3/2026}	578.98 (N.A.) {578.98}	145.62	69.25
		1005	MARREM KHULLEN TO JESSAMI SECTION IMPHAL- UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	11.64	9.21
		1006	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	13.14	14.91

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MEGHALAYA		1007	JESSAMI TO LAYNEN BRIDGE UKHRUL - JESSAMI PKG-7 (NHIDCL) (N24002227)	3-2023	6/2026 (N.A.) {6/2026}	164.89 (N.A.) {164.89}	1.46	3.28
		1008	IMPHAL-KOHIMA ROAD PKG-5A (NHIDCL) (N24002232)	9-2020	8/2026 (N.A.) {8/2026}	228.97 (N.A.) {228.97}	0.00	4.60
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1009	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (7/2025) {7/2025}	484.32 (429.70) {429.70}	295.55	83.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1010	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (3/2025) {6/2025}	553.51 (610.09) {553.51}	419.49	84.94
		1011	IMPROVEMENT/WIDENING TO 2- L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM () (NHIDCL) (N24001313)	11-2020	12/2023 (10/2025) {10/2025}	351.12 (N.A.) {351.12}	295.87	61.50
		1012	IMPROVEMENT/WIDENING TO 2- LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	425.76	31.00
		1013	IMPROVEMENT/WIDENING TO 2- LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	206.15	26.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1014	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	100.93	23.10
		1015	RANIKOR-MAHESHKHOLA-BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10-2020	4/2022 (6/2024) {2/2025}	157.86 (146.92) {157.86}	152.95	100.00
		1016	RANIKOR-MAHESHKHOLA-BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3-2021	12/2022 (6/2024) {2/2025}	260.21 (N.A.) {260.21}	239.35	100.00
		1017	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (3/2025) {3/2025}	302.88 (N.A.) {302.88}	140.20	95.00
		1018	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (12/2024) {12/2025}	359.86 (N.A.) {359.86}	232.55	89.00
		1019	RANIKOR- MAHESHKHOLA-BAGHMARA PKG-2 (NHIDCL) (N24001541)	11-2021	6/2024 (12/2024) {5/2025}	283.50 (N.A.) {283.50}	256.07	96.93
		1020	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	210.58	28.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1021	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	281.90	23.00
		1022	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	297.79	24.00
		1023	DAINADUBI-DARUGIRI PKG-1B (NHIDCL) (N24002233)	3-2023	3/2027 (N.A.) {3/2027}	705.83 (N.A.) {705.83}	0.31	-
MIZORAM	RAILWAYS	1024	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2025 (N.A.) {7/2025}	6,527.45 (5,021.45) {8,213.72}	7,948.91	96.00
	ROAD TRANSPORT AND HIGHWAYS	1025	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (N.A.) {6/2025}	519.09 (N.A.) {785.65}	667.78	96.60
		1026	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (N.A.) {5/2024}	640.07 (N.A.) {1,286.35}	1,192.26	98.90
		1027	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (N.A.) {6/2025}	473.18 (N.A.) {688.25}	539.93	94.38

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1028	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (N.A.) {6/2025}	537.82 (N.A.) {789.05}	768.85	96.82
		1029	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (N.A.) {5/2025}	518.53 (N.A.) {906.76}	847.17	97.20
		1030	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (N.A.) {5/2025}	404.29 (N.A.) {750.32}	654.75	97.71
		1031	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (N.A.) {5/2025}	428.11 (N.A.) {746.39}	606.93	97.90
		1032	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (N.A.) {6/2024}	206.88 (N.A.) {219.33}	265.18	100.00
		1033	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (N.A.) {6/2025}	292.24 (N.A.) {331.17}	291.20	93.20

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1034	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (4/2024) {4/2024}	233.25 (N.A.) {233.25}	172.09	100.00
		1035	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (N.A.) {3/2026}	698.44 (N.A.) {698.45}	499.26	59.40
		1036	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (N.A.) {3/2026}	740.58 (N.A.) {740.58}	362.71	57.40
		1037	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9-2021	5/2023 (N.A.) {5/2024}	492.94 (N.A.) {492.94}	354.89	90.50
		1038	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWLRRANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {12/2025}	523.78 (N.A.) {523.78}	643.63	78.00
		1039	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	250.46	65.10
		1040	ZORINPUI- HMAWNGBU- LONGMASU (NH-502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	67.12	1.12
MULTI STATE	COAL	1041	NILJAI EXPANSION (DEEP) OC (3.5 MTY) (WCL) (N06000154)	8-2016	3/2022 (3/2025) {3/2025}	319.76 (319.76) {319.76}	183.67	98.00
		1042	BINA KAKRI AMALGAMATION OCP 14 MTPA (NCL) (N06000192)	8-2020	3/2024 (N.A.) {3/2027}	836.42 (N.A.) {836.42}	768.64	58.20

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DPIIT</u>	1043	NATIONAL INDUSTRIAL CORRIDOR PROJECT (DMIC FOR DPIIT) (N40000001)	9-2011	3/2027 (3/2032) {3/2032}	20,084.00 (26,684.00) {26,684.00}	4,969.89	50.99
	<u>PETROLEUM</u>	1044	KOCHI-KOOTTANAD- BANGALORE-MANGALORE PIPELINE PHASE-II (GAIL) (N16000285)	6-2009	12/2012 (12/2025) {12/2025}	2,915.00 (5,909.00) {5,909.00}	4,191.90	93.80
		1045	SRIKAKULAM ANGUL PIPELINE PROJECT (GAIL) (N16000388)	9-2019	7/2022 (6/2025) {6/2025}	2,658.34 (N.A.) {2,658.34}	2,173.30	94.20
		1046	DHAMRA HALDIA PIPELINE PROJECT (GAIL) (N16000391)	3-2020	11/2022 (12/2025) {12/2025}	1,030.65 (N.A.) {1,030.65}	831.80	86.30
		1047	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT (GAIL) (N16000398)	6-2020	5/2023 (6/2025) {6/2025}	7,844.25 (N.A.) {7,844.25}	6,266.00	93.80
		1048	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS (IOCL) (N16000426)	6-2019	12/2029 (3/2030) {3/2030}	169.00 (N.A.) {169.00}	74.64	27.20
		1049	NORTH EAST GAS GRID (IGGL) (N16000439)	11-2020	3/2024 (7/2025) {3/2027}	9,265.00 (9,265.00) {9,265.00}	6,270.19	84.51
		1050	GURDASPUR JAMMU PIPELINE (GAIL) (N16000531)	7-2023	7/2026 (7/2026) {7/2026}	521.92 (521.92) {521.92}	121.50	33.56

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	1051	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P (PGCIL) (N18000249)	12-2014	12/2018 (3/2025) {3/2029}	4,754.42 (9,129.32) {9,129.32}	7,602.44	81.00
		1052	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES (PGCIL) (N18000250)	12-2014	12/2018 (3/2025) {6/2025}	5,111.33 (6,700.00) {6,700.00}	5,276.39	95.80
		1053	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM (PGCIL) (N18000328)	2-2022	4/2025 (N.A.) {6/2025}	318.12 (N.A.) {318.12}	169.75	95.00
		1054	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM (PGCIL) (N18000330)	3-2022	12/2024 (N.A.) {7/2025}	288.71 (N.A.) {288.71}	144.79	48.00
		1055	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000331)	2-2022	9/2023 (N.A.) {6/2025}	359.47 (N.A.) {359.47}	314.16	84.00
		1056	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000332)	5-2022	11/2023 (N.A.) {8/2025}	1,666.00 (N.A.) {1,666.00}	1,490.62	90.30
		1057	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B (PGCIL) (N18000337)	7-2022	6/2023 (N.A.) {9/2025}	4,546.26 (N.A.) {4,546.26}	2,785.35	91.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1058	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION (PGCIL) (N18000343)	10-2022	10/2025 (N.A.) {10/2025}	307.87 (N.A.) {307.87}	184.31	89.00
		1059	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B (PGCIL) (N18000352)	3-2023	11/2024 (N.A.) {8/2025}	3,546.94 (N.A.) {3,546.94}	2,202.14	89.00
		1060	ER WR TRANSMISSION LIMITED (PGCIL) (N18000353)	3-2023	3/2025 (N.A.) {5/2025}	281.16 (N.A.) {281.16}	162.14	91.00
	RAILWAYS	1061	NANGALDAM-TALWARA(NL),NR (NR) (220100188)	3-1981	12/2025 (1/2027) {6/2027}	2,018.00 (603.00) {2,017.96}	1,579.04	75.00
		1062	LALITPUR-SATNA-REWA- SINGRULI NL, (NCR) (WCR) (220100232)	9-1998	3/2027 (N.A.) {3/2025}	8,913.94 (63.57) {8,248.50}	2,520.04	43.00
		1063	CHHAPRA-BALLIA UP (NER) (N22000134)	3-2013	2/2025 (N.A.) {12/2025}	941.05 (954.00) {1,045.82}	1,001.52	95.50
		1064	CHOTTAUDEPUR-DHAR(NL) (WR) (N22000138)	4-2007	12/2026 (12/2027) {12/2027}	1,793.65 (1,793.63) {1,793.63}	1,619.35	59.00
		1065	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) (WR) (N22000139)	4-2007	2/2027 (2/2027) {2/2027}	1,942.00 (1,873.10) {2,873.11}	2,913.16	59.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1066	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) (NCR) (N22000148)	4-2011	3/2025 (N.A.) {12/2024}	2,912.96 (N.A.) {3,845.60}	1,024.32	-
		1067	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR (NCR) (N22000158)	4-2010	2/2019 (N.A.) {12/2026}	746.83 (N.A.) {746.83}	389.88	30.00
		1068	NEW BONGAIGAON-RANGIA- KAMAKGHYA DOUBLING (NFR) (N22000183)	4-2013	8/2024 (N.A.) {10/2024}	2,047.51 (N.A.) {2,832.35}	3,709.47	99.51
		1069	NEW BG LINE FROM BALURGHAT TO HILLY NFR (NFR) (N22000206)	4-2010	3/2027 (N.A.) {3/2027}	1,208.67 (N.A.) {1,181.57}	412.99	7.00
		1070	NEW BG LINE FROM JAGBANI TO BIRATNAGAR (NFR) (N22000207)	4-2010	3/2022 (12/2026) {12/2026}	401.65 (485.96) {485.96}	361.33	86.00
		1071	MURKONGSELEK-PASIGHAT NL (NFR) (N22000208)	4-2011	3/2025 (N.A.) {11/2025}	435.06 (N.A.) {1,252.49}	752.82	53.00
		1072	PIRPAINTI-JASIDIH (ER) (N22000219)	4-2013	3/2028 (3/2028) {3/2028}	2,555.03 (N.A.) {2,610.84}	1,124.78	45.00
		1073	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION (SCR) (N22000261)	4-2012	2/2025 (N.A.) {3/2025}	1,953.00 (N.A.) {1,952.68}	1,755.99	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1074	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL (NR) (N22000274)	4-2007	3/2024 (N.A.) {3/2025}	1,053.23 (N.A.) {1,053.00}	578.92	99.00
		1075	RAYADURGA-TUMKUR NL (SWR) (N22000279)	4-2007	9/2015 (N.A.) {2/2028}	2,495.59 (2,495.59) {2,495.59}	1,645.12	60.00
		1076	HOTGI-KUDGI-GADAG (SWR) (N22000333)	3-2015	12/2024 (N.A.) {2/2026}	1,877.81 (1,877.81) {2,458.87}	2,513.53	89.00
		1077	KAZIPET-BALHRSHA (SCR) (N22000367)	4-2015	1/2025 (N.A.) {1/2025}	2,594.59 (N.A.) {2,909.00}	2,797.55	-
		1078	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT (NHSRCL) (N22000463)	12-2015	8/2027 (N.A.) {8/2027}	108,000.00 (N.A.) {108,000.00}	76,441.00	51.50
		1079	WESTERN DEDICATED FREIGHT CORRIDOR (DFCC) (N22000464)	11-2007	3/2022 (N.A.) {3/2020}	51,101.00 (51,101.00) {51,101.00}	47,476.00	83.00
		1080	CHANDIGARH-BADDI (NR) (N22000467)	4-2007	6/2025 (12/2026) {12/2026}	1,540.13 (1,540.14) {1,540.14}	941.19	28.00
		1081	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) (SER) (N22000506)	3-2019	12/2024 (N.A.) {6/2026}	2,400.00 (N.A.) {1,866.31}	1,979.58	58.00
	ROAD TRANSPORT AND HIGHWAYS	1082	VARANASI-AURANGABAD KM.786 TO KM.978.40 (NHAI) (N24000182)	9-2011	3/2014 (N.A.) {6/2025}	2,848.00 (N.A.) {3,241.56}	3,901.66	90.02

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1083	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 (NHA) (N24001628)	11-2021	2/2025 (8/2025) {8/2025}	2,155.95 (N.A.) {2,155.95}	1,280.30	66.80
		1084	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O (NHA) (N24001629)	4-2022	11/2024 (5/2025) {5/2025}	796.65 (N.A.) {796.65}	417.88	83.55
	SHIPPING AND PORTS	1085	JAL MARG VIKAS PROJECT (IWA) (N25000072)	1-2018	3/2023 (12/2025) {12/2025}	5,369.18 (5,061.15) {5,061.15}	3,414.95	68.38
	TELECOMMUNI CATIONS	1086	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (N26000114)	3-2020	6/2021 (11/2021) {6/2025}	461.42 (461.42) {461.42}	166.02	81.00
		1087	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LABEL SWITCHING (IPMPLS) NETWORK and (BSNL) (N26000115)	3-2023	3/2024 (7/2024) {3/2025}	239.60 (N.A.) {239.60}	175.17	100.00
		1088	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (N26000116)	5-2023	8/2024 (11/2024) {6/2025}	645.13 (N.A.) {645.13}	346.27	86.89
		1089	PLANNING ENGINEERING SUPPLY INSTALLATION TESTING COMMISSIONING INTEGRATION and ANNUAL MAINTENANCE OF (BSNL) (N26000117)	6-2023	6/2025 (N.A.) {6/2025}	24,556.35 (24,544.55) {24,544.55}	7,941.00	92.30

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1090	OPTICAL TRANSPORT NETWORK (OTN) PH-4 IN BSNL (BSNL) (N26000118)	2-2024	8/2025 (N.A.) {8/2025}	810.99 (N.A.) {810.99}	570.00	99.35
	<u>URBAN DEVELOPMENT</u>	1091	DELHI GHAZIABAD MEERUT RRTS CORRIDOR (NCRTC) (N28000134)	3-2019	6/2025 (N.A.) {6/2025}	30,274.00 (N.A.) {30,274.00}	25,204.71	85.50
<u>NAGALAND</u>	<u>PETROLEUM</u>	1092	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	4.54	17.50
	<u>RAILWAYS</u>	1093	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2026 (N.A.) {12/2029}	6,663.20 (6,663.20) {6,663.20}	4,611.24	71.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1094	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3-2016	9/2019 (11/2022) {5/2025}	373.07 (534.41) {534.41}	382.50	99.81
		1095	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (9/2025) {9/2025}	429.52 (794.74) {794.74}	321.40	90.84
		1096	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (2/2023) {4/2025}	387.00 (688.12) {688.12}	389.81	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1097	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (8/2024) {4/2025}	500.09 (698.81) {698.81}	393.53	100.00
		1098	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (8/2022) {8/2025}	215.79 (N.A.) {215.79}	127.85	77.10
		1099	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (6/2023) {9/2025}	323.98 (N.A.) {323.98}	112.43	52.47
		1100	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3-2017	11/2020 (2/2023) {2/2023}	217.35 (N.A.) {217.35}	214.18	100.00
		1101	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3-2019	12/2022 (1/2023) {1/2023}	237.51 (N.A.) {237.51}	215.47	100.00
		1102	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (9/2024) {6/2026}	277.44 (N.A.) {277.44}	168.88	66.12
		1103	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (6/2025) {6/2025}	159.85 (342.29) {159.85}	101.93	29.36

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1104	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (4/2023) {8/2025}	202.36 (N.A.) {202.36}	75.17	30.80
		1105	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9-2020	4/2022 (5/2024) {12/2025}	315.63 (N.A.) {315.63}	116.70	74.23
		1106	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	114.35	63.20
		1107	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3-2020	6/2022 (10/2022) {6/2023}	278.95 (N.A.) {278.95}	166.29	100.00
		1108	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (11/2025) {11/2025}	330.80 (N.A.) {330.80}	168.02	91.97
		1109	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (11/2026) {11/2026}	232.29 (350.88) {232.29}	69.98	14.42
		1110	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3-2020	6/2022 (9/2022) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.40
		1111	PEREN-DIMAPUR SECTION PKG- 2 (NHIDCL) (N24001406)	7-2021	3/2023 (9/2025) {9/2025}	258.52 (N.A.) {258.52}	83.96	77.90

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1112	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	62.08	66.76
		1113	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (6/2026) {6/2026}	252.19 (N.A.) {252.19}	11.97	14.50
		1114	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3-2021	7/2024 (6/2025) {6/2025}	297.24 (N.A.) {297.24}	137.57	76.20
		1115	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (3/2025) {3/2025}	226.44 (N.A.) {226.44}	140.24	100.00
		1116	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3-2022	12/2024 (N.A.) {1/2025}	605.36 (N.A.) {605.36}	273.21	100.00
		1117	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (6/2025) {6/2025}	192.93 (N.A.) {192.93}	103.62	88.60
		1118	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {12/2025}	177.77 (199.02) {199.02}	43.33	61.13

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1119	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO- AVANGKHU SECTION OF NH- 202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	92.24	49.95
		1120	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO- AVANGKHU SECTION OF NH- 202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	39.97	22.28
		1121	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO- AVANGKHU SECTION OF NH- 202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	159.36	59.20
ODISHA	COAL	1122	BASUNDHARA (WEST) OC EXTN(7.00 MTY) (MCL) (N06000112)	5-2014	3/2019 (N.A.) {3/2027}	479.15 (N.A.) {479.15}	267.10	63.04
		1123	SIARMAL OCP (40.00MTY) (MCL) (N06000113)	2-2021	3/2029 (N.A.) {3/2029}	5,194.96 (N.A.) {5,194.96}	3,436.40	51.07
		1124	INTEGRATED LAKHANPUR- BELPAHAR-LILARI OCP (MCL) (N06000167)	5-2018	3/2027 (N.A.) {3/2027}	2,434.75 (N.A.) {2,434.75}	1,749.33	60.87
		1125	REORGANISATION OF BHARATPUR OCP EXPANSION (MCL) (N06000171)	11-2018	3/2029 (N.A.) {3/2029}	2,838.87 (N.A.) {2,838.87}	1,743.39	44.60
		1126	TALABIRA II AND III OCP (NLC) (N06000189)	7-2017	1/2027 (N.A.) {1/2027}	2,401.07 (N.A.) {2,401.07}	1,626.71	62.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1127	NAINI COAL MINE (SCCL) (N06000203)	3-2020	3/2024 (N.A.) {3/2027}	494.30 (N.A.) {494.30}	491.33	80.00
		1128	GOPALJI-KANIHA OCP (MCL) (N06000229)	4-2022	3/2028 (N.A.) {3/2028}	6,107.87 (N.A.) {6,107.87}	1,694.01	17.39
		1129	BALARAM EXPANSION OCP (MCL) (N06000230)	8-2020	3/2029 (N.A.) {3/2029}	3,504.21 (N.A.) {3,504.21}	1,022.30	50.17
		1130	SUBHADRA OCP (MCL) (N06000249)	5-2021	3/2029 (3/2029) {3/2029}	1,693.81 (N.A.) {1,693.81}	1,180.35	39.30
		1131	NLC TALABIRA THERMAL POWER PROJECT (PHASE-1: 3 X 800 MW) (NLC) (N06000270)	1-2024	5/2029 (3/2030) {3/2030}	27,213.00 (N.A.) {27,213.00}	1,556.46	1.55
		1132	RPR OF HINGULA EXPANSION OCP (MCL) (N06000285)	11-2022	3/2029 (N.A.) {3/2029}	1,561.85 (N.A.) {1,561.85}	47.49	3.57
		1133	BHUBANESWARI EXPANSION OCP (MCL) (N06000286)	3-2024	3/2031 (N.A.) {3/2031}	5,366.28 (N.A.) {5,366.28}	0.82	3.39
		1134	BALABHADRA OCP (MCL) (N06000288)	4-2023	3/2030 (N.A.) {3/2030}	978.44 (N.A.) {978.44}	209.50	1.86
		1135	INTEGRATED KULDA GARJANBAHAL OCP (MCL) (N06000289)	4-2023	3/2030 (N.A.) {3/2030}	3,563.50 (N.A.) {3,563.50}	6.72	1.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	DEPARTMENT OF HIGHER EDUCATION	1136	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR (CPWD EDUCATION) (N28000126)	1-2019	3/2022 (N.A.) {6/2025}	790.79 (N.A.) {790.79}	701.39	96.00
	MINES	1137	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT (NALCO) (N10000010)	12-2014	4/2021 (9/2025) {9/2025}	4,103.00 (5,677.40) {5,677.40}	3,751.02	73.01
		1138	UTKAL D AND E COAL BLOCK (NALCO) (N10000011)	5-2016	1/2020 (11/2023) {3/2024}	534.00 (N.A.) {1,021.97}	826.19	86.50
		1139	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (NALCO) (N10000012)	12-2015	11/2020 (9/2025) {8/2027}	355.00 (581.00) {581.00}	163.55	12.60
		1140	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN (NALCO) (N10000013)	11-2017	4/2021 (5/2025) {5/2025}	483.00 (483.00) {495.00}	383.19	88.87
		1141	POTTANGI BAUXITE MINES (NALCO) (N10000016)	5-2018	12/2024 (N.A.) {5/2025}	1,437.00 (N.A.) {1,381.00}	649.96	50.90
		1142	CONSTRUCTION OF RED MUD POND - II AT NALCO DAMANJODI ODISHA (NALCO) (N10000017)	9-2019	3/2023 (5/2024) {5/2024}	225.79 (N.A.) {270.66}	5.00	100.00
	PETROLEUM	1143	ADDITIONAL STORAGE TANKS AT PARADIP (IOCL) (N16000361)	11-2018	9/2021 (12/2024) {3/2025}	462.30 (552.44) {552.44}	493.72	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	1144	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY (IOCL) (N16000396)	7-2020	1/2024 (4/2025) {4/2026}	13,805.00 (N.A.) {13,805.00}	7,173.59	89.20
		1145	EASTERN REGION EXPANSION SCHEME XXIX (PGCIL) (N18000351)	3-2023	11/2025 (N.A.) {11/2025}	524.04 (N.A.) {524.04}	359.97	99.00
		1146	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) (NTPC) (N18000364)	8-2022	5/2027 (N.A.) {12/2027}	11,844.00 (N.A.) {12,539.00}	3,218.10	21.40
	RAILWAYS	1147	KHURDA ROAD- BOLANGIR(NL)ECOR (ECOR) (220100284)	4-1994	12/2026 (12/2026) {12/2026}	3,550.00 (3,791.66) {5,089.37}	4,690.64	84.00
		1148	TALCHER- BIMALAGARH(NL)(ECOR) (ECOR) (220100328)	4-2005	3/2025 (N.A.) {3/2026}	1,928.10 (N.A.) {1,928.07}	1,686.57	40.00
		1149	BHADRAK - NERGUNDI 3RD LINE (ECOR) (N22000316)	3-2013	11/2024 (1/2026) {1/2026}	1,284.39 (1,284.39) {1,284.39}	1,257.23	80.00
		1150	JAGADALPUR-KORAPUT DOUBLING (ECOR) (N22000376)	4-2015	3/2024 (N.A.) {3/2022}	1,547.38 (N.A.) {1,547.38}	1,273.36	93.50
		1151	KORAPUT - SINGAPUR ROAD DOUBLING (ECOR) (N22000379)	4-2015	12/2027 (3/2026) {3/2026}	2,362.00 (2,361.74) {2,361.74}	1,752.26	78.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1152	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE (ECOR) (N22000380)	4-2015	3/2027 (N.A.) {8/2026}	820.61 (N.A.) {810.02}	573.95	-
		1153	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. (ECOR) (N22000381)	4-2015	3/2026 (11/2025) {11/2025}	1,172.92 (N.A.) {2,022.75}	1,906.43	80.00
		1154	VIZIANAGARAM -SAMABALPUR 3RD LINE (RVNL) (N22000409)	1-1991	12/2026 (N.A.) {12/2026}	4,803.16 (N.A.) {4,803.16}	4,691.52	-
		1155	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL (IRCON) (N22000418)	4-2016	3/2020 (N.A.) {12/2025}	5,200.00 (N.A.) {5,200.00}	0.00	17.40
		1156	JEYPORE MALKANGIRI NEW LINE (ECOR) (N22000516)	2-2018	7/2033 (N.A.) {7/2033}	2,344.00 (N.A.) {642.69}	220.78	90.00
		1157	JEYPORE NABARANGPUR NEWLINE (ECOR) (N22000517)	7-2017	7/2028 (N.A.) {7/2028}	748.00 (N.A.) {747.91}	0.00	-
		1158	TALCHER - ANGUL NEW LINE WITH Y CONNECTION AT TALCHER (ECOR) (N22000518)	7-2018	12/2026 (N.A.) {12/2026}	278.96 (495.00) {494.62}	29.50	-
		1159	KODINGAMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (ECOR) (N22000519)	8-2022	8/2027 (N.A.) {8/2027}	190.90 (N.A.) {190.90}	10.00	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1160	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION (ECOR) (N22000520)	9-2022	9/2027 (N.A.) {3/2028}	189.93 (N.A.) {189.93}	14.04	-
		1161	BRUNDAMAL-JHARSUGUDA- FLYOVER CONNECTION FOR JOINING DN LINE (ECOR) (N22000521)	12-2009	12/2026 (N.A.) {12/2026}	296.51 (N.A.) {297.00}	302.50	10.00
		1162	BAGHUAPAL FLY OVER (20 KM) (ECOR) (N22000522)	8-2019	8/2027 (8/2027) {8/2027}	183.00 (257.97) {257.97}	0.83	-
		1163	ROURKELA-BONDAMUNDA A- CABIN 5TH LINE (10 KM) (UMBRELLA WORK PB#57/2019- 20/NR) (SER) (N22000571)	9-2022	9/2026 (N.A.) {2/2026}	209.75 (N.A.) {244.99}	59.29	10.00
	ROAD TRANSPORT AND HIGHWAYS	1164	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S (NHAI) (N24000619)	9-2016	8/2019 (N.A.) {5/2025}	2,510.04 (N.A.) {2,510.04}	1,181.34	99.38
		1165	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO (NHAI) (N24000715)	12-2017	7/2020 (N.A.) {6/2025}	686.65 (565.00) {686.65}	574.26	97.65
		1166	REHABILITATION AND UP- GRADATION OF EXISTING 2- LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE ((NHAI) (N24000733)	1-2018	8/2022 (N.A.) {12/2025}	633.68 (492.83) {633.68}	560.38	85.60

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1167	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG (NHAI) (N24000734)	1-2018	8/2021 (N.A.) {6/2025}	614.48 (503.30) {757.12}	664.48	100.00
		1168	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON (NHAI) (N24000736)	1-2018	9/2020 (N.A.) {6/2025}	686.65 (504.09) {1,015.16}	479.81	97.50
		1169	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141) (NHAI) (N24000738)	1-2018	9/2021 (N.A.) {7/2025}	999.00 (1,152.70) {1,152.70}	498.82	80.58
		1170	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) ((NHAI) (N24000739)	1-2018	6/2021 (5/2025) {5/2025}	503.88 (609.03) {609.03}	536.89	99.50
		1171	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. (MoRTH) (N24000912)	8-2016	2/2017 (N.A.) {8/2025}	287.70 (N.A.) {293.66}	275.42	98.66
		1172	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA (MoRTH) (N24000914)	12-2016	8/2018 (N.A.) {9/2025}	223.50 (N.A.) {223.50}	220.50	92.00
		1173	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA (MoRTH) (N24000917)	3-2018	8/2018 (N.A.) {6/2025}	199.16 (N.A.) {199.16}	155.10	98.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1174	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 (NHAI) (N24001647)	8-2020	3/2022 (N.A.) {5/2025}	200.00 (154.73) {154.73}	150.38	99.62
		1175	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8 (NHAI) (N24001665)	12-2021	10/2024 (N.A.) {12/2025}	1,592.00 (1,592.00) {1,592.00}	1,067.86	76.49
		1176	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130- CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE-OD (NHAI) (N24001666)	12-2021	9/2024 (N.A.) {8/2025}	714.00 (714.00) {714.00}	569.08	92.07
		1177	6L GREENFIELD KALIAGURA ? BAUNSAGUAR SECTION OF NH- 130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG (NHAI) (N24001667)	9-2021	5/2024 (N.A.) {10/2025}	1,734.00 (1,734.00) {1,734.00}	1,203.09	83.99
		1178	6L OF BADAUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH-130-CD (PACKAGE ? OD-3) (NHAI) (N24001668)	3-2021	4/2024 (N.A.) {6/2025}	1,249.00 (N.A.) {1,249.00}	465.59	84.06
		1179	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH-130-CD (PACKAGE ? OD-1) (NHAI) (N24001669)	2-2021	3/2024 (N.A.) {6/2025}	586.00 (N.A.) {586.00}	240.33	87.60
		1180	6L OF KARKI ? KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH-130-CD (PACKAGE ? OD-4) (NHAI) (N24001670)	2-2021	3/2024 (N.A.) {5/2025}	593.00 (N.A.) {593.00}	282.15	93.60

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1181	6L OF HATIBENA - BADAUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130-CD (PACKAGE ? OD-2) (NHAI) (N24001671)	2-2021	3/2024 (N.A.) {5/2025}	925.00 (N.A.) {925.00}	460.47	97.00
		1182	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE ? (NHAI) (N24001678)	8-2021	6/2024 (N.A.) {12/2025}	1,460.00 (1,460.00) {1,460.00}	947.94	87.92
		1183	CONSTRUCTION OF ROAD FROM KM 0/0 TO 72/0 OF NH-26 SUCH AS 4 LANE FROM KM 0/0 TO 21/0 (BARGARH TO BAR (MoRTH) (N24001857)	6-2020	12/2023 (8/2025) {8/2025}	414.24 (N.A.) {414.24}	307.52	97.00
		1184	WIDENING AND STRENGTHENING TO 2L+PS INCLUDING LA OF KANDARPUR- BALIKUDA FROM KM 277/500 TO 318/970 OF (MoRTH) (N24001858)	3-2022	6/2025 (N.A.) {12/2025}	499.79 (N.A.) {499.79}	280.32	36.83
		1185	CONSTRUCTION OF BYPASS ON NH-59 FROM KM 336/350 TO 349/910 (13.56 KM) NEAR BERHAMPUR TOWN INCLUDING (MoRTH) (N24001859)	3-2021	3/2024 (N.A.) {8/2025}	196.94 (N.A.) {196.94}	68.15	15.00
		1186	CONSTRUCTION OF BYPASS TO NAYAGARH TOWN FROM KM 235.469 TO 252.482 OF NH-57 INCLUDING LAND ACQUISITI (MoRTH) (N24001860)	1-2022	4/2025 (N.A.) {8/2025}	300.33 (N.A.) {300.33}	199.19	50.00
		1187	CONSTRUCTION OF BYPASS TO KHORDHA TOWN FROM KM 294/000 TO 300/300 ON NH-57 INCLUDING LA IN THE STATE (MoRTH) (N24001861)	2-2022	11/2024 (8/2025) {8/2025}	157.49 (N.A.) {157.49}	69.00	31.74

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1188	CONSTRUCTION OF BYPASS ROAD TO BALANGIR TOWN FROM KM 72/400 (DESING KM 0/0) TO KM 79/800 (DESIGN KM (MoRTH) (N24001862)	2-2022	10/2025 (11/2025) {11/2025}	238.78 (N.A.) {238.78}	39.26	28.00
		1189	CONSTRUCTION OF 5 HL BRIDGES AT KM 379/000 (PANGAM), KM 439/400 (POTTERU), KM 444/237 (KONGURUKONDA) (MoRTH) (N24001863)	3-2021	6/2024 (10/2025) {8/2025}	154.05 (N.A.) {154.05}	47.47	30.00
		1190	CONSTRUCTION OF FOUR LANE ROB AND ITS APPROACHES IN LIEU OF EXISTING LEVEL CROSSING NO. RV-71 AT KM (MoRTH) (N24001864)	11-2021	6/2025 (N.A.) {8/2025}	154.49 (N.A.) {154.49}	59.92	32.00
		1191	CONSTRUCTION OF 4 LANE ROB WITH APPROACHES IN LIEU OF LC NO. RV-172 AT KM 176.00 OF NH-201 (PRESENT (MoRTH) (N24001865)	12-2021	5/2025 (8/2025) {8/2025}	324.09 (N.A.) {324.09}	103.11	35.00
		1192	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM. (NHAI) (N24002078)	12-2023	12/2025 (N.A.) {12/2025}	711.00 (N.A.) {711.00}	111.90	47.80
		1193	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002079)	12-2023	12/2025 (N.A.) {12/2025}	742.25 (N.A.) {742.25}	186.57	51.75
		1194	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002080)	12-2023	12/2025 (N.A.) {12/2025}	762.75 (N.A.) {762.75}	152.76	51.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1195	3L MAJOR BRIDGE OVER RIVER BRAHMANI AT KM. 401.250 (DUBURI CHANDIKHOLE SECTION) OF NH 200 (NEW NH 5 (NHAI) (N24002081)	8-2022	1/2025 (N.A.) {12/2026}	153.61 (N.A.) {153.61}	14.22	34.49
		1196	WIDENING AND STRENGTHENING TO 2L+PS FROM KM 0.000 TO 40.000 (DHAUGAON- PODAMARI SECTION) OF NH 326 I (MoRTH) (N24002135)	3-2022	2/2026 (N.A.) {2/2026}	186.52 (N.A.) {186.52}	45.90	35.00
		1197	WIDENING AND STRENGTHENING TO 4L+PS/2L+PS FROM KM 0.000 TO 35.800 (KUAKHIA - MANGALPUR SECTION) OF N (MoRTH) (N24002136)	3-2022	2/2026 (N.A.) {2/2026}	636.10 (N.A.) {636.10}	260.43	33.06
		1198	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE ? PARADIP SECTION OF NH-53 (OLD NH (NHAI) (N24002219)	3-2024	10/2026 (N.A.) {10/2026}	882.45 (N.A.) {882.45}	1.70	11.05
	STEEL	1199	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY (SAIL) (N12000122)	11-2020	5/2023 (3/2025) {3/2025}	377.18 (N.A.) {377.18}	434.90	
		1200	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP (SAIL) (N12000125)	1-2022	5/2025 (N.A.) {7/2025}	970.18 (N.A.) {970.18}	664.38	89.40

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
PUNJAB	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1201	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. (CPWD EDUCATION) (N28000142)	10-2019	5/2022 (N.A.) {7/2025}	348.24 (N.A.) {348.24}	237.84	90.00
	<u>PETROLEUM</u>	1202	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB (HPCL) (N16000402)	5-2020	2/2023 (9/2024) {12/2025}	1,421.46 (N.A.) {1,421.46}	1,153.95	95.60
		1203	BHATINDA SANGRUR PIPELINE (HPCL) (N16000440)	11-2021	5/2024 (2/2025) {6/2025}	367.00 (397.00) {397.00}	329.59	89.00
		1204	CGD PROJECT AT PATHANKOT DISTRICT (IOCL) (N16000488)	3-2022	3/2030 (9/2033) {9/2033}	151.00 (N.A.) {151.00}	8.43	2.00
	<u>RAILWAYS</u>	1205	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI (NR) (N22000502)	6-2009	8/2016 (N.A.) {8/2025}	404.00 (N.A.) {404.00}	190.00	100.00
		1206	235 (NR) (N22000589)	9-2020	3/2025 (N.A.) {6/2025}	235.00 (N.A.) {235.00}	3.88	98.00
		1207	FEROZPUR - PATTI (25.72 KM) (NR) (N22000614)	4-2017	3/2027 (N.A.) {3/2027}	299.74 (N.A.) {781.00}	0.00	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1208	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL- BUDHLADA (MoRTH) (N24000907)	3-2018	8/2020 (N.A.) {7/2024}	293.10 (N.A.) {315.00}	306.60	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1209	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 (MoRTH) (N24000909)	10-2017	10/2019 (N.A.) {12/2025}	1,069.59 (N.A.) {1,069.59}	739.08	-
		1210	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 (MoRTH) (N24000910)	3-2018	11/2020 (N.A.) {6/2024}	170.57 (192.48) {150.00}	96.38	79.00
		1211	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO (NHAI) (N24001415)	12-2020	4/2024 (7/2024) {7/2024}	881.00 (N.A.) {881.00}	882.83	89.33
		1212	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI (NHAI) (N24001416)	12-2020	1/2024 (3/2025) {3/2025}	989.66 (N.A.) {989.66}	324.77	31.08
		1213	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO (NHAI) (N24001417)	12-2020	4/2024 (9/2025) {9/2025}	1,234.40 (N.A.) {1,234.40}	792.35	57.84
		1214	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO (NHAI) (N24001418)	12-2020	4/2024 (9/2025) {9/2025}	1,094.46 (N.A.) {1,094.46}	802.93	61.96
		1215	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- (NHAI) (N24001419)	2-2021	4/2024 (11/2024) {11/2024}	1,269.96 (N.A.) {1,269.96}	585.86	43.45

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1216	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA- SRIHARGOBINDPUR- (NHA) (N24001420)	2-2021	4/2024 (12/2025) {12/2025}	853.66 (N.A.) {853.66}	132.99	15.33
		1217	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA (NHA) (N24001630)	7-2021	2/2025 (N.A.) {2/2025}	1,501.02 (N.A.) {1,501.02}	372.00	71.00
		1218	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD (NHA) (N24001631)	3-2021	10/2024 (N.A.) {10/2024}	1,525.31 (N.A.) {1,525.31}	368.00	85.00
		1219	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM (NHA) (N24001632)	1-2021	5/2024 (6/2025) {8/2025}	1,741.86 (2,281.02) {2,281.02}	1,278.00	96.00
		1220	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA ? RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR (NHA) (N24001636)	5-2021	12/2024 (10/2026) {10/2026}	1,368.91 (1,368.91) {1,368.91}	163.58	15.31
		1221	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K (NHA) (N24001637)	3-2021	1/2025 (N.A.) {1/2025}	1,754.84 (N.A.) {1,754.84}	1,082.62	34.70
		1222	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6 (NHA) (N24001638)	11-2021	7/2024 (8/2025) {8/2025}	646.42 (646.42) {646.42}	481.67	95.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1223	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE (NHAI) (N24001639)	5-2020	12/2024 (8/2025) {8/2025}	864.23 (864.23) {864.23}	434.88	61.00
		1224	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N (NHAI) (N24001640)	3-2021	11/2024 (N.A.) {11/2024}	1,229.38 (N.A.) {1,229.38}	729.77	45.30
		1225	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR (NHAI) (N24001641)	3-2021	10/2024 (12/2025) {12/2025}	1,641.75 (N.A.) {1,641.75}	187.88	26.30
		1226	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI (NHAI) (N24001642)	2-2021	8/2024 (12/2025) {12/2025}	1,474.77 (N.A.) {1,474.77}	441.47	73.26
		1227	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I (NHAI) (N24001643)	12-2020	6/2024 (6/2025) {6/2025}	857.91 (N.A.) {857.91}	127.71	39.50
		1228	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV (NHAI) (N24001644)	12-2020	9/2023 (9/2025) {9/2025}	524.88 (416.58) {416.58}	157.14	73.00
		1229	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION OF NH-354 SECTION ARIFKES-FEROZEPUR- MUKTS (MoRTH) (N24001960)	3-2021	10/2023 (N.A.) {4/2025}	263.19 (N.A.) {220.00}	22.48	42.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1230	WORK OF WIDENING/UPGRADATION OF 2- LANE WITH PAVED SHOULDER OF SRI MUKTSAR SAHIB TO MALOUT ROAD FROM (MoRTH) (N24001961)	3-2022	10/2023 (N.A.) {4/2025}	152.58 (N.A.) {152.58}	8.49	69.00
		1231	6L OF JODHPUR ROMANA (BATHINDA) - MANDI DABWALI (PUNJAB HARYANA BORDER) SECTION OF NH-54 FROM KM. 0. (NHAI) (N24002075)	12-2020	8/2025 (8/2025) {8/2025}	757.13 (757.00) {757.00}	246.51	97.00
		1232	6L AMRITSAR-BATHINDA GREENFIELD SECTION FROM JN. WITH BHAGTA BHAI KA- BHADAUR ROAD NEAR DYALPURA BHAI (NHAI) (N24002076)	3-2021	10/2025 (6/2026) {6/2026}	2,029.17 (2,029.00) {2,029.00}	84.23	43.00
		1233	6L ACCESS CONTROLLED LUDHIANA-BATHINDA GREENFIELD HIGHWAY FROM JN. WITH AMRITSAR-BATHANDA GREENFIELD (NHAI) (N24002091)	6-2021	9/2025 (3/2026) {3/2026}	906.51 (906.51) {906.51}	221.31	48.40
		1234	6-LANE AMRITSAR-BATHINDA GREENFIELD SECTION OF NH- 754A FROM JUNCTION WITH MOGA JALANDHAR ROAD (NH-70 (NHAI) (N24002092)	3-2021	10/2025 (N.A.) {10/2025}	1,801.37 (N.A.) {1,801.37}	1,003.20	40.83
		1235	6L OF AMBALA-CHANDIGARH GREENFIELD SECTION FROM KM. 0.000 TO KM. 25.000 WITH 4L SPUR TO LALRU FROM K (NHAI) (N24002098)	3-2022	10/2025 (N.A.) {10/2025}	1,641.66 (N.A.) {1,641.66}	154.00	45.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1236	4L OF EXISTING BEAS ? BABA BAKALA - DERA BABA NANAK SECTION FROM START OF BATALA BYPASS TILL INTERSE (NHAI) (N24002100)	10-2021	6/2025 (N.A.) {6/2025}	1,003.38 (N.A.) {1,003.38}	275.45	68.59
		1237	4L OF BEAS-MEHTA-BATALA- DERA BABA NANAK FROM INTERSECTION WITH JALANDHAR-AMRITSAR HIGHWAY (NH-3) NEA (NHAI) (N24002101)	8-2021	6/2025 (12/2025) {12/2025}	809.51 (N.A.) {809.51}	218.47	50.96
		1238	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I SPUR-I) FROM JN. WITH KAPURTHALA - SULTANPUR LODHI ROAD (NH (NHAI) (N24002102)	1-2020	4/2026 (N.A.) {4/2027}	2,165.23 (N.A.) {2,165.23}	167.03	19.01
RAJASTHAN	CIVIL AVIATION	1239	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT (AAI) (N04000101)	5-2022	11/2024 (10/2025) {10/2025}	480.00 (N.A.) {480.00}	217.20	60.00
		1240	UDAIPUR AIRPORT- CONSTRUCTION OF NEW INTEGRATED PASSENGER TERMINAL BUILDING (AAI) (N04000104)	6-2023	3/2026 (N.A.) {3/2026}	887.00 (N.A.) {887.00}	300.51	59.14
	COAL	1241	NLCIL 300 MW SOLAR POWER PROJECT (PART OF 510 MW CPSU SCHEME) (NLC) (N06000269)	3-2023	9/2024 (N.A.) {9/2025}	1,813.00 (N.A.) {1,813.00}	579.82	65.00
	PETROLEUM	1242	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE (IOCL) (N16000435)	12-2021	10/2024 (12/2025) {12/2025}	9,028.00 (N.A.) {9,028.00}	6,597.37	79.96

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1243	CGD PROJECT IN TONK, SAWAI MADHOPUR, DAUSA, KARAUJI (HPCL) (N16000496)	3-2022	3/2030 (N.A.) {3/2030}	1,751.00 (N.A.) {1,751.00}	292.81	24.20
		1244	SETTING UP OF PETROCHEMICAL EVACUATION MARKETING TERMINAL (PEMT) AT BARMER (HPCL) (N16000512)	12-2023	12/2026 (N.A.) {12/2026}	461.05 (N.A.) {461.05}	77.86	40.60
		1245	RAJASTHAN REFINERY PROJECT (HPCLRRL(JV)) (N16000513)	10-2017	10/2022 (3/2025) {12/2025}	43,129.00 (72,937.00) {72,937.00}	56,949.70	86.40
		1246	CGD PROJECTS AT FAZILKA (EXCEPT AREA ALREADY AUTHORIZED) GANGANAGAR AND HANUMANGARH DISTRICTS (BPCL) (N16000520)	12-2022	6/2030 (N.A.) {6/2030}	3,207.00 (N.A.) {3,207.00}	298.80	19.80
	POWER	1247	SAMBHU KI BHURJ-II SOLAR 300MW (NTPC) (N18000286)	3-2020	9/2021 (N.A.) {3/2025}	1,782.00 (12.00) {1,782.00}	1,369.88	95.00
		1248	BHENSARA 320 MW (NTPC) (N18000293)	1-2021	7/2022 (N.A.) {3/2025}	1,221.73 (1,521.00) {1,221.73}	1,133.99	-
		1249	NOKH PLOT-1 SOLAR PV PROJECT 245MW (NTPC) (N18000320)	3-2022	8/2023 (N.A.) {6/2025}	1,352.71 (N.A.) {1,352.71}	1,057.36	45.00
		1250	NOKH PLOT-2 SOLAR PV PROJECT 245MW (NTPC) (N18000321)	3-2022	8/2023 (N.A.) {3/2025}	1,409.52 (N.A.) {1,409.52}	1,403.89	95.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1251	NOKH PLOT-3 SOLAR PV PROJECT 245MW (NTPC) (N18000322)	3-2022	8/2023 (N.A.) {5/2025}	1,426.94 (N.A.) {1,426.94}	1,170.29	80.00
		1252	BHADLA-II 500MW SOLAR PV PROJECT (NTPC) (N18000347)	6-2022	3/2024 (N.A.) {9/2025}	2,598.92 (N.A.) {2,598.92}	1,705.70	12.00
		1253	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART (PGCIL) (N18000356)	3-2023	9/2024 (N.A.) {9/2025}	1,433.28 (N.A.) {1,433.28}	956.47	90.70
		1254	300 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000368)	5-2022	11/2023 (N.A.) {8/2025}	1,677.12 (N.A.) {1,677.12}	1,036.45	85.00
		1255	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III, PART E1 (PGCIL) (N18000373)	8-2023	2/2025 (N.A.) {9/2025}	688.74 (N.A.) {688.74}	411.00	91.00
		1256	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART H (PGCIL) (N18000374)	10-2023	4/2025 (N.A.) {8/2025}	2,211.00 (N.A.) {2,211.00}	1,227.63	57.00
		1257	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART C1 (PGCIL) (N18000375)	10-2023	4/2025 (10/2025) {10/2025}	1,796.00 (N.A.) {1,796.00}	929.48	67.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1258	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART B1 (PGCIL) (N18000376)	9-2023	4/2025 (N.A.) {8/2025}	2,191.00 (N.A.) {2,191.00}	1,103.26	64.00
		1259	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART J (PGCIL) (N18000378)	12-2022	3/2025 (4/2026) {4/2026}	331.00 (N.A.) {331.00}	8.66	26.00
		1260	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART E2 (PGCIL) (N18000379)	11-2023	6/2025 (N.A.) {9/2025}	428.00 (N.A.) {428.00}	0.00	35.00
		1261	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART A [BIKANER III N (PGCIL) (N18000386)	12-2023	12/2025 (N.A.) {12/2025}	2,998.00 (N.A.) {2,998.00}	729.98	42.20
		1262	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART D [NEEMRANA II B (PGCIL) (N18000387)	12-2023	12/2025 (N.A.) {12/2025}	2,056.00 (N.A.) {2,056.00}	847.00	47.00
		1263	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PH- III PART D [SIKAR KHETRI TRANSMISSION] (PGCIL) (N18000389)	2-2024	8/2025 (N.A.) {8/2025}	2,000.00 (N.A.) {2,000.00}	823.00	50.90
		1264	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) PART-B (JAISALMER/BARMER COMPLEX) (PGCIL) (N18000391)	8-2024	8/2026 (N.A.) {8/2026}	3,279.00 (N.A.) {3,279.00}	134.00	10.90

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1265	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-C (PGCIL) (N18000393)	8-2024	8/2026 (N.A.) {8/2026}	2,227.00 (N.A.) {2,227.00}	123.00	13.50
		1266	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-E (PGCIL) (N18000394)	8-2024	8/2026 (N.A.) {8/2026}	3,251.00 (N.A.) {3,251.00}	241.00	11.60
		1267	ADDITIONAL TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM BHADLA-III PS AS PART OF RAJASTHAN REZ P (PGCIL) (N18000396)	8-2024	2/2026 (N.A.) {2/2026}	369.00 (N.A.) {369.00}	0.00	1.00
		1268	TRANSMISSION SYSTEM STRENGTHENING FOR INTERCONNECTIONS OF BHADLA-III AND BIKANER III COMPLEX [SPV NA (PGCIL) (N18000397)	8-2024	8/2026 (N.A.) {8/2026}	1,382.00 (N.A.) {1,382.00}	0.00	1.00
		1269	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BAR (PGCIL) (N18000401)	11-2024	11/2026 (N.A.) {11/2026}	2,735.00 (N.A.) {2,735.00}	0.00	-
		1270	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6GW)] [BIKANER COMPLEX (PGCIL) (N18000403)	11-2024	11/2026 (N.A.) {11/2026}	5,969.00 (N.A.) {5,969.00}	0.00	-
		1271	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6 GW)] [BIKANER COMPLE (PGCIL) (N18000404)	11-2024	11/2026 (N.A.) {11/2026}	5,357.00 (N.A.) {5,357.00}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1272	RAJASTHAN REZ PH-V (PART-1: 4 GW) [SIROHI/NAGAUER] COMPLEX (PGCIL) (N18000414)	3-2025	3/2027 (N.A.) {3/2027}	5,028.00 (N.A.) {5,028.00}	0.00	-
		1273	AUGMENTATION AT FATEHGARH-II PS, FATEHGARH- IV PS (SECTION-II) AND BARMER- I (PGCIL) (N18000415)	3-2025	12/2026 (N.A.) {12/2026}	404.00 (N.A.) {404.00}	0.00	-
	<u>RAILWAYS</u>	1274	AGRA FORT-BANDIKUI (NCR) (N22000553)	6-2022	6/2027 (5/2026) {5/2026}	1,389.81 (N.A.) {987.83}	42.46	12.00
		1275	GUDHA THATHANA MITHRI TEST TRACK FOR RDSO (NWR) (N22000593)	4-2019	3/2025 (N.A.) {6/2025}	528.48 (N.A.) {500.85}	351.06	80.00
		1276	DEDICATED TEST TRACK FOR RDSO (PHASE II) (NWR) (N22000594)	11-2021	11/2026 (N.A.) {12/2025}	466.42 (N.A.) {466.22}	718.22	80.00
		1277	DOUBLING BETWEEN CHURU- RATANGARH (42.81 KM) (NWR) (N22000605)	2-2023	2/2028 (N.A.) {6/2025}	422.60 (N.A.) {422.60}	189.74	72.00
		1278	SAWAIMADHOPUR - BYPASS LINE (6.98 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NWR) (N22000607)	12-2022	6/2026 (N.A.) {1/2026}	304.00 (239.54) {239.54}	117.12	25.00
		1279	GC OF NATHDWARA - DEVGARH MADARIYA (82.5KM) (NWR) (N22000608)	1-2023	6/2028 (N.A.) {12/2026}	968.92 (N.A.) {968.92}	377.63	38.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	1280	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA (NHAI) (N24000795)	2-2018	4/2021 (5/2025) {5/2025}	741.86 (649.00) {649.00}	672.53	99.21
		1281	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. (MoRTH) (N24001411)	12-2020	10/2023 (N.A.) {12/2025}	379.23 (N.A.) {379.23}	263.62	96.10
		1282	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR (MoRTH) (N24001527)	12-2021	5/2024 (12/2025) {12/2025}	411.40 (N.A.) {411.40}	213.61	69.00
		1283	WIDENING OF PACHPADRA- BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH- 25 ON EPC MODE IN THE (MoRTH) (N24001528)	1-2022	12/2024 (8/2025) {8/2025}	194.88 (N.A.) {194.88}	105.69	75.46
		1284	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH-68) IN THE STATE OF RAJASTHAN ON EPC M (MoRTH) (N24001529)	12-2021	8/2024 (5/2025) {5/2025}	451.66 (N.A.) {451.66}	401.78	99.00
		1285	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN- LALSOT-KAROLI-DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH (MoRTH) (N24001530)	12-2021	9/2024 (N.A.) {8/2025}	150.11 (N.A.) {150.11}	74.83	83.00
		1286	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR (NHAI) (N24001557)	3-2022	11/2024 (5/2025) {5/2025}	1,636.15 (N.A.) {1,636.15}	791.63	91.22

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1287	4L OF KARWAR (KM. 281.980 OF NH-62 NAGPUR ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II) (NHAI) (N24001558)	11-2021	8/2024 (5/2025) {5/2025}	736.75 (N.A.) {736.75}	253.43	93.25
		1288	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE -0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK (NHAI) (N24001559)	9-2021	6/2024 (4/2025) {4/2025}	672.35 (N.A.) {672.35}	392.56	99.50
		1289	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6) (NHAI) (N24001563)	10-2019	8/2023 (5/2025) {5/2025}	846.59 (N.A.) {846.59}	167.25	98.00
		1290	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-7) (NHAI) (N24001564)	10-2019	7/2023 (5/2025) {5/2025}	662.08 (N.A.) {662.08}	124.06	96.50
		1291	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA (NHAI) (N24001567)	11-2019	10/2022 (6/2025) {6/2025}	1,272.97 (N.A.) {1,272.97}	628.93	85.50
		1292	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N (NHAI) (N24001568)	11-2019	5/2023 (4/2025) {4/2025}	1,119.35 (N.A.) {1,119.35}	1,447.44	99.80
		1293	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M (NHAI) (N24001573)	11-2019	12/2022 (4/2025) {4/2025}	1,658.06 (N.A.) {1,658.06}	180.53	99.90

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1294	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) JUNCTION WITH NH (NHAI) (N24001612)	7-2020	1/2024 (12/2025) {12/2025}	1,788.69 (N.A.) {1,788.69}	960.26	73.93
		1295	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FOR FATEHPUR BYPASS, MANDAWA BYPASS AND JHUNJHUNU BYPAS (MoRTH) (N24001866)	3-2022	8/2024 (N.A.) {6/2025}	186.29 (N.A.) {186.29}	142.69	78.00
		1296	UPGRADATION OF TWO LANE PAVED SHOULDER FROM SHAHPURA TO THANAGAZI OF NH-248A ON EPC MODE IN THE STAT (MoRTH) (N24001867)	3-2022	7/2024 (N.A.) {6/2025}	174.34 (N.A.) {174.34}	111.08	88.00
		1297	Sagwara Bypass and Garhi- Partapur Bypass of NH-927A in the State of Rajasthan. (MoRTH) (N24001868)	3-2022	8/2025 (N.A.) {6/2025}	187.65 (N.A.) {187.65}	114.57	83.00
		1298	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF GHAGARIYA- MUNABAO SECTION FROM KM (MoRTH) (N24001869)	12-2022	8/2025 (N.A.) {8/2025}	235.15 (N.A.) {235.15}	152.69	99.00
		1299	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FROM CHARBHUJA AT DESIGN KM 0.00 (EXISTING KM 150.00) TO (MoRTH) (N24001927)	2-2022	9/2025 (N.A.) {9/2025}	838.43 (N.A.) {838.43}	405.87	95.00
		1300	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER NORTHERN BYPASS PHASE-II OF KOTA CITY FROM DESIGN CHAINAG (MoRTH) (N24001928)	3-2022	4/2025 (N.A.) {12/2025}	317.74 (N.A.) {317.74}	136.23	12.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1301	ADDITIONAL STRUCTURES ON 6LGURGAON-JAIPUR SECTION OF NH-48 BETWEEN KM 42.700 TO KM 273.00 (NHAI) (N24002058)	8-2022	6/2024 (6/2025) {6/2025}	409.64 (N.A.) {409.64}	238.22	77.10
		1302	UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF HANUMANGARH TO KENCHIYAN OF NH 54 ON EPC MODE IN THE ST (MoRTH) (N24002167)	3-2024	10/2026 (N.A.) {10/2026}	334.64 (N.A.) {334.64}	123.00	40.00
		1303	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM NEECHLI ODEN (NATHDWARA) AT DESIGN KM 88.800 TO BHATE (MoRTH) (N24002168)	3-2023	10/2026 (N.A.) {10/2026}	606.61 (N.A.) {606.61}	116.00	15.00
SIKKIM	CIVIL AVIATION	1304	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	24.98	9.90
	DEPARTMENT OF HIGHER EDUCATION	1305	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8-2020	1/2025 (N.A.) {1/2025}	314.06 (N.A.) {303.55}	157.24	76.00
	POWER	1306	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	4,249.86	67.08
		1307	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,439.46	87.07
	RAILWAYS	1308	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	5/2015 (12/2027) {12/2027}	7,876.92 (11,963.43) {11,963.43}	8,569.25	76.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	1309	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (5/2022) {12/2023}	375.80 (N.A.) {375.80}	288.56	96.55
		1310	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11-2017	10/2020 (8/2023) {4/2024}	290.05 (N.A.) {290.05}	218.36	100.00
		1311	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {6/2025}	402.94 (N.A.) {402.94}	247.12	76.54
		1312	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (11/2024) {7/2025}	295.97 (N.A.) {295.97}	248.39	95.22
		1313	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3-2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	100.00
		1314	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {4/2025}	311.00 (N.A.) {273.78}	257.86	94.94
		1315	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (8/2024) {4/2025}	345.38 (395.59) {395.59}	362.61	90.82

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1316	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (10/2023) {12/2025}	183.31 (439.56) {439.56}	355.31	51.85
		1317	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (8/2024) {12/2025}	262.84 (414.20) {414.20}	221.86	47.56
		1318	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (10/2023) {12/2025}	292.80 (N.A.) {292.80}	202.92	60.80
		1319	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (10/2024) {12/2025}	230.45 (244.91) {244.91}	206.95	82.32
		1320	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (7/2025) {3/2026}	493.42 (478.79) {478.79}	302.83	55.21
		1321	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (6/2025) {12/2026}	816.79 (786.60) {786.60}	326.82	50.60
		1322	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1-2021	9/2023 (4/2025) {12/2025}	332.20 (348.92) {348.92}	149.38	41.04

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
TAMIL NADU		1323	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (4/2025) {12/2025}	410.60 (379.30) {379.30}	234.27	73.22
		1324	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (1/2026) {1/2026}	385.15 (N.A.) {385.15}	170.32	81.11
	CIVIL AVIATION	1325	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI (AAI) (N04000074)	6-2018	2/2022 (6/2026) {6/2026}	2,467.00 (N.A.) {2,467.00}	1,586.75	70.00
		1326	DEVELOPMENT OF TUTICORIN AIRPORT (AAI) (N04000090)	6-2019	3/2022 (4/2025) {4/2025}	380.87 (451.74) {451.74}	358.88	100.00
	COAL	1327	JAWAHAR KHANI OPENCAST (JK OC) MINE (SCCL) (N06000259)	12-2021	3/2025 (N.A.) {3/2026}	297.88 (N.A.) {297.88}	46.37	20.00
		1328	50 MW SOLAR POWER PROJECT -NEYVELI MINED OUT AREA (NLC) (N06000279)	5-2023	6/2025 (N.A.) {6/2025}	218.03 (N.A.) {218.03}	137.84	37.00
	FINANCE	1329	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI (CPWD FOR FINANC) (N28000109)	11-2017	11/2021 (N.A.) {11/2022}	348.77 (N.A.) {348.77}	223.39	100.00
	MINES	1330	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (NALCO) (N10000014)	9-2017	6/2019 (3/2024) {12/2024}	166.62 (163.17) {163.17}	135.63	65.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	1331	IRUGUR-DEVANGONTHI POL PIPELINE (BPCL) (N16000234)	11-2012	2/2017 (10/2025) {10/2025}	678.00 (1,732.00) {1,732.00}	600.83	56.70
		1332	CBR 9 MMTPA PROJECT (CPCL) (N16000434)	1-2021	6/2025 (N.A.) {6/2025}	31,580.00 (31,580.00) {36,354.00}	1,321.70	10.20
		1333	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI (IOCL) (N16000438)	1-2022	7/2024 (6/2025) {6/2025}	827.00 (887.71) {887.71}	568.48	84.79
		1334	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI) (IOCL) (N16000455)	1-2022	7/2024 (5/2026) {5/2026}	829.00 (N.A.) {829.00}	245.35	58.70
		1335	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS (IOCL) (N16000486)	3-2022	3/2030 (N.A.) {12/2030}	501.00 (N.A.) {501.00}	101.45	5.30
		1336	CGD PROJECTS AT THE NILGIRIS AND ERODE DISTRICTS (BPCL) (N16000521)	12-2022	3/2030 (N.A.) {3/2030}	3,685.00 (N.A.) {3,685.00}	193.42	10.40
	POWER	1337	TRANSMISSION SYSTEM UNDER ISTS FOR EVACUATION OF POWER FROM KUDANKULAM UNIT - 3 & 4 (2X1000 MW) (PGCIL) (N18000408)	1-2025	7/2028 (N.A.) {7/2028}	548.00 (N.A.) {548.00}	0.00	-
	RAILWAYS	1338	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP (MRTP) (N22000028)	4-2006	7/2024 (5/2025) {5/2025}	734.01 (734.01) {981.83}	632.33	98.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1339	TIDIVANAM-NAGARI (NL) (SR) (N22000085)	9-2006	9/2016 (3/2028) {3/2028}	3,631.34 (3,631.34) {3,631.34}	854.85	14.00
		1340	CHENNAI BEACH-CHENNAI EGMORE (4.3 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SR) (N22000568)	3-2022	3/2026 (2/2025) {3/2025}	359.60 (274.20) {274.20}	264.96	95.00
		1341	MORAPPUR-DHARMAPURI (SR) (N22000618)	2-2019	3/2028 (3/2027) {3/2027}	358.95 (N.A.) {358.95}	39.07	1.00
		1342	KARAIKAL PERALAM(23KM)-NEW LINE PROJECT (SR) (N22000625)	1-2019	3/2026 (3/2025) {6/2025}	304.22 (N.A.) {373.42}	298.21	80.00
		1343	NAGAPATTINAM THIRUTURAIPUNDI (38KM)- NEW LINE PROJECT (SR) (N22000626)	7-2008	3/2026 (3/2027) {3/2027}	677.12 (N.A.) {788.05}	142.44	19.00
	ROAD TRANSPORT AND HIGHWAYS	1344	FOUR LANNING OF CHOLOPURAM-THANJAVUR (NHAI) (N24000697)	8-2017	9/2020 (N.A.) {5/2025}	1,176.37 (N.A.) {1,176.37}	1,325.06	99.50
		1345	4-LANNING OF STHIYATHOPU- CHOLOPURAM (NHAI) (N24000708)	9-2017	8/2020 (4/2025) {4/2025}	1,227.87 (N.A.) {1,227.87}	1,406.21	96.10
		1346	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 (NHAI) (N24000826)	3-2018	10/2022 (5/2025) {5/2025}	505.35 (N.A.) {837.69}	376.61	99.75

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1347	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON (NHAI) (N24001428)	3-2018	11/2021 (12/2024) {12/2024}	998.70 (1,358.32) {1,358.32}	975.68	98.32
		1348	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER (NHAI) (N24001429)	3-2018	11/2021 (12/2024) {12/2024}	1,294.47 (1,588.40) {1,588.40}	865.37	98.68
		1349	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH- 45A ON HAM (NHAI) (N24001430)	3-2018	1/2022 (12/2024) {12/2024}	2,120.40 (2,565.63) {2,565.63}	1,588.17	99.80
		1350	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH- 45A ON HAM UN (NHAI) (N24001431)	3-2018	10/2020 (8/2025) {8/2025}	1,872.68 (2,661.51) {2,756.09}	1,299.72	61.40
		1351	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 (MoRTH) (N24001455)	2-2022	8/2022 (N.A.) {3/2025}	191.33 (207.97) {207.97}	100.42	100.00
		1352	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83) (NHAI) (N24001600)	10-2020	5/2023 (5/2025) {5/2025}	434.12 (N.A.) {434.12}	268.92	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1353	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 (NHA) (N24001601)	1-2019	1/2023 (6/2025) {6/2025}	1,051.69 (N.A.) {1,051.69}	587.09	81.54
		1354	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) (NHA) (N24001602)	1-2019	12/2022 (5/2025) {5/2025}	1,409.38 (N.A.) {1,409.38}	658.19	90.91
		1355	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) (NHA) (N24001603)	1-2019	10/2022 (5/2025) {5/2025}	1,518.53 (N.A.) {1,607.54}	915.40	100.00
		1356	4-LANING OF MELUR - PILLAYARPATTI - KARAUKUDI SECTION OF NH-338, NH-36, NH- 383 (NHA) (N24001605)	6-2018	3/2022 (N.A.) {6/2025}	1,103.86 (N.A.) {1,103.86}	568.15	82.00
		1357	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH-744A (MADURAI RING ROAD) (NHA) (N24001606)	12-2018	3/2022 (8/2025) {8/2025}	854.94 (N.A.) {854.94}	400.13	74.72
		1358	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS (NHA) (N24001692)	1-2022	9/2024 (2/2025) {6/2025}	467.99 (N.A.) {468.00}	24.19	78.12
		1359	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 (NHA) (N24001693)	9-2021	10/2024 (N.A.) {10/2024}	1,751.18 (N.A.) {1,757.27}	49.69	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1360	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM (NHAI) (N24001694)	2-2019	12/2023 (12/2024) {12/2024}	1,243.57 (N.A.) {1,243.57}	171.63	-
		1361	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH- 844 (PKG-III) FROM KM.60+100 TO KM.94+460 (NHAI) (N24001696)	2-2019	8/2023 (12/2024) {12/2024}	1,291.37 (N.A.) {1,291.37}	215.02	-
		1362	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM (NHAI) (N24001716)	7-2022	8/2023 (12/2024) {12/2024}	186.50 (242.40) {242.40}	17.15	100.00
		1363	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K (NHAI) (N24001717)	11-2020	8/2024 (N.A.) {3/2026}	1,155.49 (1,525.10) {1,525.10}	489.94	53.45
		1364	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2 (NHAI) (N24001718)	12-2020	7/2024 (N.A.) {8/2025}	843.48 (1,077.40) {1,068.60}	431.31	90.40
		1365	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT (NHAI) (N24001719)	2-2021	7/2024 (N.A.) {10/2025}	2,948.31 (3,605.73) {3,605.73}	808.77	73.80
		1366	BANGALORE CHENNAI EXPRESSWAY PHASE-III ? PACKAGE I (GUDIPALA TO WALAJHPET) FROM KM 156.000 TO KM 1 (NHAI) (N24001720)	10-2020	5/2024 (N.A.) {8/2025}	1,023.91 (1,438.62) {1,438.62}	635.04	83.57

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1367	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 (NHA) (N24001721)	2-2019	5/2024 (8/2025) {3/2026}	1,008.99 (1,360.53) {1,360.53}	303.48	47.65
		1368	6L OF MADURAVOYAL TO SRIPERUMBUDUR SECTION FROM KM. 13.800 TO KM. 37.000 OF NH-4 THROUGH STATE HIGH (NHA) (N24001722)	11-2021	2/2023 (N.A.) {12/2024}	463.44 (463.07) {463.44}	334.80	99.00
		1369	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091 (NHA) (N24001723)	10-2018	2/2021 (N.A.) {6/2025}	707.90 (766.51) {766.51}	526.39	88.95
		1370	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48 (NHA) (N24001725)	1-2019	5/2021 (N.A.) {1/2025}	819.89 (1,314.82) {922.85}	415.60	57.32
		1371	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 ? 29/250 INCLUDING LA AND SHIFTING OF NH-234 (MoRTH) (N24001828)	1-2022	11/2024 (N.A.) {5/2025}	221.03 (243.95) {243.95}	176.50	85.00
		1372	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH- 83) INCLU (MoRTH) (N24001829)	10-2022	11/2024 (N.A.) {5/2025}	172.15 (N.A.) {172.15}	157.48	99.00
		1373	CONSTRUCTION OF STRR (WEST SIDE)-NH948A- BALAGONDAPALLI (TAMIL NADU) TO KARNATAKA/TAMIL NADU BORDER F (NHA) (N24001968)	4-2022	5/2025 (N.A.) {5/2025}	1,260.74 (N.A.) {1,260.74}	487.46	44.95

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1374	4L OF THIRUMANGALAM TO VADUGAPATTI SECTION FROM KM 0.000 TO KM 36.000 OF NH- 744 (NHAI) (N24002084)	3-2022	2/2025 (N.A.) {8/2025}	1,076.97 (N.A.) {1,076.97}	540.46	86.82
		1375	CONSTRUCTION OF NEW DOUBLE TIER 4 LANE ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI (NHAI) (N24002107)	3-2023	5/2026 (N.A.) {5/2026}	1,382.00 (N.A.) {1,382.00}	0.00	-
		1376	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002108)	3-2023	5/2026 (N.A.) {5/2026}	1,618.96 (N.A.) {1,618.96}	0.00	-
		1377	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002109)	3-2023	5/2026 (N.A.) {5/2026}	1,301.37 (N.A.) {1,301.37}	0.00	-
		1378	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002110)	3-2023	5/2026 (N.A.) {5/2026}	1,207.40 (N.A.) {1,207.40}	0.00	-
		1379	FOUR LANING OF MUGAIYUR TO MARAKKANAM SECTION OF NH- 332A FROM KM 31.000 TO KM 62.000 (NHAI) (N24002111)	2-2019	12/2025 (12/2025) {12/2025}	825.94 (1,116.13) {1,116.13}	311.35	36.66
		1380	SIX LANING OF TUTICORIN PORT ROAD SECTION OF NH-7A (NEW NH-138) FROM KM 0.000 TO KM 6.140 [EFFECTIVE (NHAI) (N24002112)	3-2023	7/2024 (N.A.) {6/2025}	200.30 (N.A.) {200.30}	103.35	79.60

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1381	4L OF LEFT-OVER WORKS INCLUDING ADDITIONAL STRUCTURES FROM KERALA/TAMIL NADU BORDER TO KANYAKUMARI S (NHAI) (N24002113)	3-2023	8/2025 (N.A.) {8/2025}	1,141.78 (N.A.) {1,141.78}	412.13	41.02
		1382	4L OF VADUGAPATTI TO THERKUVENGANALLUR (RAJAPALYAM) SECTION FROM KM 36.000 TO KM 71.600 OF NH744 UND (NHAI) (N24002114)	2-2022	4/2025 (N.A.) {10/2025}	1,097.59 (N.A.) {1,317.06}	678.59	94.60
		1383	WIDENING TO 4L/4L+PS AND STRENGTHENING IN SELECTED STRETCHES FROM KM 0/8 TO 50/570 OF NH 532 INCLUD (MoRTH) (N24002151)	3-2022	1/2024 (N.A.) {7/2025}	257.14 (294.70) {294.70}	228.36	82.00
		1384	WIDENING FROM 2L+PS TO 4L/4L+PS AND IMPROVEMENTS THE SELECTED STRETHCES FROM KM 26/5 - 81/2 INCLU (MoRTH) (N24002152)	3-2023	11/2023 (N.A.) {11/2025}	274.84 (N.A.) {274.84}	243.81	100.00
		1385	STRENGTHENING OF 2L+PS FROM KM 17/8 ? 18/2, CONSTRUCTION OF 2L+PS FROM KM 18/2 TO KM 20/0 AND CONSTR (MoRTH) (N24002153)	3-2023	2/2024 (N.A.) {8/2025}	169.68 (N.A.) {169.68}	112.18	70.00
		1386	CONSTRUCTION OF BYPASS TO MADURAI - ACHAMBATHU - VIRATIPATHU IN KM 6/850 - 10/382 OF NH 49 EXTN. (NE (MoRTH) (N24002165)	3-2022	8/2026 (N.A.) {8/2026}	238.97 (260.07) {260.07}	95.44	44.00
		1387	ACCESS CONTROLLED HIGHWAY OF 4 LANE WITH PAVED SHOULDERS FROM TIRUVALLUR (DESIGN CHAINAGE KM 17+56) (NHAI) (N24002216)	12-2024	12/2026 (N.A.) {12/2026}	1,376.10 (N.A.) {1,376.10}	0.00	5.11

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
TELANGANA	COAL	1388	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 (SCCL) (N06000161)	3-2017	3/2022 (N.A.) {3/2026}	413.84 (N.A.) {413.84}	397.54	85.00
		1389	GODAVARIKHANI COAL MINE (SCCL) (N06000202)	7-2019	3/2023 (N.A.) {3/2026}	438.98 (N.A.) {438.98}	171.96	70.00
		1390	VENKATESH KHANI COAL MINE (SCCL) (N06000204)	10-2020	3/2023 (N.A.) {3/2027}	484.51 (N.A.) {484.51}	318.12	55.00
		1391	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT (SCCL) (N06000210)	11-2015	3/2023 (N.A.) {3/2026}	489.62 (N.A.) {489.62}	405.54	70.00
		1392	RCE OF INDARAM OPENCAST PROJECT (SCCL) (N06000211)	8-2017	3/2021 (N.A.) {3/2025}	349.28 (N.A.) {424.81}	402.64	80.00
		1393	RCE OF KALYANIKHANI OPENCAST PROJECT (SCCL) (N06000213)	3-2016	3/2020 (N.A.) {3/2026}	384.32 (N.A.) {384.32}	255.02	75.00
		1394	RCE OF KAKATHIYAKHANI OC - 2 PROJECT (SCCL) (N06000214)	8-2017	3/2020 (N.A.) {3/2026}	442.42 (N.A.) {442.42}	203.00	63.00
		1395	GOLETI OPENCAST MINE (SCCL) (N06000258)	7-2021	3/2026 (N.A.) {3/2026}	345.60 (N.A.) {345.60}	68.47	20.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>HEALTH AND FAMILY WELFARE</u>	1396	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR (HITES) (N21000031)	12-2018	7/2024 (N.A.) {12/2025}	1,110.55 (N.A.) {1,110.55}	734.90	81.62
		1397	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD (CPWD FOR HEALTH) (N28000098)	10-2016	3/2020 (1/2025) {1/2025}	209.84 (281.05) {281.05}	253.13	98.50
	<u>RAILWAYS</u>	1398	MANOHARABAD-KOTHPALL NEW LINE(SCR) (SCR) (N22000032)	4-2006	3/2027 (N.A.) {3/2025}	1,160.00 (N.A.) {3,014.00}	1,510.20	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1399	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT (MoRTH) (N24000245)	1-2014	3/2016 (9/2019) {9/2019}	270.00 (N.A.) {270.00}	0.00	72.15
		1400	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR (MoRTH) (N24000247)	10-2014	2/2017 (N.A.) {2/2017}	295.47 (N.A.) {295.47}	224.42	99.00
		1401	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM (MoRTH) (N24000248)	3-2015	1/2017 (N.A.) {1/2017}	153.21 (N.A.) {153.21}	100.96	94.00
		1402	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON (MoRTH) (N24000980)	10-2016	2/2019 (N.A.) {2/2019}	298.32 (N.A.) {298.32}	178.47	98.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1403	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ (MoRTH) (N24000981)	10-2016	3/2019 (N.A.) {3/2019}	248.83 (N.A.) {248.83}	173.79	100.00
		1404	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE (MoRTH) (N24000982)	1-2017	5/2019 (N.A.) {5/2019}	244.54 (N.A.) {244.54}	174.35	99.00
		1405	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH (MoRTH) (N24000983)	1-2017	10/2019 (N.A.) {10/2019}	196.52 (N.A.) {196.52}	125.53	96.00
		1406	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI (MoRTH) (N24000984)	1-2017	12/2019 (N.A.) {12/2019}	283.00 (N.A.) {283.00}	259.15	99.00
		1407	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION (MoRTH) (N24000986)	1-2017	5/2019 (N.A.) {5/2019}	300.00 (N.A.) {300.00}	239.93	96.00
		1408	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH (MoRTH) (N24000987)	1-2018	5/2020 (N.A.) {5/2020}	283.15 (N.A.) {283.15}	270.01	93.00
		1409	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 (MoRTH) (N24000988)	1-2018	12/2019 (N.A.) {12/2019}	230.03 (N.A.) {230.03}	231.31	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1410	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 (MoRTH) (N24000989)	2-2018	6/2020 (N.A.) {6/2020}	206.13 (N.A.) {206.13}	190.94	98.00
		1411	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT (MoRTH) (N24000990)	2-2018	11/2019 (N.A.) {11/2019}	294.13 (N.A.) {294.13}	198.75	87.00
		1412	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC (MoRTH) (N24000993)	3-2018	9/2020 (N.A.) {9/2020}	322.81 (N.A.) {322.81}	315.23	98.00
		1413	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES (MoRTH) (N24000994)	3-2018	7/2020 (N.A.) {2/2026}	626.76 (N.A.) {626.76}	272.64	45.00
		1414	REHABILITATION AND UP- GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR (MoRTH) (N24000996)	1-2017	10/2019 (N.A.) {10/2019}	605.08 (N.A.) {605.08}	413.37	100.00
		1415	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL ? MALLAMPALLY SECTION OF NH- 365 (MoRTH) (N24000997)	3-2018	7/2019 (N.A.) {7/2019}	192.67 (N.A.) {192.67}	176.37	92.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1416	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR (MoRTH) (N24000998)	1-2019	(N.A.) { }	193.19 (N.A.) {249.72}	222.58	95.00
		1417	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED (GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM (NHAI) (N24001482)	8-2022	10/2024 (N.A.) {10/2024}	772.11 (N.A.) {772.11}	515.01	75.21
		1418	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM VILLAGE TO CHINTAGUDEM V (NHAI) (N24001483)	2-2022	9/2024 (N.A.) {9/2024}	637.11 (N.A.) {637.11}	398.90	82.00
		1419	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUDEM VILLAGE TO RECHERLA (NHAI) (N24001484)	9-2022	2/2024 (12/2024) {12/2024}	804.69 (N.A.) {804.69}	510.12	87.00
		1420	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH- 65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 (NHAI) (N24001522)	1-2021	1/2024 (12/2024) {12/2024}	1,307.95 (N.A.) {1,307.95}	707.34	99.79
		1421	6 LANING OF EXISTING 4-LANE STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000, (NHAI) (N24001555)	3-2022	1/2025 (N.A.) {1/2025}	955.49 (N.A.) {955.49}	226.99	35.96

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1422	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44 (NHAI) (N24001556)	12-2021	7/2024 (N.A.) {7/2024}	521.53 (N.A.) {521.53}	247.45	48.76
		1423	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 (NHAI) (N24001625)	1-2022	1/2025 (N.A.) {7/2025}	1,227.57 (N.A.) {1,227.57}	288.58	46.50
		1424	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM (NHAI) (N24001626)	2-2022	1/2025 (N.A.) {1/2025}	972.06 (N.A.) {972.06}	408.48	64.42
		1425	WIDENING AND STRENGTHENING OF EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FRO (MoRTH) (N24002000)	3-2021	7/2024 (N.A.) {7/2024}	317.19 (N.A.) {317.19}	162.21	70.00
		1426	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF MEDAK - SIDDIPET SECTION FROM KM 0/0 TO KM 69/978 OF NH- (MoRTH) (N24002001)	1-2022	1/2025 (N.A.) {6/2025}	882.18 (N.A.) {882.18}	206.02	71.00
		1427	WIDENING AND IMPROVEMENT OF EXISTING CARRIAGE WAY TO 2 LANE WITH PAVED SHOULDERS FROM KM. 86/160 TO (MoRTH) (N24002002)	1-2022	12/2024 (N.A.) {12/2024}	423.48 (N.A.) {423.48}	149.27	71.00
		1428	REHABILITATION AND UP-GRADATION OF VALIGONDA TO THORRUR SECTION TO TWO LANE WITH PAVED SHOULDERS FRO (MoRTH) (N24002003)	1-2022	12/2024 (N.A.) {12/2024}	549.28 (N.A.) {549.28}	103.51	70.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1429	REHABILITATION AND UPGRADATION OF LB-NAGAR TO MALKAPUR SECTION TO 6- LANE MAIN CARRIAGEWAY WITH SERVI (MoRTH) (N24002004)	3-2021	7/2024 (N.A.) {6/2025}	545.11 (N.A.) {545.11}	191.56	76.00
		1430	WIDENING TO TWO LANE WITH PAVED SHOULDERS OF 'BODHAN BASAR BHAINSA ' SECTION FROM KM 38/900 TO 95/3 (MoRTH) (N24002005)	3-2022	3/2025 (N.A.) {6/2025}	644.45 (N.A.) {644.45}	182.85	93.00
		1431	ONSTRUCTION OF 4-LANE FLYOVER AT AMBERPET-X ROAD, HYDERABAD ON NH-202 IN THE STATE OF TELANGANA (MoRTH) (N24002006)	10-2017	6/2023 (N.A.) {6/2023}	186.71 (N.A.) {186.71}	149.64	92.00
		1432	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/000 TO KM 79/300 OF KALWAKURTHY - KOLLAPUR SECTI (MoRTH) (N24002007)	3-2022	7/2025 (N.A.) {7/2025}	886.69 (N.A.) {886.69}	90.46	59.00
		1433	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF SIDDIPET-ELKATHURTHY SECTION FROM KM 69/978 TO KM 133/6 (MoRTH) (N24002008)	1-2022	12/2024 (N.A.) {12/2024}	578.85 (N.A.) {578.85}	172.76	79.00
		1434	WIDENING AND STRENGTHENING TO 2/4 LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR ? CHINCHOLI SECTION FROM (MoRTH) (N24002009)	1-2022	1/2025 (N.A.) {7/2025}	703.68 (N.A.) {703.68}	193.39	61.00
		1435	WIDENING AND STRENGTHENING TO 4 LANE / 2- LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR- CHINCHOLI SECTION (MoRTH) (N24002010)	3-2022	3/2024 (N.A.) {10/2025}	631.49 (N.A.) {631.49}	7.92	25.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1436	IMPROVEMENT OF GEOMETRICS OF THONDUPALLY TO KOTHUR FROM KM 22.300 TO KM 34.14 OF NH-44-RCW (NHAI) (N24002082)	2-2022	9/2024 (N.A.) {1/2026}	541.58 (N.A.) {541.58}	34.78	-
		1437	FOUR LANING OF KARIMNAGAR- WARANGAL SECTION OF NH-563 FROM DESIGN CH.48.860 KM NEAR SH-1 CH.170.400 K (NHAI) (N24002083)	3-2022	7/2025 (N.A.) {7/2025}	2,146.86 (2,413.00) {2,414.46}	917.28	69.15
		1438	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM-VIJAYAWADA) (NHAI) (N24002190)	3-2023	8/2026 (N.A.) {8/2026}	983.00 (N.A.) {983.00}	0.00	8.50
		1439	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM - VIJAYAWADA) (NHAI) (N24002236)	3-2023	3/2025 (N.A.) {3/2027}	832.62 (N.A.) {832.62}	0.00	-
TRIPURA	PETROLEUM	1440	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (9/2025) {9/2025}	656.00 (N.A.) {656.00}	395.18	81.15
	ROAD TRANSPORT AND HIGHWAYS	1441	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (2/2024) {12/2024}	277.50 (302.02) {302.02}	260.38	99.94
		1442	KAILASHAHAR TO KHOWAI PKG- 4 (NHIDCL) (N24001309)	11-2020	6/2022 (10/2023) {11/2024}	159.13 (171.50) {171.50}	84.33	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1443	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {4/2025}	201.99 (N.A.) {287.47}	148.22	100.00
		1444	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (N.A.) {12/2025}	354.79 (N.A.) {354.79}	34.08	-
		1445	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (5/2025) {5/2025}	456.88 (N.A.) {456.88}	122.23	49.17
		1446	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {11/2025}	195.95 (N.A.) {195.95}	38.10	38.44
		1447	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	18.44	7.96
		1448	REHABILITATION AND UP- GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	7.56	16.61
		1449	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	46.60	31.45
		1450	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	11.96	27.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1451	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	0.00	-
		1452	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	63.55	18.60
		1453	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM SECTION PKG-4 (NHIDCL) (N24002228)	1-2024	12/2026 (N.A.) {12/2026}	726.90 (N.A.) {726.90}	0.00	2.25
UTTAR PRADESH	CIVIL AVIATION	1454	CCS INTERNATIONAL AIRPORT , LUCKNOW (AAI) (N04000077)	6-2018	9/2021 (10/2026) {10/2026}	1,383.00 (1,938.00) {3,291.81}	2,631.82	79.95
		1455	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 (AAI) (N04000094)	3-2021	12/2022 (5/2025) {5/2025}	242.14 (328.00) {358.00}	344.58	99.90
		1456	PRAYAGRAJ AIRPORT - CONSTRUCTION OF NEW TERMINAL BUILDING, SECOND LINK TAXI TRACK, APRON EXPANSION, (AAI) (N04000102)	5-2023	11/2024 (6/2025) {6/2025}	185.75 (274.38) {274.38}	192.24	91.00
		1457	AGRA: DEVELOPMENT OF NEW CIVIL ENCLAVE AT AGRA AIRPORT. (AAI) (N04000113)	6-2024	7/2026 (N.A.) {7/2026}	579.00 (N.A.) {579.00}	46.91	11.00
		1458	VARANASI: DEVELOPMENT OF LAL BAHADUR SHASTRI INTERNATIONAL AIRPORT, VARANASI. (AAI) (N04000114)	7-2024	7/2027 (N.A.) {7/2027}	2,869.65 (N.A.) {2,869.65}	225.89	14.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	COAL	1459	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW (NLC) (N06000152)	7-2016	11/2021 (10/2025) {10/2025}	17,237.00 (21,780.94) {21,780.94}	19,780.67	90.41
		1460	KHADIA EXPANSION OCP (NCL) (N06000208)	6-2021	3/2025 (N.A.) {3/2027}	491.67 (N.A.) {491.67}	163.58	13.12
	HOME AFFAIRS	1461	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI (CPWD FOR MHA) (N45000003)	5-2019	1/2022 (3/2023) {3/2023}	199.31 (N.A.) {199.31}	86.49	85.00
	PETROLEUM	1462	60 KTA POLYPROPYLENE PROJECT (GAIL) (N16000429)	3-2019	4/2024 (4/2024) {6/2025}	910.56 (1,299.02) {1,299.02}	956.00	95.30
		1463	AUGMENTATION OF FACILITIES AT MATHURA BITUMEN PLANT (IOCL) (N16000505)	4-2022	4/2025 (12/2026) {12/2026}	260.12 (N.A.) {260.12}	1.03	25.00
		1464	GRASS-ROOT TERMINAL AT MIRZAPUR UTTAR PRADESH (IOCL) (N16000506)	9-2022	6/2026 (N.A.) {11/2026}	980.45 (N.A.) {980.45}	177.07	49.49
		1465	CITY GAS DISTRIBUTION PROJECTS AT LAKHIMPUR KHERI , SITAPUR, BAHRAICH, SHRAVASTI,BALRAMPUR, (BPCL) (N16000525)	12-2022	6/2030 (N.A.) {6/2030}	16,654.00 (N.A.) {16,654.00}	527.19	9.40
	POWER	1466	KHURJA SUPER THERMAL POWER PROJECT (THDCIL) (N18000272)	3-2019	9/2023 (N.A.) {6/2025}	11,089.42 (N.A.) {13,276.16}	12,251.20	95.20

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1467	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III (2X800 MW) (NTPC) (N18000382)	3-2024	2/2030 (N.A.) {2/2030}	17,195.31 (N.A.) {17,195.31}	1,302.80	0.50
		1468	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-4: 3.5 GW): PART A (PGCIL) (N18000407)	12-2024	12/2026 (N.A.) {12/2026}	5,846.00 (N.A.) {5,846.00}	0.00	-
	RAILWAYS	1469	VARANASI-MODHOSINGH- ALLAHABAD DOUBLING (RVNL) (N22000401)	4-2015	12/2024 (N.A.) {12/2024}	2,018.23 (N.A.) {2,018.23}	1,780.22	-
		1470	2880.4 (ECR) (N22000417)	8-2015	8/2024 (N.A.) {1/2025}	2,880.40 (2,880.40) {2,880.40}	3,074.78	100.00
		1471	KARAILA ROAD - SHAKTINAGAR DOUBLING (ECR) (N22000419)	8-2015	8/2024 (N.A.) {12/2024}	762.97 (762.97) {762.97}	808.96	100.00
		1472	BURHWAL - GONDA - 3RD RUNNING LINE. (NER) (N22000468)	4-2016	3/2025 (N.A.) {9/2025}	1,015.59 (N.A.) {1,117.80}	1,092.11	48.00
		1473	SHAHGANJ-BHATNI-PHEPHNA- INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. (NER) (N22000470)	4-2016	12/2024 (N.A.) {5/2025}	1,177.96 (N.A.) {2,050.00}	2,042.60	80.50
		1474	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING (NCR) (N22000495)	3-2018	3/2026 (N.A.) {3/2027}	4,329.53 (N.A.) {4,329.53}	1,963.36	45.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1475	JHANSI BINA DOUBLING (NCR) (N22000496)	9-2016	3/2022 (N.A.) {3/2027}	2,002.00 (N.A.) {2,001.00}	1,717.20	90.00
		1476	MATHURA-JHANSI-3RD LINE (273.80 KM) (RVNL) (N22000501)	6-2016	12/2024 (N.A.) {12/2024}	5,323.39 (N.A.) {5,190.26}	5,046.07	-
		1477	SURFACE TRIANGLE LINE BETWEEN BHADURA STATION AND NEW CROSSING STN KARMA DOUBLING (ECR) (N22000525)	10-2022	10/2027 (N.A.) {10/2027}	199.96 (N.A.) {199.96}	55.09	-
		1478	MUGHALSARAI - ALLAHABAD - 3RD LINE (NCR) (N22000544)	8-2019	12/2026 (N.A.) {12/2026}	2,649.44 (N.A.) {2,390.00}	83.10	55.00
		1479	ALIGARH-HARDUAGANJ FLYOVER (22 KM) (NCR) (N22000545)	4-2020	6/2026 (N.A.) {6/2026}	1,456.89 (1,244.13) {1,456.89}	10.14	8.10
		1480	LALITPUR - BIRARI WITH FLYOVER AT LALITPUR (NCR) (N22000546)	3-2017	12/2024 (N.A.) {6/2025}	356.09 (N.A.) {356.00}	196.15	65.00
		1481	ALIGARH-DAUD KHAN - 3RD LINE 6.9 KM AND CONSTRUCTION OF FLYOVER AT DAUD KHAN (NCR) (N22000562)	4-2019	12/2025 (N.A.) {12/2025}	451.99 (779.49) {779.49}	99.70	38.10
		1482	ALLAHABAD-BAMHRAULI - 4TH LINE (10 KM) WITH FLY-OVER AT SUBEDARGANJ (NCR) (N22000563)	4-2019	3/2026 (N.A.) {3/2026}	494.11 (N.A.) {494.11}	42.61	42.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1483	BHANDAI - FLYOVER FOR ETAWAH BOUND DOWN TRAINS (NCR) (N22000564)	4-2019	12/2025 (N.A.) {3/2026}	187.21 (N.A.) {250.17}	1.29	8.00
		1484	SAHJANWA - DOHRIGHAT (NER) (N22000565)	8-2019	3/2029 (N.A.) {12/2027}	371.77 (N.A.) {1,319.75}	551.74	2.50
		1485	BAHRAICH - NANPARA - NEPALGANJ (56.15 KM) (NER) (N22000566)	7-2020	12/2024 (N.A.) {6/2025}	950.00 (N.A.) {341.66}	300.63	21.50
		1486	BAHRAICH SRAVASTI BALRAMPUR (TULSIPUR) (NER) (N22000569)	10-2018	10/2030 (N.A.) {3/2028}	4,939.78 (N.A.) {4,939.78}	1,079.60	5.00
		1487	JANGHAI PRATAPGARH AMETHI DOUBLING (NR) (N22000583)	11-2017	3/2025 (N.A.) {12/2025}	721.72 (N.A.) {1,100.00}	39.22	70.00
		1488	BARABANKI MALHAUR 3RD AND 4TH LINE (32.84 KM) (NR) (N22000590)	1-2019	3/2025 (1/2026) {12/2025}	323.85 (N.A.) {407.00}	5.17	58.00
		1489	DOUBLING BETWEEN JAUNPUR JN-ZAFFARABAD (6.28 KM) (NR) (N22000591)	3-2023	12/2026 (N.A.) {12/2026}	177.33 (N.A.) {177.33}	0.89	10.00
		1490	JANGHAI-PHAPHAMAU - DOUBLING WITH ELECTRIFICATION (46.79 KM) (RVNL) (N22000596)	11-2018	3/2025 (N.A.) {3/2025}	357.48 (N.A.) {409.38}	362.09	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1491	BHATNI - AUNRIHAR WITH ELECTRIFICATION (125 KM) (EXCL INDARA - MAU (116.95 KM)) (RVNL) (N22000598)	5-2018	12/2024 (N.A.) {2/2025}	2,529.46 (N.A.) {2,529.46}	1,636.33	-
		1492	MATHURA - VRINDAVAN (11 KM) (NCR) (N22000612)	8-2022	6/2025 (N.A.) {6/2025}	402.88 (N.A.) {402.88}	0.00	-
		1493	DOMINGARH - GORAKHPUR - GORAKHPUR CANTT - KUSUMHI - 3RD RUNNING LINE (21.15 KM) (NER) (N22000613)	11-2016	2/2025 (N.A.) {7/2025}	351.03 (N.A.) {500.37}	464.91	86.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1494	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE - I) ON EASTERN SIDE OF NH 24B (MoRTH) (N24000331)	12-2019	4/2022 (N.A.) {6/2025}	282.41 (N.A.) {319.96}	276.35	88.00
		1495	4-LANNING OF HARIDWAR- NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 (NHAI) (N24000564)	3-2016	7/2020 (6/2025) {6/2025}	1,408.00 (1,659.12) {1,659.12}	1,319.36	88.01
		1496	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA (NHAI) (N24000798)	3-2018	11/2021 (N.A.) {6/2025}	2,140.93 (N.A.) {2,140.93}	2,067.09	98.90
		1497	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN (NHAI) (N24001306)	10-2020	3/2023 (N.A.) {5/2024}	724.60 (N.A.) {724.60}	569.96	96.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1498	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD (MoRTH) (N24001421)	7-2018	2/2024 (N.A.) {8/2025}	1,948.25 (N.A.) {1,948.25}	1,082.99	77.00
		1499	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH- 24A INCLUDING RETAINING W (MoRTH) (N24001424)	3-2021	9/2023 (N.A.) {1/2025}	185.09 (269.81) {269.81}	266.35	100.00
		1500	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM (MoRTH) (N24001456)	4-2020	2/2024 (N.A.) {1/2025}	199.39 (212.96) {199.39}	200.01	100.00
		1501	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH-730C F (MoRTH) (N24001457)	4-2020	7/2024 (N.A.) {9/2025}	172.50 (169.56) {172.50}	106.04	73.00
		1502	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP (MoRTH) (N24001461)	4-2020	3/2024 (N.A.) {7/2025}	236.47 (N.A.) {236.47}	145.81	87.00
		1503	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH-92 FROM KM.30.000 TO 57.346 UNDER GNHCP (MoRTH) (N24001462)	4-2020	7/2024 (N.A.) {7/2025}	211.09 (N.A.) {211.09}	147.58	95.00
		1504	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00 (MoRTH) (N24001464)	3-2021	8/2023 (N.A.) {5/2025}	264.86 (N.A.) {264.86}	122.82	84.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1505	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO (MoRTH) (N24001469)	11-2021	5/2024 (N.A.) {7/2025}	307.11 (N.A.) {307.11}	199.38	88.00
		1506	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH-730C FROM KM.0.00 TO 52.770 UNDER GNHCP (MoRTH) (N24001471)	4-2020	11/2024 (N.A.) {6/2025}	325.24 (340.16) {325.24}	284.33	96.00
		1507	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR) (MoRTH) (N24001479)	3-2021	5/2024 (N.A.) {6/2025}	395.62 (392.03) {395.62}	281.93	72.00
		1508	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH-334A (PURKAJI-LAKSAR-HARIDWAR ROAD) TO TW (MoRTH) (N24001480)	10-2021	4/2024 (N.A.) {3/2025}	227.06 (N.A.) {227.06}	141.89	100.00
		1509	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO (NEAR MOHAND) OF GANESHPUR ? DEHRADUN SECTION FROM K (NHAI) (N24001523)	3-2021	10/2023 (5/2025) {5/2025}	836.24 (N.A.) {836.24}	792.55	98.85
		1510	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR ? DEHRADUN SECTION FROM (NHAI) (N24001524)	3-2021	10/2023 (5/2025) {5/2025}	990.28 (N.A.) {990.28}	997.62	98.78

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1511	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF (MoRTH) (N24001587)	3-2020	9/2024 (N.A.) {6/2025}	262.37 (343.77) {343.77}	278.90	84.00
		1512	4L SPUR OF SHAMLI- MUZZAFARNAGAR CONNECTING NH-709AD (PANIPAT-SHAMLI- MUZZAFARNAGAR) AND NH-58 (MEERUT (NHAI) (N24001726)	1-2023	8/2024 (N.A.) {8/2024}	391.26 (N.A.) {391.26}	14.12	80.30
		1513	IMPROVEMENT AND UP- GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF KHUTAR B (NHAI) (N24001727)	3-2022	2/2025 (N.A.) {2/2025}	762.62 (N.A.) {762.62}	557.37	92.85
		1514	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT ? SHAMLI ? MUZZAFARNAGAR) AND NH- 709A (KARN (NHAI) (N24001729)	8-2022	4/2024 (N.A.) {7/2025}	326.79 (N.A.) {329.79}	109.08	96.00
		1515	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) (NHAI) (N24001730)	12-2021	1/2025 (N.A.) {3/2025}	1,384.79 (N.A.) {1,384.79}	657.94	97.98
		1516	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 (NHAI) (N24001731)	12-2021	5/2025 (5/2025) {5/2025}	2,470.64 (N.A.) {2,335.00}	691.28	85.70
		1517	IMPROVEMENT AND UP- GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS (NHAI) (N24001732)	12-2021	10/2024 (N.A.) {7/2025}	540.97 (N.A.) {540.97}	270.14	88.09

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1518	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.-MAVIKALAN) TO VILL.-LOHADDA FROM K (NHAI) (N24001733)	3-2022	8/2024 (N.A.) {7/2025}	1,602.48 (N.A.) {1,602.48}	432.16	90.00
		1519	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-LOHADDA TO VILL.-KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. (NHAI) (N24001734)	3-2022	8/2024 (N.A.) {7/2025}	1,335.45 (N.A.) {1,335.45}	449.57	77.00
		1520	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-KHYAWARI TO VILL.-LATIFPUR AT SAHARANPUR BYPASS FROM KM (NHAI) (N24001735)	3-2022	8/2024 (N.A.) {7/2025}	1,428.19 (N.A.) {1,428.19}	510.01	83.00
		1521	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-KARAUNDA MAHAJAN TO VILL.-KHYAWARI FROM KM. 56.500 TO K (NHAI) (N24001736)	1-2022	8/2024 (N.A.) {7/2025}	1,159.96 (N.A.) {1,159.96}	515.16	98.69
		1522	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG-III (NHAI) (N24001737)	11-2021	4/2024 (N.A.) {4/2024}	923.15 (N.A.) {923.15}	455.61	100.00
		1523	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV (NHAI) (N24001738)	9-2021	10/2023 (12/2024) {12/2024}	300.79 (N.A.) {300.79}	122.56	74.53
		1524	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U (NHAI) (N24001739)	10-2019	11/2023 (12/2024) {12/2024}	1,779.83 (N.A.) {2,200.00}	1,066.00	99.80

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1525	4L OF SHAMLI BYAPSS- SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH- 709B, PKG-II (NHAI) (N24001744)	5-2019	11/2022 (N.A.) {7/2025}	779.17 (N.A.) {779.17}	64.10	96.45
		1526	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N (NHAI) (N24001745)	12-2021	7/2025 (7/2025) {7/2025}	1,972.10 (N.A.) {1,936.00}	466.64	61.53
		1527	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4-LANE ON EPC MODE IN THE STATE OF UTTAR (NHAI) (N24001746)	3-2021	4/2024 (6/2025) {6/2025}	364.47 (N.A.) {364.47}	202.47	90.72
		1528	4 LANING OF NAJIBABAD BYPASS OF NH-119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH-74 (NHAI) (N24001753)	2-2022	6/2024 (4/2025) {4/2025}	570.98 (578.02) {578.02}	400.10	95.10
		1529	SPUR OF MEERUT-GARH- MUKTESHWAR SECTION(NH- 709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN (NHAI) (N24001754)	1-2022	10/2024 (N.A.) {10/2024}	953.79 (N.A.) {953.79}	384.66	66.29
		1530	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH (NHAI) (N24001755)	10-2019	3/2023 (12/2024) {12/2024}	1,936.68 (N.A.) {2,458.03}	1,380.90	100.00
		1531	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR (NHAI) (N24001772)	8-2021	3/2024 (12/2024) {12/2024}	1,147.26 (N.A.) {1,147.26}	81.34	60.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1532	4L BYPASSES FOR JAGATPUR, B4ABUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA (NHAI) (N24001815)	12-2022	11/2024 (N.A.) {11/2024}	1,699.00 (1,078.00) {1,699.00}	64.39	100.00
		1533	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 (NHAI) (N24001826)	2-2019	2/2022 (6/2025) {12/2025}	927.77 (N.A.) {1,603.00}	1,202.77	91.25
		1534	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 (NHAI) (N24001830)	6-2020	11/2023 (12/2024) {12/2024}	2,002.79 (N.A.) {2,002.79}	1,989.85	99.00
		1535	4L FROM MATHURA BYPASS (START) AT EXISTING KM. 154.20 OF NH-44 TO GAJU VILLAGE AT KM 32.982 OF NH-53 (NHAI) (N24001851)	1-2022	3/2025 (N.A.) {3/2025}	1,738.20 (N.A.) {1,738.20}	742.13	65.00
		1536	6L OF AGRA BYPASS (NORTHERN) CONNECTING KM. 174.500 OF NH-2 (NEW NH-19) TO KM. 141.000 OF YAMUNA EXP (NHAI) (N24001852)	10-2021	2/2025 (N.A.) {2/2025}	957.62 (N.A.) {957.62}	832.80	86.00
		1537	CONSTRUCTION OF LEFT OUT PORTION OF AGRA INNER RING ROAD CONNECTING VILLAGE DEORI TO NH-44 VILLAGE B (NHAI) (N24001853)	10-2021	9/2024 (3/2025) {3/2025}	772.05 (N.A.) {772.05}	593.39	67.50
		1538	CONSTRUCTION OF 4-LANE GREEN FIELD HIGHWAY FROM KM. 35.000 TO KM. 49.155 OF NH- 731A WITH PAVED SHOUL (MoRTH) (N24001929)	1-2022	10/2025 (N.A.) {10/2025}	697.66 (N.A.) {697.66}	318.74	93.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1539	BALANCE WORKS OF 4-LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 (NEW NH NO. 09) FROM KM. 0.000 (KM 1 (NHAI) (N24001992)	8-2022	2/2024 (5/2025) {5/2025}	199.31 (199.38) {199.38}	204.84	89.46
		1540	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER HIGHWAY FROM DESIGN CH.0.000 TO CH.49.200 OF NH- 731B ON (MoRTH) (N24001996)	3-2022	11/2025 (N.A.) {11/2025}	640.18 (602.76) {602.76}	468.29	77.00
		1541	CONSTRUCTION OF SHOHRATGARH BYPASS ON NH- 730 UNDER EPC MODE IN THE STATE OF UTTAR PRADESH (MoRTH) (N24001997)	10-2022	5/2025 (N.A.) {8/2025}	189.31 (N.A.) {189.31}	56.13	20.00
		1542	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 90.00 TO (MoRTH) (N24002015)	11-2021	6/2025 (N.A.) {6/2025}	403.36 (328.49) {403.36}	130.45	63.00
		1543	CONSTRUCTION OF PRATAPGARH BYPASS (EXTENSION) CONNECTING NH- 31 TO NH-330 (MoRTH) (N24002016)	10-2022	6/2025 (N.A.) {8/2025}	225.17 (N.A.) {225.17}	95.68	54.00
		1544	WIDENING TO FOUR LANE WITH PAVED SHOULDER FROM DESIGN KM.49.200 TO KM.89.285 OF NH-731B ON EPC MODE (MoRTH) (N24002029)	3-2022	1/2026 (N.A.) {1/2026}	917.91 (956.30) {917.91}	583.55	44.00
		1545	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM EXISTING KM.0.000 TO KM.55.610 (DESIGN KM. 0.000 T (MoRTH) (N24002031)	12-2021	2/2026 (N.A.) {2/2026}	840.93 (773.58) {840.93}	492.26	38.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1546	CONSTRUCTION OF 4-LANE HIGHWAY WITH PAVED SHOULDERS FROM KM 49.155 TO KM 74.700 OF NH-731A ON HYBRID (MoRTH) (N24002032)	1-2022	1/2026 (N.A.) {1/2026}	1,156.72 (N.A.) {1,156.72}	365.74	55.00
		1547	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM GOGWAN JALALPUR (SHAMLI DISTRICT) TO RANIPUR (NHAI) (N24002036)	4-2022	5/2025 (N.A.) {5/2025}	1,843.59 (N.A.) {1,843.59}	843.83	49.00
		1548	GARHMUKTESHWAR (KM. 83.200 OF NH-24) TO MEERUT (KM. 9.860 OF NH-235) INCLUDING CONNECTOR TO NH-119 (NHAI) (N24002073)	10-2019	10/2023 (N.A.) {6/2025}	2,068.99 (2,171.00) {2,171.00}	209.60	53.08
		1549	WIDENING OF RAEBARELI TO PRAYAGRAJ SECTION FROM KM. 82.650 TO KM. 161.450 OF NH-30 AND LINK ROAD FRO (NHAI) (N24002085)	11-2023	3/2025 (N.A.) {3/2025}	1,470.93 (N.A.) {1,470.93}	69.56	100.00
		1550	CONSTRUCTION OF FOUR LANE HIGHWAY FORM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002086)	10-2022	7/2025 (N.A.) {7/2025}	1,706.47 (N.A.) {1,706.47}	719.13	71.10
		1551	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002087)	10-2022	10/2025 (N.A.) {10/2025}	1,493.14 (N.A.) {1,493.14}	93.30	59.87
		1552	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002088)	10-2022	8/2025 (N.A.) {8/2025}	1,493.50 (N.A.) {1,493.50}	492.86	52.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1553	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER GREENFIELD SECTION OF N (NHAI) (N24002089)	10-2022	6/2025 (N.A.) {6/2025}	617.87 (N.A.) {617.88}	106.20	67.60
		1554	CONSTRUCTION OF FOUR-LANE ?WESTERN SIDE SPUR OF RAMPUR-RUDRAPUR SECTION CONNECTING NH-24 TO NH-87 BY (NHAI) (N24002090)	3-2021	11/2024 (8/2025) {8/2025}	646.27 (N.A.) {646.27}	69.11	42.88
		1555	IMPROVEMENT , UP-GRADATION OF NH-734 SECTION OF MORADABAD - THAKURDWARA - KASHIPUR: ?PACKAGE-I: MORA (NHAI) (N24002093)	10-2022	9/2025 (N.A.) {9/2025}	1,841.92 (N.A.) {1,841.92}	384.31	48.05
		1556	IMPROVEMENT AND UP- GRADATION OF EXISTING ROAD TO 4L PS FROM KM 123.650 TO 175.080, FROM START OF SHA (NHAI) (N24002094)	9-2022	11/2025 (N.A.) {11/2025}	1,212.26 (N.A.) {1,212.26}	329.52	29.08
		1557	FOUR LANING OF SONAULI GORAKHPUR SECTION OF NH 29E (NEW NH 24) FROM DESIGN CH. 0.000 TO DESIGN CH. 7 (NHAI) (N24002095)	12-2021	3/2025 (N.A.) {3/2025}	2,555.50 (N.A.) {2,555.50}	951.47	56.97
		1558	CONSTRUCTION OF 4 LANE GREEN FIELD NORTHERN EAST SIDE GORAKHPUR BYPASS (26.616 KMS) STARTING FROM NH (NHAI) (N24002096)	2-2023	1/2026 (N.A.) {1/2026}	1,973.98 (N.A.) {1,973.98}	736.14	46.76
		1559	STRENGTHENING OF EXISTING 4L AYODHYA BYPASS SECTION FROM DESIGN KM.121.600 TO KM. 144.020 OF NH 28 ((NHAI) (N24002097)	2-2023	9/2025 (N.A.) {8/2025}	526.45 (N.A.) {526.45}	228.37	83.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1560	CONSTRUCTION OF RING ROAD AROUND KANPUR FROM KM.000 TO KM. 23.325 (CHACHENDI SACHENDI I TO MAHARAJPU (NHAI) (N24002104)	1-2023	6/2026 (N.A.) {6/2026}	1,754.00 (N.A.) {1,754.00}	326.84	31.50
		1561	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS (PHASE-I) FROM DESIGN KM 43+200 (AT MAHUWARI VI (NHAI) (N24002105)	8-2023	6/2026 (N.A.) {6/2026}	1,378.36 (N.A.) {739.00}	192.88	25.10
		1562	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS FROM DESIGN KM 50.860 (NABABA URF NIBI KALA UPA (NHAI) (N24002106)	8-2023	3/2025 (N.A.) {6/2025}	993.77 (N.A.) {349.48}	354.88	90.20
		1563	CONSTRUCTION OF MARIAHU BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION (KM.53.540 TO KM.59.200) (MoRTH) (N24002115)	3-2023	8/2025 (N.A.) {2/2026}	438.24 (362.39) {438.24}	202.30	31.00
		1564	REHABILITATION AND UPGRADATION FROM KM 51.600 TO KM 75.700 OF NH-321G (NUHKHAS TO ETAH SECTION) TO T (MoRTH) (N24002116)	1-2022	8/2025 (N.A.) {8/2025}	343.54 (N.A.) {343.54}	66.01	34.00
		1565	CONSTRUCTION OF JASRA BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION FROM KM. 379.670 ON NH-76 ((MoRTH) (N24002120)	2-2023	9/2025 (N.A.) {9/2025}	274.06 (N.A.) {274.06}	122.34	84.00
		1566	IMPROVEMENT AND UP- GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM. 420.00 (MoRTH) (N24002121)	1-2022	9/2025 (N.A.) {2/2026}	509.65 (N.A.) {509.65}	174.67	21.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1567	REHABILITATION AND UP-GRADATION FROM KM. 0.000 TO KM. 40.390 OF NH-730S (MAHARAJGANJ ? NICHLOUL ? TH (MoRTH) (N24002134)	3-2023	12/2025 (N.A.) {12/2025}	809.25 (N.A.) {809.25}	243.96	25.00
		1568	CONSTRUCTION OF FOUR LANE HIGHWAY WITH PAVED SHOULDER FROM KM.74.700 TO KM.112.950 OF NH-731A (I/C Y (MoRTH) (N24002138)	3-2022	6/2026 (N.A.) {6/2026}	1,141.67 (N.A.) {1,141.67}	386.39	40.00
		1569	CONSTRUCTION OF BALRAMPUR BYPASS WITH 2L FLEXIBLE PAVEMENT CONFIGURATION FROM KM.223.000 OF NH-330 T (MoRTH) (N24002150)	12-2022	2/2026 (N.A.) {2/2026}	515.69 (N.A.) {515.69}	171.73	28.00
		1570	WIDENING TO 4L RIGID PAVEMENT CONFIGURATION FROM KM 90.00 TO KM 100.800 OF NH-96 (KM 42.0 TO KM 53.3 (MoRTH) (N24002199)	12-2022	11/2026 (N.A.) {11/2026}	309.63 (N.A.) {309.63}	6.79	15.00
		1571	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER/FOUR LANE CONFIGURATION FROM EXISTING K (MoRTH) (N24002201)	1-2022	5/2027 (N.A.) {5/2027}	974.19 (N.A.) {974.19}	586.49	6.00
		1572	REHABILITATION AND UPGRADATION TO FOUR LANE ROAD FROM KM 70.500 TO KM 78.600 OF NH-92 UNDER EPC MODE (MoRTH) (N24002211)	1-2022	1/2027 (N.A.) {1/2027}	296.02 (N.A.) {296.02}	27.68	-
		1573	WIDENING AND STRENGTHENING FROM DESIGN KM. 67.280 TO KM. 88.622 OF NH-727A (SALEMPUR-MAIRWA ROAD) TO (MoRTH) (N24002212)	3-2023	7/2026 (N.A.) {7/2026}	371.89 (N.A.) {371.89}	126.17	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1574	REHABILITATION and UP-GRADATION TO 2L+PS FROM KM. 0.0 TO KM. 7.80 AND KM. 35.400 TO KM. 52.345 (DESI (MoRTH) (N24002213)	3-2023	7/2026 (N.A.) {7/2026}	701.02 (N.A.) {701.02}	242.64	-
		1575	CONSTRUCTION OF AMETHI BYPASS (PART-II) AT KM.30.050 OF NH-931 UNDER EPC MODE IN THE STATE OF UTTAR (MoRTH) (N24002214)	12-2022	2/2027 (N.A.) {2/2027}	283.86 (N.A.) {283.86}	58.89	-
		1576	WIDENING TO 4L FROM KM.108.50 TO 139.00 OF NH-135A PKG-II (JAUNPUR TO AKBARPUR SECTION) ON HAM IN TH (MoRTH) (N24002234)	3-2023	3/2027 (N.A.) {3/2027}	1,511.57 (N.A.) {1,511.57}	124.06	-
		1577	CONSTRUCTION OF RAEBARELI RING ROAD (PHASE-2) WITH FOUR LANE CONFIGURATION FOR RAEBARELI CITY IN THE (MoRTH) (N24002235)	3-2022	5/2027 (N.A.) {5/2027}	1,273.72 (N.A.) {1,273.72}	330.12	-
	URBAN DEVELOPMENT	1578	KANPUR METRO RAIL PROJECT (LMRCL) (N28000144)	5-2019	3/2024 (N.A.) {12/2026}	11,076.48 (N.A.) {11,076.48}	8,651.58	72.00
		1579	AGRA METRO RAIL PROJECT (LMRCL) (N28000145)	5-2019	3/2024 (N.A.) {12/2026}	8,379.62 (N.A.) {8,379.62}	4,902.53	53.40
	WATER RESOURCES	1580	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH (UP JalNigam) (N30000021)	1-2019	12/2021 (1/2020) {3/2025}	231.79 (234.03) {234.03}	141.79	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1581	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH (UP JalNigam) (N30000024)	2-2019	6/2022 (N.A.) {12/2025}	681.78 (N.A.) {690.71}	13.34	22.00
UTTARAKHAND	CIVIL AVIATION	1582	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN (AAI) (N04000085)	7-2018	9/2020 (9/2024) {9/2024}	456.86 (500.00) {500.00}	483.86	100.00
	POWER	1583	TEHRI PUMPED STORAGE PLANT(1000MW) (THDCIL) (N18000010)	7-2006	7/2010 (6/2022) {9/2025}	1,657.00 (4,825.60) {7,877.81}	7,854.76	98.10
		1584	TAPOVAN-VISHNUGAD HEP (4X130MW) (NTPC) (N18000014)	11-2006	3/2013 (12/2021) {4/2029}	2,978.48 (N.A.) {10,907.00}	6,736.09	72.40
		1585	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT (THDCIL) (N18000042)	8-2008	6/2013 (N.A.) {3/2027}	2,491.58 (3,860.35) {6,630.60}	4,652.11	70.00
		1586	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW (NTPC) (N18000142)	7-2012	8/2017 (N.A.) {8/2017}	1,527.00 (N.A.) {1,527.00}	149.93	-
	RAILWAYS	1587	RISHIKESH - KARNAPRAYAG NEW LINE (RVNL) (N22000406)	4-2011	12/2025 (N.A.) {3/2025}	38,953.15 (N.A.) {24,659.00}	18,820.04	-
	ROAD TRANSPORT AND HIGHWAYS	1588	4-LANING OF KASHIPUR- SITARGANJ SECTION (AMR) (N24000465)	11-2012	8/2016 (N.A.) {8/2016}	605.84 (N.A.) {605.84}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1589	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 (NHIDCL) (N24000741)	3-2018	11/2020 (3/2024) {3/2024}	274.31 (N.A.) {274.31}	505.22	97.31
		1590	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI (NHIDCL) (N24000742)	3-2018	11/2020 (N.A.) {3/2024}	403.36 (N.A.) {403.36}	678.04	98.93
		1591	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA (NHIDCL) (N24000743)	3-2018	11/2020 (N.A.) {3/2024}	417.24 (N.A.) {417.24}	688.40	99.88
		1592	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000772)	12-2017	12/2019 (N.A.) {12/2019}	257.34 (N.A.) {257.34}	232.69	100.00
		1593	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000773)	12-2017	12/2019 (N.A.) {12/2019}	200.34 (253.43) {200.34}	227.98	100.00
		1594	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 (MoRTH) (N24000774)	12-2017	12/2019 (N.A.) {12/2019}	248.22 (N.A.) {248.22}	236.80	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1595	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000775)	6-2017	6/2019 (3/2023) {3/2023}	282.08 (N.A.) {282.08}	234.97	100.00
		1596	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG (MoRTH) (N24000776)	11-2017	11/2019 (N.A.) {11/2019}	232.81 (N.A.) {232.81}	201.58	100.00
		1597	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION (MoRTH) (N24000777)	11-2017	11/2019 (N.A.) {11/2019}	283.51 (N.A.) {283.51}	278.51	100.00
		1598	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000778)	11-2017	11/2019 (N.A.) {11/2019}	266.52 (N.A.) {266.52}	250.34	100.00
		1599	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR (MoRTH) (N24000779)	2-2018	2/2020 (3/2023) {3/2023}	418.88 (N.A.) {418.88}	339.71	94.00
		1600	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K (MoRTH) (N24000780)	2-2018	(4/2023) {4/2023}	293.68 (N.A.) {293.68}	244.25	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1601	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN (MoRTH) (N24000781)	5-2018	5/2020 (12/2023) {12/2023}	248.00 (N.A.) {248.00}	120.50	65.56
		1602	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 (MoRTH) (N24000782)	3-2018	(N.A.) { }	460.73 (N.A.) {461.00}	0.00	-
		1603	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) (NHIDCL) (N24000855)	3-2018	7/2022 (N.A.) {9/2026}	1,383.78 (N.A.) {1,383.78}	1,391.00	63.61
		1604	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER (MoRTH) (N24001130)	8-2016	12/2017 (N.A.) {12/2017}	234.88 (273.49) {234.88}	237.19	100.00
		1605	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR ? DEHRADUN SECTION FROM KM. (NHAI) (N24001525)	3-2021	3/2024 (5/2025) {5/2025}	169.08 (N.A.) {169.08}	105.77	99.99
		1606	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF (NHAI) (N24001526)	8-2021	10/2024 (8/2025) {8/2025}	1,377.79 (1,384.11) {1,377.79}	679.10	53.05
		1607	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) (NHAI) (N24001553)	3-2022	2/2025 (7/2025) {7/2025}	1,092.90 (1,092.90) {1,092.90}	463.92	81.20

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1608	4L POANTA SAHEB?MEDNIPUR FROM KM. 435.65 TO KM. 458.65 OF NH-07(PKG-1) (NHAI) (N24001990)	6-2022	5/2025 (6/2025) {6/2025}	524.54 (683.26) {683.26}	91.94	73.37
		1609	ACCESS ROAD/BRIDGE CONNECTIVITY FROM NH-09 AT KM.40 NEAR JAGBUDA BRIDGE (INDIA) TO BOUNDARY PILLAR (NHAI) (N24001991)	5-2022	9/2024 (11/2026) {11/2026}	314.31 (N.A.) {314.31}	229.70	68.16
		1610	CONSTRUCTION FOR MITIGATION MEASURES KM 368.00-UTTARAKHAND-TO KM 433.00 ON NH-07-PKG-1 (NHIDCL) (N24002163)	12-2023	12/2025 (N.A.) {12/2025}	216.88 (N.A.) {216.88}	76.07	73.00
		1611	CONSTRUCTION FOR MITIGATION MEASURES KM 450.00-UTTARAKHAND-TO KM 468.00 ON NH-07-PKG-3 (NHIDCL) (N24002164)	12-2023	12/2025 (N.A.) {12/2025}	250.33 (N.A.) {250.33}	57.10	48.00
		1612	CONSTRUCTION FOR MITIGATION MEASURES PKG-2 (NHIDCL) (N24002206)	12-2023	6/2026 (N.A.) {6/2026}	259.64 (N.A.) {259.64}	4.16	20.00
WEST BENGAL	CIVIL AVIATION	1613	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA (AAI) (N04000080)	1-2016	3/2020 (12/2023) {12/2023}	458.00 (N.A.) {458.00}	251.64	100.00
		1614	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA (AAI) (N04000081)	1-2019	11/2021 (5/2023) {5/2023}	389.71 (N.A.) {397.00}	396.61	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1615	NSCBI AIRPORT KOLKATA: RE- CONSTRUCTION OF RIGID POSITIONS OF SECONDARY RUNWAY, 'K' AND 'A' TAXIWAY (AAI) (N04000109)	4-2023	10/2025 (N.A.) {10/2025}	328.30 (N.A.) {328.30}	79.39	36.00
		1616	BAGDOGRA AIRPORT: DEVELOPMENT OF NEW CIVIL ENCLAVE AT BAGDOGRA AIRPORT. SUB-HEAD : CONSTRUCTION OF N (AAI) (N04000115)	8-2024	3/2027 (N.A.) {3/2027}	1,549.00 (N.A.) {1,549.00}	181.32	8.00
	COAL	1617	RANIGANJ MASTER PLAN (ECL) (N06000163)	8-2009	8/2019 (N.A.) {8/2019}	2,661.73 (N.A.) {5,146.48}	779.50	42.00
		1618	SIDULI MINE (OC AND UG) (ECL) (N06000165)	5-2018	3/2027 (N.A.) {3/2027}	535.18 (N.A.) {535.17}	4.75	14.00
		1619	NAKRAKONDA KUMARDIH B OCP (ECL) (N06000170)	8-2018	3/2029 (N.A.) {3/2029}	502.68 (N.A.) {502.67}	70.02	25.50
		1620	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT (ECL) (N06000191)	4-2020	3/2026 (3/2026) {3/2026}	483.65 (N.A.) {483.65}	54.87	12.00
		1621	2.0 MTPA BHOJUDIH NLW WASHERY (BCCL) (N06000195)	12-2015	9/2020 (N.A.) {5/2025}	384.57 (N.A.) {384.57}	347.98	97.00
		1622	SONEPUR BAZARI EXPANSION OC (ECL) (N06000220)	7-2021	3/2029 (N.A.) {3/2029}	5,365.88 (5,366.00) {5,365.88}	550.61	17.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1623	EXPANSION PR OF JHANJRA UG (5.00 MTY) (ECL) (N06000223)	4-2020	3/2029 (N.A.) {3/2029}	1,210.12 (N.A.) {1,210.12}	478.77	38.00
		1624	MOHANPUR EXPANSION OC PHASE II (ECL) (N06000236)	11-2020	3/2026 (N.A.) {3/2026}	888.99 (N.A.) {888.99}	73.31	30.00
		1625	BONJEMEHARI EXPANSION OCP (ECL) (N06000244)	8-2021	3/2026 (3/2026) {3/2026}	570.12 (N.A.) {570.11}	81.09	16.00
		1626	ITAPARA OC (ECL) (N06000272)	12-2023	3/2030 (N.A.) {3/2030}	929.10 (N.A.) {929.10}	63.74	7.00
		1627	UCE OF TILABONI UG (ECL) (N06000276)	1-2023	3/2029 (N.A.) {3/2029}	749.07 (N.A.) {749.07}	51.59	10.00
		1628	UCE OF PARASEA BELBAID REORGANISATION UG (ECL) (N06000277)	1-2023	3/2029 (3/2028) {3/2028}	389.10 (N.A.) {389.10}	130.56	16.00
		1629	PARASCOLE JAMBAD OCP (ECL) (N06000281)	11-2024	3/2037 (N.A.) {3/2037}	1,193.55 (N.A.) {1,193.55}	0.00	-
	DEPARTMENT OF HIGHER EDUCATION	1630	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED (CPWD EDUCATION) (N28000146)	3-2020	6/2020 (N.A.) {5/2024}	193.83 (N.A.) {193.83}	207.35	-
	HOME AFFAIRS	1631	NSG AT KOLKATA (CPWD FOR MHA) (N28000104)	10-2014	4/2018 (N.A.) {8/2025}	162.88 (210.83) {210.83}	193.91	92.50

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>MINES</u>	1632	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA (CPWD) (N10000015)	4-2019	4/2022 (N.A.) {8/2026}	255.37 (N.A.) {255.37}	68.66	36.00
	<u>PETROLEUM</u>	1633	DURGAPUR-HALDIA PIPELINE PROJECT (GAIL) (N16000275)	3-2017	12/2020 (12/2025) {12/2025}	1,740.00 (2,433.15) {2,433.15}	2,182.20	89.50
		1634	CITY GAS DISTRIBUTION IN WEST BENGAL (HPCL) (N16000392)	3-2019	3/2031 (3/2031) {3/2031}	5,830.20 (N.A.) {5,830.20}	875.27	32.52
		1635	HALDIA PANAGARH PIPELINE PROJECT (HPCL) (N16000478)	11-2022	11/2025 (N.A.) {11/2025}	1,010.00 (N.A.) {1,010.00}	526.55	76.78
		1636	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS (IOCL) (N16000491)	3-2022	3/2030 (N.A.) {6/2031}	609.00 (N.A.) {609.00}	60.43	2.10
		1637	CGD PROJECT IN WEST BENGAL 11TH ROUND (HPCL) (N16000498)	6-2022	6/2030 (N.A.) {6/2030}	2,628.00 (N.A.) {2,628.00}	308.32	21.70
		1638	CITY GAS DISTRIBUTION PROJECTS AT ALIPURDUAR AND COOCH BEHAR (BPCL) (N16000522)	12-2022	3/2030 (N.A.) {3/2030}	1,017.00 (N.A.) {1,017.00}	158.78	29.80
	<u>POWER</u>	1639	RAMMAM-III HEPP (3X40 MW) (NTPC) (N18000178)	9-2014	9/2019 (12/2024) {3/2029}	1,381.84 (N.A.) {1,803.00}	1,302.76	43.68

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	1640	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER (ER) (220100272)	4-2000	3/2019 (2/2026) {2/2026}	1,188.91 (N.A.) {2,582.49}	1,247.41	75.00
		1641	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA- BARASAI VIA BIMANBANDER (MTP) (KOMRCL) (N22000108)	4-2010	8/2026 (N.A.) {3/2016}	4,829.60 (N.A.) {2,397.72}	197.20	17.00
		1642	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) (RVNL) (N22000109)	4-2010	12/2026 (N.A.) {12/2025}	2,298.42 (N.A.) {2,733.86}	392.98	-
		1643	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) (RVNL) (N22000110)	4-2010	12/2025 (N.A.) {3/2026}	8,964.35 (N.A.) {8,964.35}	7,387.40	-
		1644	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. (RVNL) (N22000111)	4-2010	12/2026 (N.A.) {12/2026}	4,834.54 (N.A.) {4,834.54}	3,918.86	-
		1645	PURULIA TO KOTSHILA DOUBLING (39.1 KM) (SER) (N22000510)	4-2018	12/2024 (N.A.) {3/2025}	393.83 (N.A.) {393.83}	302.80	100.00
		1646	AZIMGANJ-MURSHIDABAD (JIYAGANJ) INCL. RLY. BRIDGE OVER RIVER BHAGIRATHI (ER) (N22000609)	10-2001	2/2024 (N.A.) {2/2024}	164.33 (N.A.) {187.05}	160.82	100.00

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1647	NAHATI - RANAGHAT 3RD LINE (MM OF KALINARAYANPUR - KRISHNANAGAR) (ER) (N22000624)	7-2015	3/2025 (N.A.) {3/2025}	1,000.00 (N.A.) {283.54}	165.74	44.00
		1648	EAST WEST METRO CORRIDOR KOLKATA (KOMRCL) (N22000628)	2-2009	9/2016 (N.A.) {9/2016}	4,874.58 (8,575.00) {10,442.41}	0.00	-
		1649	KALIPAHARI - BAKHTARNAGAR 5TH LINE (17.61 KM) (ER) (N22000630)	4-2024	6/2027 (N.A.) {6/2027}	350.46 (N.A.) {350.46}	0.00	-
		1650	SITARAMPUR BYE - PASS LINE (6.59 KM) (ER) (N22000631)	2-2023	3/2027 (N.A.) {3/2027}	461.64 (N.A.) {461.64}	24.54	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1651	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) (NHAI) (N24000463)	12-2015	6/2018 (5/2024) {8/2023}	1,083.00 (1,414.01) {1,414.01}	1,080.05	100.00
		1652	SIX-LANING OF BARWA ADDA- PANAGARH (NHAI) (N24000515)	4-2014	9/2016 (N.A.) {3/2025}	1,665.00 (N.A.) {4,972.99}	4,972.99	100.00
		1653	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU (NHAI) (N24000788)	3-2018	9/2022 (12/2022) {12/2025}	841.57 (708.30) {708.30}	11,121.30	95.78
		1654	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H (MoRTH) (N24000874)	3-2016	11/2018 (12/2023) {7/2025}	271.17 (291.20) {291.20}	199.72	82.34

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1655	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. (MoRTH) (N24000880)	2-2018	9/2020 (1/2024) {2/2025}	426.18 (426.18) {426.18}	364.92	100.00
		1656	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 (NHAI) (N24001747)	3-2020	9/2024 (N.A.) {9/2024}	2,193.23 (2,314.00) {2,314.00}	2,085.00	97.50
		1657	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA (NHAI) (N24001748)	3-2021	9/2024 (N.A.) {9/2025}	2,200.93 (N.A.) {2,621.41}	2,621.41	96.83
		1658	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE (NHAI) (N24001749)	8-2021	8/2023 (N.A.) {6/2025}	557.55 (N.A.) {567.31}	473.25	91.41
		1659	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA (NHAI) (N24001750)	8-2018	12/2021 (N.A.) {7/2025}	622.04 (N.A.) {622.04}	565.40	91.34
		1660	DEVELOPMENT TO 4/6-LANNING OF NH-31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 (MoRTH) (N24001850)	3-2022	9/2025 (9/2025) {9/2025}	995.04 (995.04) {995.04}	383.34	47.90
		1661	CONSTRUCTION OR 4 LANE RANIGANJ BYPASS OF LENGTH 5 261 KM ON NH 60 NEW NH 14 FROM KM 273 00 OF NH (MoRTH) (N24002184)	3-2023	3/2026 (3/2026) {3/2026}	410.83 (N.A.) {410.83}	152.32	28.99

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1662	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF LEVEL CROSSING NO 10 B T AT KM 307 050 OF NH 60 B (MoRTH) (N24002191)	3-2016	8/2025 (N.A.) {8/2025}	155.87 (N.A.) {155.87}	21.68	9.49
	STEEL	1663	REBUILDING OF COKE OVEN BATTERY NO.4 OF DURGAPUR STEEL PLANT (SAIL) (N12000132)	11-2023	12/2026 (N.A.) {12/2026}	916.78 (N.A.) {916.78}	86.34	4.85
		1664	INSTALLATION OF NEW BAR MILL AT DURGAPUR STEEL PLANT (SAIL) (N12000138)	9-2024	6/2027 (N.A.) {6/2027}	2,115.44 (N.A.) {2,115.44}	61.67	4.50
		1665	UP-GRADATION OF BLAST FURNACE NO. 3 AT DURGAPUR STEEL PLANT (SAIL) (N12000139)	9-2024	6/2026 (N.A.) {6/2026}	758.09 (N.A.) {758.09}	0.00	1.80
		1666	REVAMPING OF AIR POLLUTION CONTROL SYSTEMS OF SP-1 AT DURGAPUR STEEL PLANT (SAIL) (N12000140)	11-2024	5/2026 (N.A.) {5/2026}	196.40 (N.A.) {196.40}	0.19	0.80
		1667	THIRD LADLE FURNACE IN SECONDARY REFINERY UNIT AT IISCO STEEL PLANT (SAIL) (N12000141)	11-2024	7/2026 (N.A.) {7/2026}	227.96 (N.A.) {227.96}	2.58	18.98
	WATER RESOURCES	1668	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA (KMDA) (N30000032)	5-2018	2/2022 (N.A.) {8/2025}	198.43 (224.69) {286.97}	75.88	95.00
		1669	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA (KMDA) (N30000034)	8-2017	9/2022 (1/2023) {12/2026}	307.12 (N.A.) {653.67}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th April 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1670	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY- CHINSURAH (KMDA) (N30000042)	5-2018	2/2022 (9/2020) {3/2025}	160.00 (154.73) {154.73}	87.35	90.00
			Total			2,793,673.76 (894,145.91) {3,104,364.43}	16,81,479.95	

Abbreviations used in the Report

AGENCY_NAME	AGENCY_NAME_SHORT
AIRPORT AUTHORITY OF INDIA LIMITED	AAI
ARTIFICIAL LIMBS MANUFACTURING CORPM. OF INDIA	ALIMCO
BHARAT ALUMINUM CORPORATION	BALCO
BHABHA ATOMIC RESEARCH CENTRE	BARC
BHARAT COKING COAL LIMITED	BCCL
BRAHMAPUTRA CRECKER & POLYMER LTD.	BCPL
BHAVINI LIMITED	BHAVNI
BHARAT HEAVY ELECTRICALS LIMITED	BHEL
BANGALORE METRO RAIL CORPORATION LIMITED	BMRCL
BOKARO STEEL PLANT	BOKARO STEEL PL
BRAHMAPUTRA BOARD	BPB
BHARAT PETROLEUM CORPORATION LIMITED	BPCL
BORDER ROAD ORGANISATION	BRO
BONGAIGAON REFINERY PETROLEUM LIMITED	BRPL
BHARAT SANCHAR NIGAM LIMITED	BSNL
Bihar Urban Infrastructure Development Corporation Ltd	BUIDCO
BRAHMAPUTRA VALLY FERTILISER CORPORATION	BVFC
CENTRE FOR DEVELOPMENT OF TELEMATICS, TELECOM, TECHNOLOGY	C-DOT
CENTRAL COAL FIELDS LIMITED	CCL
CONTAINER CORPORATION OF INDIA	CCOI
CHENAB VALLEY POWER CORPORATION LIMITED	CHENAB VALLEY P
CHENNAI METRO RAIL LTD	CMRL
CHENNAI PETROLEUM CORPORATION LIMITED	CPCL
CENTRAL PUBLIC WORKS DEPARTMENT	CPWD
CPWD OF HIGHER EDUCATION	CPWD EDUCATION
CPWD FOR DEFENCE	CPWD FOR DEFENC
CPWD FOR FINANCE	CPWD FOR FINANC
CPWD FOR HEALTH	CPWD FOR HEALTH
CPWD FOR MHA	CPWD FOR MHA
CPWD FOR POWER	CPWD FOR POWER
CPWD FOR RURAL	CPWD FOR RURAL
CPWD FOR TELECOM	CPWD FOR TELECO
CPWD FOR RENEWABLE ENERGY	CPWD R ENERGY
CENTRAL RAILWAYS	CR
COCHIN REFINERY LIMITED	CRL
COCHIN SHIPYARD LTD	CSL
CHENAB VELLEY POWER PROJECTS [P] LIMITED	CVPPPL
DUMMY AGENCY	DA
DEDICATED FREIGHT CORRIDOR CORPORATION OF INDIA LTD	DFCC
DIRECTORATE GENERAL OF CIVIL AVIATION	DGCA
Delhi Jal Board	DJB
Delhi Mumbai Industrial Corridor	DMIC
DMIC FOR DPIIT	DMIC FOR DPIIT
DELHI METRO RAIL CORPORATION	DMRC
DEPARTMENT OF TELECOMMUNICATION	DOT
Department for Promotion of Industry and Internal Trade	DPIIT
DAMODAR VALLEY CORPORATION	DVC
EASTERN COAL FIELDS LIMITED	ECL
EAST COAST RAILWAY	ECOR
EAST CENTRAL RAILWAYS	ECR

AGENCY_NAME	AGENCY_NAME_SHORT
EDCIL(India) Limited	EDCIL
ENNORE PORT LTD.	ENNORE PORT LTD
ENNORE TANK TERMINAL PVT.LTD.	ENNORE TANK
EASTERN RAILWAYS	ER
FERTILISER AND CHEMICAL TRIVANCORE	FACT
FREIGHT OPERATION INFORMATION SYSTEM	FOIS
SETTING UP FILM AND TELEVISION INSTITUTE	FTI
GAS AUTHORITY OF INDIA LIMITED	GAIL
GOA SHIPYARD LIMITED	GSL
HEALTH & FAMILY WELFARE	H&FW
HINDUSTAN AERONAUTICS LTD	HAL
HINDUSTAN COPPER LIMITED	HCL
HALDIA FERTILISER CORPORATION	HFC
HLL Infra Tech Services Limited	HITES
HYDERABAD METRO RAIL LTD	HMRL
HINDUSTAN PETROLEUM CORPORATION LIMITED	HPCL
HPCL Rajasthan Refinery Limited(JV)	HPCLRRL(JV)
HPOIL Gas Pvt. Ltd	HPOIL(JV)
HOSPITAL SERVICES CONSULTANCY CORPORATION LTD	HSCC
HINDUSTAN STEELWORK CONSTRUCTION LIMITED	HSCL
HINDUSTHAN STEELWORKS CONSTRUCTION LIMITED	HSCL
HSCL FOR DONER	HSCL FOR DONER
HSCL FOR RURAL	HSCL FOR RURAL
HSCL FOR WATER	HSCL FOR WATER
INDIAN FARMERS FERTILISER CORPORATION	IFFCO
INDIRA GANDHI CENTRE FOR ATOMIC RESEARCH	IGCAR
INDRADHANUSH GAS GRID LTD	IGGL
India International Convention and Expo Centre	IICC
IICC FOR DPIIT	IICC FOR DPIIT
INDIAN IRON STEEL COMPANY	IISCO
Indian Institute of Technology, Kharagpur	IITKGP
INDIAN OIL CORPORATION LIMITED	IOCL
INDIAN PETRO-CHEMICAL CORPORATION LIMITED	IPCL
Indian Railway Construction Company Limited	IRCON
INDIAN STRATEGIC PETROLEUM RESERVES LTD	ISPRL
INDIAN TELEPHONE INDUSTRY	ITI
Inland Waterways Authority of India	IWAI
INLAND WATER TRANSPORT	IWT
JAWAHAR LAL NEHRU NATIONAL URBAN RENEWAL MISSION	JNNURM
JWAAHARLAL NEHRU PORT TRUST	JNPT
Jharkhand Urban Infrastructure Development Company Ltd	JUIDCO
Kolkata Metropolitan Development Authority	KMDA
KOCHI METRO RAIL CORPORATION LTD	KMRCL
KOLKATA METRO RAIL CORPORATION LIMITED	KOMRCL
KAMARAJAR PORT LIMITED	KPL
KONKAN RAILWAY	KR
Rail Infrastructure Development Company	KRIDE
KOCHI REFINERIES LIMITED	KRL
Kochi Salem Pipeline Private Limited(JV)	KSPPL(JV)
LINE DOUBLING	LD
LUCKNOW METRO RAIL CORPORATION LIMITED	LMRCL
MANGALORE REFINERY AND PETROCHEMICALS LIMITED	MANGALORE REFIN

AGENCY_NAME	AGENCY_NAME_SHORT
MAHANADI COAL FIELDS LIMITED	MCL
MECON LIMITED	MECON LIMITED
AHMEDABAD METRO RAIL	MEGA
MADRAS FERTILISER LIMITED	MFL
Munitions India Limited	MIL
MAHARASTRA METRO RAIL CORPORATION LTD.	MMRC
MUMBAI METRO RAIL CORPORATION LTD	MMRCL
MINISTRY OF WATER RESOURCES	MOWR
Madhya Pradesh Metro Rail Co Limited	MPMRCL
Maharashtra Rail Infrastructure Development Corporation Limited	MRIDC
MANGALORE REFINARY LIMITED	MRL
METROPOLITAN RAPID TRANSPORT PROJECTS	MRTP
Mumbai Railway Vikas Corporation	MRVC
MAHANAGAR TELEPHONE NIGAM LIMITED	MTNL
MUMBAI PORT TRUST	MUMBAI PORT TRU
Armoured Vehicles Nigam Limited	MVNL
MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)	MoRTH
NATIONAL ALUMINUM COMPANY LIMITED (NALCO)	NALCO
NATRIIP IMPLEMENTATION SOCIETY	NATIS
NATIONAL BUILDING CONSTRUCTION CORPORATION LTD	NBCC
NBCC FOR COMMERCE	NBCC FOR COMMER
NBCC FOR HEALTH	NBCC FOR HEALTH
NORTHERN COAL FIELDS LIMITED	NCL
NORTH CENTRAL RAILWAY	NCR
NATIONAL CAPITAL REGION TRANSPORT CORP	NCRTC
NATIONAL CENTRE OF EXCELLENCE	NCoE
NORTH EAST ELECTRIC POWER CORPORATION	NEEPCO
NORTH EAST GAS GRID	NEGG
NORTH EASTERN RAILWAY	NER
National Film Archive of India	NFAI
NUCLEAR FUEL CORPORATION	NFC
NATIONAL FERTILISER LIMITED	NFL
NORTH EAST FRONTIER RAILWAY	NFR
NATIONAL HIGHWAYS AUTHORITY OF INDIA	NHAI
NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.	NHIDCL
NATIONAL HYDRO-ELECTRIC POWER CORPORATION	NHPC
National High Speed Rail Corporation Limited	NHSRCL
NEW LINE	NL
NEYVELI LIGNITE CORPORATION	NLC
NATIONAL MISSION FOR CLEAN GANGA	NMCG
NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)	NMDC
NAGPUR METRO RAIL CORPORATION LTD	NMRCL
NATIONAL PROJECTS CONSTRUCTION CORPORATION LIMITED	NPCC
NUCLEAR POWER CORPORATION OF INDIA LIMITED	NPCIL
NORTHERN RAILWAY	NR
NUMALIGARH REFINERY LIMITED	NRL
SETTING UP OF NEW RAILWAY ZONES	NRZ
NATIONAL THERMAL POWER CORPORATION	NTPC
NORTH WESTERN RAILWAY	NWR
OIL INDIA LIMITED	OIL
OIL & NATURAL GAS CORPORATION LIMITED	ONGC
PATNA METRO RAIL CORPORATION	PATNA METRO RAI

AGENCY_NAME	AGENCY_NAME_SHORT
PAWAN HANS HELICOPTERTERS LTD.	PAWAN HANS HELI
POWER GRID CORPORATION OF INDIA LIMITED	PGCIL
PORT TRUST	PORT TRUST
Polavaram Project Authority	PPA
RASHTRIYA CHEMICAL & FERTILISER LIMITED	RCF
RAILWAY ELECTRIFICATION	RE
RASTRIYA ISPAT NIGAM LIMITED	RINL
RAIL INDIA TECHNICAL AND ECONOMIC SERVICE	MITES
MITES OF HIGHER EDUCATION	MITES OF HIGHER
RAIL VIKAS NIGAM LTD.	RVNL
SIGNALLING & TELECOMMUNICATIONS	S&T
STEEL AUTHORITY OF INDIA LIMITED (SAIL)	SAIL
SINGARENI COLLIERS COMPANY LIMITED	SCCL
SOUTH CENTRAL RAILWAY	SCR
SOUTH-EASTERN COAL FIELDS LIMITED	SECL
SOUTH EAST CENTRAL RAILWAY	SECR
SOUTH EASTERN RAILWAY	SER
SER(GC) GAUGE CONVERSION	SER(GC
SHIPPING CRP. OF INDIA	SHIPP.
SATLUJ JAL VIDYUT NIGAM LIMITED	SJVN
SOUTHERN RAILWAY	SR
SOUTH WESTERN RAILWAY	SWR
Sikkim University	Sikkim Universi
THDC INDIA LIMITED	THDCIL
TUTICORIN PORT TRUST	TUTICORIN
URANIUM CORPORATION OF INDIA LIMITED	UCIL
URBAN DEVELOPMENT	UD
Uttarakhand Pey Jal Nigam	UKJalNigam
Uttar Pradesh Jal Nigam	UPJalNigam
VISAKHAPATNAM PORT TRUST	VPT
Varanasi Smart City	Varanasi Smart
WAPCOS	WAPCOS
WESTERN COAL FIELDS LIMITED	WCL
WEST CENTRAL RAILWAY	WCR
WESTERN RAILWAY	WR
WORKSHOPS & PRODUCTION UNIT	WS&PU



Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
