



सत्यमेव जयते



OCMS

Ministry of Statistics & Programme Implementation


Government of India
Ministry of Statistics and Programme Implementation

475th — *Flash Report on* **Central Sector Infrastructure** **Projects** —



(Rs. 150 crore & above)

May 2025











CONTENTS

Synopsis	1-2
List of Tables	3-203
Table:-1. Overview of Ongoing Projects: Sector-wise Distribution.....	3-4
Table:-2. Overview of Ongoing Projects: State-wise Distribution.....	5-6
Table:-3. Project List: Completed during May 2025.....	7-11
Table:-4. Project List: Added during May 2025.....	12-13
Table:-5. Project List: Frozen/Deleted during May 2025.....	14-14
Table:-6. Project List: Ongoing Projects of North-East Region.....	15-38
Table:-7. Project List: Ongoing Projects as of 31st May 2025.....	39-203




SYNOPSIS

Flash Report - Central Sector Infrastructure Projects Costing Rs. 150 crore & above

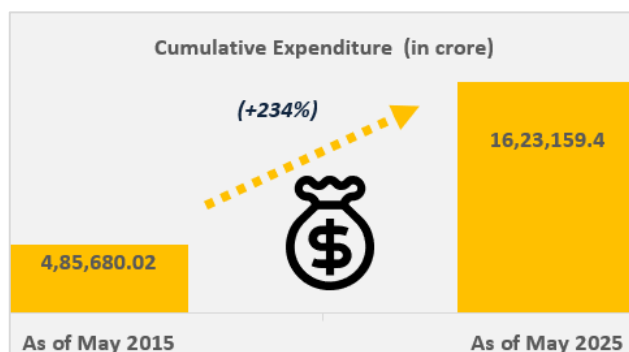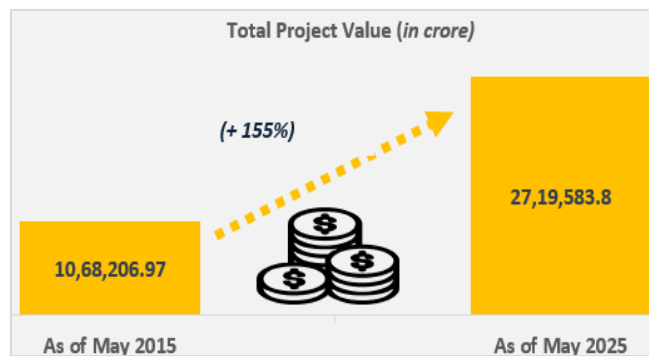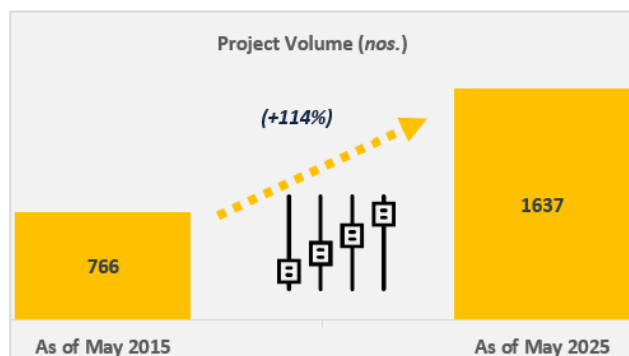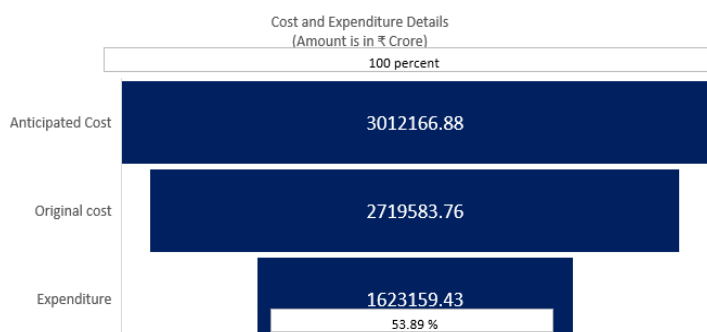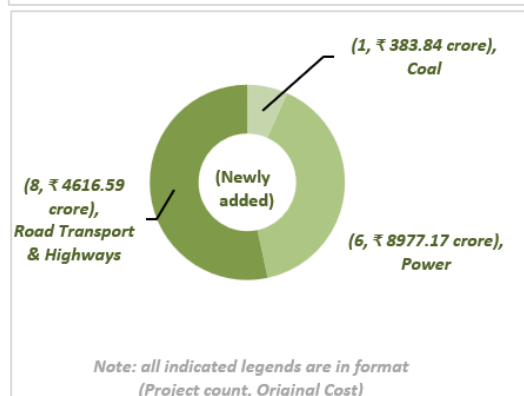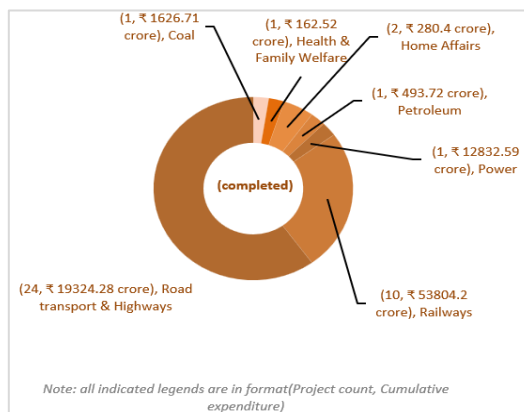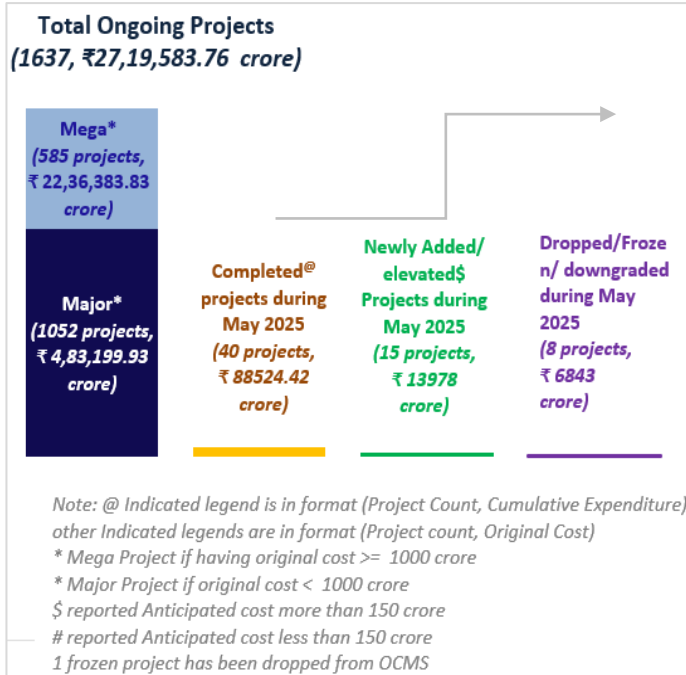


Sectoral Comparison : Major Sectors (as per count)
[Outer Ring: Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

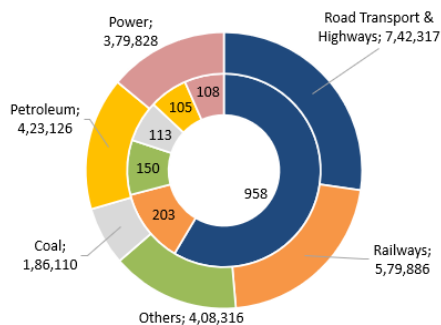


*Others include Water Resources, Civil Aviation, Urban Development, Department of Higher Education, Steel, Health & Family welfare, Mines, Telecommunications, Home Affairs, Finance, DPIIT, Shipping & Ports, and Social Justice

State Comparison : Major States (as per count)
[Outer Ring: Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

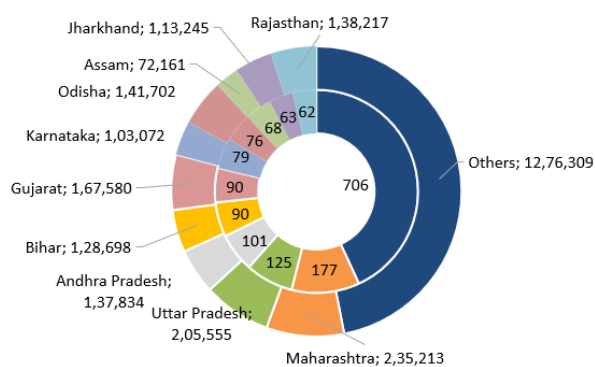

*Others include Tamilnadu, Madhya Pradesh, Delhi, Chhattisgarh, Haryana, Jammu & Kashmir, West Bengal, Kerala, Arunachal Pradesh, Punjab, Telangana, Uttarakhand, Himachal Pradesh, Manipur, Sikkim, Nagaland, Mizoram, Meghalaya, Tripura, Goa, A&N Island, Ladakh and Multistate

Sectoral Distribution of total 672 projects with reported Physical Progress between 80-100%

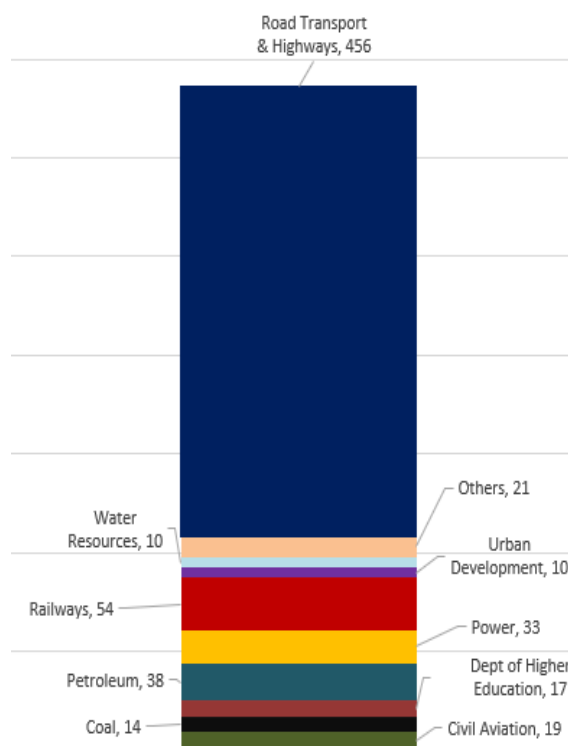

Note: This report is as of May 2025, based on the (non-exhaustive) list of projects and information as reported by Line Ministries/ implementing agencies on the OCMS (www.cspm.gov.in) portal latest by 8th June 2025.

LIST OF TABLES

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	CIVIL AVIATION	38	26,718.18 (27,878.25) {30,473.90}	17,738.02
2	COAL	113	186,109.83 (190,653.87) {195,483.12}	66,730.38
3	DEPARTMENT OF HIGHER EDUCATION	20	9,680.92 (10,152.14) {10,271.25}	7,192.52
4	DPIIT	2	24,857.00 (31,457.00) {32,085.00}	16,231.95
5	FINANCE	2	577.27 (577.27) {569.04}	399.67
6	HEALTH AND FAMILY WELFARE	7	7,150.98 (7,459.11) {7,194.19}	4,900.15
7	HOME AFFAIRS	3	1,663.54 (2,539.11) {2,539.11}	2,193.78
8	MINES	8	7,559.78 (9,356.73) {9,845.57}	6,034.59
9	PETROLEUM	105	423,126.00 (474,335.56) {484,488.77}	2,44,464.96
10	POWER	108	379,828.26 (403,113.29) {457,814.84}	2,23,684.20
11	RAILWAYS	203	579,886.47 (569,688.23) {599,321.52}	3,97,884.96
12	ROAD TRANSPORT AND HIGHWAYS	958	742,316.73 (770,508.11) {781,211.20}	3,87,038.64
13	SHIPPING AND PORTS	1	5,369.18 (5,061.15) {5,061.15}	3,441.55
14	SOCIAL JUSTICE	1	170.99 (170.99) {170.99}	73.80
15	STEEL	20	16,297.20 (20,228.73) {20,228.73}	7,838.89
16	TELECOMMUNICATIONS	6	26,961.69 (26,949.89) {26,949.89}	9,650.92
17	URBAN DEVELOPMENT	27	265,881.46 (272,720.33) {286,578.30}	2,00,218.70

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
18	WATER RESOURCES	15	15,428.28 (15,429.03) {61,880.31}	27,441.75
	Total	1637	2,719,583.76 (2,838,278.79) {3,012,166.88}	16,23,159.43

*Either Revised or Original Cost

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	ANDAMAN AND NICOBAR ISLANDS	10	2,956.02 (3,029.18) {3,010.04}	1,826.00
2	ANDHRA PRADESH	101	137,833.86 (138,333.19) {186,185.06}	99,775.15
3	ARUNACHAL PRADESH	14	45,061.06 (45,210.96) {64,937.64}	30,118.63
4	ASSAM	68	72,160.68 (72,644.55) {80,137.49}	50,194.44
5	BIHAR	90	128,697.89 (141,442.84) {153,398.13}	96,957.04
6	CHHATTISGARH	50	75,244.87 (79,134.30) {79,609.36}	35,044.70
7	DELHI	21	90,609.18 (96,063.03) {94,869.54}	76,426.03
8	GOA	3	1,201.05 (1,201.05) {1,287.55}	479.89
9	GUJARAT	90	167,579.54 (173,666.23) {174,375.70}	86,950.93
10	HARYANA	24	60,500.88 (69,284.79) {69,434.48}	34,812.67
11	HIMACHAL PRADESH	28	34,458.32 (35,488.00) {34,472.16}	18,362.46
12	JAMMU AND KASHMIR	53	73,422.59 (74,733.70) {81,014.68}	36,996.50
13	JHARKHAND	63	113,244.62 (117,005.23) {116,157.04}	64,794.39
14	KARNATAKA	79	103,071.74 (104,310.55) {103,281.26}	48,548.52
15	KERALA	31	63,956.46 (69,579.05) {70,159.90}	36,274.03
16	LADAKH	6	2,474.97 (2,634.64) {2,634.64}	1,336.77
17	MADHYA PRADESH	55	111,980.58 (111,381.98) {118,179.99}	39,850.90

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
18	MAHARASHTRA	177	235,212.75 (239,003.84) {263,997.81}	1,39,123.44
19	MANIPUR	33	25,919.61 (23,907.05) {33,831.42}	19,613.61
20	MEGHALAYA	15	6,827.06 (6,818.08) {6,837.26}	3,427.30
21	MIZORAM	17	14,519.38 (13,013.38) {18,688.72}	15,940.70
22	MULTI STATE	50	331,866.08 (337,419.07) {350,641.22}	2,48,890.31
23	NAGALAND	25	13,894.53 (15,243.21) {14,942.18}	8,322.44
24	ODISHA	76	141,702.20 (143,692.35) {146,380.41}	64,716.85
25	PUNJAB	37	37,339.85 (37,800.41) {38,239.81}	14,582.90
26	RAJASTHAN	62	138,216.71 (168,368.04) {167,962.23}	91,585.48
27	SIKKIM	20	20,540.04 (25,022.71) {25,866.28}	18,480.28
28	TAMIL NADU	61	88,967.98 (94,410.41) {99,894.68}	24,829.27
29	TELANGANA	52	29,124.48 (29,461.83) {31,449.35}	14,511.12
30	TRIPURA	14	7,910.17 (7,947.06) {8,032.54}	1,291.48
31	UTTAR PRADESH	125	205,554.60 (213,896.31) {217,968.91}	1,06,018.10
32	UTTARAKHAND	31	58,781.06 (63,618.31) {63,170.51}	44,929.76
33	WEST BENGAL	56	78,752.95 (83,513.46) {91,118.89}	48,147.34
	Total	1637	2,719,583.76 (2,838,278.79) {3,012,166.88}	16,23,159.43

*Either Revised or Original Cost

Table:-3. Project List: Completed during May 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
COAL					
	1	TALABIRA II AND III OCP (NLC) (N06000189) (ODISHA)	2,401.07	01/2027	1,626.71
HEALTH AND FAMILY WELFARE					
	2	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) (CPWD FOR HEALTH) (N28000112) (KERALA)	150.29	03/2020	162.52
HOME AFFAIRS					
	3	NSG AT KOLKATA (CPWD FOR MHA) (N28000104) (WEST BENGAL)	162.88	04/2018	193.91
	4	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI (CPWD FOR MHA) (N45000003) (UTTAR PRADESH)	199.31	01/2022	86.49
PETROLEUM					
	5	ADDITIONAL STORAGE TANKS AT PARADIP (IOCL) (N16000361) (ODISHA)	462.30	09/2021	493.72
POWER					
	6	PARBATI HEP (4X200 MW) (NHPC) II (NHPC) (180100210) (HIMACHAL PRADESH)	3,919.59	09/2009	12,832.59
RAILWAYS					
	7	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR (NR) (220100133) (JAMMU AND KASHMIR)	37,012.00	08/2024	42,328.83
	8	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING (NFR) (N22000183) (MULTI STATE)	2,047.51	08/2024	3,709.47

Table:-3. Project List: Completed during May 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	9	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING (RVNL) (N22000401) (UTTAR PRADESH)	2,018.23	12/2024	1,780.22
	10	2880.4 (ECR) (N22000417) (UTTAR PRADESH)	2,880.40	08/2024	3,074.78
	11	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL (IRCON) (N22000418) (ODISHA)	5,200.00	03/2020	389.00
	12	KARAILA ROAD - SHAKTINAGAR DOUBLING (ECR) (N22000419) (UTTAR PRADESH)	762.97	08/2024	808.96
	13	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI (NR) (N22000502) (PUNJAB)	404.00	08/2016	190.00
	14	DARBHANGA - BYPASS LINE CONNECTING SHISHO HALT AND KAKARGHATI EXCL DARBHANGA YARD (7.64 KM) (ECR) (N22000523) (BIHAR)	983.62	06/2025	417.57
	15	AZIMGANJ-MURSHIDABAD (JIYAGANJ) INCL. RLY. BRIDGE OVER RIVER BHAGIRATHI (ER) (N22000609) (WEST BENGAL)	164.33	02/2024	160.82
	16	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS (WR) (N22000505) (GUJARAT)	537.31	03/2024	944.55
ROAD TRANSPORT AND HIGHWAYS					
	17	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON (NHAI) (N24001428) (TAMIL NADU)	998.70	11/2021	975.68

Table:-3. Project List: Completed during May 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	18	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM (NHAI) (N24001430) (TAMIL NADU)	2,120.40	01/2022	1,588.17
	19	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475) (NAGALAND)	605.36	12/2024	273.21
	20	CONSTRUCTION OF 4-LANE NH-344P-PACKAGE-4 (FROM KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA (NHAI) (N24001532) (HARYANA)	694.00	11/2023	1,466.82
	21	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP (NHAI) (N24001533) (HARYANA)	1,690.23	12/2023	1,462.45
	22	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP (NHAI) (N24001534) (HARYANA)	1,334.04	01/2024	1,048.12
	23	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI (NHAI) (N24001536) (HARYANA)	817.00	07/2022	986.08
	24	2L PS OF SATNA - MAIHAR SECTION OF NH-135BG FROM KM 80.800 TO KM 120.125 (NHAI) (N24001616) (MADHYA PRADESH)	428.04	10/2023	351.97
	25	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20 (NHAI) (N24001708) (BIHAR)	2,156.22	06/2024	1,397.72
	26	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G (NHAI) (N24001711) (BIHAR)	939.43	03/2023	1,030.75

Table:-3. Project List: Completed during May 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	27	ADDITIONAL WORKS (2VUPS, MR-10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE-DEWAS SECTION OF N (NHAI) (N24001765) (MADHYA PRADESH)	207.77	07/2024	147.24
	28	BALANCE WORK OF 4L OF INDORE-GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF (NHAI) (N24001768) (MADHYA PRADESH)	323.51	04/2023	246.27
	29	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU (NHAI) (N24001788) (GUJARAT)	2,271.86	12/2023	2,655.78
	30	4L BYPASSES FOR JAGATPUR, B4ABUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA (NHAI) (N24001815) (UTTAR PRADESH)	1,699.00	11/2024	1,033.72
	31	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF GHAGARIYA- MUNABAO SECTION FROM KM (MoRTH) (N24001869) (RAJASTHAN)	235.15	08/2025	152.69
	32	WIDENING OF RAEBARELI TO PRAYAGRAJ SECTION FROM KM. 82.650 TO KM. 161.450 OF NH-30 AND LINK ROAD FRO (NHAI) (N24002085) (UTTAR PRADESH)	1,470.93	03/2025	1,088.30
	33	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389) (NAGALAND)	206.53	06/2022	119.25
	34	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391) (ARUNACHAL PRADESH)	294.04	04/2022	147.13
	35	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360) (MEGHALAYA)	260.21	12/2022	239.35

Table:-3. Project List: Completed during May 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	36	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN (NHAI) (N24000709) (MADHYA PRADESH)	950.27	02/2020	643.90
	37	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179) (NAGALAND)	217.35	11/2020	214.18
	38	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180) (NAGALAND)	237.51	12/2022	215.47
	39	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. (NHAI) (N24000567) (GUJARAT)	998.18	08/2019	1,105.25
	40	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU (NHAI) (N24000570) (GUJARAT)	763.08	08/2019	734.78
		Total	81,224.62		88,524.42

Table:-4. Project List: Added during May 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
COAL	1	50 MW WIND POWER PROJECT PART OF 150 MW SECI HYBRID (NLC) (N06000292) (GUJARAT)	7-2022	383.84 (N.A.) {383.84}	6/2025 (Jan-2026) {1/2026}
	2	NOKH SOLAR PV PROJECT 735 MW (NTPC) (N18000418) (RAJASTHAN)	3-2022	4,189.17 (4,378.17) {4,378.17}	4/2024 (Jul-2025) {7/2025}
POWER	3	TRANSMISSION SCHEME FOR INTEGRATION OF DAVANAGERE / CHITRADURGA AND BELLARY REZ IN KARNATAKA (PGCIL) (N18000419) (KARNATAKA)	3-2025	3,453.00 (N.A.) {3,453.00}	3/2027 (N.A.) {3/2027}
	4	IMPLEMENTATION OF LILO OF BOTH CIRCUITS OF 400KV VIDHYACHAL PS TO SASAN D/C LINE AT HINDALCO SWITCHY (PGCIL) (N18000420) (HARYANA)	2-2025	370.00 (N.A.) {370.00}	12/2026 (N.A.) {12/2026}
	5	EASTERN REGION EXPANSION SCHEME: 43 [ERES: 43] (PGCIL) (N18000421) (BIHAR)	5-2025	343.00 (N.A.) {343.00}	5/2026 (N.A.) {5/2026}
	6	EASTERN REGION EXPANSION SCHEME: 44 [ERES: 44] (PGCIL) (N18000422) (BIHAR)	5-2025	409.00 (N.A.) {409.00}	5/2026 (N.A.) {5/2026}
	7	TRANSMISSION SYSTEM FOR STRENGTHENING TO FACILITATE EVACUATION OF POWER FROM BHADLA/BIKANER COMPLEX (PGCIL) (N18000423) (UTTAR PRADESH)	12-2024	213.00 (N.A.) {213.00}	6/2026 (N.A.) {6/2026}
	8	CONSTRUCTION OF 4 LANE GAURIPUR BYPASS ON NH-17 IN THE STATE OF ASSAM (MoRTH) (N24002237) (ASSAM)	3-2024	421.15 (N.A.) {421.15}	10/2026 (N.A.) {10/2026}
	9	CONSTRUCTION OF 2 LANE BARPETA BYPASS FROM KM 77+900(BARADI) TO KM 86+150(DEURIKUCHI) (LENGTH=8.25K (MoRTH) (N24002238) (ASSAM)	3-2023	173.65 (N.A.) {173.65}	8/2026 (N.A.) {8/2026}

Table:-4. Project List: Added during May 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
ROAD TRANSPORT AND HIGHWAYS	10	IMPROVEMENT AND WIDENING TWO LANNIG WITH PAVED SHOULDER OF NATIONAL HIGHWAY 127B FROM KM 31.500 (GOE (MoRTH) (N24002239) (MEGHALAYA)	12-2023	504.00 (N.A.) {504.00}	5/2027 (N.A.) {5/2027}
	11	IMPROVEMENT AND UP-GRADATION OF NH-227B (84 KOSI PARIKRAMA MARG) PACKAGE ?I, FROM KM 228.920 (JAGARN (MoRTH) (N24002240) (UTTAR PRADESH)	3-2022	912.50 (N.A.) {912.50}	11/2026 (N.A.) {11/2026}
	12	IMPROVEMENT AND UP-GRADATION OF NH-227B (84 KOSI PARIKRAMA MARG) PACKAGE ?III, FROM KM.47.800 (GOSAI (MoRTH) (N24002241) (UTTAR PRADESH)	3-2022	587.97 (N.A.) {587.97}	11/2026 (N.A.) {11/2026}
	13	CHOITHAR TO MARREM KHULLEN SECTION IMPHAL- UKHRUL - JESSAMI PKG-5 (NHIDCL) (N24002242) (MANIPUR)	3-2023	564.05 (N.A.) {564.05}	3/2027 (N.A.) {3/2027}
	14	SILCHAR- CHURAI BARI PKG-5 (NHIDCL) (N24002243) (ASSAM)	2-2024	1,258.13 (N.A.) {1,258.13}	10/2027 (N.A.) {10/2027}
	15	IMPHAL - KHONGSANG - JIRIBAM PKG-2 (NHIDCL) (N24002244) (MANIPUR)	3-2021	195.14 (N.A.) {195.14}	3/2026 (N.A.) {3/2026}
Grand Total				13,977.60 (4,378.17) {14,166.60}	

Table:-5. Project List: Frozen/Deleted during May 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore	Progress (%)
POWER						
	1	NOKH PLOT-1 SOLAR PV PROJECT 245MW (NTPC) (N18000320) (RAJASTHAN)	1,352.71	08/2023	1,057.36	N.A.
	2	NOKH PLOT-2 SOLAR PV PROJECT 245MW (NTPC) (N18000321) (RAJASTHAN)	1,409.52	08/2023	1,403.89	N.A.
	3	NOKH PLOT-3 SOLAR PV PROJECT 245MW (NTPC) (N18000322) (RAJASTHAN)	1,426.94	08/2023	1,170.29	N.A.
ROAD TRANSPORT AND HIGHWAYS						N.A.
	4	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026) (ASSAM)	643.42	12/2025	69.47	N.A.
	5	HOSPET-BELLARY-KARNATAKA AP BORDER (NHAI) (N24000603) (KARNATAKA)	1,167.42	03/2019	1,028.39	N.A.
	6	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259) (NAGALAND)	315.63	04/2022	116.70	N.A.
	7	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353) (MANIPUR)	195.14	12/2022	61.81	N.A.
	8	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361) (SIKKIM)	332.20	09/2023	149.38	N.A.
		Total	6,842.98		5,057.29	

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ARUNACHAL PRADESH	CIVIL AVIATION	1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (Jun-2025) {6/2025}	645.63 (732.00) {732.00}	693.71	99.72
	POWER	2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	24,213.84	96.49
		3	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	3,306.40	15.74
	ROAD TRANSPORT AND HIGHWAYS	4	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (Mar-2024) {12/2024}	180.57 (244.10) {180.57}	160.46	96.62
		5	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (Jun-2025) {12/2025}	1,718.59 (1,718.59) {1,718.59}	728.21	73.64
		6	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (May-2023) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59
		7	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA- HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (Feb-2025) {2/2025}	301.06 (N.A.) {301.06}	198.22	81.06
		8	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	398.18	95.84

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		9	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	194.62	42.69
		10	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (Aug-2024) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		11	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (Feb-2024) {6/2025}	184.88 (N.A.) {184.88}	99.32	97.42
		12	HUNLI TO HAYULIANG PKG-1 (NHIDCL) (N24002222)	2-2024	2/2028 (N.A.) {2/2028}	1,262.43 (N.A.) {1,262.43}	12.12	2.35
		13	HUNLI TO ITHUN BRIDGE SECTION (NHIDCL) (N24002223)	2-2024	1/2027 (N.A.) {1/2027}	275.50 (N.A.) {275.50}	7.61	6.01
		14	PANGO TO JORGING ROAD PKG-1 (NHIDCL) (N24002224)	1-2024	7/2027 (N.A.) {7/2027}	898.19 (N.A.) {898.19}	7.08	4.06
ASSAM	CIVIL AVIATION	15	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (Aug-2025) {8/2025}	1,142.00 (N.A.) {2,333.00}	1,884.13	87.93
	COAL	16	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290)	7-2022	11/2030 (N.A.) {11/2030}	159.77 (N.A.) {159.77}	81.45	0
		17	TIRAP OCP (CIL) (N06000291)	11-2022	11/2027 (N.A.) {11/2027}	289.46 (N.A.) {289.46}	105.59	0

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	HEALTH AND FAMILY WELFARE	18	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (Apr-2023) {6/2025}	875.00 (873.92) {860.00}	787.90	99.52
	PETROLEUM	19	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	99.52	23.8
		20	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	97.22	91
		21	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	255.51	56.1
		22	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	172.04	45.3
		23	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (Dec-2024) {6/2025}	543.91 (726.93) {726.93}	491.56	93.95
		24	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	16,013.82	74.01
		25	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	9,447.83	85.06
		26	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (May-2026) {5/2026}	412.00 (595.20) {595.20}	396.08	82.8

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		27	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (Sep-2026) {9/2026}	277.00 (N.A.) {277.00}	180.17	66.4
		28	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (Apr-2025) {7/2025}	860.00 (N.A.) {860.00}	535.46	96.5
		29	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (Mar-2024) {6/2025}	430.76 (N.A.) {430.76}	319.86	83.66
		30	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	86.75	33.1
		31	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (Jul-2027) {7/2027}	156.36 (156.36) {156.36}	41.02	31.5
		32	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (Jul-2027) {7/2027}	384.04 (N.A.) {384.04}	94.00	34.4
	<u>RAILWAYS</u>	33	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2026 (N.A.) {3/2027}	4,059.65 (N.A.) {4,983.94}	3,652.94	92.31
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	34	BILASIPURA- GUWAHATI ROAD PKG-1 (NHIDCL) (N24002225)	2-2024	8/2027 (N.A.) {8/2027}	1,081.15 (N.A.) {1,081.15}	33.93	2.76
		35	SILCHAR-JIRIBAM PKG-1 (NHIDCL) (N24002226)	1-2024	1/2028 (N.A.) {1/2028}	957.95 (N.A.) {957.95}	0.00	16.25

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		36	BILASIPURA- GUWAHATI ROAD PKG-2 (NHIDCL) (N24002229)	11-2023	6/2027 (N.A.) {6/2027}	1,338.61 (N.A.) {1,338.61}	0.50	0
		37	BADARPUR ? CHURABARI PKG-6 (NHIDCL) (N24002230)	3-2024	3/2027 (N.A.) {3/2027}	870.00 (N.A.) {870.00}	0.00	0
		38	KARIMGANI - SUTARKANDI SECTION ON SILCHAR-CHURABARI PKG-7 (NHIDCL) (N24002231)	2-2024	2/2027 (N.A.) {2/2027}	791.79 (N.A.) {791.79}	0.00	0
		39	CONSTRUCTION OF 4 LANE GAURIPUR BYPASS ON NH-17 IN THE STATE OF ASSAM (MoRTH) (N24002237)	3-2024	10/2026 (N.A.) {10/2026}	421.15 (N.A.) {421.15}	0.00	0
		40	CONSTRUCTION OF 2 LANE BARPETA BYPASS FROM KM 77+900(BARADI) TO KM 86+150(DEURIKUCHI) (LENGTH=8.25K (MoRTH) (N24002238)	3-2023	8/2026 (N.A.) {8/2026}	173.65 (N.A.) {173.65}	0.00	0
		41	SILCHAR- CHURABARI PKG-5 (NHIDCL) (N24002243)	2-2024	10/2027 (N.A.) {10/2027}	1,258.13 (N.A.) {1,258.13}	0.00	0
		42	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	279.87	42.68
		43	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	183.63	45.53
		44	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.87	100

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		45	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	537.26	38.6
		46	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	983.58	64.03
		47	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	297.50	54.88
		48	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	404.51	68.8
		49	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (1,019.17) {925.47}	192.50	30.65
		50	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	335.20	66.96
		51	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.76	100
		52	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	158.15	81.63
		53	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,408.80	62.1

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		54	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (May-2025) {12/2025}	261.13 (N.A.) {261.13}	68.75	57.42
		55	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (Apr-2025) {12/2025}	217.50 (N.A.) {217.50}	88.99	68.03
		56	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {5/2025}	625.64 (N.A.) {625.64}	556.44	100
		57	FOUR LANING OF SRIRAMPUR-DHUBRI PKG- 2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {6/2025}	909.02 (N.A.) {909.02}	532.44	98.92
		58	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (Sep-2024) {6/2024}	175.00 (N.A.) {175.00}	200.80	100
		59	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	654.60	77.1
		60	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {5/2025}	457.72 (N.A.) {457.72}	366.34	100
		61	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	110.76	35.7
		62	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {7/2025}	458.59 (N.A.) {458.59}	198.15	65.62

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		63	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {3/2026}	535.03 (N.A.) {535.03}	102.23	34.15
		64	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	409.15	67.3
		65	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	393.82	65.95
		66	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	454.34	63.7
		67	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	305.73	94.97
		68	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	290.20	95.71
		69	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {7/2025}	204.10 (N.A.) {204.10}	143.45	96.02
		70	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	537.09	46.78

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		71	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	304.61	27.07
		72	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	422.31	25.57
		73	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	242.91	73.5
		74	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	129.18	16.28
		75	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (Jun-2025) {8/2025}	216.49 (241.52) {216.49}	111.59	85.83
		76	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	217.18	97.76
		77	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {6/2025}	437.39 (N.A.) {437.39}	574.56	96.95
		78	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	515.52	76.95
		79	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH- 52 (NHIDCL) (N24000431)	1-1991	6/2019 (Jun-2019) {7/2025}	520.01 (N.A.) {520.01}	305.76	97.9

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		80	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (Jul-2021) {12/2025}	289.99 (N.A.) {289.99}	233.23	88.03
		81	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {7/2025}	294.17 (N.A.) {294.17}	389.75	97.88
		82	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {7/2025}	252.00 (N.A.) {330.30}	219.65	91.31
MANIPUR	CIVIL AVIATION	83	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (Mar-2026) {3/2026}	499.00 (N.A.) {499.00}	154.47	40.36
	RAILWAYS	84	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	12/2026 (Mar-2028) {3/2028}	14,322.79 (12,274.06) {22,234.60}	15,338.76	69
	ROAD TRANSPORT AND HIGHWAYS	85	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (Jun-2025) {9/2025}	292.24 (N.A.) {292.24}	130.66	89.88
		86	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (Jun-2025) {10/2025}	365.53 (N.A.) {365.53}	156.31	77.36
		87	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3-2020	6/2022 (Jan-2025) {6/2025}	167.95 (204.12) {167.95}	88.05	69.89
		88	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7-2020	8/2022 (Feb-2025) {6/2025}	177.76 (N.A.) {177.76}	89.67	80.53

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		89	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (Jun-2025) {12/2025}	379.39 (N.A.) {379.39}	218.03	70.31
		90	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (Jan-2026) {3/2026}	410.68 (N.A.) {410.68}	147.81	68.79
		91	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (Sep-2025) {12/2025}	504.76 (N.A.) {504.76}	183.15	76.52
		92	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (Feb-2025) {3/2025}	152.11 (N.A.) {152.11}	73.48	100
		93	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (Aug-2025) {8/2025}	315.56 (N.A.) {315.56}	137.81	88.54
		94	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (Jul-2025) {12/2025}	579.63 (N.A.) {579.63}	172.65	72
		95	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (Mar-2025) {6/2025}	310.76 (N.A.) {310.76}	129.15	96.77
		96	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (Mar-2025) {12/2025}	226.32 (N.A.) {226.32}	105.78	74.48
		97	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (Jan-2025) {9/2025}	188.36 (N.A.) {188.36}	126.71	100

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		98	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (Sep-2024) {11/2025}	234.08 (N.A.) {234.08}	139.45	92.82
		99	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (Oct-2024) {2/2025}	467.41 (N.A.) {467.41}	264.83	100
		100	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (Jan-2025) {1/2026}	477.86 (N.A.) {477.86}	246.09	84.6
		101	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (Nov-2024) {12/2025}	311.18 (N.A.) {311.18}	190.96	83.5
		102	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (May-2025) {10/2025}	211.70 (N.A.) {211.70}	83.79	70.72
		103	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (Mar-2025) {10/2025}	467.00 (N.A.) {467.00}	193.81	77.8
		104	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (Jan-2025) {1/2025}	185.80 (N.A.) {185.80}	117.78	100
		105	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (Jan-2025) {12/2025}	483.87 (N.A.) {483.87}	278.89	92.94
		106	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (Feb-2025) {3/2025}	198.77 (N.A.) {198.77}	127.86	100
		107	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (Mar-2025) {12/2025}	673.27 (N.A.) {673.27}	382.37	79.47

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		108	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (Mar-2026) {3/2026}	578.98 (N.A.) {578.98}	153.92	71.25
		109	MARREM KHULLEN TO JESSAMI SECTION IMPHAL- UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	17.79	11.93
		110	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	13.14	15.9
		111	IMPHAL - KHONGSANG - JIRIBAM PKG-2 (NHIDCL) (N24002244)	3-2021	3/2026 (N.A.) {3/2026}	195.14 (N.A.) {195.14}	0.00	7.19
		112	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (Dec-2025) {3/2026}	760.16 (N.A.) {760.16}	148.98	60.6
		113	IMPHAL-KOHIMA ROAD PKG-5A (NHIDCL) (N24002232)	9-2020	8/2026 (N.A.) {8/2026}	228.97 (N.A.) {228.97}	0.00	5.96
		114	JESSAMI TO LAYNEN BRIDGE UKHRUL - JESSAMI PKG-7 (NHIDCL) (N24002227)	3-2023	6/2026 (N.A.) {6/2026}	164.89 (N.A.) {164.89}	1.46	6.5
		115	CHOITHAR TO MARREM KHULLEN SECTION IMPHAL- UKHRUL - JESSAMI PKG-5 (NHIDCL) (N24002242)	3-2023	3/2027 (N.A.) {3/2027}	564.05 (N.A.) {564.05}	0.00	0
MEGHALAYA	DEPARTMENT OF HIGHER EDUCATION	116	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (Jul-2025) {7/2025}	484.32 (429.70) {494.52}	270.55	84

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	117	DAINADUBI-DARUGIRI PKG-1B (NHIDCL) (N24002233)	3-2023	3/2027 (N.A.) {3/2027}	705.83 (N.A.) {705.83}	0.31	1.55
		118	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10-2020	4/2022 (Jun-2024) {2/2025}	157.86 (146.92) {157.86}	152.95	100
		119	IMPROVEMENT AND WIDENING TWO LANNIG WITH PAVED SHOULDER OF NATIONAL HIGHWAY 127B FROM KM 31.500 (GOE (MoRTH) (N24002239)	12-2023	5/2027 (N.A.) {5/2027}	504.00 (N.A.) {504.00}	0.00	0
		120	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	221.86	28
		121	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	292.69	25.52
		122	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	297.79	24
		123	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	207.20	26
		124	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	101.98	24

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		125	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (Dec-2024) {5/2026}	359.86 (N.A.) {359.86}	233.26	87
		126	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (N.A.) {3/2025}	302.88 (N.A.) {302.88}	228.68	96
		127	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11-2021	6/2024 (Dec-2024) {5/2025}	283.50 (N.A.) {283.50}	257.26	100
		128	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM () (NHIDCL) (N24001313)	11-2020	12/2023 (Oct-2025) {10/2025}	351.12 (N.A.) {351.12}	295.88	62.5
		129	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	434.11	31
		130	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (Mar-2025) {6/2025}	553.51 (610.09) {553.51}	432.78	92.01
MIZORAM	RAILWAYS	131	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2025 (N.A.) {6/2025}	6,527.45 (5,021.45) {8,213.72}	8,001.88	97
	ROAD TRANSPORT AND HIGHWAYS	132	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (N.A.) {4/2025}	519.09 (N.A.) {785.65}	670.91	97.51

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		133	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (N.A.) {5/2024}	640.07 (N.A.) {1,286.35}	1,195.84	98.9
		134	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (N.A.) {4/2025}	473.18 (N.A.) {688.25}	541.04	94.7
		135	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (N.A.) {5/2025}	537.82 (N.A.) {789.05}	778.16	99.82
		136	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (N.A.) {5/2025}	518.53 (N.A.) {906.76}	849.68	97.9
		137	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (N.A.) {5/2025}	404.29 (N.A.) {750.32}	666.58	100
		138	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (N.A.) {5/2025}	428.11 (N.A.) {746.39}	613.69	98.7
		139	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (N.A.) {6/2024}	206.88 (N.A.) {219.33}	265.34	100
		140	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (N.A.) {10/2024}	292.24 (N.A.) {331.17}	294.60	93.2

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		141	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	263.48	68.8
		142	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWL RANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {12/2025}	523.78 (N.A.) {523.78}	366.81	80.51
		143	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (Apr-2024) {4/2024}	233.25 (N.A.) {233.25}	172.09	100
		144	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (N.A.) {3/2026}	698.44 (N.A.) {698.45}	496.84	59.4
		145	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (N.A.) {3/2026}	740.58 (N.A.) {740.58}	364.34	57.4
		146	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9-2021	5/2023 (N.A.) {5/2024}	492.94 (N.A.) {492.94}	365.86	90.5
		147	ZORINPUI- HMAWNGBU-LONGMASU (NH- 502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	33.56	3
<u>NAGALAND</u>	<u>PETROLEUM</u>	148	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	6.12	18
	<u>RAILWAYS</u>	149	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2026 (N.A.) {12/2029}	6,663.20 (6,663.20) {6,663.20}	4,789.15	73
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	150	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	62.08	67.82

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		151	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7-2021	3/2023 (Sep-2025) {9/2025}	258.52 (N.A.) {258.52}	89.46	79.7
		152	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	100.51	54.28
		153	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	50.60	26.58
		154	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	163.84	62.02
		155	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (Jun-2026) {6/2026}	252.19 (N.A.) {252.19}	14.25	17.9
		156	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3-2021	7/2024 (Dec-2025) {12/2025}	297.24 (N.A.) {297.24}	137.76	79.47
		157	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (Mar-2025) {3/2025}	226.44 (N.A.) {226.44}	140.24	100
		158	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (Sep-2025) {9/2025}	192.93 (N.A.) {192.93}	105.41	92.82

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		159	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {12/2025}	177.77 (199.02) {199.02}	46.94	61.25
		160	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3-2016	9/2019 (Nov-2022) {5/2025}	373.07 (534.41) {534.41}	382.50	99.81
		161	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (Sep-2025) {9/2025}	429.52 (794.74) {794.74}	321.40	91.49
		162	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (Feb-2023) {4/2025}	387.00 (688.12) {688.12}	392.01	100
		163	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (Aug-2024) {4/2025}	500.09 (698.81) {698.81}	393.53	100
		164	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU- MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (Aug-2022) {8/2025}	215.79 (N.A.) {215.79}	130.20	79.58
		165	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU- MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (Jun-2023) {9/2025}	323.98 (N.A.) {323.98}	119.94	59.68
		166	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	119.20	65.06

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		167	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3-2020	6/2022 (Oct-2022) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
		168	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (Nov-2025) {11/2025}	330.80 (N.A.) {330.80}	171.89	92.44
		169	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (Nov-2026) {11/2026}	232.29 (350.88) {232.29}	70.90	14.7
		170	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (Sep-2024) {6/2026}	277.44 (N.A.) {277.44}	168.88	67.81
		171	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (Jun-2025) {12/2025}	159.85 (342.29) {159.85}	103.95	29.9
		172	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (Apr-2023) {8/2025}	202.36 (N.A.) {202.36}	75.39	31.02
SIKKIM	CIVIL AVIATION	173	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	24.99	12
	DEPARTMENT OF HIGHER EDUCATION	174	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8-2020	1/2025 (N.A.) {1/2025}	314.06 (N.A.) {303.55}	157.24	80

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	175	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	4,341.50	67.67
		176	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,486.30	88.51
	RAILWAYS	177	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	5/2015 (Dec-2027) {12/2027}	7,876.92 (11,963.43) {11,963.43}	8,569.25	80
	ROAD TRANSPORT AND HIGHWAYS	178	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {4/2025}	311.00 (N.A.) {273.78}	257.86	95.12
		179	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (Aug-2024) {10/2025}	345.38 (395.59) {395.59}	362.61	91.24
		180	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {6/2025}	402.94 (N.A.) {402.94}	247.12	76.54
		181	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (Nov-2024) {7/2025}	295.97 (N.A.) {295.97}	249.80	95.66
		182	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3-2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	100
		183	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (May-2022) {12/2023}	375.80 (N.A.) {375.80}	288.56	96.55

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		184	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11-2017	10/2020 (Aug-2023) {4/2024}	290.05 (N.A.) {290.05}	218.36	100
		185	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (Jan-2026) {1/2026}	385.15 (N.A.) {385.15}	170.32	81.3
		186	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (Apr-2025) {12/2025}	410.60 (379.30) {379.30}	234.98	74.58
		187	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (Oct-2024) {12/2025}	230.45 (244.91) {244.91}	206.95	82.32
		188	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (Jul-2025) {3/2026}	493.42 (478.79) {478.79}	305.20	58.28
		189	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (Jun-2025) {12/2026}	816.79 (786.60) {786.60}	332.24	51.45
		190	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (Oct-2023) {12/2025}	292.80 (N.A.) {292.80}	202.92	60.9
		191	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (Oct-2023) {12/2025}	183.31 (439.56) {439.56}	355.31	51.19

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		192	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (Aug-2024) {12/2025}	262.84 (414.20) {414.20}	221.86	47.57
TRIPURA	PETROLEUM	193	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (Sep-2025) {9/2025}	656.00 (N.A.) {656.00}	415.86	82.2
	ROAD TRANSPORT AND HIGHWAYS	194	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM SECTION PKG-4 (NHIDCL) (N24002228)	1-2024	12/2026 (N.A.) {12/2026}	726.90 (N.A.) {726.90}	0.00	3.1
		195	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	73.41	22
		196	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH- 8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	26.34	8.38
		197	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	9.34	16.61
		198	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	52.82	34.61
		199	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	26.37	31.5
		200	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	0.00	2

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		201	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (N.A.) {12/2025}	354.79 (N.A.) {354.79}	34.08	0
		202	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {12/2025}	195.95 (N.A.) {195.95}	38.10	45.3
		203	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (May-2025) {5/2025}	456.88 (N.A.) {456.88}	122.23	49.88
		204	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (Feb-2024) {12/2024}	277.50 (302.02) {302.02}	260.38	99.94
		205	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {4/2025}	201.99 (N.A.) {287.47}	148.22	100
		206	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (Oct-2023) {11/2024}	159.13 (171.50) {171.50}	84.33	100
			Total			206,832.53 (50,841.50) {253,273.53}	1,47,388.88	

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ANDAMAN AND NICOBAR ISLANDS	CIVIL AVIATION	1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR (AAI) (N04000073)	10-2013	9/2018 (Jun-2023) {6/2023}	417.23 (707.73) {707.73}	698.80	100.00
	RAILWAYS	2	LUDHIANA KILA RAIPUR (19 KMS) WITH FREIGHT LINE AT GILL STATION ON LDH- JHL SECTION (NR) (N22000584)	3-2019	3/2025 (Dec-2025) {1/2026}	235.72 (N.A.) {235.72}	55.79	55.00
	ROAD TRANSPORT AND HIGHWAYS	3	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N (NHIDCL) (N24000745)	3-2017	12/2019 (Mar-2023) {6/2025}	409.85 (N.A.) {409.85}	214.23	95.10
		4	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O (NHIDCL) (N24000749)	3-2018	9/2020 (Nov-2022) {7/2025}	234.27 (N.A.) {234.27}	126.50	82.97
		5	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 (MoRTH) (N24000820)	11-2017	11/2019 (N.A.) {11/2019}	237.80 (N.A.) {238.00}	222.13	98.00
		6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000821)	11-2017	11/2019 (N.A.) {11/2019}	257.34 (N.A.) {238.00}	214.90	100.00
		7	AJANTHA TO BULDHANA (MoRTH) (N24001008)	2-2017	7/2019 (N.A.) {12/2023}	401.00 (401.00) {401.00}	260.08	97.00
		8	MAJOR BRIDGE OVER MIDDLE STRAIT CREEK (NHIDCL) (N24002207)	12-2024	2/2026 (N.A.) {2/2026}	371.80 (207.99) {207.99}	0.00	4.68
		9	PACKAGE-3A (NHIDCL) (N24002208)	2-2018	9/2025 (Mar-2024) {9/2025}	207.54 (154.01) {154.01}	16.21	39.27
		10	PACKAGE-3B (NHIDCL) (N24002209)	2-2018	11/2025 (N.A.) {11/2025}	183.47 (N.A.) {183.47}	17.36	32.38
ANDHRA PRADESH	CIVIL AVIATION	11	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT (AAI) (N04000091)	4-2020	3/2023 (Aug-2025) {8/2025}	611.80 (N.A.) {611.80}	444.75	74.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		12	RAJAHMUNDY AIRPORT: CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUD (AAI) (N04000103)	12-2022	8/2025 (N.A.) {8/2025}	347.15 (347.15) {347.15}	75.17	44.50
		13	KADAPPA AIRPORT- CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUDING MA (AAI) (N04000106)	3-2023	1/2026 (Jan-2026) {1/2026}	265.91 (265.91) {265.91}	39.49	27.00
		14	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE (CPWD EDUCATION) (N42000005)	2-2019	6/2020 (N.A.) {6/2020}	655.34 (N.A.) {655.34}	366.21	95.00
		15	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC (CPWD EDUCATION) (N42000007)	9-2019	9/2022 (N.A.) {6/2024}	588.72 (656.39) {656.39}	630.55	100.00
		16	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT (ONGC) (N16000247)	3-2016	6/2020 (Mar-2025) {6/2025}	34,012.00 (N.A.) {34,012.00}	33,149.29	96.40
	PETROLEUM	17	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY (HPCL) (N16000432)	9-2021	6/2024 (Mar-2026) {3/2026}	160.00 (220.00) {220.00}	50.04	58.30
		18	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS (IOCL) (N16000485)	3-2022	3/2030 (N.A.) {3/2030}	1,420.00 (N.A.) {1,420.00}	152.86	6.10
		19	MULTI-PRODUCT PIPELINE FROM KRISHNAPATNAM COASTAL INSTALLATION TO THE PROPOSED INSTALLATION AT HYDER (BPCL) (N16000499)	9-2019	3/2025 (N.A.) {10/2025}	1,932.00 (N.A.) {1,932.00}	1,491.65	92.60
		20	HP TRIJET UNIT IN VR (HPCL) (N16000535)	7-2024	7/2027 (N.A.) {7/2027}	193.00 (N.A.) {193.00}	0.38	23.00
		21	CONSTRUCTION OF AVIATION FUEL FARM FACILITIES AT BHOGAPURAM AIRPORT (HPCL) (N16000538)	8-2024	3/2026 (N.A.) {3/2026}	240.00 (N.A.) {240.00}	19.32	35.30

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		22	VISAKHA RAIPUR PIPELINE PROJECT (HPCL) (N16000539)	9-2024	9/2027 (N.A.) {9/2027}	2,212.00 (N.A.) {2,212.00}	4.32	4.73
	POWER	23	TRANSMISSION SCHEME FOR SOLAR ENERGY ZONE IN ANANTHPURAM (2500MW) AND KURNOOL (1000MW) (PGCIL) (N18000380)	9-2023	3/2025 (N.A.) {9/2025}	1,249.00 (N.A.) {1,249.00}	568.70	56.70
		24	AUGMENTATION OF 1500MVA 3RD 765/400KV TRANSFORMATION CAPACITY AT KURNOOL NEW SUBSTATION (PGCIL) (N18000395)	5-2023	9/2025 (N.A.) {9/2025}	164.00 (N.A.) {164.00}	60.00	21.00
		25	TRANSMISSION SYSTEM FOR INTEGRATION OF KURNOOL-IV REZ PHASE- I (FOR 4.5 GW) (PGCIL) (N18000413)	3-2025	3/2027 (N.A.) {3/2027}	5,000.00 (N.A.) {5,000.00}	0.00	N.A.
		26	TRANSMISSION SYSTEM STRENGTHENING AT KURNOOL- III PS FOR INTEGRATION OF ADDITIONAL RE GENERATION PRO (PGCIL) (N18000416)	3-2025	3/2027 (N.A.) {3/2027}	2,886.00 (N.A.) {2,886.00}	0.00	N.A.
	RAILWAYS	27	KOTLPALLI-NARASAPUR (NL) (SCR) (SCR) (220100265)	12-2001	3/2028 (N.A.) {3/2027}	2,500.98 (N.A.) {2,500.98}	1,141.44	18.00
		28	NADIKUDE-SRI KALAHASTI (SCR) (N22000286)	4-2011	5/2027 (N.A.) {5/2027}	2,312.00 (N.A.) {3,122.35}	1,935.77	35.00
		29	GUNTUR-GUNTAKAL (SCR) (N22000368)	4-2016	12/2025 (N.A.) {12/2025}	3,733.37 (N.A.) {3,887.48}	3,534.39	N.A.
		30	VIJAYAWADA-GUDUR (RVNL) (N22000369)	4-2015	11/2024 (N.A.) {12/2024}	6,654.00 (N.A.) {6,238.67}	5,883.89	N.A.
		31	KOTTAVALSA - KORAPUT DOUBLING (ECOR) (N22000377)	4-2015	3/2022 (N.A.) {3/2022}	2,499.71 (N.A.) {2,499.71}	1,950.16	70.00
		32	PENUKONDA-DHARMAVARAM, EXCL. DHARMAVARAM (41.5 KM) (SWR) (N22000555)	4-2019	3/2026 (N.A.) {12/2025}	294.67 (307.66) {307.66}	206.80	60.00
		33	MALUGUR-PALASAMUDRAM (17.98 KM) (PB#29/NR/2022-23) (SWR) (N22000556)	9-2022	12/2025 (N.A.) {12/2026}	323.14 (342.41) {342.41}	46.89	12.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		34	DOUBLING BETWEEN GOOTY-PENDAKALLU (29.225) (SCR) (N22000585)	3-2023	3/2027 (N.A.) {3/2027}	351.83 (N.A.) {351.83}	0.00	N.A.
		35	VIJAYAWADA KAZIPET BYEPASS LINE (SCR) (N22000586)	4-2016	12/2025 (N.A.) {12/2025}	647.37 (N.A.) {226.72}	242.64	N.A.
		36	RENIGUNTA WADI GOOTY - BYPASS (SCR) (N22000587)	4-2016	12/2025 (N.A.) {12/2025}	302.00 (N.A.) {302.00}	219.08	50.00
	ROAD TRANSPORT AND HIGHWAYS	37	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES (MoRTH) (N24000301)	3-2015	10/2015 (May-2021) {5/2021}	271.45 (N.A.) {271.45}	238.23	100.00
		38	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 (NHAI) (N24000811)	3-2018	12/2020 (Dec-2022) {12/2024}	314.43 (N.A.) {348.72}	85.61	69.64
		39	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 (MoRTH) (N24000931)	11-2016	5/2017 (N.A.) {11/2024}	290.15 (N.A.) {236.16}	205.02	90.00
		40	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG (MoRTH) (N24000937)	3-2018	8/2018 (N.A.) {11/2024}	289.67 (290.00) {285.29}	254.19	98.50
		41	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD (MoRTH) (N24000964)	8-2016	1/2017 (N.A.) {5/2025}	350.61 (N.A.) {411.18}	407.92	98.20
		42	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 (MoRTH) (N24000969)	1-2017	9/2017 (N.A.) {6/2025}	263.45 (N.A.) {263.45}	208.15	85.00
		43	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) (NHAI) (N24001301)	11-2019	1/2024 (N.A.) {7/2024}	1,601.10 (N.A.) {1,601.10}	1,425.64	91.05

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		44	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT (MoRTH) (N24001386)	8-2020	3/2021 (N.A.) {6/2025}	222.61 (N.A.) {222.61}	120.46	95.00
		45	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI (NHAI) (N24001476)	9-2021	9/2022 (Sep-2024) {6/2025}	517.05 (N.A.) {655.06}	520.94	91.97
		46	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP (NHAI) (N24001477)	9-2021	9/2022 (Sep-2024) {6/2025}	622.00 (N.A.) {817.91}	541.73	75.96
		47	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16 (NHAI) (N24001817)	2-2019	3/2023 (Oct-2024) {10/2024}	757.45 (N.A.) {757.45}	607.76	99.41
		48	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) (NHAI) (N24001818)	2-2021	1/2025 (N.A.) {1/2025}	818.73 (N.A.) {1,105.00}	563.32	24.92
		49	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) (NHAI) (N24001819)	3-2021	1/2025 (N.A.) {1/2025}	1,102.63 (N.A.) {1,303.00}	1,107.66	94.17
		50	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) (NHAI) (N24001820)	2-2021	12/2024 (N.A.) {12/2024}	1,484.83 (N.A.) {1,768.00}	1,523.09	91.85
		51	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPELEM TO GUDIP (NHAI) (N24001821)	11-2020	10/2024 (N.A.) {10/2024}	1,137.74 (N.A.) {1,289.00}	1,256.44	97.10
		52	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE (NHAI) (N24001822)	12-2020	10/2024 (N.A.) {10/2024}	1,075.27 (N.A.) {1,307.00}	1,100.55	84.80

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		53	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH- 71(PACKAGE-I) - N/05060/01002/A (NHAI) (N24001823)	1-2022	1/2025 (Jan-2023) {1/2025}	1,852.12 (N.A.) {1,787.00}	777.18	90.00
		54	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP (NHAI) (N24001824)	3-2020	1/2024 (Dec-2024) {12/2024}	1,863.09 (N.A.) {2,238.00}	1,227.61	98.76
		55	6L KANTAKAPALLE ? SABBAVARAM SECTION OF NH-130CD ROAD FROM KM 445.100 TO KM 464.662 (PKG-4) (NHAI) (N24001836)	2-2021	10/2024 (N.A.) {3/2026}	824.29 (N.A.) {924.00}	514.33	75.54
		56	6L JAKKUVA ? KORLAM SECTION OF NH- 130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) (NHAI) (N24001837)	2-2021	3/2024 (Jul-2024) {12/2025}	663.60 (N.A.) {768.00}	463.08	98.80
		57	6L ALURU - JAKKUVA SECTION OF NH- 130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) (NHAI) (N24001838)	2-2021	3/2024 (N.A.) {12/2025}	922.50 (N.A.) {1,128.68}	534.48	84.03
		58	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA (NHAI) (N24001841)	12-2022	9/2025 (N.A.) {2/2026}	912.94 (N.A.) {912.94}	238.71	57.40
		59	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 (NHAI) (N24001842)	12-2022	11/2025 (N.A.) {11/2025}	750.81 (N.A.) {750.81}	145.15	49.10
		60	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH (NHAI) (N24001843)	12-2022	11/2025 (N.A.) {11/2025}	992.89 (N.A.) {992.89}	197.36	43.90
		61	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. (NHAI) (N24001844)	12-2022	10/2025 (N.A.) {10/2025}	1,058.90 (N.A.) {1,058.90}	249.94	45.04

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		62	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 (NHAI) (N24001845)	2-2023	10/2025 (N.A.) {10/2025}	1,253.24 (N.A.) {1,253.24}	156.38	20.09
		63	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. (NHAI) (N24001846)	2-2023	10/2025 (N.A.) {10/2025}	1,200.42 (N.A.) {1,200.42}	98.18	7.20
		64	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA (NHAI) (N24001847)	1-2023	11/2025 (N.A.) {11/2025}	956.14 (N.A.) {956.14}	215.17	40.20
		65	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTALA 196.000 KM. PACK (NHAI) (N24001848)	2-2023	10/2025 (N.A.) {10/2025}	909.02 (N.A.) {909.02}	129.52	18.10
		66	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 (NHAI) (N24001849)	5-2022	7/2025 (N.A.) {9/2025}	1,063.72 (N.A.) {1,063.72}	467.74	77.09
		67	CONSTRUCTION OF 4-LANE HIGHWAY FROM SAMARLAKOTA TO ACHAMPETA JUNCTION (FROM KM. 0.000 TO KM. 12.250) (NHAI) (N24001856)	5-2023	8/2025 (N.A.) {8/2025}	648.75 (N.A.) {648.75}	240.26	60.74
		68	2L+PS FROM KM. 0+000 TO KM. 32+000 (MUDIGUBBA TO PUTTAPARTHI) OF NH-342 (MoRTH) (N24001932)	3-2022	9/2024 (N.A.) {6/2025}	401.72 (N.A.) {401.72}	139.07	80.00
		69	NH440 RAYACHOTY TOVEMPALLI 2LPS (MoRTH) (N24001934)	12-2021	5/2024 (N.A.) {7/2025}	439.82 (N.A.) {439.82}	119.72	26.73
		70	4 LANE WITH PAVED SHOULDER FROM KM 0.000 TO KM 51.119 OF TADIPATRI TO MUDDANUR OF NH67 (MoRTH) (N24001935)	3-2022	8/2025 (N.A.) {8/2025}	724.17 (N.A.) {724.17}	229.73	97.38

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		71	NH165 FROM KM 0.000 TO KM 64.020 PAMARRU TO AKIVEEDU SECTION TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001939)	3-2020	9/2023 (N.A.) {12/2025}	529.24 (N.A.) {529.24}	224.81	51.78
		72	2LPS FROM KM36.400 TO KM. 107.224 OF NH167BG FROM DUTTALUR TO KAVALI SECTION (MoRTH) (N24001942)	3-2021	7/2024 (N.A.) {3/2025}	423.67 (N.A.) {423.67}	145.72	60.53
		73	NH167AD FROM MACHERLA TO DACHEPALLI FROM KM.0.000 TO 43.659 TO 2LPS (MoRTH) (N24001951)	1-2022	1/2025 (N.A.) {1/2025}	403.22 (N.A.) {403.22}	201.69	97.00
		74	NH 167 B KADAPA NELLORE BORDER TO CSPURAM I.E. FROM KM 58.635 TO KM 99.409 (MoRTH) (N24001952)	3-2022	8/2025 (N.A.) {8/2025}	285.50 (N.A.) {285.50}	204.29	95.00
		75	NH-30-BHADRACHALAM TO KONTA SECTION 2LPS (MoRTH) (N24001953)	12-2021	9/2024 (N.A.) {3/2025}	388.71 (N.A.) {388.71}	159.29	80.00
		76	WIDENING TO 2LPS OF RAMPACHODAVARAM - KOYYURU SECTION OF NH516E FROM KM.43.700 TO KM 113.820 (MoRTH) (N24001954)	3-2022	1/2025 (N.A.) {1/2025}	568.12 (N.A.) {568.12}	215.09	91.05
		77	GUDIWADA TOWN 2 LANE ROB AND ROAD IMPROVEMENT OF NH165 IN REPLACEMENT OF LC NO 3ESPL3 AT KM 231.700 (MoRTH) (N24001955)	3-2022	5/2025 (N.A.) {5/2025}	317.22 (N.A.) {317.22}	84.57	80.00
		78	2LPS FROM GONDIGUDA TO ARAKU BHALLAGUDA KM 27.480 TO KM 51.772 SECTION OF NH 516E (MoRTH) (N24001956)	8-2020	9/2023 (N.A.) {12/2024}	296.66 (N.A.) {296.66}	190.30	87.49
		79	2LPS OF KOYYURU TO CHAPRATHIPALEM SECTION OF NH 516E (MoRTH) (N24001957)	8-2020	7/2024 (N.A.) {6/2025}	349.29 (N.A.) {349.29}	114.53	76.00
		80	2LPS OF CHAPRATHIPALEM TO LAMBASINGI SECTION OF NH 516E (MoRTH) (N24001958)	8-2020	10/2024 (N.A.) {6/2025}	311.22 (N.A.) {311.22}	85.45	72.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		81	4 LANE FROM KM 56.400 TO KM 120.300 FROM B.KOTHAPALLI JUNCTION TO GORANTLA OF NH 716G (MoRTH) (N24001959)	3-2022	9/2025 (N.A.) {9/2025}	839.98 (N.A.) {839.98}	146.12	67.00
		82	4L GREENFIELD ROAD CONNECTING NORTH AND SOUTH INDUSTRIAL CLUSTER OF KHANDALERU CREEK NEAR KRISHNAPAT (NHAI) (N24001979)	8-2022	9/2025 (N.A.) {9/2025}	609.43 (N.A.) {609.43}	25.24	52.45
		83	4 LANING OF NH 544D FROM EXISTING KM 346.300 OF NH 44 (DESIGN CHAINAGE KM 0.000) TO KM 39.380 (DESIG (NHAI) (N24001980)	10-2022	7/2025 (N.A.) {7/2025}	907.76 (N.A.) {907.76}	388.40	81.35
		84	CONSTRUCTION OF SIX LANING OF NAIDUPETA JUNCTION - TURPUKANUPUR SECTION FROM KM.57+046 TO KM.91+927 (NHAI) (N24001981)	7-2022	10/2025 (N.A.) {10/2025}	1,398.84 (N.A.) {1,398.84}	58.68	16.00
		85	4L PS FROM KURNOOL (EXISTING KM. 5.400 OF NH-40/DESIGN KM.0.000) TO MANDLEM (EXISTING KM.38.000/DESI (NHAI) (N24001982)	3-2023	10/2025 (N.A.) {10/2025}	827.39 (N.A.) {827.39}	333.74	99.15
		86	4 LANING FROM EXISTING KM 39.380 (DESIGN CH. 37.000) TO KM 74.450 (DESIGN CH. 69.000) OF MUCHUKOTA ? (NHAI) (N24001983)	10-2022	8/2025 (N.A.) {8/2025}	972.63 (N.A.) {1,055.23}	309.39	53.38
		87	4L PS FROM MANDLEM (EXISTING KM. 38.000/DESIGN KM.30.600) TO ATMAKUR (EXISTING KM.73.000/DESIGN KM 6 (NHAI) (N24001984)	3-2023	10/2025 (N.A.) {10/2025}	887.28 (N.A.) {887.28}	293.88	84.50
		88	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-II) FROM KM.96.000 TO KM 127.000 (BAIREDDYPALLE TO BANGAR (NHAI) (N24001985)	3-2021	6/2025 (N.A.) {6/2025}	1,942.94 (2,171.00) {2,171.00}	1,694.18	61.25

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		89	4L OF PILERU TO KALUR SECTION FROM KM 55.900 TO KM 92.800 AND KM 94.500 TO KM 95.717 (NHAI) (N24001986)	10-2023	4/2025 (N.A.) {4/2025}	1,047.32 (N.A.) {1,047.32}	301.20	88.00
		90	CONSTRUCTION OF 1 NOS ROB, 2 NOS VUPS, SERVICE ROADS, PROVISION OF LIGHTING AND CONSTRUCTION OF OTHE (NHAI) (N24001987)	6-2023	12/2024 (N.A.) {12/2024}	152.05 (N.A.) {152.05}	136.12	76.63
		91	6L OF CHITTOOR TO THATCHUR FROM KUMARAJAPET TO VEERA KAVERI RAJA PURAM FROM KM 43.800 TO KM 61.380 O (NHAI) (N24001988)	2-2021	10/2025 (N.A.) {10/2025}	591.99 (703.00) {703.00}	496.65	65.28
		92	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED HIGHWAY FROM CHILLAKURU CROSS ROAD TO TURPUKANUPUR KM 0+000 (NHAI) (N24002033)	7-2022	12/2025 (N.A.) {12/2025}	909.47 (N.A.) {909.47}	97.03	30.40
		93	COMPLETION OF BALANCE WORKS PENDING IN BIT AND PIECES (INCOMPLETE STRETCH AT 7 LOCATIONS) AND LISTED (NHAI) (N24002103)	9-2022	1/2025 (N.A.) {6/2025}	166.52 (N.A.) {166.52}	57.29	98.00
		94	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NARAYANMPET (CH. 203+500) TO CHANDRASEKHARPURAM (CH. 22 (NHAI) (N24002122)	2-2024	2/2026 (N.A.) {2/2026}	813.66 (N.A.) {813.66}	91.70	22.17
		95	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM CHANDRASEKHARAPURAM (CH. 228+000) TO POLAVARAM (CH. 260 (NHAI) (N24002123)	2-2024	2/2026 (N.A.) {2/2026}	1,292.65 (N.A.) {1,292.65}	135.26	16.00
		96	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM POLAVARAM (CH. 260+000) TO MARRIPUDI (CH. 285+500) OF [(NHAI) (N24002124)	2-2024	2/2026 (N.A.) {2/2026}	747.29 (N.A.) {747.29}	142.64	30.80

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		97	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MARRIPUDI (CH. 285+500) TO SOMAVARAPPADU (CH. 314+600) (NHAI) (N24002125)	2-2024	2/2026 (N.A.) {2/2026}	976.40 (N.A.) {976.40}	229.68	41.00
		98	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM SOMAVARAPPADU (CH.314.600) TO MUPPAVARAM (CH.343+240) O (NHAI) (N24002126)	2-2024	2/2026 (N.A.) {2/2026}	1,103.89 (N.A.) {1,103.89}	133.88	14.50
		99	4-LANE WITH PAVED SHOULDERS FROM KM 32/0 TO KM 79/650 (DESIGN CHAINAGE KM 32+000 TO KM 78+760) PUTTA (MoRTH) (N24002139)	3-2023	12/2025 (N.A.) {11/2025}	1,318.57 (N.A.) {1,318.57}	201.00	56.00
		100	SOMAYAJULAPALLI ? DHONE SECTION OF NH ? 340B FROM KM.0/0 TO 56/200 [DESIGN CH. KM 0/00 TO KM 53/33] (MoRTH) (N24002140)	4-2023	12/2025 (N.A.) {12/2025}	629.73 (N.A.) {629.73}	103.00	62.00
		101	2-LANE WITH PAVED SHOULDER CONFIGURATION OF LAMBASINGI TO PADERU SECTION (KM 205+000 TO KM 253+974) (MoRTH) (N24002142)	8-2023	11/2025 (N.A.) {11/2025}	361.24 (N.A.) {361.24}	7.00	26.00
		102	BYPASS ROAD TO ADONI TOWN CONNECTING NH-167 (HAGARI - JADCHARLA ROAD) FROM KM.62/700 TO 71/400 IN KU (MoRTH) (N24002143)	8-2023	2/2026 (N.A.) {2/2026}	361.24 (N.A.) {361.24}	109.65	56.00
		103	VODAREVU-CHILAKALURIPET SECTION (DESIGN CHAINAGE 0+00 TO 47+000) OF NH- 167A (PACKAGE-I) (MoRTH) (N24002144)	8-2023	2/2026 (N.A.) {2/2026}	1,064.24 (N.A.) {1,064.24}	80.00	60.00
		104	TADIPATRI BYPASS (KM 0+000 TO KM 6+285) OF 4-LANE ON NH-67 IN ANANTAPURAMU (MoRTH) (N24002145)	11-2023	3/2026 (N.A.) {3/2026}	159.66 (N.A.) {159.66}	11.95	63.50

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		105	KURNOOL/KADAPA BORDER- JAMMALAMADUGU SECTION OF NH-167K I.E. DESIGN CH. KM 248+010 TO KM 269+900 (MoRTH) (N24002146)	11-2023	11/2025 (N.A.) {11/2025}	292.63 (N.A.) {292.63}	61.36	20.00
		106	DORNALA TO KUNTA JUNCTION FROM DESIGN CHAINAGE KM 244+000 TO 267+990 SECTION OF NH-765 (PACKAGE-2) (MoRTH) (N24002147)	12-2022	1/2024 (N.A.) {3/2026}	244.83 (N.A.) {244.83}	104.32	74.00
		107	PADERU BYPASS (KM 0+000 TO KM 13+000) OF 2- LANE WITH PAVED SHOULDER ON NH- 516E (MoRTH) (N24002148)	3-2023	3/2024 (N.A.) {2/2026}	244.43 (N.A.) {244.43}	22.77	N.A.
		108	DAVUALAPALLY TO MALLAPALEM SECTION {DESIGN CH. KM 133+922 TO KM 154+216 (EXISTING CH. KM 133+922 TO (MoRTH) (N24002149)	1-2024	2/2024 (N.A.) {2/2026}	393.61 (N.A.) {393.61}	40.00	24.00
		109	DEVELOPMENT OF SIX LANE ACCESS CONTROLLED GREEN FIELD HIGHWAY FROM KAVULAKUNTALA (KM.196+000) TO NARA (NHAI) (N24002215)	2-2023	2/2027 (N.A.) {2/2027}	1,092.18 (N.A.) {1,092.18}	0.14	N.A.
		110	ACCESS CONTROLLED HIGHWAY OF 4 LANE WITH PAVED SHOULDERS FROM TN/AP BORDER (DESIGN CHAINAGE KM 61+51 (NHAI) (N24002217)	12-2024	12/2026 (N.A.) {12/2026}	1,346.82 (N.A.) {1,346.82}	37.35	7.40
	<u>WATER RESOURCES</u>	111	POLAVARAM IRRIGATION PROJECT (PPA) (N30000002)	2-2009	3/2020 (Mar-2027) {12/2027}	10,151.04 (N.A.) {55,548.87}	23,775.68	76.00
	<u>CIVIL AVIATION</u>	112	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (Jun-2025) {6/2025}	645.63 (732.00) {732.00}	693.71	99.72
	<u>POWER</u>	113	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	24,213.84	96.49
		114	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	3,306.40	15.74
<u>ARUNACHAL PRADESH</u>								

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	115	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (Mar-2024) {12/2024}	180.57 (244.10) {180.57}	160.46	96.62
		116	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (Jun-2025) {12/2025}	1,718.59 (1,718.59) {1,718.59}	728.21	73.64
		117	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (May-2023) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59
		118	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA- HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (Feb-2025) {2/2025}	301.06 (N.A.) {301.06}	198.22	81.06
		119	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	398.18	95.84
		120	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	194.62	42.69
		121	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (Aug-2024) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		122	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (Feb-2024) {6/2025}	184.88 (N.A.) {184.88}	99.32	97.42
		123	HUNLI TO HAYULIANG PKG-1 (NHIDCL) (N24002222)	2-2024	2/2028 (N.A.) {2/2028}	1,262.43 (N.A.) {1,262.43}	12.12	2.35

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		124	HUNLI TO ITHUN BRIDGE SECTION (NHIDCL) (N24002223)	2-2024	1/2027 (N.A.) {1/2027}	275.50 (N.A.) {275.50}	7.61	6.01
		125	PANGO TO JORGING ROAD PKG-1 (NHIDCL) (N24002224)	1-2024	7/2027 (N.A.) {7/2027}	898.19 (N.A.) {898.19}	7.08	4.06
ASSAM	CIVIL AVIATION	126	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (Aug-2025) {8/2025}	1,142.00 (N.A.) {2,333.00}	1,884.13	87.93
	COAL	127	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290)	7-2022	11/2030 (N.A.) {11/2030}	159.77 (N.A.) {159.77}	81.45	N.A.
		128	TIRAP OCP (CIL) (N06000291)	11-2022	11/2027 (N.A.) {11/2027}	289.46 (N.A.) {289.46}	105.59	N.A.
	HEALTH AND FAMILY WELFARE	129	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (Apr-2023) {6/2025}	875.00 (873.92) {860.00}	787.90	99.52
	PETROLEUM	130	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (Dec-2024) {6/2025}	543.91 (726.93) {726.93}	491.56	93.95
		131	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	16,013.82	74.01
		132	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	9,447.83	85.06
		133	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (May-2026) {5/2026}	412.00 (595.20) {595.20}	396.08	82.80
		134	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (Sep-2026) {9/2026}	277.00 (N.A.) {277.00}	180.17	66.40

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		135	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (Apr-2025) {7/2025}	860.00 (N.A.) {860.00}	535.46	96.50
		136	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (Mar-2024) {6/2025}	430.76 (N.A.) {430.76}	319.86	83.66
		137	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	86.75	33.10
		138	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (Jul-2027) {7/2027}	156.36 (156.36) {156.36}	41.02	31.50
		139	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (Jul-2027) {7/2027}	384.04 (N.A.) {384.04}	94.00	34.40
		140	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	97.22	91.00
		141	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	255.51	56.10
		142	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	172.04	45.30
		143	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	99.52	23.80
	RAILWAYS	144	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2026 (N.A.) {3/2027}	4,059.65 (N.A.) {4,983.94}	3,652.94	92.31
	ROAD TRANSPORT AND HIGHWAYS	145	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {6/2025}	437.39 (N.A.) {437.39}	574.56	96.95

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		146	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DSIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	515.52	76.95
		147	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH- 52 (NHIDCL) (N24000431)	1-1991	6/2019 (Jun-2019) {7/2025}	520.01 (N.A.) {520.01}	305.76	97.90
		148	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (Jul-2021) {12/2025}	289.99 (N.A.) {289.99}	233.23	88.03
		149	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {7/2025}	294.17 (N.A.) {294.17}	389.75	97.88
		150	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {7/2025}	252.00 (N.A.) {330.30}	219.65	91.31
		151	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	217.18	97.76
		152	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (Jun-2025) {8/2025}	216.49 (241.52) {216.49}	111.59	85.83
		153	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,408.80	62.10
		154	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (May-2025) {12/2025}	261.13 (N.A.) {261.13}	68.75	57.42
		155	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (Apr-2025) {12/2025}	217.50 (N.A.) {217.50}	88.99	68.03

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		156	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.76	100.00
		157	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	158.15	81.63
		158	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (1,019.17) {925.47}	192.50	30.65
		159	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	335.20	66.96
		160	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {5/2025}	625.64 (N.A.) {625.64}	556.44	100.00
		161	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {7/2025}	204.10 (N.A.) {204.10}	143.45	96.02
		162	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {6/2025}	909.02 (N.A.) {909.02}	532.44	98.92
		163	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (Sep-2024) {6/2024}	175.00 (N.A.) {175.00}	200.80	100.00
		164	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION-HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	654.60	77.10
		165	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {5/2025}	457.72 (N.A.) {457.72}	366.34	100.00
		166	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	110.76	35.70
		167	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {7/2025}	458.59 (N.A.) {458.59}	198.15	65.62

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		168	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {3/2026}	535.03 (N.A.) {535.03}	102.23	34.15
		169	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	409.15	67.30
		170	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	393.82	65.95
		171	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	454.34	63.70
		172	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	305.73	94.97
		173	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	290.20	95.71
		174	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	537.09	46.78
		175	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	304.61	27.07
		176	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	422.31	25.57
		177	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	242.91	73.50

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		178	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	129.18	16.28
		179	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.87	100.00
		180	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	537.26	38.60
		181	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	983.58	64.03
		182	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	297.50	54.88
		183	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	404.51	68.80
		184	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	279.87	42.68
		185	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY) (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	183.63	45.53
		186	BILASIPURA- GUWAHATI ROAD PKG-1 (NHIDCL) (N24002225)	2-2024	8/2027 (N.A.) {8/2027}	1,081.15 (N.A.) {1,081.15}	33.93	2.76
		187	SILCHAR-JIRIBAM PKG-1 (NHIDCL) (N24002226)	1-2024	1/2028 (N.A.) {1/2028}	957.95 (N.A.) {957.95}	0.00	16.25
		188	BILASIPURA- GUWAHATI ROAD PKG-2 (NHIDCL) (N24002229)	11-2023	6/2027 (N.A.) {6/2027}	1,338.61 (N.A.) {1,338.61}	0.50	N.A.

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		189	BADARPUR ? CHURABARI PKG-6 (NHIDCL) (N24002230)	3-2024	3/2027 (N.A.) {3/2027}	870.00 (N.A.) {870.00}	0.00	N.A.
		190	KARIMGANI - SUTARKANDI SECTION ON SILCHAR-CHURABARI PKG-7 (NHIDCL) (N24002231)	2-2024	2/2027 (N.A.) {2/2027}	791.79 (N.A.) {791.79}	0.00	N.A.
		191	CONSTRUCTION OF 4 LANE GAURIPUR BYPASS ON NH-17 IN THE STATE OF ASSAM (MoRTH) (N24002237)	3-2024	10/2026 (N.A.) {10/2026}	421.15 (N.A.) {421.15}	0.00	N.A.
		192	CONSTRUCTION OF 2 LANE BARPETA BYPASS FROM KM 77+900(BARADI) TO KM 86+150(DEURIKUCHI) (LENGTH=8.25K (MoRTH) (N24002238)	3-2023	8/2026 (N.A.) {8/2026}	173.65 (N.A.) {173.65}	0.00	N.A.
		193	SILCHAR- CHURABARI PKG-5 (NHIDCL) (N24002243)	2-2024	10/2027 (N.A.) {10/2027}	1,258.13 (N.A.) {1,258.13}	0.00	N.A.
BIHAR	CIVIL AVIATION	194	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II (AAI) (N04000082)	5-2018	10/2022 (Jun-2025) {6/2025}	1,216.90 (N.A.) {1,216.90}	1,008.79	89.66
		195	DARBHANGA:DEVELOPMENT OF NEW CIVIL ENCLAVE AT DARBHANGA, BIHAR. SH- CONSTRUCTION OF NEW TERMINAL BUI (AAI) (N04000112)	7-2024	7/2026 (N.A.) {7/2026}	911.66 (N.A.) {911.66}	122.51	18.00
	DEPARTMENT OF HIGHER EDUCATION	196	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA (CPWD EDUCATION) (N28000100)	2-2016	6/2017 (N.A.) {1/2024}	496.18 (496.00) {460.00}	390.15	100.00
		197	PERMANENT CAMPUS FOR IIM BODH GAYA (CPWD EDUCATION) (N42000009)	9-2018	9/2020 (N.A.) {3/2025}	375.00 (N.A.) {375.00}	342.18	100.00
	PETROLEUM	198	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA (IOCL) (N16000386)	1-2020	4/2023 (Aug-2026) {8/2026}	14,810.00 (18,113.00) {18,113.00}	10,898.63	85.70
		199	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA (IOCL) (N16000423)	6-2019	12/2029 (Mar-2030) {3/2030}	163.00 (N.A.) {163.00}	95.19	40.10

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		200	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI (IOCL) (N16000453)	1-2022	4/2025 (N.A.) {5/2026}	389.00 (N.A.) {389.00}	36.61	33.70
		201	CITY GAS DISTRIBUTION PROJECTS AT GOPALGANJ SIWAN WEST CHAMPARAN EAST CHAMPARAN AND DEORIA DISTRICTS (BPCL) (N16000523)	12-2022	6/2030 (N.A.) {6/2030}	3,919.00 (N.A.) {3,919.00}	376.96	13.30
		202	CITY GAS DISTRIBUTION PROJECTS AT DARBHANGA, MADHUBANI, SUPAUL, SITAMARHI AND SHEOHAR DISTRICTS (BPCL) (N16000524)	12-2022	3/2030 (N.A.) {3/2030}	3,638.00 (N.A.) {3,638.00}	381.17	19.70
	POWER	203	BARH STPP(3X660MW) NTPC (NTPC) (180100242)	2-2005	10/2011 (Jul-2023) {3/2025}	8,692.97 (21,312.11) {21,312.11}	22,290.14	95.00
		204	BUXAR THERMAL POWER PLANT (1320 MW) (SJVN) (N18000194)	3-2019	1/2024 (N.A.) {10/2025}	10,439.09 (N.A.) {14,390.09}	11,676.00	90.92
		205	EASTERN REGION EXPANSION SCHEME: 43 [ERES: 43] (PGCIL) (N18000421)	5-2025	5/2026 (N.A.) {5/2026}	343.00 (N.A.) {343.00}	0.00	N.A.
		206	EASTERN REGION EXPANSION SCHEME: 44 [ERES: 44] (PGCIL) (N18000422)	5-2025	5/2026 (N.A.) {5/2026}	409.00 (N.A.) {409.00}	0.00	N.A.
	RAILWAYS	207	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) (ECR) (220100257)	4-1997	12/2024 (N.A.) {3/2027}	614.45 (614.45) {614.45}	483.35	52.00
		208	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR (ECR) (220100303)	4-2003	12/2014 (N.A.) {12/2026}	2,066.78 (2,087.36) {2,087.36}	2,334.96	73.00
		209	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR (NFR) (N22000087)	9-2006	12/2024 (N.A.) {6/2025}	2,650.00 (2,132.03) {4,412.25}	3,917.04	90.00
		210	SAKRI-HASANPUR ROAD (NL) (ECR) (N22000171)	4-1999	(N.A.) {3/2027}	325.00 (735.20) {735.20}	603.44	78.00
		211	ARARIA-SUPAUL (NL) (ECR) (N22000177)	4-2008	3/2024 (N.A.) {5/2025}	1,605.17 (1,605.17) {1,605.17}	1,697.58	65.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		212	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC (ECR) (N22000181)	4-2009	3/2022 (N.A.) {3/2026}	819.00 (548.00) {783.83}	544.31	75.00
		213	SAMASTIPUR-DARBANGHA (ECR) (N22000329)	5-2015	3/2025 (N.A.) {10/2025}	519.33 (519.33) {519.33}	640.68	80.00
		214	KIUL - GAYA DOUBLING PROJECT (ECR) (N22000349)	12-2015	9/2024 (N.A.) {2/2025}	2,462.11 (1,200.20) {1,771.07}	1,866.29	99.00
		215	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE (ECR) (N22000350)	12-2015	12/2024 (N.A.) {12/2025}	2,373.64 (1,491.47) {1,600.00}	1,763.21	77.00
		216	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM (ECR) (N22000472)	4-2016	12/2024 (N.A.) {6/2025}	1,215.54 (1,215.54) {1,215.54}	1,577.26	91.00
		217	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM (ECR) (N22000473)	4-2016	6/2024 (N.A.) {5/2025}	1,586.22 (1,185.73) {1,300.00}	1,477.91	96.00
		218	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN- BIHARSHARIF, (ECR) (N22000476)	4-1991	3/2023 (N.A.) {5/2025}	1,473.30 (803.09) {2,722.16}	2,786.29	90.00
		219	BARAUNI- BACHWARA 3RD AND 4TH LINE (ECR) (N22000524)	7-2022	7/2027 (N.A.) {12/2025}	486.00 (N.A.) {486.00}	128.43	33.00
		220	JHAJHA - BATIA (UMBRELLA WORK PB#23/2018-19/NR) (ECR) (N22000526)	2-2019	6/2028 (N.A.) {12/2026}	496.47 (N.A.) {496.47}	22.53	N.A.
		221	SONENAGAR BYE PASS LINE FROM CHIRALAPOTHU TO BAGHA BISHUNPUR (ECR) (N22000528)	10-2022	10/2027 (N.A.) {12/2026}	234.00 (223.69) {223.69}	22.57	N.A.
		222	KATIHAR-KUMEDPUR AND KATIHAR- MUKURIA (64.5 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NFR) (N22000570)	8-2022	8/2027 (N.A.) {8/2026}	745.00 (N.A.) {942.64}	336.83	35.00
	ROAD TRANSPORT AND WATERWAYS	223	PATNA-MUZAFFARPUR (NHAI) (N24000165)	8-2010	2/2013 (N.A.) {6/2025}	671.30 (N.A.) {671.30}	1,830.13	98.87

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Highways	224	4-LANNING OF CHAPRA-HAJIPUR (NHAI) (N24000187)	1-2011	7/2013 (Jan-2026) {1/2026}	575.00 (N.A.) {575.00}	573.48	89.81
		225	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR (MoRTH) (N24000382)	1-2014	10/2019 (Jun-2025) {6/2025}	675.00 (N.A.) {780.77}	764.69	96.00
		226	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 (NHAI) (N24000480)	12-2015	4/2019 (Mar-2025) {7/2025}	1,041.10 (567.00) {639.58}	553.73	97.58
		227	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 (NHAI) (N24000507)	12-2015	12/2019 (N.A.) {8/2025}	1,167.45 (N.A.) {1,182.94}	753.72	99.43
		228	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 (MoRTH) (N24000531)	2-2016	11/2018 (N.A.) {5/2025}	319.68 (N.A.) {503.28}	453.00	99.00
		229	CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-I- KM 40.00 TO KM 65.400 AND K (MoRTH) (N24000576)	2-2016	5/2016 (N.A.) {5/2025}	178.85 (N.A.) {278.54}	232.61	98.00
		230	PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-III-KM 156.5 (MoRTH) (N24000578)	2-2016	5/2016 (N.A.) {5/2025}	553.30 (N.A.) {706.39}	712.38	98.00
		231	FOUR LANING OF GAYA-HISUA-RAJGIRI- NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR (MoRTH) (N24000579)	1-2014	10/2016 (Jun-2025) {6/2025}	1,408.85 (N.A.) {2,138.16}	1,738.55	97.00
		232	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN (NHAI) (N24000665)	3-2017	3/2020 (Dec-2025) {12/2025}	672.89 (893.92) {893.92}	714.74	86.71

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		233	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 (NHAI) (N24000696)	8-2017	2/2022 (Oct-2024) {6/2025}	950.64 (1,161.00) {1,168.33}	1,156.29	99.53
		234	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 (NHAI) (N24000714)	12-2017	10/2024 (Apr-2025) {12/2026}	2,598.00 (N.A.) {1,978.01}	1,410.14	77.46
		235	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I (NHAI) (N24000723)	1-2018	12/2021 (Aug-2025) {12/2025}	573.70 (644.50) {726.99}	492.33	82.27
		236	DEVELOPMENT OF NEWLY DECLARED NH- 527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER (NHAI) (N24000813)	3-2018	11/2021 (Dec-2024) {8/2025}	496.20 (470.18) {470.18}	399.41	98.25
		237	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND (MoRTH) (N24000943)	9-2018	6/2024 (May-2026) {5/2026}	1,478.40 (N.A.) {1,478.40}	941.27	70.00
		238	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 (MoRTH) (N24001201)	2-2019	9/2024 (N.A.) {9/2026}	2,926.42 (N.A.) {2,926.42}	1,300.42	56.00
		239	BALANCE WORK OF 4- LANING OF PATNA- GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT (NHAI) (N24001303)	10-2013	12/2020 (Dec-2024) {12/2024}	649.90 (N.A.) {750.00}	711.53	98.30
		240	BALANCE WORK OF 4- LANING OF PATNA- GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE (NHAI) (N24001304)	10-2013	11/2020 (Dec-2024) {12/2024}	446.97 (598.48) {740.50}	638.80	96.30

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		241	BALANCE WORK OF 4- L ANING OF PATNA- GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA (NHAI) (N24001305)	10-2013	11/2020 (Dec-2024) {12/2024}	464.09 (605.53) {765.12}	698.25	97.30
		242	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N (NHAI) (N24001371)	10-2019	8/2023 (Apr-2026) {4/2026}	1,101.99 (N.A.) {1,101.99}	874.95	77.40
		243	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH- 119D (PKG-III) (NHAI) (N24001697)	2-2023	2/2025 (N.A.) {12/2025}	1,358.00 (N.A.) {1,358.00}	188.08	19.06
		244	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH (NHAI) (N24001698)	8-2022	8/2024 (Dec-2025) {12/2025}	1,198.02 (N.A.) {1,198.02}	14.85	N.A.
		245	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT- GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH-3 (NHAI) (N24001699)	3-2022	12/2024 (Dec-2025) {12/2025}	312.58 (N.A.) {312.58}	196.82	82.06
		246	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO (NHAI) (N24001700)	12-2021	3/2024 (Dec-2024) {12/2024}	552.55 (553.00) {553.00}	378.25	86.60
		247	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU (NHAI) (N24001701)	4-2022	4/2024 (Sep-2025) {9/2025}	1,769.50 (N.A.) {1,769.50}	51.61	N.A.
		248	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT-GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH: (NHAI) (N24001702)	12-2021	9/2024 (N.A.) {6/2025}	184.90 (185.00) {185.00}	164.63	99.78

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		249	6 L OF AURANGABAD TO BIHAR- JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N (NHAI) (N24001703)	2-2022	5/2025 (N.A.) {5/2025}	786.81 (787.00) {787.00}	0.00	8.30
		250	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI (NHAI) (N24001704)	3-2021	3/2024 (Sep-2025) {9/2025}	1,020.84 (N.A.) {1,020.84}	118.96	N.A.
		251	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C (NHAI) (N24001705)	3-2022	3/2024 (Dec-2025) {12/2025}	1,485.66 (N.A.) {1,485.66}	35.16	N.A.
		252	BAKHTIYARPUR RAJauli PKG-II FROM KM 54.405 TO KM 101.630 NH20 (NHAI) (N24001709)	9-2020	4/2023 (Dec-2024) {12/2024}	897.45 (N.A.) {1,090.00}	1,037.63	97.85
		253	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO (NHAI) (N24001712)	8-2020	7/2023 (May-2025) {5/2025}	690.00 (N.A.) {690.00}	770.73	98.80
		254	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI?MOTIHARI- RAXAUL SECTION OF NH-28A FRO (NHAI) (N24001715)	12-2018	10/2020 (N.A.) {1/2024}	333.60 (466.59) {461.41}	460.38	100.00
		255	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH 122B FROM KM 29.730 TO KM 72.348 IN STATE OF BIH (MoRTH) (N24001870)	2-2022	11/2024 (N.A.) {11/2025}	624.43 (N.A.) {624.43}	280.98	82.00
		256	WIDENING AND STRENGTHENING FROM KM 70.15 TO KM 121.025 OF NH-80 (MoRTH) (N24001875)	3-2021	1/2025 (N.A.) {6/2025}	477.54 (N.A.) {477.54}	334.36	90.00
		257	WIDENING and STRENGTHENING FROM KM132.895 TO KM 190.15 NH-80 (MoRTH) (N24001876)	3-2021	3/2024 (N.A.) {9/2025}	566.15 (N.A.) {566.15}	239.20	56.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		258	CONSTRUCTION OF NEW 4-LANE BRIDGE (PARALLEL TO EXISTING VIKRAMASHILA SETU)FROM KM 8+920 TO KM 13+375 (MoRTH) (N24001877)	7-2020	5/2027 (N.A.) {5/2027}	1,110.23 (N.A.) {1,110.23}	425.49	40.00
		259	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH-319A FROM KM 0 TO KM 45 IN STATE OF BIHAR UNDER (MoRTH) (N24001878)	2-2022	12/2024 (N.A.) {7/2025}	427.29 (N.A.) {427.29}	197.04	78.00
		260	CONSTRUCTION OF PROPOSED 4_LANE REVELGUNJ BYPASS NH-19 IN THE STATE OF BIHAR ON EPC MODE CONNECTING (MoRTH) (N24001879)	3-2022	7/2025 (N.A.) {7/2025}	295.24 (N.A.) {295.24}	77.05	53.00
		261	CONSTRUCTION OF 6- LANE BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD (NH- (NHAI) (N24002062)	3-2023	9/2027 (N.A.) {9/2027}	3,012.27 (N.A.) {3,012.27}	263.36	9.12
		262	BALANCE WORK - WB-10 (GANDAK BRIDGE) KM 402.00 TO KM 440.00 (DEVANPUR - KOTWA) (NHAI) (N24002063)	12-2021	1/2024 (N.A.) {3/2026}	210.05 (N.A.) {210.05}	104.35	69.00
		263	PERMANENT RECTIFICATION OF 3 NOS. OF BLACK SPOTS IN PROJECT HIGHWAY NH-27 OF U.P BORDER - DEWAPUR - (NHAI) (N24002064)	12-2022	12/2025 (N.A.) {12/2025}	381.80 (N.A.) {381.80}	115.37	48.00
		264	4L GREENFIELD ALIGNMENT OF AMAS TO SHIVRAMPUR FROM 0.000 KM. TO 55.002 KM. OF NH 119 D (PKG-I) (NHAI) (N24002065)	2-2022	3/2025 (N.A.) {3/2025}	1,390.92 (N.A.) {1,390.92}	17.54	22.56
		265	4L GREENFIELD ALIGNMENT OF SHIVRAMPUR TO RAMNAGAR FROM KM. 55.002 TO KM. 109.300 OF NH 119 D (PKG-I) (NHAI) (N24002066)	2-2022	7/2025 (N.A.) {7/2025}	1,494.31 (N.A.) {1,494.31}	38.28	4.59

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		266	IMPROVEMENT OF 2 LANE WITH PAVED SHOULDER OF STRETCH FROM BIKRAMGANJ DAWATH MELAYABAGH NAWANAGR -DUM (MoRTH) (N24002133)	3-2021	3/2025 (N.A.) {6/2025}	178.63 (N.A.) {178.63}	116.16	91.00
		267	CONSTRUCTION OF 4 LANE ROB AND ITS APPROACHES AT THE LEVEL OF CROSSING (L C NO. 29-B) OF KM 29 (EKAN (MoRTH) (N24002193)	3-2023	7/2026 (N.A.) {7/2026}	201.08 (N.A.) {201.08}	25.42	25.00
		268	CONSTRUCTION OF 6-LANE ELEVATED / EXTRA DOSE CABLE BRIDGE ON RIVER GANGA PARALLEL TO AND WESTERN SID (MoRTH) (N24002194)	1-2024	11/2027 (N.A.) {11/2027}	3,064.45 (N.A.) {3,064.45}	78.87	2.00
		269	ESTIMATE FOR IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM RAMNAGAR TO ROSEDA FROM (KM 3.500 TO 4 (MoRTH) (N24002195)	1-2022	4/2026 (N.A.) {4/2026}	495.16 (N.A.) {495.16}	129.17	10.00
		270	CONSTRUCTION OF BHABHUA BYPASS FROM CH. 10+800 (DESIGN CH. 10+800) TO CH. 19+860 (DESIGN CH. 18+150) (MoRTH) (N24002196)	2-2022	3/2026 (N.A.) {7/2026}	179.86 (N.A.) {179.86}	25.07	0.03
		271	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM JUNCTION OF NH-22 NEAR HAJIPUR TO JUNCTION OF NH-12 (MoRTH) (N24002197)	2-2024	2/2026 (N.A.) {2/2026}	226.15 (N.A.) {226.15}	9.77	13.00
		272	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF BH/WBBORDER-AMDABAD-MANIHARI SECTION FROM DESIGN KM (MoRTH) (N24002198)	1-2022	3/2026 (N.A.) {3/2026}	353.27 (N.A.) {353.27}	25.33	N.A.
		273	PERMANENT RECTIFICATION OF 4 NOS. OF BLACKSPOTS ON NH 27 OF KOTWA MEHSI MUZAFFARPUR SECTION FROM (NHAI) (N24002220)	12-2022	11/2026 (N.A.) {11/2026}	410.75 (N.A.) {410.75}	35.27	25.07

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		274	4L OF GREENFIELD ALIGNMENT FROM KM. 47.000 TO KM. 89.210 OF BALBHADARPUR TO BELA NAWDA SECTION OF NH (NHAI) (N24002221)	2-2022	3/2026 (N.A.) {3/2026}	2,185.75 (N.A.) {2,185.75}	513.47	11.48
	URBAN DEVELOPMENT	275	PATNA METRO RAIL CORPORATION LIMITED (PATNA METRO RAI) (N28000148)	2-2019	6/2024 (N.A.) {9/2024}	13,365.77 (N.A.) {13,925.50}	3,158.18	44.00
	WATER RESOURCES	276	SEWER NETWORK SPS AND STP BEGUSARAI (BUIDCO) (N30000026)	3-2018	7/2021 (Dec-2019) {4/2025}	230.06 (N.A.) {230.06}	261.47	97.00
		277	I AND D AND STP WORKS FOR BHAGALPUR (BUIDCO) (N30000027)	10-2017	9/2020 (Nov-2020) {4/2025}	254.13 (413.29) {413.29}	126.67	90.00
		278	SEWER NETWORKS SPS AND STP HAJIPUR (BUIDCO) (N30000035)	3-2018	8/2021 (Mar-2018) {6/2025}	305.19 (N.A.) {305.19}	346.46	95.00
		279	SEWER NETWORKS, SPS AND STP, MUNGER (BUIDCO) (N30000036)	3-2018	10/2021 (Mar-2018) {6/2024}	294.02 (350.79) {522.85}	428.70	100.00
		280	SAIDPUR SEWER NETWORK PATNA (BUIDCO) (N30000039)	4-2015	1/2021 (N.A.) {6/2022}	268.63 (N.A.) {493.85}	491.13	100.00
		281	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK (BUIDCO) (N30000044)	3-2017	5/2021 (Mar-2017) {2/2023}	277.42 (253.98) {277.42}	355.31	100.00
		282	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA (BUIDCO) (N30000050)	8-2017	6/2022 (N.A.) {12/2025}	578.89 (453.83) {578.89}	164.87	52.00
		283	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA (BUIDCO) (N30000051)	8-2017	6/2022 (N.A.) {12/2025}	824.00 (734.09) {824.00}	384.17	55.00
CHHATTISGARH	COAL	284	GEVRA EXPANSION OCP (SECL) (35-70) MTY (SECL) (060100093)	6-2010	3/2023 (Mar-2026) {3/2026}	11,816.40 (N.A.) {11,816.40}	6,596.25	77.20
		285	PELMA OCP(15.00MTY) (SECL) (N06000045)	10-2022	3/2023 (N.A.) {3/2033}	1,624.59 (N.A.) {1,725.04}	15.53	17.00
		286	CHHAL OC SEAM -III (6.00 MTY) (SECL) (N06000104)	12-2013	3/2022 (Jun-2025) {6/2025}	610.63 (N.A.) {610.63}	576.24	85.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		287	AMERA OC RCE (SECL) (N06000123)	2-2015	3/2018 (Mar-2026) {3/2026}	335.97 (N.A.) {335.97}	86.98	42.00
		288	AMGAON OPENCASST PROJECT RCE (SECL) (N06000135)	7-2015	3/2020 (Mar-2026) {3/2026}	316.10 (N.A.) {316.10}	188.33	71.00
		289	MAHAMAYA OPENCASST PROJECT (SECL) (N06000164)	5-2018	3/2026 (N.A.) {3/2026}	410.26 (N.A.) {410.26}	180.18	38.00
		290	JHIRIA WEST OPENCASST PROJECT (SECL) (N06000166)	1-2024	3/2029 (N.A.) {3/2029}	366.94 (N.A.) {366.94}	33.37	41.00
		291	BAROUD OC EXPANSION (3-10 MTY) (SECL) (N06000197)	8-2020	3/2029 (N.A.) {3/2029}	2,309.80 (N.A.) {2,309.80}	911.51	41.00
		292	JAMPALI OCP RCE (SECL) (N06000198)	5-2020	3/2024 (Mar-2025) {6/2025}	278.64 (N.A.) {278.64}	209.34	82.00
		293	PORDA CHINTAPANI OCP (10 MTY) (SECL) (N06000199)	12-2020	3/2029 (N.A.) {3/2029}	2,310.12 (N.A.) {2,310.12}	47.65	10.00
		294	DIPKA OC EXPANSION 40 MTY (SECL) (N06000200)	12-2020	3/2029 (N.A.) {3/2029}	5,241.40 (N.A.) {5,241.40}	2,820.23	37.30
		295	JAGANNATHPUR OC RCE (3.0 MTY) (SECL) (N06000232)	7-2016	3/2020 (Mar-2026) {3/2026}	459.49 (N.A.) {459.49}	263.51	92.00
		296	KATKONA RO UG PROJECT (1.74 MTY) (SECL) (N06000274)	1-2023	3/2029 (N.A.) {3/2029}	329.22 (N.A.) {329.22}	60.38	2.00
	DEPARTMENT OF HIGHER EDUCATION	297	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. (CPWD EDUCATION) (N28000141)	3-2020	7/2022 (Feb-2024) {3/2024}	808.62 (879.22) {808.62}	640.70	100.00
	POWER	298	WESTERN REGION EXPANSION SCHEME XXV (PGCIL) (N18000350)	2-2023	11/2023 (N.A.) {6/2025}	385.84 (N.A.) {385.84}	369.79	93.00
		299	LARA SUPER THERMAL POWER PROJECT, STAGE-II (2X800 MW) (NTPC) (N18000381)	8-2023	6/2028 (N.A.) {6/2028}	15,530.00 (N.A.) {15,530.00}	1,636.45	6.50
	RAILWAYS	300	KIRANDUL - JAGDALPUR DOUBLING (ECOR) (N22000318)	12-2012	3/2020 (N.A.) {3/2024}	1,588.70 (N.A.) {1,553.11}	1,526.84	94.80
		301	JHARSUGUDA-BILASPUR 4TH LINE (SECR) (N22000484)	4-2015	10/2024 (Dec-2023) {12/2025}	2,140.34 (2,135.34) {2,135.34}	2,280.80	88.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		302	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I (IRCON) (N22000489)	4-2013	9/2018 (N.A.) {3/2026}	3,055.00 (N.A.) {3,438.39}	3,117.24	92.80
		303	Gauge conversion of Raipur(Kendri)-Dhamtari and Abhanpur-Rajim branch (67.20 km) (SECR) (N22000572)	7-2011	10/2024 (N.A.) {6/2025}	1,171.30 (N.A.) {1,171.30}	617.69	82.00
		304	NIPANIA-BHATAPRA (14.4 KM) 4TH LINE (PB#72/NR/2022-23) (SECR) (N22000573)	9-2022	12/2026 (N.A.) {12/2026}	170.49 (N.A.) {170.49}	0.13	2.00
		305	4TH LINE - BHATAPARA-HATHBAND (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000574)	12-2022	12/2026 (N.A.) {12/2026}	177.03 (N.A.) {177.03}	6.23	2.00
		306	4TH LINE - BHILAI-BHILAI NAGAR (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000575)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {177.34}	1.72	2.00
		307	4TH LINE - DADHAPARA-BELHA (9.2 KM) (PB#72/NR/2022-23) (SECR) (N22000576)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {169.06}	15.66	30.00
		308	4TH LINE - RAJNANDGAON-DONGARHGARH (31.2 KM) (PB#72/NR/2022-23) (SECR) (N22000577)	9-2022	9/2026 (N.A.) {9/2026}	328.34 (N.A.) {328.34}	36.65	20.00
		309	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (N22000579)	9-2022	9/2026 (N.A.) {9/2026}	167.64 (N.A.) {167.64}	0.00	N.A.
		310	DOUBLING OF BORIDAND - AMBIKAPUR () SURAJPUR (SECR) (N22000580)	6-2022	6/2030 (N.A.) {3/2027}	1,376.20 (1,242.94) {1,242.94}	193.79	12.00
		311	DALLIRAJHARA - ROWGHAT (95 KM) {PART OF DALLIRAJHARA-JAGDALPUR (235 KM)} (RVNL) (N22000602)	3-2008	6/2025 (N.A.) {6/2025}	1,627.56 (N.A.) {1,627.56}	1,349.09	N.A.
		312	CHIRIMIRI-NAGPUR HALT (SECR) (N22000616)	10-2018	6/2030 (N.A.) {6/2030}	241.00 (N.A.) {241.00}	0.00	N.A.
	ROAD TRANSPORT AND HIGHWAYS	313	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 (MoRTH) (N24001217)	1-2016	8/2016 (N.A.) {6/2025}	497.14 (572.66) {572.66}	385.27	60.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		314	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION (MoRTH) (N24001221)	1-2016	10/2016 (N.A.) {3/2025}	624.98 (N.A.) {731.50}	620.67	100.00
		315	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI (MoRTH) (N24001222)	3-2016	7/2016 (N.A.) {12/2025}	452.94 (N.A.) {435.61}	322.59	70.00
		316	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. (MoRTH) (N24001227)	3-2018	1/2019 (N.A.) {5/2025}	349.03 (N.A.) {349.03}	316.52	98.00
		317	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A (MoRTH) (N24001228)	11-2017	5/2019 (N.A.) {5/2025}	188.80 (N.A.) {188.80}	136.81	97.00
		318	DEVELOPMENT OF SIX LANE SARGI- BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA (NHAI) (N24001588)	12-2021	1/2025 (N.A.) {12/2025}	1,470.73 (N.A.) {1,470.73}	646.79	79.00
		319	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA (NHAI) (N24001593)	11-2021	9/2024 (N.A.) {4/2026}	1,368.19 (N.A.) {1,368.19}	896.51	96.40
		320	4 LANE OF BILASPUR TO URGAPUR PROJECT (KM 0.00 TO KM 70.2) OF NH-130A (NHAI) (N24001611)	4-2020	3/2024 (N.A.) {12/2025}	1,855.59 (2,523.86) {2,523.86}	594.46	93.03
		321	UP GRADATION OF NH 930 SHERPAR TO KOHKA FROM KM 67.880 TO KM 114.860 TO TWO LANE WITH PAVED SHOULDER (MoRTH) (N24001917)	3-2020	5/2024 (N.A.) {6/2025}	278.97 (N.A.) {278.97}	206.61	87.00
		322	UP GRADATION OF NH 130C ABHANPUR TO PAUND FROM NK KM 0.000 TO KM. 40.380 TO TWO LANE WITH PAVED SHOU (MoRTH) (N24001919)	12-2020	9/2023 (Feb-2025) {6/2025}	193.16 (N.A.) {193.16}	103.83	81.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		323	UPGRADATION OF NH 130A MUNGELI TO PONDII FROM NH KM. 51.600 TO KM. 77.870 KM. 80.970 TO 96.970 TO 2 (MoRTH) (N24001920)	3-2021	9/2024 (N.A.) {5/2025}	218.57 (N.A.) {218.57}	136.26	89.00
		324	DEVELOPMENT OF SIX LANE BASANWAHI-MARANGPURI OF NH 130 CD FROM KM.99+500 TO 124+661 UNDER RAIPUR VIS (NHAI) (N24002017)	3-2022	10/2025 (N.A.) {9/2026}	1,307.16 (N.A.) {1,307.16}	252.68	33.05
		325	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 1 SECTION OF NH 53 FROM CH 0.000 TO CH 44.50 (NHAI) (N24002045)	6-2022	7/2025 (N.A.) {7/2025}	1,828.00 (N.A.) {1,828.00}	543.14	44.72
		326	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 2 SECTION OF NH 53 FROM CH 44+500 TO CH.92+230 I (NHAI) (N24002046)	6-2022	5/2025 (N.A.) {5/2025}	1,958.94 (1,959.00) {1,958.94}	690.46	40.01
	STEEL	327	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 (NMDC) (N12000124)	11-2015	6/2023 (Jul-2024) {12/2025}	2,907.00 (5,427.06) {5,427.06}	2,926.87	79.20
		328	SCREENING PLANT-III AT KIRANDUL (NMDC) (N12000127)	3-2021	8/2024 (N.A.) {1/2026}	2,092.97 (2,718.84) {2,718.84}	1,491.20	70.81
		329	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (NMDC) (N12000130)	7-2021	11/2024 (N.A.) {12/2025}	282.44 (349.75) {349.75}	232.34	80.66
		330	REPLACEMENT OF CONVERTER VESSELS, TRUNNION RINGS, SUPPORT SYSTEM AND INSTALLATION OF SECONDARY EMISS (SAIL) (N12000131)	10-2023	6/2026 (N.A.) {6/2026}	471.83 (N.A.) {471.83}	92.37	24.87
		331	REBUILDING OF COKE OVEN BATTERY NO.7 AND 8 OF BHILAI STEEL PLANT (SAIL) (N12000134)	11-2023	10/2025 (N.A.) {10/2025}	884.10 (N.A.) {884.10}	394.99	69.46

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
DELHI		332	REPLACEMENT OF HOT LEVELLER-1 OF PLATE MILL AT BHILAI STEEL PLANT (SAIL) (N12000137)	7-2024	7/2026 (N.A.) {7/2026}	198.62 (N.A.) {198.62}	0.00	5.74
	URBAN DEVELOPMENT	333	CONSTRUCTION 729 QUARTERS (TYPE II- 180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI (CPWD) (N28000149)	5-2019	9/2020 (Oct-2024) {10/2024}	299.97 (299.97) {299.97}	272.05	92.00
	CIVIL AVIATION	334	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR (AAI) (N04000076)	11-2016	4/2020 (Apr-2024) {4/2024}	303.80 (374.98) {351.21}	344.65	100.00
	DPIIT	335	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE (IICC FOR DPIIT) (N40000002)	11-2017	12/2019 (N.A.) {4/2025}	4,773.00 (N.A.) {5,401.00}	4,969.89	100.00
	FINANCE	336	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA (NPCC) (N07000001)	7-2018	4/2022 (N.A.) {4/2022}	228.50 (N.A.) {220.27}	176.28	85.00
	HOME AFFAIRS	337	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI (CPWD FOR MHA) (N28000071)	10-2013	10/2019 (N.A.) {9/2024}	1,219.21 (2,091.53) {2,091.53}	1,947.12	100.00
		338	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI (CPWD FOR MHA) (N45000002)	6-2019	7/2022 (N.A.) {9/2025}	277.35 (N.A.) {277.35}	107.00	64.00
	RAILWAYS	339	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE (NR) (N22000281)	4-2012	3/2023 (N.A.) {6/2026}	586.36 (N.A.) {699.00}	174.22	45.00
	ROAD TRANSPORT AND HIGHWAYS	340	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR (NHAI) (N24001771)	6-2020	12/2024 (N.A.) {12/2024}	1,479.22 (N.A.) {1,479.22}	1,491.26	99.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		341	6L ACCESS CONTROLLED HIGHWAY FROM DND MAHARANI BAGH JN. WITH JAIPUR PUSHTA ROAD OF NH 148NA FROM (NHAI) (N24001773)	5-2020	7/2024 (N.A.) {9/2025}	1,467.44 (N.A.) {1,942.89}	1,189.56	90.39
		342	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-)0.70 (NHAI) (N24001777)	7-2020	10/2023 (N.A.) {6/2025}	2,171.80 (N.A.) {2,171.80}	958.13	99.99
		343	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) (NHAI) (N24001779)	3-2018	9/2022 (N.A.) {9/2025}	2,507.00 (N.A.) {3,030.73}	1,155.70	95.01
		344	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O (NHAI) (N24001781)	1-2018	10/2021 (N.A.) {6/2025}	2,067.67 (N.A.) {2,160.00}	1,496.49	99.35
		345	DEVELOPMENT OF 6L UER II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM (NHAI) (N24001825)	7-2020	10/2023 (N.A.) {7/2025}	1,894.96 (N.A.) {1,894.96}	741.88	94.65
	TELECOMMUNICATIONS	346	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT (CPWD FOR TELECO) (N28000115)	10-2014	3/2018 (N.A.) {10/2025}	248.20 (N.A.) {248.20}	236.27	98.00
	URBAN DEVELOPMENT	347	DELHI MRTS PHASE-III (DMRC) (N28000056)	9-2011	3/2016 (Aug-2021) {8/2021}	38,585.00 (43,095.35) {40,180.91}	40,614.90	100.00
	I	348	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR (NBCC) (N28000105)	7-2016	(N.A.) {}	2,694.00 (N.A.) {2,694.00}	2,247.61	N.A.
		349	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I (CPWD) (N28000128)	10-2016	7/2021 (N.A.) {6/2024}	1,180.00 (N.A.) {1,100.80}	36.69	2.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		350	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I (CPWD) (N28000129)	10-2016	3/2022 (N.A.) {6/2024}	1,128.00 (N.A.) {1,128.00}	709.96	66.00
		351	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS (DMRC) (N28000135)	7-2019	3/2025 (N.A.) {3/2026}	24,948.65 (N.A.) {24,948.65}	16,065.03	65.67
		352	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI (CPWD) (N28000153)	1-2022	11/2024 (May-2025) {5/2025}	646.52 (N.A.) {646.52}	489.53	93.00
		353	REDEVELOPMENT OF GPRA AT NETAJI NAGAR NEW DELHI PACKAGE 2 (NBCC) (N28000156)	10-2016	3/2024 (Jun-2025) {3/2025}	1,536.72 (N.A.) {1,536.72}	491.35	90.00
	<u>WATER RESOURCES</u>	354	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD ? 10MG/L (DJB) (N30000014)	3-2017	12/2022 (N.A.) {3/2025}	665.78 (N.A.) {665.78}	782.51	100.00
<u>GOA</u>	<u>CIVIL AVIATION</u>	355	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. (AAI) (N04000095)	11-2017	9/2021 (Aug-2025) {8/2025}	255.69 (255.69) {255.69}	119.89	85.00
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	356	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. (CPWD EDUCATION) (N42000002)	5-2019	8/2021 (N.A.) {12/2024}	303.90 (N.A.) {390.40}	360.00	99.30
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	357	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM. 508.000 TO KM. 513.150 INCLUDING APPROACHES ON N (MoRTH) (N24002181)	4-2023	4/2026 (N.A.) {4/2026}	641.46 (N.A.) {641.46}	0.00	N.A.
<u>GUJARAT</u>	<u>CIVIL AVIATION</u>	358	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT (AAI) (N04000088)	1-2018	8/2022 (Dec-2024) {12/2024}	1,405.00 (N.A.) {1,405.00}	1,304.42	100.00
		359	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. (AAI) (N04000093)	8-2018	2/2021 (Mar-2025) {3/2025}	353.25 (N.A.) {353.25}	348.78	100.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		360	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1. (AAI) (N04000099)	6-2022	12/2025 (N.A.) {12/2025}	1,305.00 (1,143.95) {1,143.95}	604.50	57.00
	COAL	361	50 MW WIND POWER PROJECT PART OF 150 MW SECI HYBRID (NLC) (N06000292)	7-2022	6/2025 (Jan-2026) {1/2026}	383.84 (N.A.) {383.84}	303.50	41.00
	PETROLEUM	362	REDEVELOPMENT OF SANTHAL FIELD (ONGC) (N16000279)	2-2017	3/2026 (N.A.) {3/2026}	1,162.56 (N.A.) {1,162.56}	1,156.83	94.10
		363	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY (IOCL) (N16000382)	11-2019	5/2023 (Mar-2024) {6/2025}	5,251.00 (5,894.00) {5,894.00}	4,682.50	99.60
		364	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY (IOCL) (N16000409)	9-2020	8/2024 (Dec-2025) {12/2025}	18,936.00 (N.A.) {18,936.00}	10,871.57	81.90
		365	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM (IOCL) (N16000411)	10-2020	8/2023 (Jun-2025) {6/2025}	1,614.00 (N.A.) {1,614.00}	1,117.38	96.21
		366	REDEVELOPMENT OF LINCH FIELD (ONGC) (N16000428)	4-2021	3/2025 (N.A.) {7/2025}	631.03 (860.04) {860.04}	399.66	75.80
		367	REDEVELOPMENT OF SOBHASAN COMPLEX (ONGC) (N16000431)	8-2021	2/2026 (N.A.) {2/2026}	885.63 (1,286.67) {1,286.67}	584.23	71.40
		368	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD (ONGC) (N16000444)	1-2022	11/2024 (N.A.) {11/2025}	621.40 (N.A.) {621.40}	137.69	21.40
		369	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT (IOCL) (N16000454)	1-2022	9/2024 (N.A.) {5/2026}	328.00 (N.A.) {328.00}	97.01	47.40
		370	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT (ONGC) (N16000477)	5-2022	2/2025 (N.A.) {9/2025}	249.43 (N.A.) {249.43}	209.40	93.00
		371	KALOL REDEVELOPMENT PROJECT (ONGC) (N16000481)	8-2022	3/2027 (N.A.) {3/2027}	1,487.41 (N.A.) {1,487.41}	952.00	60.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		372	OLD PIPE LINE REPLACEMENT (OPRP) GROUP-A (ONGC) (N16000483)	7-2021	7/2025 (N.A.) {7/2025}	173.03 (N.A.) {169.84}	140.45	84.00
		373	REVAMPING OF SV STATIONS, GAS TERMINAL AND KRIBHCO TERMINAL (ONGC) (N16000514)	11-2022	8/2026 (N.A.) {8/2026}	837.34 (N.A.) {837.34}	183.33	45.10
	POWER	374	GUJARAT 200 MW (GUVNL TENDER) (NTPC) (N18000295)	1-2021	7/2022 (Mar-2026) {3/2026}	842.27 (1,049.61) {1,049.61}	769.67	65.10
		375	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) (NTPC) (N18000296)	5-2021	9/2022 (Apr-2025) {4/2025}	674.92 (726.79) {726.79}	572.53	100.00
		376	Bagodara Solar Power Project (SJVN) (N18000297)	5-2021	10/2022 (N.A.) {12/2025}	339.35 (N.A.) {339.35}	317.59	51.22
		377	DAYAPAR WIND ENERGY PROJECT 150MW (NTPC) (N18000319)	11-2021	5/2023 (Jun-2025) {6/2025}	937.80 (N.A.) {937.80}	800.11	100.00
		378	DAYAPAR WIND ENERGY PROJECT 200MW (NTPC) (N18000345)	7-2022	3/2025 (Jan-2026) {1/2026}	1,316.02 (N.A.) {1,316.02}	324.36	26.00
		379	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK) (NTPC) (N18000346)	9-2022	9/2024 (Feb-2026) {2/2026}	7,179.54 (N.A.) {7,179.54}	5,017.87	85.00
		380	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) (NTPC) (N18000349)	11-2022	3/2024 (Mar-2026) {3/2026}	1,442.60 (N.A.) {1,442.60}	793.56	2.00
		381	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK (PGCIL) (N18000357)	3-2023	12/2024 (N.A.) {6/2025}	922.30 (N.A.) {922.30}	823.07	88.70
		382	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT (PGCIL) (N18000358)	3-2023	3/2025 (N.A.) {6/2025}	815.12 (N.A.) {815.12}	738.03	94.60

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		383	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK (PGCIL) (N18000359)	3-2023	12/2024 (N.A.) {6/2025}	966.79 (N.A.) {966.79}	859.00	93.60
		384	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000360)	3-2023	3/2025 (N.A.) {9/2025}	1,167.55 (N.A.) {1,167.55}	950.00	86.10
		385	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000361)	3-2023	3/2025 (N.A.) {9/2025}	2,820.99 (N.A.) {2,820.99}	2,418.00	76.50
		386	KHAVDA 1200MW (4X300MW) IN KHAVDA RE PARK (NTPC) (N18000365)	6-2023	12/2024 (Jan-2026) {1/2026}	6,283.81 (N.A.) {6,283.81}	1,752.69	40.00
		387	DAYAPAR WIND- III (HYBRID TRANCHE-V) (NTPC) (N18000366)	5-2023	1/2025 (Mar-2026) {3/2026}	1,095.01 (N.A.) {1,095.01}	345.26	16.00
		388	TS FOR EVACUATION OF POWER FROM POTENTIAL RE ZONE IN KHAVDA AREA OF GUJARAT UNDER PH-IV PART E3 (PGCIL) (N18000383)	7-2023	7/2025 (N.A.) {8/2025}	334.00 (N.A.) {334.00}	33.54	18.00
		389	TS FOR EVACUATION OF ADDITIONAL 7GW RE POWER FROM KHAVDA RE PARK UNDER PHASE-III PART B [VATAMAN TRA (PGCIL) (N18000384)	12-2023	12/2025 (N.A.) {6/2026}	3,752.00 (N.A.) {3,752.00}	1,365.02	13.90
		390	TS FOR EVACUATION OF POWER FROM 7GW REZ IN KHAVDA AREA UNDER PHASE- IV PART E2 (PGCIL) (N18000390)	5-2024	5/2026 (N.A.) {5/2026}	679.00 (N.A.) {679.00}	47.74	15.00
		391	AUGMENTATION OF TRANSFORMATION CAPACITY AT JAM KHAMBHALIYA PS [GIS] [SPV NAME POWERGRID JAM KHAMBHAL (PGCIL) (N18000398)	10-2024	7/2026 (N.A.) {7/2026}	329.00 (N.A.) {329.00}	0.00	1.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		392	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000400)	10-2024	10/2026 (N.A.) {10/2026}	4,766.00 (N.A.) {4,766.00}	280.03	4.20
		393	PROVISION OF DYNAMIC REACTIVE COMPENSATION AT KHAVDA POOLING STATION 1 [KPS1] AND KHAVDA POOLING STA (PGCIL) (N18000402)	11-2024	11/2026 (N.A.) {11/2026}	501.00 (N.A.) {501.00}	0.00	1.00
		394	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000405)	11-2024	5/2029 (N.A.) {5/2029}	24,819.00 (N.A.) {24,819.00}	1,454.40	1.00
		395	600 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000406)	4-2022	3/2026 (N.A.) {3/2026}	4,100.45 (N.A.) {4,100.45}	10.36	9.00
		396	AUGMENTATION OF TRANSFORMATION CAPACITY AT KPS2 AND KPS2 (PGCIL) (N18000411)	3-2025	3/2027 (N.A.) {3/2027}	466.00 (N.A.) {466.00}	0.00	N.A.
		397	AUGMENTATION OF BANASKANTHA (RAGHANESDA) PS (GIS) (PGCIL) (N18000412)	3-2025	3/2027 (N.A.) {3/2027}	172.00 (N.A.) {172.00}	0.00	N.A.
	RAILWAYS	398	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) (WR) (N22000142)	4-2011	3/2021 (Oct-2026) {10/2026}	844.10 (844.10) {844.10}	599.22	41.00
		399	ANAND GODHRA DOUBLING PROJECT 79 KMS (WR) (N22000504)	4-2017	12/2024 (Jun-2025) {6/2025}	692.26 (692.26) {692.26}	683.44	99.00
		400	4TH LINE BETWEEN BAREJADI NANDEJ (GERATPUR)- SANAND (38.20 KM) (AHMEDABAD BYPASS). (WR) (N22000532)	2-2023	3/2027 (Feb-2027) {2/2027}	961.67 (961.67) {961.67}	103.14	16.00
		401	QUADRUPLING BETWEEN GANDHIDHAM - ADIPUR WITH Y CONNECTION AT ADIPUR FOR PROVIDING DIRECT ENTRY TOWAR (WR) (N22000533)	2-2023	12/2025 (Dec-2025) {12/2025}	152.44 (152.44) {152.44}	19.50	60.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		402	RAJKOT-KANALUS (111.20 KM) (WR) (N22000535)	10-2021	10/2026 (Jun-2026) {6/2026}	1,080.58 (1,080.58) {1,080.58}	304.58	70.00
		403	HIMMATNAGAR-KHEDBRAHMA (54.83 KM) (WR) (N22000537)	6-2022	2/2030 (Jun-2025) {6/2025}	354.99 (482.42) {482.42}	309.75	91.00
		404	PETLAD-BHADLAN (22.5 KM) (WR) (N22000538)	5-2022	5/2030 (Dec-2025) {12/2025}	202.50 (307.12) {307.12}	81.12	8.00
		405	NADIAD-PETLAD (37.26 KM) (WR) (N22000539)	5-2022	6/2030 (N.A.) {12/2025}	335.34 (461.91) {461.91}	74.11	7.00
		406	SAMLAYA-TIMBA ROAD (53.53 KM) (WR) (N22000540)	2-2023	3/2030 (Jul-2026) {7/2026}	670.00 (670.17) {670.17}	101.79	12.00
		407	SAMNI-JAMBUSAR (24.08 KM) (WR) (N22000541)	5-2022	3/2030 (Dec-2025) {12/2025}	216.72 (349.93) {349.93}	86.46	25.00
		408	VIJAPUR-AMBLIYASAN (41.53 KM) (WR) (N22000547)	5-2022	3/2030 (Jul-2025) {7/2025}	309.81 (415.38) {415.38}	240.08	85.00
		409	ADRAJ MOTI-VIAJAPUR (39.75 KM) (WR) (N22000548)	5-2022	5/2030 (Jul-2025) {5/2030}	296.54 (N.A.) {296.54}	164.47	80.00
		410	NEW BG LINE BETWEEN NALIYA-JAKHAU PORT (WR) (N22000550)	2-2023	1/2028 (Dec-2026) {12/2026}	410.46 (410.46) {410.46}	5.89	2.00
		411	NEW BG LINE INTERSECTION (5 NOS) BETWEEN GERATPUR-SANAND AND BOTAD- AHMEDABAD (16.51 KM) (PB29/NR/20) (WR) (N22000551)	10-2022	10/2027 (Feb-2027) {10/2027}	437.21 (N.A.) {437.21}	30.05	N.A.
		412	TARANGA HILL ABU ROAD VIA AMBAJI NEW LINE (NWR) (N22000592)	7-2022	7/2030 (N.A.) {12/2026}	2,798.16 (N.A.) {2,798.16}	1,063.09	12.00
		413	JUNAGARH -VISAVADAR (42.28) KM (RVNL) (N22000600)	6-2022	9/2028 (N.A.) {12/2026}	493.00 (N.A.) {492.83}	0.00	N.A.
		414	MODASA- SHAMLAJI NEW LINE (MM OF AHMEDABAD-HIMMATNAGAR-UDAIPUR (299.2 KM)) (WR) (N22000622)	9-2012	3/2027 (Feb-2026) {2/2026}	261.68 (261.68) {261.68}	191.87	55.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	415	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST (NHAI) (N24000569)	5-2016	9/2019 (May-2024) {6/2025}	723.64 (N.A.) {723.64}	562.31	97.00
		416	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 (NHAI) (N24000592)	7-2016	7/2020 (N.A.) {5/2025}	829.97 (N.A.) {829.97}	486.93	96.63
		417	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. (NHAI) (N24000649)	1-2017	12/2020 (Oct-2025) {10/2025}	1,251.11 (1,527.75) {1,527.75}	685.11	90.41
		418	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR (NHAI) (N24000834)	3-2018	10/2021 (May-2025) {7/2025}	1,161.39 (1,738.03) {1,404.00}	683.24	83.00
		419	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA (MoRTH) (N24000925)	10-2018	11/2020 (Sep-2024) {9/2024}	400.76 (394.44) {394.44}	287.04	87.00
		420	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT (MoRTH) (N24001427)	6-2020	4/2023 (Sep-2024) {9/2024}	166.21 (N.A.) {166.21}	97.12	93.00
		421	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 (NHAI) (N24001443)	5-2020	3/2024 (Jun-2025) {6/2025}	690.30 (929.95) {929.95}	841.05	93.90
		422	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION (NHAI) (N24001444)	5-2020	1/2024 (Jun-2025) {6/2025}	882.00 (1,229.37) {1,229.37}	996.88	89.28

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		423	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB (NHAI) (N24001445)	5-2020	7/2023 (May-2025) {5/2025}	691.52 (903.85) {903.85}	872.33	99.10
		424	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG (NHAI) (N24001446)	5-2020	12/2023 (May-2025) {5/2025}	894.00 (1,261.58) {1,261.58}	1,156.84	96.77
		425	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 (NHAI) (N24001515)	9-2020	2/2024 (N.A.) {3/2026}	1,542.02 (N.A.) {1,542.02}	969.47	68.35
		426	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 (NHAI) (N24001516)	9-2020	2/2024 (Aug-2025) {8/2025}	1,185.69 (N.A.) {1,185.69}	980.16	93.52
		427	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 (NHAI) (N24001518)	11-2019	9/2023 (N.A.) {8/2025}	1,669.56 (N.A.) {1,669.56}	1,066.35	96.90
		428	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 (NHAI) (N24001519)	9-2020	11/2023 (N.A.) {7/2025}	1,198.55 (N.A.) {1,198.55}	911.13	95.78
		429	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 (NHAI) (N24001520)	11-2019	5/2024 (N.A.) {8/2025}	1,604.06 (N.A.) {1,604.06}	1,241.40	95.73
		430	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT (NHAI) (N24001785)	3-2022	6/2025 (N.A.) {6/2025}	1,373.06 (1,085.00) {1,373.06}	656.62	87.30
		431	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU (NHAI) (N24001786)	3-2021	3/2024 (N.A.) {3/2026}	1,259.00 (2,652.24) {1,910.00}	278.29	34.08

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		432	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA (NHAI) (N24001789)	7-2020	8/2023 (N.A.) {4/2025}	1,710.30 (2,665.08) {1,927.00}	900.19	90.56
		433	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH-754K (AJ-RGBS-PACKAGE-3) (NHAI) (N24001790)	2-2020	8/2023 (Dec-2024) {12/2024}	752.30 (N.A.) {766.20}	452.13	98.14
		434	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II) (NHAI) (N24001792)	3-2021	9/2022 (N.A.) {1/2025}	536.03 (N.A.) {536.03}	480.77	100.00
		435	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) (NHAI) (N24001793)	3-2021	9/2022 (N.A.) {5/2025}	485.75 (N.A.) {485.75}	393.88	99.57
		436	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH-754K (AJ-RGBS-PACKAGE-4) (NHAI) (N24001794)	2-2020	3/2023 (Dec-2024) {12/2024}	778.15 (N.A.) {785.67}	547.22	99.70
		437	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE) (NHAI) (N24001827)	3-2022	3/2023 (N.A.) {4/2025}	162.73 (N.A.) {162.73}	131.79	100.00
		438	UPGRADATION AND STRENGTHENING TO 2 LANE PS FROM KM 95/500 TO KM 129/775 OF NH 168 G IDAR BHILODA SA (MoRTH) (N24002014)	9-2022	12/2023 (Dec-2025) {12/2025}	237.28 (N.A.) {237.28}	0.34	N.A.
		439	UPGRADATION TO 4L PS DIVIDED CARRIAGEWAY FROM PATAN (NEAR RAJPUR) TO GOJARIYA FROM KM 52.000 TO KM 1 (NHAI) (N24002034)	12-2021	3/2025 (N.A.) {3/2025}	1,181.34 (1,181.00) {1,181.34}	534.24	77.60
		440	WIDENING TO 6L OF EXISTING 4L JETPUR - GONDAL - RAJKOT SECTION FROM KM. 117.600 TO KM. 185.00 ON NH- (NHAI) (N24002035)	9-2023	9/2025 (N.A.) {9/2025}	2,070.44 (N.A.) {2,070.44}	485.44	36.96

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		441	UPGRADATION OF DHORAJI JAMKANDORNA KALAVAD SECTION OF NH 927D FROM DESIGN CHAINAGE KM 00 TO KM 58.11 (MoRTH) (N24002117)	10-2022	2/2024 (Feb-2026) {2/2026}	246.60 (291.00) {291.00}	27.57	15.00
		442	UPGRADATION TO TWO LANE WITH PAVED SHULDER CONFIGUARATION FROM KM 00 TO 47 OF NH 351 MAHUVA TO BADHA (MoRTH) (N24002118)	12-2022	2/2024 (Aug-2025) {8/2025}	173.06 (N.A.) {219.00}	0.15	N.A.
		443	WORK OF DEVELOPMENT AND CONSTRUCTION OF ELEVATED CORRIDORFROM KM 38/660 TO KM 42/690 (ISCON JUNCTION (MoRTH) (N24002182)	3-2023	3/2026 (N.A.) {3/2026}	530.20 (N.A.) {530.20}	0.00	N.A.
		444	WIDENING 2 LANE TO 4-LANE FROM KM 92/320 TO KM 115/320 (VAV CHOKDI- SATLASANA TO TO VRUNDAVAN CHOKDI, (MoRTH) (N24002183)	3-2022	3/2026 (N.A.) {3/2026}	151.13 (N.A.) {171.00}	0.00	N.A.
	URBAN DEVELOPMEN I	445	AHMEDABAD METRO RAIL PROJECT PHASE I (AMR) (N28000122)	11-2014	12/2018 (N.A.) {8/2025}	10,773.00 (N.A.) {12,924.55}	12,484.89	99.89
		446	AHMEDABAD METRO RAIL PROJECT PHASE II (AMR) (N28000137)	3-2019	3/2024 (N.A.) {12/2025}	5,384.17 (N.A.) {5,384.17}	4,032.54	85.77
		447	SURAT METRO RAIL PROJECT (AMR) (N28000138)	3-2019	3/2024 (N.A.) {6/2026}	12,020.32 (N.A.) {12,020.32}	6,882.87	66.05
HARYANA	HEALTH AND FAMILY WELFARE	448	ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT MANETHI, HARYANA. (HITES) (N21000032)	3-2019	3/2023 (Mar-2026) {3/2026}	1,294.34 (1,294.34) {1,294.34}	269.20	23.20
	HOME AFFAIRS	449	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" (CPWD FOR MHA) (N28000147)	1-2020	10/2023 (Mar-2025) {7/2025}	166.98 (170.23) {170.23}	139.66	97.00
	PETROLEUM	450	R and D CAMPUS II AT FARIDABAD (IOCL) (N16000375)	6-2019	12/2022 (Jul-2025) {3/2026}	2,281.94 (3,219.94) {3,219.94}	1,705.85	63.00
		451	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA (IOCL) (N16000412)	2-2021	9/2024 (Dec-2025) {12/2025}	34,627.00 (38,231.00) {38,231.00}	20,878.96	86.50

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		452	POLY BUTADIENE RUBBER PLANT AT PANIPAT (IOCL) (N16000458)	3-2022	3/2025 (Jun-2026) {6/2026}	1,459.00 (2,948.62) {2,948.62}	913.92	65.60
	POWER	453	IMPLEMENTATION OF LILO OF BOTH CIRCUITS OF 400KV VIDHYACHAL PS TO SASAN D/C LINE AT HINDALCO SWITCHY (PGCIL) (N18000420)	2-2025	12/2026 (N.A.) {12/2026}	370.00 (N.A.) {370.00}	0.00	N.A.
	RAILWAYS	454	DOUBLING BETWEEN BHIWANI-DOBH BAHALI (NWR) (N22000604)	2-2023	2/2028 (N.A.) {12/2025}	471.06 (N.A.) {471.06}	111.40	44.00
		455	DOUBLING BETWEEN REWARI-KATHUWAS (27.73 KM) (NWR) (N22000606)	2-2023	6/2027 (N.A.) {12/2025}	352.41 (N.A.) {352.41}	169.66	51.00
	ROAD TRANSPORT AND HIGHWAYS	456	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 (NHAI) (N24001535)	7-2020	7/2022 (May-2024) {8/2025}	899.00 (1,882.46) {1,882.46}	1,123.98	97.30
		457	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F (NHAI) (N24001633)	12-2020	12/2023 (Mar-2024) {6/2025}	1,430.88 (1,813.91) {1,813.91}	1,190.24	99.90
		458	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO (NHAI) (N24001634)	1-2021	12/2023 (Mar-2024) {6/2025}	1,306.95 (1,564.14) {1,564.14}	942.71	99.97
		459	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O (NHAI) (N24001635)	3-2022	2/2025 (N.A.) {2/2025}	1,269.50 (N.A.) {1,269.50}	151.00	52.00
		460	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH- 71 AND CONNECTING LINK FROM K (NHAI) (N24001673)	3-2020	3/2023 (Nov-2024) {6/2025}	510.97 (N.A.) {510.97}	529.00	96.75

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		461	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH-352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU (NHAI) (N24001774)	12-2020	11/2023 (N.A.) {6/2024}	1,524.03 (N.A.) {1,524.03}	1,105.08	65.54
		462	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH-11 AS A FEEDER ROUTE IN THE STATE (NHAI) (N24001775)	2-2020	1/2023 (Dec-2024) {12/2024}	808.31 (N.A.) {958.00}	917.55	100.00
		463	UPGRADATION OF EXISTING 4 LANE ISMAILABAD-AMBALA SECTION (KM. 0+000 TO KM 42+500) (PART OF AMBALA-KO (NHAI) (N24002037)	1-2023	12/2025 (N.A.) {3/2026}	609.32 (609.00) {609.00}	187.47	47.30
		464	CONSTRUCTION OF 6-LANE GREENFIELD KARNAL RING ROAD STARTING FROM NH- 44 NEAR VILLAGE SHAMGARH (DESIGN (NHAI) (N24002038)	11-2022	8/2025 (N.A.) {8/2025}	1,691.45 (1,998.00) {1,998.00}	649.71	58.76
		465	CONSTRUCTION OF 6-LANE GREENFIELD AMBALA RING ROAD STARTING FROM JUNCTION WITH SHAMLI-AMBALA SECTION (NHAI) (N24002039)	2-2023	10/2025 (N.A.) {10/2025}	1,088.64 (1,178.00) {1,178.00}	425.85	53.55
		466	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM RANIPUR BARSII (SAHARANPUR DISTRICT) TO ADHOYA (NHAI) (N24002040)	4-2022	5/2025 (N.A.) {5/2028}	1,554.21 (N.A.) {1,554.21}	522.92	54.00
		467	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM ADHOYA MUSALMANA (AMBALA DISTRICT) TO SADOPUR (NHAI) (N24002041)	4-2022	5/2025 (N.A.) {5/2025}	1,491.71 (N.A.) {1,491.71}	706.26	49.70
		468	CONSTRUCTION OF 4-LANING OF BHIWANI HANSI ROAD SECTION OF NH 148B (DESIGN LENGTH 42.934 KM) UNDER BH (NHAI) (N24002042)	11-2022	12/2025 (N.A.) {12/2025}	1,322.13 (N.A.) {1,322.13}	354.56	91.01

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
HIMACHAL PRADESH		469	CONSTRUCTION OF 4-LANE GREENFIELD JALBEHRA - SHAHBAD SECTION OF NH ? 152G FROM KM 0+000 TO KM 22+850 (NHAI) (N24002043)	3-2022	6/2025 (N.A.) {6/2025}	927.22 (1,173.66) {1,173.66}	493.79	80.50
		470	4L AMBALA - KALAAMB FROM KM. -0.800 TO KM. 33.015 OF OLD NH-72 (NHAI) (N24002044)	6-2023	6/2025 (N.A.) {6/2025}	629.16 (N.A.) {629.16}	94.00	95.00
		471	CONSTRUCTION OF GREENFIELD CONNECTIVITY TO JEWAR INTERNATIONAL AIRPORT FROM DND FARIDABAD BALLABHGAR (NHAI) (N24002048)	7-2022	6/2025 (N.A.) {3/2026}	2,414.67 (2,898.00) {2,898.00}	1,229.90	47.20
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	472	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR (CPWD EDUCATION) (N42000008)	9-2018	6/2022 (Dec-2024) {8/2025}	392.51 (N.A.) {446.43}	316.16	91.50
		473	CONSTRUCTION OF PERMANENT CAMPUSES OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND DHARAMSHAL (CPWD) (N42000011)	3-2021	11/2024 (Jul-2025) {7/2025}	512.37 (300.45) {300.45}	157.12	72.00
	<u>POWER</u>	474	LUHRI HYDROELECTRIC PROJECT (STAGE1) (SJVN) (N18000279)	11-2020	1/2026 (N.A.) {12/2028}	1,810.56 (N.A.) {3,584.53}	1,715.33	51.32
		475	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) (SJVN) (N18000291)	10-2020	11/2025 (N.A.) {3/2027}	687.97 (N.A.) {1,511.87}	874.54	66.91
		476	SUNNI DAM HYDRO ELECTRIC PROJECT (SJVN) (N18000344)	1-2023	4/2028 (N.A.) {12/2028}	2,614.51 (N.A.) {4,540.71}	942.36	29.08
	<u>RAILWAYS</u>	477	BHANUPALI-BILASPUR BERI NL (RVNL) (N22000273)	4-2008	12/2026 (N.A.) {3/2025}	13,370.29 (N.A.) {6,753.42}	5,369.57	N.A.
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	478	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH (NHAI) (N24000613)	9-2016	7/2020 (N.A.) {3/2025}	1,273.71 (N.A.) {1,478.61}	1,439.49	97.26

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		479	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M (NHAI) (N24000852)	3-2018	5/2021 (Dec-2024) {12/2024}	478.74 (N.A.) {1,514.46}	1,349.59	83.00
		480	REHABILITATION AND UPGRADATION TO 2- LANE/2-LANE WITH PAVED SHOULDERS/4- LANE CONFIGURATION OF PAONTA (MoRTH) (N24001381)	8-2020	4/2021 (N.A.) {4/2021}	272.98 (N.A.) {272.98}	140.69	100.00
		481	REHABILITATION AND UPGRADATION TO 2- LANE CONFIGURATION OF HEWNA- ASHYARI SECTION (KM 25.000 TO KM 50. (MoRTH) (N24001382)	8-2020	3/2021 (N.A.) {7/2024}	242.80 (N.A.) {242.80}	96.76	92.44
		482	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 (MoRTH) (N24001383)	8-2020	4/2021 (N.A.) {4/2021}	349.20 (N.A.) {349.20}	239.34	100.00
		483	REHABILITATION AND UPGRADATION TO 2- LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K (MoRTH) (N24001422)	2-2021	9/2021 (N.A.) {7/2024}	345.89 (N.A.) {345.89}	162.23	91.75
		484	REHABILITATION AND UPGRADATION TO 2- LANE CONFIGURATION OF HAMIRPUR- KARNOHAL SECTION (KM 141.000 TO K (MoRTH) (N24001447)	8-2020	12/2024 (N.A.) {12/2024}	371.93 (N.A.) {371.93}	154.04	81.00
		485	REHABILITATION AND UPGRADATION TO 2- LANE CONFIGURATION OF KALWAHAN- MANDI SECTION (KM 208.950 TO KM 2 (MoRTH) (N24001470)	8-2020	4/2025 (N.A.) {4/2025}	314.32 (N.A.) {314.32}	49.26	45.00
		486	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF (NHAI) (N24001808)	3-2021	12/2024 (Dec-2024) {12/2024}	1,322.95 (1,442.47) {1,442.47}	888.51	96.61

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		487	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU (NHAI) (N24001809)	5-2022	3/2024 (Dec-2024) {12/2024}	469.95 (N.A.) {280.00}	302.91	98.30
		488	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP (NHAI) (N24001810)	2-2022	6/2024 (N.A.) {6/2024}	190.60 (N.A.) {163.00}	103.48	100.00
		489	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH-20 (NEW NH-154) (PACKAGE-IB) (NHAI) (N24001811)	4-2021	6/2024 (N.A.) {5/2025}	583.93 (770.00) {770.00}	173.60	100.00
		490	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) (NHAI) (N24001812)	3-2021	5/2024 (N.A.) {12/2025}	1,002.11 (1,361.79) {1,361.76}	190.22	46.54
		491	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A (NHAI) (N24001813)	7-2021	9/2024 (N.A.) {9/2024}	1,692.05 (N.A.) {1,692.05}	942.14	21.60
		492	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS-5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001915)	3-2021	6/2026 (N.A.) {6/2026}	230.54 (N.A.) {230.54}	20.16	28.00
		493	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS 5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001916)	3-2021	5/2026 (N.A.) {5/2026}	314.67 (N.A.) {314.67}	76.05	47.00
		494	PKG NAME: 4L OF KATHLIGHAT TO SHAKRAL VILLAGE FROM KM 128.835 TO KM 146.300 OF NH- 5 (SHIMLA BYPASS (NHAI) (N24002049)	3-2022	4/2026 (N.A.) {4/2026}	1,703.48 (2,278.00) {2,278.00}	651.98	14.50
		495	REHABILITATION AND UPGRADATION TO 4L CONFIGURATION and STRENGTHENING OF SIHUNI TO RAJOL FROM KM 51.0 (NHAI) (N24002050)	2-2022	9/2025 (N.A.) {9/2025}	696.65 (698.46) {698.46}	367.62	64.80

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		496	CONSTRUCTION OF NEW 2 LANE WITH PAVED SHOULDER OF HAMIRPUR BYPASS (PACKAGE IVA) OF NH-88 (NEW NH-103 (NHAI) (N24002051)	7-2022	10/2025 (N.A.) {10/2025}	739.39 (N.A.) {739.39}	328.46	78.00
		497	REHABILITATION AND UP-GRADATION OF EXISTING ROAD TO 2L PS FROM END OF HAMIRPUR BYPASS (NEAR CHILBAHA (NHAI) (N24002052)	2-2022	4/2025 (N.A.) {4/2025}	1,146.19 (N.A.) {1,146.19}	918.84	69.27
		498	REHABILITATION AND UP-GRADATION TO 4L CONFIGURATION AND STRENGTHENING OF THANPURI TO PAROR SECTION F (NHAI) (N24002192)	6-2022	12/2025 (N.A.) {12/2025}	815.69 (815.69) {815.69}	392.01	29.20
	URBAN DEVELOPME N I	499	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D (CPWD) (N28000154)	4-2022	11/2024 (N.A.) {11/2024}	512.34 (N.A.) {512.34}	0.00	N.A.
JAMMU AND KASHMIR	CIVIL AVIATION	500	JAMMU - CONSTRUCTION OF NEW CIVIL ENCLAVE (AAI) (N04000107)	7-2022	6/2026 (N.A.) {6/2026}	861.37 (N.A.) {861.37}	144.65	30.00
	DEPARTMENT OF HIGHER EDUCATION	501	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) (CPWD EDUCATION) (N28000130)	3-2019	7/2022 (Jan-2025) {1/2025}	424.93 (N.A.) {500.91}	448.15	96.00
		502	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) (CPWD EDUCATION) (N28000131)	1-2018	4/2023 (Apr-2025) {4/2025}	676.00 (1,144.68) {1,144.68}	54.75	100.00
	HEALTH AND FAMILY WELFARE	503	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR (CPWD FOR HEALTH) (N21000029)	3-2019	9/2023 (May-2025) {5/2025}	1,404.00 (1,642.00) {1,642.00}	1,461.68	100.00
		504	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR (CPWD FOR HEALTH) (N28000150)	3-2019	9/2025 (N.A.) {11/2025}	1,828.00 (N.A.) {1,577.00}	1,285.40	64.10
	PETROLEUM	505	SETTING UP A COMMON USER PETROLEUM TERMINAL AT JAMMU FOR RE-SITEMENT OF EXISTING DEPOTS OF PSU OMCS (BPCL) (N16000500)	4-2021	3/2025 (N.A.) {3/2025}	676.89 (N.A.) {676.89}	495.30	75.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		506	CGD PROJECT AT JAMMU DISTRICTS (IOCL) (N16000527)	3-2022	3/2032 (Sep-2034) {9/2034}	538.00 (N.A.) {538.00}	4.09	0.60
	POWER	507	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) (CVPPPL) (N18000172)	10-2014	4/2020 (Jul-2025) {9/2026}	8,112.12 (N.A.) {12,727.76}	6,561.65	69.35
		508	KIRU HYDRO ELECTRIC PROJECT (CVPPPL) (N18000278)	3-2019	8/2024 (N.A.) {9/2026}	4,287.59 (N.A.) {5,409.00}	2,599.24	61.38
		509	RATLE HE PROJECT (NHPC) (N18000324)	2-2021	2/2026 (N.A.) {8/2028}	5,281.94 (N.A.) {5,281.94}	968.19	23.01
		510	KWAR HE PROJECT (CVPPPL) (N18000363)	5-2022	11/2026 (N.A.) {12/2027}	4,526.12 (N.A.) {4,526.12}	1,119.97	21.45
		511	TRANSMISSION SCHEME FOR EVACUATION OF POWER FROM RATLE HEP (850 MW) AND KIRU (624 MW): PART B (PGCIL) (N18000417)	3-2025	3/2027 (N.A.) {3/2027}	219.00 (N.A.) {219.00}	0.00	N.A.
	ROAD TRANSPORT AND HIGHWAYS	512	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A (NHAI) (N24000488)	12-2015	12/2018 (Jun-2025) {6/2025}	2,136.97 (2,644.00) {2,644.00}	2,386.51	99.50
		513	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE (NHAI) (N24000717)	12-2017	7/2021 (Jun-2025) {6/2025}	1,471.75 (1,471.75) {1,903.98}	1,716.22	98.80
		514	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA (NHIDCL) (N24000868)	3-2018	7/2021 (Aug-2023) {10/2025}	253.44 (N.A.) {253.44}	189.72	82.35
		515	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D (NHIDCL) (N24001256)	8-2020	9/2026 (N.A.) {9/2026}	6,808.69 (N.A.) {6,808.69}	3,013.84	49.92
		516	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL (NHIDCL) (N24001264)	7-2020	4/2022 (Oct-2024) {10/2026}	228.39 (N.A.) {228.39}	69.32	87.85

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		517	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K (NHIDCL) (N24001266)	7-2020	4/2022 (Nov-2023) {7/2025}	210.79 (N.A.) {210.79}	71.00	90.40
		518	KHELLANI-KHANABAL PKG-1 (NHIDCL) (N24001323)	3-2021	9/2022 (Oct-2024) {10/2024}	486.45 (N.A.) {486.45}	126.73	96.58
		519	KHELLANI-KHANABAL PKG-3 (NHIDCL) (N24001341)	3-2021	12/2022 (Oct-2024) {5/2025}	398.51 (N.A.) {398.51}	80.64	98.36
		520	KHELLANI-KHANABAL PKG-2 (NHIDCL) (N24001394)	7-2021	2/2023 (Jun-2025) {6/2026}	512.43 (N.A.) {512.43}	71.65	51.52
		521	KHELLANI-KHANABAL PKG-4 (NHIDCL) (N24001395)	7-2021	8/2023 (Dec-2025) {6/2026}	859.67 (N.A.) {859.67}	190.91	44.02
		522	KHELLANI-KHANABAL PKG-5 (NHIDCL) (N24001396)	7-2021	2/2023 (Mar-2025) {8/2025}	497.09 (N.A.) {497.09}	172.85	88.04
		523	GOHA-KHELLANI PKG-3 (NHIDCL) (N24001397)	2-2021	3/2023 (Feb-2025) {3/2025}	431.28 (433.08) {431.28}	372.31	100.00
		524	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA (NHAI) (N24001472)	9-2021	12/2023 (Jun-2024) {6/2024}	811.19 (N.A.) {811.19}	848.57	99.00
		525	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY (NHAI) (N24001511)	3-2021	2/2024 (Oct-2025) {10/2025}	2,919.96 (N.A.) {2,919.96}	2,317.82	70.00
		526	FOUR LANING OF JAMMU-AKHNOOR PKG-1 (NHIDCL) (N24001543)	7-2022	1/2025 (N.A.) {10/2025}	245.34 (N.A.) {245.34}	57.03	38.48
		527	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH-4 (NHAI) (N24001550)	9-2021	9/2024 (Dec-2025) {12/2025}	1,821.72 (1,917.32) {1,917.32}	1,005.35	83.21
		528	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5 (NHAI) (N24001551)	10-2021	9/2024 (Dec-2025) {12/2025}	3,044.02 (3,044.02) {3,044.02}	1,586.31	70.95

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		529	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B (NHAI) (N24001552)	10-2021	9/2024 (Feb-2026) {2/2026}	2,714.95 (2,714.95) {2,714.95}	1,642.02	85.37
		530	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH- (NHAI) (N24001619)	8-2022	6/2024 (Jun-2025) {6/2025}	200.05 (200.05) {208.92}	153.05	58.60
		531	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SLIP ZONES AT KM 130.550 TO KM.130.750; KM. (NHAI) (N24001620)	9-2021	10/2023 (Dec-2025) {12/2025}	442.14 (N.A.) {442.14}	341.75	19.88
		532	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL. (NHAI) (N24001621)	7-2021	8/2024 (Jun-2025) {6/2025}	614.48 (N.A.) {614.48}	187.59	7.00
		533	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX (NHAI) (N24001622)	7-2021	6/2024 (Jun-2025) {6/2025}	1,401.87 (N.A.) {1,401.87}	734.56	N.A.
		534	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM. 187.00 TO KM. 189.350 (NHAI) (N24001623)	1-2020	1/2024 (Feb-2025) {2/2025}	336.01 (N.A.) {336.01}	222.97	34.00
		535	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI (NHAI) (N24001624)	7-2019	10/2020 (Apr-2023) {9/2024}	157.05 (N.A.) {157.05}	139.54	100.00
		536	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K (NHAI) (N24001627)	7-2021	2/2025 (May-2026) {5/2026}	1,912.17 (N.A.) {1,912.17}	129.05	N.A.
		537	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B (NHIDCL) (N24001833)	7-2022	3/2025 (N.A.) {8/2025}	198.28 (N.A.) {198.28}	85.39	71.09

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		538	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 102 TO KM 13 (BRO) (N24001897)	3-2021	7/2024 (Mar-2025) {3/2024}	642.24 (N.A.) {642.24}	345.14	95.00
		539	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 30.000 TO K (BRO) (N24001898)	7-2020	11/2024 (N.A.) {11/2024}	272.49 (N.A.) {272.49}	133.66	87.24
		540	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 134.95 TO KM (BRO) (N24001899)	2-2021	7/2024 (N.A.) {3/2025}	395.25 (N.A.) {395.25}	140.42	64.00
		541	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 49.150 TO KM (BRO) (N24001900)	3-2020	8/2024 (N.A.) {3/2025}	796.97 (N.A.) {796.97}	323.85	79.00
		542	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 64.535 TO K (BRO) (N24001901)	3-2020	9/2023 (N.A.) {3/2025}	152.93 (N.A.) {152.93}	90.30	78.27
		543	CONSTRUCTION OF TWIN TUBE TUNNELS ON JAMMU KASHMIR RING ROAD (NH-244A) BETWEEN DESIGN CH. 50+600 TO (NHAI) (N24001926)	3-2023	6/2025 (N.A.) {3/2026}	939.86 (N.A.) {939.86}	475.07	64.93
		544	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER FROM (DESIGN CH. 14+200 TO 24+400), (DESIGN CH. 35+300 TO (BRO) (N24001998)	6-2022	8/2025 (N.A.) {8/2025}	832.46 (N.A.) {823.46}	227.50	46.00
		545	2L NH-1 FROM KM 8.660 TO KM 33.775 (SUMBAL TO WAYUL) TO 4L DUAL CARRIAGEWAY NH STANDARD AS PART OF S (NHAI) (N24002059)	9-2022	6/2026 (Jun-2026) {12/2026}	1,183.60 (N.A.) {1,183.60}	185.45	12.62

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		546	DELHI AMRITSAR KATRA EXPRESSWAY (PHASE-II PKG XVIII) DEVELOPMENT AND UPGRADATION OF FOUR LANE ACCESS (NHAI) (N24002060)	3-2023	11/2025 (N.A.) {3/2026}	1,107.00 (N.A.) {975.38}	338.69	38.38
		547	4/6L ACCESS CONTROL EXPRESSWAY FROM DESIGN CHAINAGE KM 515.000 TO 528.300 (KUNJWANI TO SIDHRA SECTIO (NHAI) (N24002061)	8-2022	6/2025 (N.A.) {2/2026}	2,474.47 (N.A.) {2,894.74}	923.64	38.20
		548	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM 162.800 TO KM (BRO) (N24002119)	10-2022	1/2026 (N.A.) {1/2026}	562.45 (N.A.) {562.45}	99.06	25.00
		549	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER (PATTAN BYPASS) GREENFIELD BYPASS FROM EXISTING CH. KM 24 (BRO) (N24002179)	3-2023	7/2026 (N.A.) {7/2026}	980.21 (N.A.) {980.21}	300.02	8.00
		550	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 166.100 TO KM (BRO) (N24002180)	9-2021	7/2026 (N.A.) {7/2026}	734.64 (N.A.) {734.64}	19.60	8.00
		551	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDERS (BARAMULLA BYPASS) GREENFIELD BYPASS FROM EXISTING CH. K (BRO) (N24002185)	3-2023	9/2026 (N.A.) {9/2026}	992.43 (N.A.) {992.43}	338.33	N.A.
		552	WIDENING AND STRENGTHENING OF RAFIABAD-KUPWARA-CHOWKIBAL- TANGDHAR-CHAMKOT (NH-701) ROAD FROM DESIGN (BRO) (N24002210)	3-2024	5/2027 (N.A.) {5/2027}	1,404.94 (N.A.) {1,404.94}	0.00	N.A.
JHARKHAND	COAL	553	RAJRAPPA RCE OCP (3.0 MTY) (CCL) (N06000087)	12-2009	3/2016 (N.A.) {3/2027}	510.85 (N.A.) {510.85}	488.57	75.00
		554	MURADIH UG TURN-KEY PROJECT (BCCL) (N06000096)	2-2011	4/2014 (N.A.) {1/2026}	339.88 (N.A.) {339.88}	190.48	70.00
		555	MOONIDIH XV SEAM UG (BCCL) (N06000098)	8-2011	3/2019 (N.A.) {5/2026}	1,230.27 (N.A.) {1,230.27}	605.99	81.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		556	CHITRA EAST (RCE) OCP (ECL) (N06000169)	8-2018	3/2026 (Mar-2026) {3/2026}	513.98 (N.A.) {513.98}	227.74	51.00
		557	TETARIAKHAR EXPANSION OCP (CCL) (N06000186)	11-2019	3/2023 (N.A.) {3/2027}	243.52 (N.A.) {243.52}	44.64	24.00
		558	PACHWARA SOUTH COAL BLOCK (NLC) (N06000193)	7-2013	9/2028 (N.A.) {9/2028}	2,242.92 (2,242.90) {2,242.90}	687.46	54.00
		559	PATHERDIH 2.5 NLW COAL WASHERY (BCCL) (N06000194)	10-2015	4/2018 (N.A.) {3/2026}	334.27 (N.A.) {334.27}	135.86	45.05
		560	REVISED PROJECT REPORT MAGADH EXPANSION OCP (CCL) (N06000216)	8-2020	3/2028 (N.A.) {3/2028}	7,254.37 (N.A.) {7,254.37}	1,500.33	38.00
		561	EXPANSION PROJECT AMRAPALI OCP (CCL) (N06000217)	8-2020	3/2028 (N.A.) {3/2028}	5,136.15 (N.A.) {5,136.15}	1,082.09	41.00
		562	UCE OF EPR OF NORTH URIMARI OCP (CCL) (N06000218)	7-2021	3/2029 (N.A.) {3/2029}	778.80 (N.A.) {778.80}	694.11	75.00
		563	KOTRE BASANTPUR PACHMO OCP (CCL) (N06000237)	8-2020	3/2032 (N.A.) {3/2032}	625.40 (625.40) {625.40}	441.24	41.00
		564	CHANDRAGUPT OCP (CCL) (N06000238)	8-2020	3/2032 (N.A.) {3/2032}	973.50 (N.A.) {973.50}	339.32	12.40
		565	SIRKA OCP (CCL) (N06000239)	5-2020	3/2028 (N.A.) {3/2028}	222.82 (N.A.) {222.82}	139.31	60.00
		566	JHARKHAND LAIYO OCP (CCL) (N06000240)	8-2020	3/2031 (N.A.) {3/2031}	764.57 (N.A.) {764.57}	145.80	28.00
		567	EPR TAPIN SOUTH OCP (CCL) (N06000241)	11-2020	3/2028 (N.A.) {3/2028}	230.41 (N.A.) {230.41}	21.12	18.30
		568	EPR PUNDI OCP (CCL) (N06000242)	11-2020	3/2027 (N.A.) {3/2027}	713.35 (N.A.) {713.35}	236.57	21.00
		569	EPR ROHINI KARKATA OCP (CCL) (N06000243)	1-2021	3/2028 (N.A.) {3/2028}	1,020.42 (N.A.) {1,020.42}	83.44	11.70
		570	EXPANSION OF KONAR OCP (CCL) (N06000245)	1-2022	3/2032 (N.A.) {3/2032}	799.34 (N.A.) {799.34}	416.73	32.00
		571	EXPANSION OF KARO OCP (CCL) (N06000246)	1-2022	3/2029 (N.A.) {3/2029}	908.47 (N.A.) {908.47}	217.68	21.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		572	EXPANSION OF ASHOK OCP (CCL) (N06000247)	5-2021	3/2028 (N.A.) {3/2028}	2,898.28 (N.A.) {2,898.28}	176.50	20.00
		573	AMALGAMATED NTST KUJAMA OCP 8.5 MTY (BCCL) (N06000273)	1-2023	3/2030 (N.A.) {3/2030}	4,011.85 (N.A.) {4,011.85}	397.65	25.00
		574	HURA C OC (ECL) (N06000275)	8-2022	3/2029 (N.A.) {3/2029}	859.41 (N.A.) {859.41}	448.60	62.00
		575	CHUPERBHITA- SIMLONG OCP (ECL) (N06000280)	12-2023	3/2037 (Mar-2037) {3/2037}	979.08 (N.A.) {979.08}	0.00	N.A.
		576	BLOCK-E OCP (15 MTY) (BCCL) (N06000287)	3-2024	3/2029 (N.A.) {3/2029}	5,850.83 (N.A.) {5,850.83}	5.85	2.00
	DEPARTMENT OF HIGHER EDUCATION	577	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD (CPWD EDUCATION) (N28000067)	9-2012	3/2016 (N.A.) {3/2016}	171.86 (N.A.) {171.86}	174.48	N.A.
	PETROLEUM	578	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) (ONGC) (N16000445)	11-2019	1/2024 (Mar-2025) {6/2025}	431.00 (N.A.) {431.00}	194.40	57.90
		579	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI (IOCL) (N16000480)	3-2023	2/2026 (N.A.) {2/2026}	202.07 (N.A.) {202.07}	52.94	42.91
		580	CGD PROJECT IN BIHAR JHARKHAND (HPCL) (N16000497)	6-2022	6/2030 (N.A.) {6/2030}	1,377.00 (N.A.) {1,377.00}	277.81	22.60
	POWER	581	NORTH KARANPURA STPP (3X660 MW) (NTPC) (N18000177)	2-2014	6/2019 (Oct-2022) {3/2025}	16,242.90 (N.A.) {16,242.90}	16,745.68	98.00
		582	PATRATU STPP-I (3X800MW) (NTPC) (N18000275)	11-2017	3/2023 (N.A.) {3/2026}	17,112.00 (N.A.) {17,112.00}	16,305.18	81.00
		583	BADAM COAL MINING PROJECT (NTPC) (N18000367)	2-2019	10/2024 (Apr-2027) {4/2027}	501.79 (784.39) {501.79}	305.97	59.79
		584	KERANDARI COAL MINING PROJECT (NTPC) (N18000370)	9-2015	11/2019 (Mar-2025) {3/2025}	1,553.00 (2,896.64) {2,896.64}	2,086.52	64.00
	RAILWAYS	585	KODERMA-TILAIYA (NL), ECR (ECR) (220100305)	4-2002	3/2023 (N.A.) {12/2025}	1,625.87 (1,625.87) {1,700.00}	2,013.59	80.00
		586	BONDAMUNDA RANCHI DOUBLING (SER) (N22000396)	3-2016	6/2024 (N.A.) {6/2026}	3,029.04 (3,029.04) {3,029.04}	2,390.21	84.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		587	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) (SER) (N22000508)	4-2018	6/2026 (N.A.) {6/2026}	501.52 (N.A.) {472.50}	275.86	4.00
		588	DOUBLING OF PRADHANKHUNTA JN - PATHERDIH BAZAR-BHOJUDIH (ECR) (N22000529)	11-2022	11/2027 (N.A.) {3/2026}	202.00 (349.22) {349.22}	64.10	2.00
		589	KHARAGPUR-ADITYAPUR - 3RD LINE (132 KM) (RVNL) (N22000595)	12-2015	3/2025 (N.A.) {3/2025}	3,249.98 (N.A.) {3,270.07}	2,899.45	N.A.
		590	3RD LINE BETWEEN DHANBAD SONNAGAR (RVNL) (N22000599)	11-2016	3/2026 (N.A.) {3/2026}	8,975.00 (N.A.) {7,906.38}	4,705.38	N.A.
		591	GARHWA ROAD - RAIL OVER RAIL (ECR) (N22000610)	3-2017	6/2024 (N.A.) {2/2026}	262.71 (N.A.) {262.71}	226.43	70.00
		592	GOMOH - FLYOVER FOR DOWN TRAINS (ECR) (N22000611)	1-2018	3/2023 (N.A.) {3/2026}	686.03 (N.A.) {487.73}	399.45	45.00
	ROAD TRANSPORT AND HIGHWAYS	593	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION (NHAI) (N24000726)	1-2018	11/2021 (May-2026) {5/2026}	1,155.16 (N.A.) {950.49}	657.82	73.00
		594	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I (MoRTH) (N24001216)	12-2016	9/2021 (N.A.) {12/2024}	196.00 (N.A.) {196.00}	164.21	90.10
		595	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 (NHAI) (N24001589)	9-2020	3/2024 (Dec-2024) {4/2025}	755.26 (N.A.) {1,039.00}	624.66	87.00
		596	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH-75 [REHLA / GARHWA BYPASS] (NHAI) (N24001590)	9-2020	10/2023 (Dec-2024) {1/2025}	748.99 (N.A.) {903.00}	831.75	100.00
		597	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM (NHAI) (N24001594)	2-2022	1/2025 (Mar-2025) {3/2025}	534.73 (N.A.) {534.73}	205.31	98.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		598	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH (NHAI) (N24001595)	8-2020	3/2024 (Jun-2025) {6/2025}	1,034.00 (1,879.55) {1,879.55}	41.50	96.61
		599	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF (NHAI) (N24001596)	11-2021	7/2023 (Jun-2025) {6/2025}	1,302.72 (1,504.80) {1,504.80}	875.97	71.40
		600	FOUR LANING WITH PAVED SHOULDER OF SECTION FROM KM 53.600 (GOLA ON NH-320) TO KM 81.446 (ORMANJHI ON (NHAI) (N24001854)	6-2023	6/2025 (N.A.) {6/2025}	1,214.93 (1,324.95) {1,462.00}	808.69	73.00
		601	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM 0.00 TO 44.00 (KURU-GHAGHRA SECTION) OF NH-143A INCLU (MoRTH) (N24001922)	2-2020	8/2023 (N.A.) {12/2024}	153.01 (N.A.) {153.01}	83.63	96.23
		602	WIDENING AND STRENGTHENING OF EXISTING PAVEEMNT TO TWO LANE WITH PAVED SHOULDERS FROM KM 116.00 TO K (MoRTH) (N24001923)	1-2022	7/2024 (N.A.) {12/2024}	315.21 (N.A.) {315.21}	117.26	80.00
		603	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDER/TWO LANE+ PAVED SHOULDER WITH SERVICE ROA (MoRTH) (N24001924)	3-2022	8/2025 (N.A.) {8/2025}	514.22 (N.A.) {514.22}	15.19	6.10
		604	WIDENING AND STRENGTHENING/RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDER/ TWO LANE WITH PAVED SHOUL (MoRTH) (N24001925)	3-2022	8/2025 (N.A.) {8/2025}	423.18 (N.A.) {423.18}	0.11	N.A.
		605	FOUR LANING OF KHAJURI TO WYNDHAMGANJ FROM KM 219.600 TO KM 260.483 ON NH-75 PKG SEC-V ON HAM (NHAI) (N24002053)	4-2022	9/2025 (N.A.) {9/2025}	1,232.00 (1,343.00) {1,400.00}	606.60	78.50

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		606	FOUR LANING OF BHOGU TO SANKHA FROM KM 147.450 TO KM 196.870 ON NH-75 PKG SEC-III (NHAI) (N24002054)	10-2022	11/2025 (N.A.) {11/2025}	1,390.77 (1,391.00) {1,600.00}	303.00	70.00
		607	FOUR LANING OF BASUKINATH-DEOGHAR SECTION OF NH-114A FROM KM 85.081 TO KM 130.240 UNDER NHDP PHASE-I (NHAI) (N24002055)	3-2023	12/2025 (N.A.) {12/2025}	1,444.94 (N.A.) {1,444.94}	0.00	N.A.
		608	BHARATMALA PARIYOJANA OF BOKARO JAINA MORE - GOLA SECTION OF NH-320 FROM KM. 21.110 TO KM. 53.600 IN (NHAI) (N24002056)	6-2020	6/2025 (N.A.) {6/2025}	964.64 (N.A.) {964.64}	432.70	60.24
		609	FOUR LANING OF MEHGAMA HANSDIHA SECTION OF NH-33 FROM EXISTING KM 41.900 TO 93.000 IN THE STATE OF J (NHAI) (N24002057)	12-2022	5/2025 (N.A.) {5/2025}	1,443.77 (N.A.) {1,443.77}	0.00	N.A.
	STEEL	610	NEW SINTER PLANT AT BOKARO STEEL PLANT (SAIL) (N12000095)	3-2015	10/2017 (Nov-2026) {11/2026}	1,034.01 (1,752.30) {1,752.30}	874.75	51.75
		611	REVAMPING OF OLD SUB SYSTEM OF BLAST FURNACE 3 AT BOKARO STEEL PLANT (SAIL) (N12000129)	9-2023	7/2025 (Nov-2025) {11/2025}	513.82 (N.A.) {513.82}	179.29	64.00
		612	REBUILDING OF COKE OVEN BATTERY NO.6 OF BOKARO STEEL PLANT (SAIL) (N12000133)	11-2023	11/2026 (N.A.) {11/2026}	627.31 (N.A.) {627.31}	84.56	33.00
		613	REPLACEMENT OF REMAINING 04 NOS. OF BATTERY CYCLONES WITH 04 NOS. OF ESPS IN SINTER PLANT-1 AT BSL (SAIL) (N12000135)	3-2024	6/2026 (N.A.) {6/2026}	260.37 (N.A.) {260.37}	42.86	12.00
		614	REPLACEMENT OF EXISTING GRINDERS IN CRM-I & II AT BOKARO STEEL PLANT (SAIL) (N12000142)	1-2025	1/2027 (N.A.) {1/2027}	211.94 (N.A.) {211.94}	0.00	N.A.

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		615	SECONDARY EMISSION CONTROL IN CONVERTERS OF SMS-II AT BOKARO STEEL PLANT (SAIL) (N12000143)	1-2025	10/2026 (N.A.) {10/2026}	207.13 (N.A.) {207.13}	0.00	1.00
KARNATAKA	CIVIL AVIATION	616	BELAGAVI AIRPORT- EXPANSION OF TERMINAL BUILDING AND ASSOCIATED WORKS (AAI) (N04000105)	6-2023	2/2026 (N.A.) {2/2026}	322.45 (N.A.) {322.45}	95.91	40.00
		617	HUBBALI AIRPORT - CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS (AAI) (N04000108)	6-2023	2/2026 (N.A.) {2/2026}	320.47 (N.A.) {320.47}	50.51	27.50
		618	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) (CPWD EDUCATION) (N42000006)	7-2019	3/2022 (Jun-2025) {11/2025}	851.00 (930.36) {930.36}	918.06	99.00
	PETROLEUM	619	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL (CPWD) (N42000010)	8-2021	2/2024 (Nov-2024) {11/2024}	316.25 (N.A.) {316.25}	281.32	91.00
		620	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE (HPCL) (N16000369)	12-2018	12/2022 (Aug-2025) {8/2025}	854.00 (854.00) {854.00}	696.35	99.50
		621	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE (IOCL) (N16000437)	1-2022	7/2025 (Dec-2025) {12/2025}	463.00 (500.62) {500.62}	241.69	71.10
		622	POWER SYSTEM UPGRADATION PROJECT (MANGALORE REFIN) (N16000509)	10-2023	2/2026 (N.A.) {2/2026}	385.00 (N.A.) {385.00}	122.13	56.88
		623	DEMO PLANT FOR PRODUCTION OF BIO- ATF (MANGALORE REFIN) (N16000536)	3-2024	3/2027 (N.A.) {3/2027}	364.00 (N.A.) {364.00}	16.85	6.60
	POWER	624	TS FOR INTRGRATION OF RE ZONE (PHASE II) IN KOPPAL II (PHASE A and B) AND GADAG II (PHASE A) IN KARN (PGCIL) (N18000385)	12-2023	12/2025 (N.A.) {12/2025}	2,889.00 (N.A.) {2,889.00}	891.98	28.50

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		625	TS FOR SOLAR ENERGY ZONE IN BIDAR (2500MW), KARNATAKA [BIDAR TRANSMISSION LTD] (PGCIL) (N18000388)	2-2024	2/2026 (N.A.) {2/2026}	2,148.00 (N.A.) {2,148.00}	846.60	43.80
		626	SYSTEM STRENGTHENING AT KOPPAL-II AND GADAG-II FOR INTEGRATION OF RE GENERATION PROJECTS (PGCIL) (N18000409)	1-2025	1/2027 (N.A.) {1/2027}	1,354.00 (N.A.) {1,354.00}	0.00	N.A.
		627	AUGMENTATION OF TRANSFORMATION CAPACITY AT BIDAR PS (PGCIL) (N18000410)	2-2025	2/2027 (N.A.) {2/2027}	288.00 (N.A.) {288.00}	0.00	N.A.
		628	TRANSMISSION SCHEME FOR INTEGRATION OF DAVANAGERE / CHITRADURGA AND BELLARY REZ IN KARNATAKA (PGCIL) (N18000419)	3-2025	3/2027 (N.A.) {3/2027}	3,453.00 (N.A.) {3,453.00}	0.00	N.A.
	RAILWAYS	629	TUMKUR-CHITRADURGA-DAVENGERE NL (SWR) (N22000256)	4-2011	3/2019 (N.A.) {12/2027}	1,876.00 (N.A.) {1,801.01}	498.03	12.00
		630	BAGALKOT-KUDACHI NL (SWR) (N22000258)	4-2010	3/2027 (N.A.) {3/2027}	1,378.00 (1,378.00) {1,378.00}	643.99	34.00
		631	HOSPET-HUBLI-LONDA-VASCO DAGAMA DL (RVNL) (N22000297)	4-2010	3/2027 (N.A.) {12/2026}	5,060.36 (N.A.) {3,692.60}	3,505.49	N.A.
		632	GADAG-WADI NL (SWR) (N22000299)	4-2013	3/2027 (N.A.) {3/2028}	2,841.84 (N.A.) {2,841.84}	1,306.74	29.00
		633	MARIKUPPAM - KUPPAM (SWR) (N22000308)	4-2012	3/2016 (N.A.) {12/2027}	279.54 (296.72) {296.72}	121.12	14.00
		634	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) (SWR) (N22000486)	3-1996	6/2025 (N.A.) {3/2026}	825.31 (825.31) {825.31}	687.05	83.00
		635	BAIYYAPPANAHALLI-HOSUR (48 KM) (NCRTC) (N22000542)	4-2019	3/2026 (N.A.) {3/2026}	375.67 (N.A.) {375.67}	0.00	N.A.
		636	YESHVANTHPUR-CHANNASANDRA (21.7 KM) (NCRTC) (N22000543)	4-2019	3/2026 (N.A.) {3/2026}	169.65 (N.A.) {169.65}	71.75	N.A.

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		637	BELGAUM-DHARWAD VIA KITTUR (73.10 KM) (UMBRELLA WORK PB#22/2019-20/NR) (SWR) (N22000557)	9-2020	12/2027 (N.A.) {3/2029}	1,590.80 (927.42) {927.42}	0.75	N.A.
		638	HASSAN (ALUR) - BELUR (32 KM) (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000558)	6-2019	4/2028 (N.A.) {3/2028}	748.86 (748.85) {748.85}	0.88	1.00
		639	SHIMOGA-SHIKARIPURA-RANEENNUR (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000559)	9-2019	12/2027 (N.A.) {12/2028}	1,453.73 (994.47) {994.47}	80.24	7.00
		640	BANGALORE-WHITEFIELD-BANGALORE CITY-KRISHNARAJAPURAM QUADRUPLING (SWR) (N22000621)	3-2018	6/2025 (N.A.) {2/2026}	492.87 (492.87) {492.87}	251.52	75.00
	ROAD TRANSPORT AND HIGHWAYS	641	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP (MoRTH) (N24000334)	3-2015	11/2015 (Aug-2024) {8/2024}	165.67 (N.A.) {165.67}	126.47	98.99
		642	4-LANING OF GOA/KARNATAKA BORDER- KUNDAPUR SECTION (NHAI) (N24000462)	7-2012	8/2016 (Jan-2020) {6/2025}	1,655.01 (1,990.99) {1,990.99}	1,818.50	97.80
		643	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS ? PA (MoRTH) (N24001156)	1-2017	9/2017 (May-2023) {5/2023}	166.67 (N.A.) {264.34}	192.08	100.00
		644	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH (MoRTH) (N24001157)	8-2016	2/2017 (Jul-2024) {7/2024}	175.50 (N.A.) {241.60}	178.73	90.01
		645	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 (MoRTH) (N24001158)	3-2018	6/2019 (Dec-2023) {12/2023}	159.97 (N.A.) {242.61}	113.15	100.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		646	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION (MoRTH) (N24001159)	1-2018	7/2018 (N.A.) {3/2022}	159.70 (N.A.) {159.70}	142.88	100.00
		647	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR (MoRTH) (N24001160)	9-2017	10/2018 (Apr-2022) {4/2022}	191.60 (N.A.) {191.60}	112.01	100.00
		648	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- (MoRTH) (N24001161)	12-2017	1/2019 (Apr-2022) {4/2022}	297.30 (N.A.) {318.28}	277.27	100.00
		649	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN (MoRTH) (N24001162)	3-2018	10/2018 (Nov-2022) {11/2022}	325.86 (N.A.) {386.41}	356.76	100.00
		650	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN (MoRTH) (N24001164)	10-2016	3/2017 (Jul-2022) {7/2022}	396.96 (N.A.) {396.96}	329.58	100.00
		651	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT (MoRTH) (N24001165)	11-2016	3/2017 (Oct-2021) {10/2021}	314.90 (N.A.) {314.90}	233.95	100.00
		652	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) (MoRTH) (N24001166)	3-2015	1/2016 (N.A.) {7/2024}	159.12 (N.A.) {159.12}	127.72	98.00
		653	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT (MoRTH) (N24001168)	5-2018	5/2018 (Dec-2023) {12/2023}	171.60 (N.A.) {171.60}	129.72	100.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		654	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U (MoRTH) (N24001172)	1-2017	8/2017 (N.A.) {6/2022}	291.49 (N.A.) {291.49}	238.77	100.00
		655	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH- 167 HAGARI ? JADERCELA SECTION (MoRTH) (N24001173)	2-2017	5/2019 (N.A.) {10/2025}	157.32 (188.00) {187.61}	43.16	60.00
		656	WIDENING TO 2-LANE WIH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT (MoRTH) (N24001387)	1-2017	9/2017 (May-2023) {5/2023}	264.34 (N.A.) {264.34}	201.07	100.00
		657	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA (MoRTH) (N24001388)	3-2019	12/2019 (Nov-2024) {11/2024}	423.15 (N.A.) {423.15}	268.97	82.00
		658	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN (NHAI) (N24001425)	3-2021	11/2021 (Nov-2025) {11/2025}	1,100.88 (1,687.31) {1,687.31}	1,149.04	80.28
		659	4L OF ADDAHOLE TO BANTWAL CROSS SECTION (NHAI) (N24001426)	3-2021	10/2021 (Jun-2025) {6/2025}	317.90 (572.01) {572.01}	370.84	98.00
		660	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) (NHAI) (N24001598)	1-2022	4/2025 (Apr-2025) {4/2025}	1,388.70 (1,388.70) {1,388.70}	438.61	62.50
		661	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. (NHAI) (N24001599)	3-2018	12/2022 (Dec-2022) {12/2025}	440.16 (N.A.) {440.16}	355.11	69.73
		662	BANGALORE/TN BORDER TO HOSKOTE (NHAI) (N24001674)	2-2023	2/2025 (Sep-2025) {9/2025}	1,240.60 (1,181.68) {1,181.68}	942.92	81.52

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		663	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 (NHAI) (N24001676)	12-2022	6/2025 (Mar-2026) {6/2025}	2,718.46 (N.A.) {2,718.46}	438.90	53.72
		664	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12 (NHAI) (N24001677)	11-2022	5/2024 (Apr-2025) {4/2025}	226.76 (226.76) {226.76}	86.76	71.87
		665	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 (NHAI) (N24001679)	10-2022	4/2025 (Dec-2025) {12/2025}	1,479.30 (1,479.30) {1,479.30}	676.61	93.10
		666	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE (NHAI) (N24001680)	3-2021	10/2024 (Jan-2026) {1/2026}	1,409.68 (1,808.12) {1,808.12}	1,032.44	59.00
		667	TUMKUR - NELAMANGALA(6L) (NHAI) (N24001681)	8-2022	8/2025 (Mar-2026) {3/2026}	2,032.15 (2,032.15) {2,032.15}	184.86	52.08
		668	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA (NHAI) (N24001682)	11-2021	3/2024 (Mar-2024) {12/2026}	294.62 (309.90) {309.90}	55.68	15.06
		669	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION (NHAI) (N24001684)	9-2020	1/2023 (Sep-2020) {5/2025}	688.00 (602.09) {688.00}	514.23	80.02
		670	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 (NHAI) (N24001687)	10-2021	10/2023 (Dec-2025) {12/2025}	1,331.77 (2,082.98) {2,082.98}	477.33	76.52
		671	BALANCE WORK OF CONTSRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM. 54.370 TO KM. 101.400 (BI (MoRTH) (N24001936)	3-2021	3/2023 (Jul-2024) {7/2024}	344.79 (N.A.) {344.79}	10.00	90.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		672	BALANCE WORK OF REHABILITATION AND UPGRADING TO 2LANE/2LANE WITH PAVED SHOULDER CONFIGURATION AND ST (MoRTH) (N24001937)	2-2023	2/2024 (Feb-2025) {2/2025}	398.48 (N.A.) {398.48}	5.00	50.00
		673	CONSTRUCTION OF ELEVATED CORRIDOR FROM KM. 135.650 TO 136.300 ON 63, FROM KM. 249 TO KM. 250.050 ON (MoRTH) (N24001938)	6-2021	6/2024 (Jun-2025) {6/2025}	298.00 (N.A.) {298.00}	10.70	52.00
		674	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24001940)	1-2023	1/2026 (Sep-2025) {9/2025}	166.58 (N.A.) {166.58}	3.54	N.A.
		675	WIDENING TO 4 LANE FROM KM. 133.00 TO 158.04 (DESIGN CHAINAGE KM. 130.88 TO 155.145) (SHIRUR CROSS T (MoRTH) (N24001941)	1-2023	1/2025 (Jan-2025) {1/2025}	350.69 (N.A.) {350.69}	10.00	56.00
		676	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM. 33.13 TO KM. 40.23 AND KM. 52.00 TO KM. 71.00 (EX (MoRTH) (N24001943)	9-2022	3/2024 (Jan-2025) {1/2025}	172.98 (N.A.) {172.98}	6.48	65.00
		677	WIDENING TO INTERMEDIATE/TWO LANE TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHANAGES KM 112.750 TO (MoRTH) (N24001944)	1-2023	6/2024 (Jul-2024) {7/2024}	255.88 (N.A.) {255.88}	60.99	78.24
		678	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 116.800 TO 149.070(DESIGN CHANGES) ON HOSADURGA HOL (MoRTH) (N24001945)	8-2022	2/2024 (Dec-2024) {12/2024}	170.34 (N.A.) {170.34}	4.25	72.00
		679	WIDENING TO 2 LANES WITH PAVED SHOULDER FROM KM 24.400 TO 27.270, 40.500 TO 41.900, 84.300 TO 88.20 (MoRTH) (N24001946)	11-2022	11/2024 (Nov-2024) {11/2024}	218.93 (N.A.) {218.93}	10.00	95.25

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		680	WIDENING TO EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FROM DESIGN KM 153.00 (MoRTH) (N24001947)	2-2023	2/2025 (Feb-2025) {2/2025}	177.94 (N.A.) {177.94}	6.66	47.00
		681	WIDENING TO 4 LANE FROM KM 51.60 TO 76.20 (HEBRI TO PARKALA) AND FROM KM 85.20 TO 88.90 (KARAVALI JU (MoRTH) (N24001948)	10-2022	10/2024 (Dec-2024) {12/2024}	355.72 (N.A.) {355.72}	11.32	60.00
		682	FOUR LANING OF LEFT OVER WORKS OF HOSPET BELLARY KARNATAKA/ AP BORDER FROM KM.280.080 TO KM. 375.450 (NHAI) (N24001989)	3-2023	5/2025 (N.A.) {5/2025}	830.28 (N.A.) {830.28}	652.09	75.30
		683	DEVELOPMENT OF 6 LANE ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KM. 97.000 TO KM. 162.500 MARADGI S (NHAI) (N24001993)	12-2022	10/2025 (N.A.) {10/2025}	1,589.00 (N.A.) {1,589.00}	725.46	60.70
		684	4/6L OF BANGALORE - PUNE SECTION OF BYPASS CONNECTING DHARWAD - HUBLI FROM KM. 403.80 TO KM. 433.20 (NHAI) (N24001994)	5-2022	3/2023 (Sep-2025) {9/2025}	1,135.39 (N.A.) {1,135.39}	396.27	69.60
		685	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM 422.000 TO 523.600 (CHITR (MoRTH) (N24002011)	12-2021	6/2024 (Dec-2024) {12/2024}	516.96 (N.A.) {516.96}	19.93	75.00
		686	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40.00 TO KM 75.00 (EXISTING CHAINAGES) OF MANGALOR (MoRTH) (N24002012)	3-2023	3/2025 (Mar-2025) {3/2025}	718.52 (N.A.) {718.52}	24.81	23.00
		687	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM KM.0 TO KM. 80 ON NH 548B (VIJAYAPURA-SANKESWAR SE (MoRTH) (N24002013)	3-2021	2/2022 (Oct-2024) {10/2024}	766.64 (N.A.) {766.64}	13.55	75.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		688	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24002186)	3-2024	9/2025 (N.A.) {9/2025}	166.58 (N.A.) {166.58}	3.62	N.A.
		689	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM 55.6 TO KM 90.7 (EXISTING CHAINAGES) OF NH-766C ((MoRTH) (N24002187)	2-2024	2/2026 (N.A.) {2/2026}	313.56 (N.A.) {313.56}	53.65	N.A.
		690	WIDENING TO 2L+PS FROM KM 71.00 TO 104.00 (EXISTING CHAINAGES) (SARJAPUR TO PATTADKALLU) ON BHANAPUR (MoRTH) (N24002188)	3-2024	3/2026 (N.A.) {3/2026}	445.62 (N.A.) {445.62}	33.24	N.A.
		691	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0.00 (DESIGN CHAINAGE 0.00) TO KM 23.338 (DESIGN C (MoRTH) (N24002189)	9-2024	3/2026 (N.A.) {3/2026}	196.05 (N.A.) {196.05}	2.34	N.A.
	STEEL	692	SCREENING PLANT-II, DONIMALAI (NMDCL) (N12000136)	9-2023	8/2026 (N.A.) {8/2026}	1,043.63 (N.A.) {1,043.63}	181.21	13.61
	URBAN DEVELOPMENT I	693	BANGALORE METRO RAIL PROJECT PHASE-2 (BMRCL) (N28000058)	2-2014	2/2021 (N.A.) {3/2025}	26,405.14 (N.A.) {26,405.14}	20,936.29	N.A.
		694	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B (BMRCL) (N28000151)	6-2021	6/2026 (N.A.) {6/2026}	14,788.10 (N.A.) {14,788.10}	2,424.04	N.A.
KERALA	CIVIL AVIATION	695	CALICUT AIRPORT - DEVELOPMENT OF ADDITIONAL RESA ON EITHER END ON RUNWAY 10-28 AT CALICUT AIRPORT (AAI) (N04000111)	6-2023	9/2025 (N.A.) {9/2025}	484.57 (323.98) {323.98}	74.41	18.00
	DEPARTMENT OF HIGHER EDUCATION	696	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA (CPWD EDUCATION) (N28000140)	7-2019	3/2021 (N.A.) {11/2025}	753.63 (N.A.) {753.63}	411.86	67.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	697	REPLACEMENT AND EXTENSION OF JETTY PIPELINES AT KOCHI REFINERY (BPCL) (N16000508)	3-2023	3/2026 (N.A.) {3/2026}	621.87 (N.A.) {621.87}	168.50	81.50
		698	SETTING UP POLYPROPYLENE UNIT AT KOCHI REFINERY (BPCL) (N16000530)	12-2023	10/2027 (N.A.) {10/2027}	4,460.00 (N.A.) {4,460.00}	223.50	10.10
	RAILWAYS	699	TRIVANDRUM-KANYAKUMARI DOUBLING (SR) (N22000399)	2-2015	3/2024 (N.A.) {12/2027}	1,431.90 (N.A.) {3,785.45}	3,184.42	42.10
		700	ERNAKULAM-KUMBALAM - PATCH DOUBLING (7.71 KM) (SR) (N22000619)	12-2010	3/2028 (N.A.) {12/2026}	600.82 (N.A.) {595.39}	282.48	8.00
		701	KUMBALAM-THURAVUR - PATCH DOUBLING (15.59 KM) (SR) (N22000620)	12-2011	3/2027 (N.A.) {12/2026}	812.85 (N.A.) {802.80}	280.39	7.00
	ROAD TRANSPORT AND HIGHWAYS	702	4-LANNING OF THALSERRY -MAHE BYPASS (NHAI) (N24000704)	9-2017	5/2020 (Nov-2023) {2/2024}	1,124.11 (1,573.18) {1,573.18}	1,525.92	100.00
		703	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH (NHAI) (N24000784)	2-2018	2/2023 (Dec-2024) {6/2025}	1,424.77 (2,065.95) {2,065.95}	901.96	95.01
		704	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK (MoRTH) (N24001369)	2-2017	8/2017 (Mar-2022) {8/2024}	294.28 (296.53) {296.53}	286.80	98.00
		705	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) (MoRTH) (N24001370)	2-2017	9/2017 (Jan-2023) {8/2024}	380.76 (372.87) {372.87}	347.04	100.00
		706	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE (NHAI) (N24001648)	8-2022	1/2026 (N.A.) {1/2026}	2,429.52 (N.A.) {2,429.52}	1,088.32	59.90

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		707	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 (NHAI) (N24001649)	12-2021	2/2025 (Feb-2025) {1/2026}	3,273.61 (N.A.) {3,273.61}	777.99	61.01
		708	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTTAM SECTION OF NH-66(OLD NH-47) FROM KM. 517+250 TO KM.54 (NHAI) (N24001650)	12-2021	1/2025 (Apr-2026) {4/2026}	3,635.64 (N.A.) {3,635.64}	324.02	38.97
		709	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O (NHAI) (N24001651)	9-2021	9/2024 (Mar-2026) {9/2024}	2,878.97 (N.A.) {2,878.97}	565.38	43.79
		710	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR (NHAI) (N24001652)	3-2020	6/2022 (Feb-2024) {6/2024}	210.37 (216.94) {216.94}	198.10	100.00
		711	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH ?66 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 ((NHAI) (N24001653)	11-2021	4/2025 (N.A.) {4/2025}	3,565.82 (N.A.) {3,064.11}	1,997.54	61.99
		712	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 (NHAI) (N24001654)	6-2021	3/2025 (Feb-2026) {2/2026}	2,641.37 (N.A.) {2,641.37}	607.07	76.05
		713	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX (NHAI) (N24001655)	6-2021	2/2025 (N.A.) {11/2025}	3,606.00 (3,946.56) {3,946.56}	3,120.31	71.59
		714	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. (NHAI) (N24001656)	6-2021	3/2025 (N.A.) {12/2025}	2,595.00 (N.A.) {4,009.57}	3,044.86	64.07

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		715	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC (NHAI) (N24001657)	6-2021	10/2024 (Dec-2025) {12/2025}	2,842.14 (N.A.) {2,842.14}	477.69	70.95
		716	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM (NHAI) (N24001658)	1-2021	7/2024 (Mar-2025) {3/2025}	4,265.42 (N.A.) {4,728.40}	3,474.30	99.10
		717	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH- 66(OLD NH-17) FROM DESIGN CH (NHAI) (N24001659)	2-2021	7/2024 (Mar-2025) {3/2025}	3,375.31 (3,824.07) {3,824.07}	2,351.49	98.30
		718	SIX LANING OF THALIPARAMBHA- MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH (NHAI) (N24001660)	8-2020	2/2024 (Aug-2025) {3/2026}	2,714.60 (3,557.65) {2,714.60}	1,903.94	73.00
		719	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 (NHAI) (N24001661)	10-2020	4/2024 (May-2025) {3/2026}	3,219.47 (3,898.46) {3,896.46}	2,295.21	57.90
		720	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH (NHAI) (N24001662)	5-2020	5/2024 (Nov-2021) {7/2025}	1,981.07 (2,651.79) {1,981.07}	1,540.46	96.40
		721	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ (NHAI) (N24001663)	6-2020	4/2024 (Oct-2021) {3/2026}	3,041.65 (3,867.66) {3,041.65}	2,406.40	82.10
		722	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ (NHAI) (N24001664)	6-2020	4/2024 (Oct-2021) {3/2026}	1,746.45 (2,538.06) {1,746.45}	1,262.05	82.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	URBAN DEVELOPMENT	723	WIDENING/DEVELOPMENT OF EXISTING NH-85 FROM KM 0.000 TO KM 124.636 SECTION TO 2L@L+PS SECTION IN TH (NHAI) (N24002074)	8-2022	6/2025 (N.A.) {6/2025}	1,231.74 (N.A.) {1,231.74}	452.60	48.20
		724	KOCHI METRO RAIL PROJECT PHASE II FROM JLN STADIUM TO INFOPARK VIA KAKKANAD (KMRCL) (N28000158)	7-2018	11/2026 (N.A.) {11/2026}	1,957.05 (N.A.) {1,957.05}	250.63	7.40
		725	KOCHI METRO RAIL PROJECT PHASE IB SECTION FROM S N JUNCTION TO THRIPIVITHURA (KMRCL) (N28000159)	6-2019	9/2023 (N.A.) {9/2023}	355.70 (448.00) {448.33}	448.39	100.00
LADAKH	CIVIL AVIATION	726	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT (AAI) (N04000078)	7-2018	9/2021 (Oct-2025) {10/2025}	480.33 (640.00) {640.00}	409.08	63.67
		727	KARGIL-ZANSKR PACKAGE-1 (NHIDCL) (N24001343)	3-2021	1/2023 (Dec-2024) {11/2025}	384.23 (N.A.) {384.23}	162.54	60.40
	ROAD TRANSPORT AND HIGHWAYS	728	KARGIL-ZANSKR PACKAGE-2 (NHIDCL) (N24001344)	3-2021	1/2023 (Feb-2025) {11/2025}	404.89 (N.A.) {404.89}	244.21	65.54
		729	KARGIL-ZANSKR PACKAGE-3 (NHIDCL) (N24001345)	8-2020	1/2023 (Aug-2025) {8/2025}	381.01 (N.A.) {381.01}	230.28	74.72
		730	KARGIL-ZANSKR PACKAGE-8 (NHIDCL) (N24001348)	3-2021	1/2023 (Aug-2025) {8/2025}	398.37 (N.A.) {398.37}	274.39	82.28
		731	CONSTRUCTION OF REALIGNMENT BETWEEN PANDRASS- PASHKYUN (TOTAL LENGTH 27.10 KM) ON ROAD ZOZILA-KARGIL (BRO) (N24001999)	11-2021	6/2025 (N.A.) {6/2025}	426.14 (N.A.) {426.14}	16.27	37.00
MADHYA PRADESH	CIVIL AVIATION	732	UPGRADATION OF JABALPUR AIRPORT (AAI) (N04000087)	6-2016	6/2021 (Jul-2024) {7/2024}	412.24 (N.A.) {412.24}	402.81	100.00
		733	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 (AAI) (N04000098)	10-2021	8/2023 (Aug-2024) {8/2024}	446.12 (455.00) {455.00}	451.55	100.00
	COAL	734	KANCHAN OC EXPANSION (SECL) (N06000125)	12-2014	3/2021 (Mar-2026) {3/2026}	371.04 (N.A.) {371.04}	137.20	47.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		735	AMADAND OPENCAST EXPANSION PROJECT (SECL) (N06000148)	3-2016	3/2021 (Mar-2027) {3/2027}	869.44 (N.A.) {869.44}	272.09	75.00
		736	GANDHIGRAM UG MINE (WCL) (N06000183)	8-2019	3/2026 (N.A.) {3/2026}	414.16 (N.A.) {414.16}	11.75	28.00
		737	BLOCK-B EXPANSION OPENCAST PROJECT (NCL) (N06000184)	7-2019	3/2023 (N.A.) {3/2027}	998.71 (N.A.) {998.71}	438.64	42.57
		738	NIGAH EXPANSION OCP (15 TO 25 MTPA) (NCL) (N06000196)	11-2020	3/2025 (N.A.) {3/2028}	1,729.68 (N.A.) {1,729.68}	766.06	44.29
		739	RAMPUR BATURA OC (4.0 MTY) (SECL) (N06000233)	7-2019	3/2026 (N.A.) {3/2026}	1,248.93 (N.A.) {1,248.93}	488.60	44.00
		740	TAWA III UG MINE (WCL) (N06000250)	12-2021	3/2027 (N.A.) {3/2027}	314.09 (N.A.) {324.25}	0.56	9.00
		741	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY) (WCL) (N06000257)	9-2022	3/2027 (N.A.) {3/2027}	399.20 (N.A.) {497.01}	64.13	42.00
		742	VISHNUPURI UG TO OC (WCL) (N06000260)	11-2022	3/2029 (N.A.) {3/2029}	220.62 (N.A.) {227.65}	0.00	7.00
		743	URDHAN OC (WCL) (N06000265)	1-2023	3/2031 (N.A.) {3/2031}	206.88 (N.A.) {228.42}	22.12	9.00
		744	SHARDA UG (WCL) (N06000266)	9-2023	3/2028 (N.A.) {3/2028}	166.25 (N.A.) {200.16}	1.69	11.00
	PETROLEUM	745	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF (BPCL) (N16000518)	5-2023	5/2028 (N.A.) {5/2028}	43,367.00 (N.A.) {43,367.00}	1,594.90	12.20
	POWER	746	SHAJAPUR 325MW SOLAR PV PROJECT (NTPC) (N18000348)	6-2022	3/2024 (Jun-2025) {6/2025}	1,530.49 (N.A.) {1,578.34}	1,210.05	90.00
		747	TS FOR EVACUATION POWER RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX): PART-C (PGCIL) (N18000392)	8-2024	8/2026 (N.A.) {8/2026}	2,708.00 (N.A.) {2,708.00}	189.90	21.70

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		748	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-2 5.5GW] JAISALMER/BARME (PGCIL) (N18000399)	10-2024	10/2026 (N.A.) {10/2026}	3,674.00 (N.A.) {3,674.00}	234.57	10.30
	RAILWAYS	749	RAMGANJMUHDI-BHOPAL (NL),WCR (WCR) (220100314)	4-2001	12/2025 (Dec-2025) {6/2026}	3,032.00 (3,032.46) {5,125.16}	3,423.90	69.00
		750	RATLAM-MHOW-KHANDWA-AKOLA (GC) (WR) (N22000120)	4-2008	2/2027 (Feb-2027) {2/2027}	5,677.88 (5,677.80) {6,203.51}	4,284.80	80.00
		751	KATNI - SINGRAULI DOUBLING PROJECT (WCR) (N22000351)	12-2015	12/2026 (Dec-2027) {12/2027}	2,445.29 (2,445.30) {4,353.50}	3,099.24	91.00
		752	KATNI GRADE SEPARATOR/BYE PASS (WCR) (N22000416)	8-2016	9/2024 (Jun-2025) {9/2024}	1,247.64 (1,247.64) {2,300.00}	1,427.58	89.00
		753	ANUPPUR-KATNI (SECR) (N22000485)	4-2015	12/2021 (Dec-2023) {3/2025}	1,860.94 (1,680.00) {2,311.02}	1,929.51	100.00
		754	NIMACH BADI SADRI NEW LINE PROJECT (WR) (N22000503)	4-2017	3/2022 (N.A.) {3/2026}	495.18 (N.A.) {495.18}	289.65	45.00
		755	NIMACH-RATLAM (133 KM) (WR) (N22000536)	10-2021	10/2027 (Dec-2025) {12/2025}	1,095.88 (1,095.88) {1,095.88}	1,048.60	72.00
		756	SATNA - REWA (50 KM) (WCR) (N22000554)	11-2015	3/2026 (N.A.) {3/2026}	500.00 (40.00) {500.00}	1.41	80.00
		757	INDORE BUDNI (INDORE JABALPUR) (RVNL) (N22000601)	9-2018	9/2030 (N.A.) {9/2030}	7,474.01 (N.A.) {7,393.75}	1,004.86	N.A.
	ROAD TRANSPORT AND HIGHWAYS	758	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 (MoRTH) (N24000513)	3-2015	8/2017 (Dec-2023) {6/2025}	511.83 (N.A.) {511.83}	478.84	93.06
		759	4LBERKHEDI TO GODPEHRA NH-44 (NHAI) (N24001614)	2-2022	11/2024 (N.A.) {12/2025}	524.84 (N.A.) {524.84}	2,434.64	60.00
		760	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I) (NHAI) (N24001615)	3-2021	4/2024 (Jun-2025) {6/2025}	790.78 (N.A.) {790.78}	2,139.45	77.02

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		761	KATNI BYPASS FROM KM. 359.50 TO KM. 378.50 (NHAI) (N24001618)	9-2019	9/2022 (N.A.) {2/2025}	194.40 (235.00) {235.00}	208.32	98.84
		762	4L OF CHANDESARA TO KHEDEKHAJURIYA FROM KM. 0.000 TO (-) 750 AND KM 0.000 TO KM 41.400 OF NH-752D (NHAI) (N24001759)	1-2020	6/2024 (Jun-2025) {6/2025}	909.84 (N.A.) {909.84}	502.49	99.00
		763	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] (NHAI) (N24001762)	10-2021	1/2024 (Dec-2025) {12/2025}	1,146.22 (N.A.) {1,146.22}	662.30	91.31
		764	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] (NHAI) (N24001766)	1-2022	10/2024 (N.A.) {12/2025}	1,011.29 (N.A.) {1,011.29}	284.80	70.02
		765	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND (NHAI) (N24001767)	1-2021	4/2024 (N.A.) {12/2025}	1,001.69 (N.A.) {1,001.69}	517.31	82.11
		766	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69 (NHAI) (N24001770)	2-2022	3/2024 (Mar-2025) {5/2025}	417.51 (N.A.) {417.51}	312.94	100.00
		767	2- LANE WITH PAVED SHOULDERS OF HINOTIYA TO MEHULWA FROM DESIGN KM 27+000 90F EXISTING SH-19 KM 26+5 (NHAI) (N24001921)	8-2021	9/2025 (N.A.) {9/2025}	581.65 (592.03) {581.65}	125.56	43.79
		768	CONSTRUCTION OF MIHONA BYPASS, LAHAR BYPASS, DABOH BYPASS and BHANDER BYPASS (TOTAL LENGTH 20.60 KM) (MoRTH) (N24001962)	3-2022	12/2024 (N.A.) {3/2025}	179.19 (N.A.) {179.19}	47.91	96.00
		769	UPGRADATION OF NASRULLAGANI-REHTI-BUDHNI SCCTION TO 2-LANE WITH PAVED SHOULDER FROM KM 0+150 TO KM (MoRTH) (N24001963)	12-2021	10/2024 (N.A.) {9/2025}	305.12 (N.A.) {305.12}	71.47	34.46

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		770	UPGRADATION and WIDENING OF JHARKHEDA- BERASIA - DHOLKHEDI FROM DESIGN KM 0+000 TO KM 87+900 (DESIGN (MoRTH) (N24001964)	3-2022	5/2025 (N.A.) {5/2025}	365.21 (N.A.) {365.21}	112.27	64.00
		771	REHABILITATION AND UPGRADATION OF KURWAI?MUNGAOLI?CHANDERI ROAD SECTION OF NH-346, FROM DESIGN CHAIN (MoRTH) (N24001965)	3-2022	2/2025 (N.A.) {12/2025}	386.49 (N.A.) {386.49}	77.42	48.77
		772	BALANCE WORK FOR REHABILITATION AND UP-GRADATION OF SIDHI-SINGRAULI FROM KM 82.400 TO KM 187.993 SEC (MoRTH) (N24001966)	12-2020	4/2023 (N.A.) {6/2025}	529.44 (N.A.) {529.44}	378.40	62.00
		773	4L GREENFIELD RUDHI TO DESHGAON (PKG V OF BETUL-KHANDWA/DESHGAON) - N/04015/06003/MP (NHAI) (N24001967)	11-2018	10/2025 (N.A.) {10/2025}	521.21 (N.A.) {521.21}	98.23	39.80
		774	REHABILITATION AND UPGRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION OF JIRAPUR-SUSNER-MP- RJ B (MoRTH) (N24002018)	1-2022	3/2025 (N.A.) {3/2025}	239.72 (232.22) {232.22}	73.40	100.00
		775	UPGRADATION OF DINDORI-SAGARTOLA- KABICHABUTRA (MP-CG BORDER) SECTION OF NH -45 FROM KM 0+00(DESIGN) (MoRTH) (N24002019)	1-2022	9/2025 (N.A.) {9/2025}	329.14 (319.09) {319.09}	52.70	50.12
		776	CONSTRUCTION OF KAITHI-PADARIA KALA BYPASS, PATNA-TAMOLI BYPASS, JASO BYPASS , NAGOD BYPASS (TOTAL L (MoRTH) (N24002020)	3-2022	10/2025 (N.A.) {10/2025}	158.36 (158.00) {158.36}	22.68	30.00
		777	BALANCE WORK OF 4L OF NAURADEHI SANCTUARY DE-SCOPED STRETCH OF HIRAN RIVER TO SINDOOR RIVER FROM KM. (NHAI) (N24002067)	1-2021	7/2023 (N.A.) {4/2025}	178.18 (N.A.) {178.18}	161.64	94.65

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		778	CONSTRUCTION OF 4-LANE FROM BARELA TO MANEGAON SECTION OF NH-30 FROM DESIGN CH. 2.900 TO DESIGN CH. (NHAI) (N24002068)	12-2022	3/2025 (N.A.) {12/2025}	652.33 (N.A.) {652.33}	334.34	73.16
		779	CONSTRUCTION OF ADDITIONAL 3 LANE WITH PAVED SHOULDER (DESIGN LENGTH 8.87 KM) AS REALIGNMENT OF BAKA (NHAI) (N24002069)	7-2022	12/2024 (N.A.) {12/2024}	209.29 (N.A.) {209.29}	140.22	100.00
		780	INDORE - EDLABAD (PKG-II) [TEJAJINAGAR TO BALWARA] (NHAI) (N24002070)	1-2022	1/2025 (N.A.) {1/2026}	1,162.80 (N.A.) {1,162.80}	493.76	80.00
		781	CONSTRUCTION OF (I) 4-LANE HIGHWAY FROM VIDISHA TO HINOTIYA FROM KM. 0.000 TO KM. 27.000 (LENGTH=27 (NHAI) (N24002077)	9-2022	12/2025 (N.A.) {12/2025}	1,000.63 (N.A.) {1,000.63}	210.15	50.72
		782	FOUR LANING OF RAGHOGARH (DESIGN CH.29.300/EXISTING CH. 29.555) TO NANASA (DESIGN CH.92.971/EXISTING (NHAI) (N24002166)	3-2024	3/2026 (Mar-2026) {3/2026}	799.20 (N.A.) {799.20}	306.27	35.04
		783	BALANCE WORKS OF 4 LANE DIVIDED CARRIAGEWAY OF MISSING LINK SECTION OF NH-39 (REWA BYPASS) FROM JUNC (NHAI) (N24002200)	4-2024	4/2026 (N.A.) {4/2026}	355.36 (N.A.) {355.36}	39.06	34.40
	<u>SOCIAL JUSTICE</u>	784	CENTRE FOR DISABILITY SPORTS (CPWD) (N38000001)	2-2019	3/2024 (N.A.) {3/2024}	170.99 (N.A.) {170.99}	73.80	74.00
	<u>URBAN DEVELOPMENT</u>	785	BHOPAL METRO RAIL (MPMRCL) (N28000124)	11-2018	2/2023 (Jun-2028) {6/2028}	6,941.40 (N.A.) {6,941.40}	2,970.09	40.90
		786	INDORE METRO RAIL (MPMRCL) (N28000125)	11-2018	2/2023 (Dec-2028) {12/2028}	7,500.80 (N.A.) {7,500.80}	3,724.27	52.99
<u>MAHARASHTRA</u>	<u>CIVIL AVIATION</u>	787	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT (AAI) (N04000079)	3-2017	4/2021 (Dec-2023) {12/2023}	475.39 (N.A.) {520.00}	532.99	100.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		788	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM (AAI) (N04000096)	6-2017	12/2020 (Apr-2024) {4/2024}	255.68 (270.00) {270.00}	267.86	100.00
	COAL	789	AMALGAMATED YEKONA-I YEKONA-II (WCL) (N06000132)	8-2015	3/2025 (N.A.) {3/2025}	727.28 (N.A.) {727.28}	530.02	86.00
		790	UKNI DEEP OC (WCL) (N06000179)	1-2019	3/2021 (Mar-2025) {3/2025}	237.06 (N.A.) {318.14}	163.86	91.00
		791	GHONSA EXPANSION DEEP OC (WCL) (N06000205)	3-2021	3/2028 (N.A.) {3/2029}	184.71 (N.A.) {241.72}	9.25	6.00
		792	SASTI EXPANSION OC (WCL) (N06000206)	8-2020	3/2026 (N.A.) {3/2026}	319.04 (N.A.) {371.59}	68.64	24.00
		793	DHUPTALA OC(SASTI UG TO OC) (WCL) (N06000209)	10-2021	3/2028 (N.A.) {3/2028}	711.00 (N.A.) {720.87}	159.15	33.00
		794	ADASA UG TO OC (1.50 MTY) (WCL) (N06000219)	11-2018	3/2024 (Mar-2025) {3/2025}	316.00 (N.A.) {333.43}	208.20	78.00
		795	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) (WCL) (N06000222)	2-2020	3/2027 (N.A.) {3/2027}	822.88 (N.A.) {1,184.33}	578.89	48.00
		796	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) (WCL) (N06000226)	9-2018	3/2024 (Mar-2025) {3/2025}	235.90 (N.A.) {313.34}	116.46	87.00
		797	SAONER UG MINE I EXPANSION (WCL) (N06000251)	1-2022	3/2028 (N.A.) {3/2028}	228.64 (N.A.) {253.51}	118.34	27.00
		798	SINGHORI DEEP OC (WCL) (N06000252)	5-2022	3/2029 (N.A.) {3/2029}	335.75 (N.A.) {421.84}	22.01	16.00
		799	MAKARDHOKDA I EXPANSION OC (WCL) (N06000253)	6-2022	3/2026 (N.A.) {3/2026}	361.87 (N.A.) {497.06}	33.90	12.00
		800	BHATADI EXPANSION OC (WCL) (N06000254)	5-2022	3/2028 (N.A.) {3/2028}	580.60 (N.A.) {729.86}	61.33	17.00
		801	NEW MAJARI UG TO OC (3.0 MTY) (WCL) (N06000255)	9-2022	3/2027 (N.A.) {3/2027}	402.27 (N.A.) {496.38}	47.99	27.00
		802	BHANEGAON OC (1.15MTY) (WCL) (N06000256)	9-2022	3/2028 (N.A.) {3/2028}	405.20 (N.A.) {494.60}	10.21	7.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		803	GOKUL EXPANSION OC (WCL) (N06000264)	4-2021	3/2026 (N.A.) {3/2026}	309.58 (N.A.) {456.95}	3.65	7.00
		804	KOLGAON EXPANSION (DEEP) OC (WCL) (N06000267)	9-2023	3/2027 (N.A.) {3/2027}	198.71 (N.A.) {206.19}	0.55	5.00
		805	AMALGAMATED GAURI PAUNI EXPANSION OC (WCL) (N06000271)	3-2024	3/2030 (N.A.) {3/2030}	1,225.21 (N.A.) {1,428.25}	52.83	17.00
		806	GAURI CENTRAL OCM (WCL) (N06000278)	6-2024	3/2030 (N.A.) {3/2030}	973.07 (N.A.) {1,015.07}	0.00	N.A.
		807	BALLARPUR NORTHWEST OC MINE (WCL) (N06000282)	12-2022	3/2029 (N.A.) {3/2029}	360.18 (N.A.) {360.18}	0.00	N.A.
		808	NORTHERN EXTENSION OF MUNGOLI NIRGUDA DEEP OC (WCL) (N06000283)	6-2024	3/2029 (N.A.) {3/2029}	1,024.91 (N.A.) {1,184.44}	0.00	N.A.
		809	AMALGAMATED GONDEGAON - GHATROHAN EXPANSION OCM (WCL) (N06000284)	9-2024	3/2029 (N.A.) {3/2029}	668.54 (N.A.) {871.59}	0.00	N.A.
	DEPARTMENT OF HIGHER EDUCATION	810	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI (CPWD EDUCATION) (N28000117)	1-2018	7/2020 (Nov-2023) {2/2024}	223.37 (275.00) {230.00}	141.16	100.00
	HEALTH AND FAMILY WELFARE	811	500 BEDDED HOSPITAL INCLUDING 50 SUPERSPECIALITY BEDS FOR ESIC AT PUNE (CPWD) (N21000033)	7-2022	9/2025 (N.A.) {9/2025}	429.25 (N.A.) {429.25}	99.08	N.A.
	PETROLEUM	812	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS (ONGC) (N16000213)	12-2015	4/2018 (Dec-2023) {6/2025}	3,190.69 (3,375.90) {3,375.90}	3,023.97	89.00
		813	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND (GAIL) (N16000430)	5-2019	4/2025 (Oct-2025) {10/2025}	8,797.00 (11,256.00) {11,256.00}	6,367.78	83.78
		814	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL (BPCL) (N16000442)	4-2021	6/2024 (N.A.) {4/2025}	1,164.69 (N.A.) {1,164.69}	873.03	82.20

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		815	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY (IOCL) (N16000446)	9-2021	10/2023 (Jun-2025) {6/2025}	378.00 (N.A.) {378.00}	142.31	90.60
		816	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI (BPCL) (N16000452)	5-2022	3/2024 (N.A.) {9/2024}	423.39 (N.A.) {423.39}	253.13	75.50
		817	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA) (IOCL) (N16000456)	9-2022	8/2025 (N.A.) {3/2026}	165.00 (N.A.) {165.00}	78.60	65.93
		818	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK (ONGC) (N16000470)	6-2022	10/2025 (N.A.) {2/2026}	4,144.41 (6,406.90) {6,406.90}	3,203.26	80.50
		819	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS (IOCL) (N16000487)	3-2022	3/2030 (N.A.) {9/2031}	865.00 (N.A.) {865.00}	63.81	2.80
		820	ANDHERI RESIDENTIAL TOWERS MUMBAI (IOCL) (N16000503)	6-2017	5/2025 (Jun-2026) {6/2026}	281.35 (389.67) {389.67}	216.88	50.50
		821	CONSTRUCTION OF ADDITIONAL TANKAGES AND ALLIED FACILITIES AT JNPT TERMINAL (IOCL) (N16000504)	4-2022	10/2024 (Aug-2026) {8/2026}	341.43 (436.14) {436.14}	239.13	47.52
		822	INSTALLATION OF INDEPENDENT DE- AROMATIZED SOLVENTS PRODUCTION FACILITIES AT MUMBAI REFINERY (BPCL) (N16000507)	3-2023	7/2025 (N.A.) {7/2025}	405.00 (N.A.) {405.00}	181.00	78.20
		823	PART REPLACEMENT PIPELINE PROJECT (PRPP) (ONGC) (N16000515)	11-2022	5/2024 (Dec-2024) {11/2025}	1,219.48 (N.A.) {1,145.10}	678.98	87.00
		824	POL AND LOBS INSTALLATIONS WITH RECEIPT PIPELINES AT RASAYANI (BPCL) (N16000519)	5-2023	5/2026 (N.A.) {5/2026}	2,585.00 (N.A.) {2,585.00}	463.12	53.80

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		825	MHN TCPP PGC BGC PROJECT (MTPBP) (ONGC) (N16000526)	2-2024	5/2026 (N.A.) {5/2026}	2,329.45 (N.A.) {2,354.23}	523.00	40.50
		826	PRP-VIII GROUP B (NH AND BS ASSET) (ONGC) (N16000533)	6-2024	5/2026 (N.A.) {2/2026}	2,379.84 (N.A.) {2,379.84}	1,362.62	57.80
		827	HP TDAE UNIT IN MUMBAI REFINERY (HPCL) (N16000534)	6-2024	4/2026 (N.A.) {4/2026}	240.00 (N.A.) {240.00}	26.53	26.30
		828	INTEGRATED DEVELOPMENT OF 4 CONTRACT AREAS UNDER DSF2 (ONGC) (N16000537)	5-2023	4/2027 (N.A.) {4/2027}	6,183.79 (N.A.) {6,183.79}	0.00	12.60
		829	LUBE MODERNIZATION AND BOTTOM UPGRADATION PROJECT (HPCL) (N16000540)	12-2024	3/2028 (N.A.) {3/2028}	4,679.00 (N.A.) {4,679.00}	171.65	4.20
	POWER	830	BIKANER SOLAR POWER PROJECT (SJVN) (N18000335)	4-2022	5/2024 (N.A.) {9/2025}	5,491.89 (532.00) {5,491.89}	4,229.40	76.00
		831	TS FOR EVACUATION OF 7GW RE INJECTION AT KHAVDA PS UNDER PHASE- IV PART E4 (PGCIL) (N18000377)	11-2023	7/2025 (N.A.) {9/2025}	224.00 (N.A.) {224.00}	2.64	6.00
	RAILWAYS	832	AHMEDNAGAR-PARLI VAIJNATH(NL) CR (CR) (220100181)	2-1997	3/2026 (N.A.) {1/2026}	2,539.00 (N.A.) {4,957.27}	4,858.62	97.00
		833	MUMBAI URBAN TRANSPORT PROJECT PHASE-II (MRTP) (N22000092)	4-2008	3/2014 (N.A.) {3/2014}	8,087.11 (N.A.) {918.53}	7,110.54	77.30
		834	WARDHA-NANDED MAHARASHTRA (CR) (N22000231)	4-2008	3/2027 (N.A.) {1/2026}	3,445.48 (N.A.) {3,445.34}	3,121.26	47.00
		835	KALYAN-KASARA 3RD LINE (CR) (N22000233)	4-2011	12/2025 (N.A.) {12/2026}	792.89 (N.A.) {1,395.79}	876.77	50.00
		836	WARDHA-SEWAGRAM NGP 3RD LINE (CR) (N22000250)	4-2012	12/2025 (N.A.) {2/2026}	540.02 (N.A.) {540.02}	733.95	80.00
		837	WARDHA-BALHARSHAH - 3RD LINE (132 KM) (CR) (N22000356)	2-2015	12/2025 (N.A.) {3/2026}	1,384.72 (N.A.) {1,384.72}	1,580.25	67.00
		838	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) (CR) (N22000358)	2-2015	3/2027 (N.A.) {3/2027}	2,449.91 (N.A.) {2,449.91}	1,732.39	50.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		839	PUNE-MIRAJ-LONDA (467 KM) (CR) (N22000359)	2-2015	2/2025 (N.A.) {5/2025}	3,627.47 (3,627.00) {7,037.24}	4,624.86	84.00
		840	DAUND - MANMAD (236 KM) (CR) (N22000360)	2-2016	12/2025 (N.A.) {1/2026}	2,081.27 (N.A.) {2,081.27}	2,723.05	88.00
		841	MANMAD - JALGAON - 3RD LINE (160 KM) (CR) (N22000361)	2-2016	12/2024 (N.A.) {3/2026}	1,035.16 (N.A.) {1,558.75}	1,675.57	80.00
		842	WARDHA - NAGPUR - 4TH LINE (76 KM) (CR) (N22000362)	2-2016	12/2025 (N.A.) {2/2026}	638.00 (N.A.) {637.95}	962.97	80.00
		843	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) (SECR) (N22000420)	9-2016	12/2024 (N.A.) {12/2026}	3,544.92 (N.A.) {3,544.25}	3,041.12	95.00
		844	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (WR) (N22000434)	3-2010	10/2024 (N.A.) {3/2024}	311.00 (N.A.) {311.36}	0.00	N.A.
		845	WADSA-GADHCHIROLI NEW LINE (52.36 KM) (SECR) (N22000480)	6-2018	3/2027 (N.A.) {12/2026}	1,886.05 (N.A.) {1,880.61}	778.67	25.00
		846	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (N22000511)	8-2022	8/2027 (N.A.) {3/2029}	955.00 (N.A.) {2,089.25}	117.54	N.A.
		847	SOLAPUR-TULJAPUR-OSMANABAD (UMBRELLA WORK) (CR) (N22000513)	1-2019	3/2028 (N.A.) {12/2027}	904.92 (N.A.) {2,933.01}	1,139.92	10.00
		848	DHULE (BORVIHIR)-NARDANA (UMBRELLA WORK) (CR) (N22000514)	1-2019	12/2026 (N.A.) {3/2028}	492.76 (N.A.) {1,158.99}	198.74	5.00
		849	KALYAN-MURBAD VIA ULHASNAGAR (UMBRELLA WORK) (CR) (N22000515)	2-2023	3/2027 (N.A.) {3/2027}	836.12 (N.A.) {836.12}	9.29	N.A.
		850	BARAMATI - LONAND (CR) (N22000615)	2-1999	3/2027 (N.A.) {3/2027}	736.44 (N.A.) {1,843.90}	692.52	50.00
		851	MUMBAI URBAN TRANSPORT PROJECT IIIA (MRVC) (N22000627)	4-2019	12/2027 (N.A.) {12/2027}	33,690.00 (N.A.) {33,690.00}	812.06	N.A.

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		852	NAGPUR- NAGBHIR RAILWAY LINE GAUGE CONVERSION PROJECT (MRIDC) (N22000629)	10-2019	6/2024 (N.A.) {10/2025}	1,400.00 (N.A.) {2,383.00}	1,774.90	86.00
	ROAD TRANSPORT AND HIGHWAYS	853	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM (MoRTH) (N24000332)	1-2015	(N.A.) {}	225.81 (N.A.) {225.81}	167.96	96.00
		854	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN (NHAI) (N24000442)	12-2015	3/2019 (Nov-2023) {7/2025}	649.50 (N.A.) {649.50}	623.65	93.43
		855	NAGPUR RING ROAD PACKAGE-2 (NHAI) (N24000560)	3-2016	7/2019 (Mar-2024) {5/2025}	591.66 (N.A.) {591.66}	632.92	99.99
		856	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000584)	3-2016	(N.A.) {12/2023}	1,142.62 (1,907.03) {1,142.62}	1,056.08	95.17
		857	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000585)	3-2016	(N.A.) {}	1,101.58 (N.A.) {1,101.58}	608.53	N.A.
		858	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) (NHAI) (N24000656)	3-2017	3/2020 (Jul-2022) {12/2025}	744.64 (N.A.) {1,007.00}	467.65	95.20
		859	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) (NHAI) (N24000659)	3-2017	3/2017 (May-2021) {5/2025}	1,059.73 (1,071.00) {1,071.00}	928.19	97.25
		860	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF (NHAI) (N24000851)	3-2018	7/2021 (N.A.) {12/2025}	1,162.92 (1,182.87) {1,182.87}	412.38	59.00
		861	SARSAM TO KOTHARI (MoRTH) (N24001002)	2-2016	7/2019 (N.A.) {12/2023}	545.64 (N.A.) {545.64}	232.64	93.68
		862	AKOLA TO AKOT (MoRTH) (N24001003)	1-2017	6/2019 (N.A.) {12/2023}	313.95 (N.A.) {313.95}	270.26	99.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		863	DIGRAS DARWAH KARANJA (MoRTH) (N24001013)	1-2017	6/2019 (N.A.) {12/2023}	391.06 (391.00) {391.06}	287.60	92.76
		864	DAHEGAON TO KUHI (MoRTH) (N24001017)	1-2017	6/2019 (N.A.) {12/2023}	228.89 (229.00) {228.89}	154.82	99.00
		865	BHANDARA TO GHOTITOK (MoRTH) (N24001018)	1-2017	6/2019 (N.A.) {6/2019}	392.83 (393.00) {392.83}	274.75	100.00
		866	AMD1 TO SAONER (MoRTH) (N24001021)	1-2017	6/2019 (N.A.) {12/2023}	396.91 (397.00) {396.91}	289.79	98.69
		867	WADI TO ASOLA (MoRTH) (N24001022)	1-2017	9/2019 (N.A.) {12/2023}	363.82 (364.00) {363.82}	154.65	93.15
		868	RALEGAON TO RAMTIRTH (MoRTH) (N24001046)	1-2017	7/2019 (N.A.) {8/2023}	210.81 (N.A.) {210.81}	210.81	96.50
		869	VITA TO NAGAJ (MoRTH) (N24001050)	3-2018	12/2019 (N.A.) {12/2023}	304.58 (305.00) {304.58}	154.68	68.39
		870	KARAD PATAN CHIPLUN GUHAGAR (MoRTH) (N24001057)	2-2017	6/2019 (N.A.) {10/2023}	407.19 (407.00) {407.19}	323.02	90.00
		871	KARWANDI TO RAJURI (MoRTH) (N24001058)	3-2018	12/2019 (N.A.) {3/2024}	276.95 (277.00) {276.95}	160.94	92.06
		872	PALPHATA TO PHULAMBARI (MoRTH) (N24001060)	3-2018	12/2019 (N.A.) {12/2023}	227.19 (227.00) {227.19}	141.92	95.00
		873	NANDED TO JALKOT (MoRTH) (N24001069)	12-2017	9/2019 (N.A.) {9/2019}	456.93 (457.00) {456.93}	278.22	95.00
		874	PUNE TO MALE VILLAGE (MoRTH) (N24001078)	3-2018	12/2019 (N.A.) {12/2023}	228.31 (N.A.) {228.31}	100.97	93.83
		875	ARDHAPUR TO HIMAYATNAGAR (MoRTH) (N24001079)	12-2017	6/2020 (N.A.) {12/2023}	426.06 (426.00) {426.06}	271.40	96.25
		876	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER (MoRTH) (N24001080)	3-2018	12/2019 (N.A.) {10/2023}	256.15 (N.A.) {256.15}	126.62	98.00
		877	PUNE RAIGARH DISTRICT BORDER TO MANGAON (MoRTH) (N24001082)	3-2018	12/2019 (N.A.) {12/2023}	223.46 (N.A.) {223.46}	123.46	100.00
		878	KOLDE TO KHETIYA (MoRTH) (N24001090)	1-2017	7/2019 (N.A.) {12/2023}	509.18 (N.A.) {509.18}	283.13	94.81

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		879	SATARA TO MHASWAD (MoRTH) (N24001092)	1-2017	7/2019 (N.A.) {12/2023}	653.46 (N.A.) {653.46}	369.62	N.A.
		880	MHASWAD TO TEMBHURNI (MoRTH) (N24001099)	1-2017	7/2019 (N.A.) {12/2023}	488.60 (N.A.) {488.60}	279.42	76.50
		881	KURUDWADI TO PANDHARPUR (MoRTH) (N24001101)	1-2017	7/2019 (N.A.) {11/2023}	307.63 (N.A.) {307.63}	232.57	96.27
		882	PANDHARPUR TO SANGOLA (MoRTH) (N24001102)	7-2017	7/2019 (N.A.) {12/2023}	218.38 (N.A.) {218.38}	182.63	99.78
		883	PEN TO KHOPOLI (MoRTH) (N24001106)	3-2018	3/2018 (N.A.) {1/2024}	301.39 (302.00) {301.39}	170.12	82.07
		884	PANCHARAL TO MANDANGHAR (MoRTH) (N24001107)	7-2018	5/2020 (N.A.) {5/2020}	381.08 (302.00) {381.08}	45.66	N.A.
		885	NASRATPUR TO BARASGAON (MoRTH) (N24001112)	7-2016	9/2019 (N.A.) {9/2019}	406.54 (407.00) {406.54}	274.30	N.A.
		886	INDAPUR TO VADPALE (MoRTH) (N24001114)	1-2017	12/2019 (N.A.) {3/2024}	1,202.52 (1,656.94) {1,202.52}	1,450.82	61.42
		887	PAITHAN TO SHIRUR (MoRTH) (N24001122)	3-2017	6/2019 (N.A.) {3/2024}	341.80 (N.A.) {341.80}	226.19	78.60
		888	SHIRUR TO KHARDA (MoRTH) (N24001123)	2-2017	6/2019 (N.A.) {12/2023}	381.77 (N.A.) {381.77}	199.48	83.93
		889	AURANGABAD TO SILLOD (MoRTH) (N24001124)	2-2017	6/2019 (N.A.) {12/2023}	456.32 (541.93) {456.32}	355.54	94.07
		890	SILLOD TO FARDAPUR (MoRTH) (N24001125)	2-2017	6/2019 (N.A.) {12/2023}	337.46 (432.98) {337.46}	335.30	91.56
		891	BHOGAN KHURD TO KASHEDI (MoRTH) (N24001132)	9-2017	6/2021 (N.A.) {12/2023}	743.21 (743.00) {743.21}	911.64	88.69
		892	KANTE TO WAKED (MoRTH) (N24001134)	3-2016	11/2019 (N.A.) {12/2024}	1,230.02 (1,230.00) {1,230.02}	791.80	N.A.
		893	PARLI PIMPLA DAHIGUDA (MoRTH) (N24001138)	2-2017	6/2019 (N.A.) {8/2023}	205.72 (206.00) {205.72}	85.71	100.00
		894	UPGRADATION OF ADHALGAON-JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH (MoRTH) (N24001448)	11-2021	2/2022 (N.A.) {2/2022}	223.35 (N.A.) {223.35}	209.36	87.88

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		895	REPANPALLI TO SIRONCHA (MoRTH) (N24001468)	3-2022	6/2022 (N.A.) {6/2024}	282.07 (N.A.) {282.07}	34.65	N.A.
		896	TUNNEL AT KHAMBATI Ghat SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0 (NHAI) (N24001486)	2-2019	2/2022 (Dec-2024) {8/2025}	493.00 (N.A.) {493.00}	399.49	76.49
		897	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL-ALANDI SECTION (NHAI) (N24001488)	9-2021	9/2023 (Dec-2024) {5/2025}	618.45 (N.A.) {618.45}	639.23	96.20
		898	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) (NHAI) (N24001493)	12-2022	12/2024 (N.A.) {11/2025}	1,749.86 (N.A.) {1,749.86}	1,848.81	68.18
		899	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 ((NHAI) (N24001495)	11-2022	11/2024 (N.A.) {9/2025}	930.00 (N.A.) {930.00}	620.60	76.50
		900	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH- 965G (SAINT TUKARAM MARG) (NHAI) (N24001502)	9-2021	9/2023 (Jun-2025) {6/2025}	624.45 (580.15) {580.15}	420.42	0.50
		901	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH-965G (SAINT TUKARAM MARG) (NHAI) (N24001503)	9-2021	9/2023 (Jan-2025) {3/2025}	667.66 (666.21) {666.21}	610.63	3.00
		902	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) (NHAI) (N24001504)	5-2022	5/2024 (Jun-2025) {6/2025}	1,260.00 (N.A.) {1,260.00}	665.73	97.00
		903	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) (NHAI) (N24001505)	3-2022	3/2024 (Jun-2025) {6/2025}	1,549.02 (N.A.) {1,549.02}	699.00	82.91
		904	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) (NHAI) (N24001506)	2-2022	2/2024 (Jun-2025) {6/2025}	2,747.00 (N.A.) {2,747.00}	1,125.16	80.02

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		905	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) (NHAI) (N24001507)	11-2022	5/2024 (Jun-2025) {6/2025}	1,124.00 (N.A.) {1,124.00}	483.84	73.13
		906	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) (NHAI) (N24001508)	11-2022	10/2024 (Jun-2025) {6/2025}	1,450.00 (N.A.) {1,450.00}	718.65	84.05
		907	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XV) [KM. 20.200 TO KM. 43.000 OF SPUR] (AKLOLI - AMNE) (NHAI) (N24001521)	11-2022	10/2024 (Jul-2025) {7/2025}	990.00 (N.A.) {990.00}	406.91	73.00
		908	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) (NHAI) (N24001546)	1-2023	1/2025 (N.A.) {1/2025}	1,025.20 (N.A.) {1,025.20}	453.39	44.22
		909	BALANCE WORKS OF 4L PANVEL-INDAPUR SECTION OF NH-66 (OLD NH-17) FROM KM 42.300 (KASU) TO KM 84.600 ((NHAI) (N24001607)	10-2022	5/2024 (Dec-2025) {12/2025}	332.00 (N.A.) {332.00}	273.33	64.63
		910	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) (NHAI) (N24001608)	9-2021	7/2025 (N.A.) {7/2025}	2,208.68 (N.A.) {2,208.68}	565.20	74.50
		911	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH-66(OLD NH-17) FROM KM 0.000 (PANVEL) TO (NHAI) (N24001609)	1-2023	12/2023 (Jun-2025) {6/2025}	151.26 (N.A.) {151.26}	153.77	86.38
		912	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL ? ALANDI S (NHAI) (N24001610)	1-2022	5/2024 (Mar-2025) {5/2025}	1,833.73 (N.A.) {1,833.73}	539.18	95.64
		913	FOUR LANING OF AURANGABAD-PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA . (NHAI) (N24001795)	10-2022	7/2024 (Jun-2025) {12/2024}	490.40 (N.A.) {289.00}	275.78	95.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		914	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B (NHAI) (N24001796)	3-2022	10/2024 (Apr-2025) {4/2025}	1,013.33 (1,013.33) {1,111.33}	355.07	62.01
		915	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800 (NHAI) (N24001797)	10-2021	1/2024 (N.A.) {5/2025}	815.77 (N.A.) {815.77}	732.70	100.00
		916	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH-53 (NHAI) (N24001798)	2-2021	11/2023 (N.A.) {5/2025}	540.21 (N.A.) {540.21}	457.05	100.00
		917	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J (NHAI) (N24001799)	2-2021	10/2023 (N.A.) {10/2025}	1,166.96 (N.A.) {1,251.00}	1,078.65	81.00
		918	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794) (NHAI) (N24001804)	12-2019	9/2022 (Jun-2024) {12/2025}	1,654.07 (N.A.) {980.00}	887.38	95.75
		919	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH-166 (PKG ? II) (NHAI) (N24001834)	5-2023	5/2025 (N.A.) {5/2025}	839.00 (N.A.) {839.00}	441.05	56.50
		920	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH-166 (PKG?III) (NHAI) (N24001835)	5-2023	5/2025 (N.A.) {5/2025}	986.00 (N.A.) {986.00}	508.04	54.60
		921	REHABILITATION AND UP-GRADATION TO 4 LANE ROAD WITH PAVED SHOULDER CONFIGURATION OF SECTION FROM UND (MoRTH) (N24001880)	3-2022	7/2025 (N.A.) {7/2025}	778.18 (N.A.) {778.18}	135.78	N.A.
		922	CONSTRUCTION OF NEW FOUR LANE BYPASS TO PARBHANI CITY (PARWA TO ASOLA) KM 463/265 TO KM 481/180 (DES (MoRTH) (N24001882)	3-2022	10/2024 (N.A.) {10/2024}	496.64 (N.A.) {496.64}	0.00	8.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		923	CONSTRUCTION OF 4 LANE FLYOVER AT NAGPUR RTO CHOWK TO NAGPUR UNIVERSITY CAMPUS FROM CH 2/250 TO 5/10 (MoRTH) (N24001883)	3-2021	3/2024 (N.A.) {4/2024}	478.83 (N.A.) {478.83}	233.48	65.00
		924	REHABILITATION AND UPGRADATION OF SATANA TO MANGRUL (CHANDWAD) SECTION OF NH752 G DESIGN CH: KM 64.0 (MoRTH) (N24001884)	3-2023	5/2025 (N.A.) {5/2025}	428.80 (N.A.) {428.80}	54.11	30.69
		925	REHABILITATION AND UP-GRADATION OF JINTUR- SHIRAD SHAHAPUR SECTION KM 258.300 TO KM 306.300 [DESIGN (MoRTH) (N24001885)	2-2023	12/2024 (N.A.) {12/2024}	414.81 (N.A.) {414.81}	0.00	N.A.
		926	DEVELOPMENT/WIDENING OF TALEGAON ? CHAKAN ? SHIKRAPUR ? NHAVARA SECTION OF NH 548DG (NHAVARA TO CHOU (MoRTH) (N24001886)	10-2022	8/2024 (N.A.) {8/2024}	304.68 (N.A.) {304.68}	97.09	59.00
		927	REHABILITATION AND UPGRADATION OF BHOKARDAN TO KUMBHARI FATA DESIGN CH. (KM 13+500 TO 17+00) AND RAJ (MoRTH) (N24001887)	8-2022	6/2024 (N.A.) {6/2024}	291.37 (N.A.) {291.37}	102.94	78.44
		928	UP-GRADATION OF TIRORA-GONDIA, STATE HIGHWAY FROM EXISTING KM 163+213 (ON SH-335, TIRORA) TO KM 191+ (MoRTH) (N24001888)	8-2021	4/2023 (N.A.) {5/2024}	288.14 (N.A.) {288.14}	63.01	46.31
		929	2 LANE + PS PIMPLNER TO SATANA - [DESIGN CHAINAGE KM 21.427 TO 64.00] OF NH-752G] (MoRTH) (N24001889)	9-2019	7/2021 (N.A.) {12/2023}	277.81 (N.A.) {277.81}	148.68	90.00
		930	REHABILITATION AND UPGRADATION OF PARLI TO SIRSALA SECTION OF NH-361F (KM 136+700 TO 115+000) (LENGT (MoRTH) (N24001890)	2-2023	12/2024 (N.A.) {12/2024}	261.82 (N.A.) {261.82}	70.59	46.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		931	BALANCE WORK OF REHABILITATION AND UP-GRADATION TO NH-166F FROM MAHAD JUNCTION (AT KM 123/400 ON NH- (MoRTH) (N24001891)	7-2021	11/2023 (N.A.) {3/2024}	256.54 (N.A.) {256.54}	80.10	60.00
		932	REHABILITATION AND UPGRADATION OF SHIRAPUR JUNCTION TO SHIVAJI CHOWK (DESIGN CHAINAGE KM. 130+00 TO (MoRTH) (N24001892)	2-2023	12/2024 (N.A.) {12/2024}	245.61 (N.A.) {245.61}	43.39	33.00
		933	2 LANE + PS ASTHAMODE - TIVATYAL [DESIGN CH. KM 24.300 - 62.00] [KM 134.98-172.95 OF NH-63] (MoRTH) (N24001894)	9-2019	7/2021 (N.A.) {12/2023}	228.82 (N.A.) {228.82}	144.54	95.44
		934	REHABILITATION AND UPGRADATION TO TWO LANES WITH PAVED SHOULDER CONFIGURATION FROM WATUR TO CHARTHANA (MoRTH) (N24001895)	11-2021	9/2023 (N.A.) {12/2023}	228.01 (N.A.) {228.01}	103.01	99.00
		935	UPGRADATION AND REHABILITATION OF SECTION OF NH 361 F FROM PARLI (00/000) TO GANGAKHED (30/400) TO (MoRTH) (N24001896)	11-2021	9/2023 (N.A.) {4/2024}	224.44 (N.A.) {224.44}	75.34	45.63
		936	REHABILITATION AND UP-GRADATION OF SABALKHED TO ASHTI SECTION FROM KM 37+900 TO KM 55+100 AND CHINCH (MoRTH) (N24001902)	12-2022	9/2024 (N.A.) {9/2024}	213.32 (N.A.) {213.32}	20.00	34.00
		937	REHABILITATION AND UP-GRADATION OF MUDKHED TO NANDED SECTION FROM KM. 372+000 TO KM 388+400 OF NH 16 (MoRTH) (N24001903)	8-2022	4/2025 (N.A.) {4/2025}	206.54 (N.A.) {206.54}	21.36	N.A.
		938	KOPARGAON TO SAVALI VIHIR SECTION (MoRTH) (N24001904)	9-2022	7/2024 (N.A.) {7/2024}	195.38 (N.A.) {195.38}	29.59	19.76
		939	CONSTRUCTION OF MAJOR BRIDGE ACROSS MANJRA RIVER NEAR YESGI VILLAGE @ KM, 166/500 ON NH 63 TQ BILOLI (MoRTH) (N24001905)	10-2021	8/2023 (N.A.) {12/2023}	188.69 (N.A.) {188.69}	111.26	95.80

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		940	UP-GRADATION TO 4 LANING OF DAULTABAD T-POINT TO MALIWADA [FROM DESIGN KM.0.000 TO KM 4.000] AND UPG (MoRTH) (N24001906)	8-2022	3/2024 (N.A.) {3/2024}	185.59 (N.A.) {185.59}	63.56	48.00
		941	CONSTRUCTION OF SIX LANE FLYOVER AT KATRAJ JUNCTION AT KM, 3/880 OF NH 548- DD (VADGAON - KATRAJ - KO (MoRTH) (N24001907)	6-2021	2/2024 (N.A.) {3/2024}	169.15 (N.A.) {169.15}	36.94	35.96
		942	UPGRADATION OF EXISTING 2 LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDERS RIGID PAVEMENT FROM DESI (MoRTH) (N24001908)	12-2021	5/2024 (N.A.) {5/2024}	167.97 (N.A.) {167.97}	35.28	36.76
		943	STRENGTHING AND WIDINING OF EXISTING CARRIAGEWAY TO 10 M IN KM, 156/160 TO 229/160 (TEMBHURNI - KUSL (MoRTH) (N24001909)	11-2021	6/2024 (N.A.) {6/2024}	157.72 (N.A.) {157.72}	55.38	90.41
		944	REHABILITATION AND UPGRADATION OF JAMKHEDE TO SAUTADA SECTION OF NH548 D (FROM KM 195.375 TO KM 208.7 (MoRTH) (N24001910)	9-2022	7/2024 (N.A.) {7/2024}	157.62 (N.A.) {157.62}	13.86	17.03
		945	PANGAON TO DHARMAPURI AND PARALI TO INJEGAON 2L+PS (MoRTH) (N24001911)	3-2018	7/2024 (N.A.) {12/2023}	152.03 (N.A.) {152.03}	81.35	97.57
		946	4L OF INDORA CHOWK TO PACHPAOLI AND AGRASEN CHOWK - ASHOKA CHOWK (NHAI) (N24002071)	3-2023	6/2026 (N.A.) {6/2026}	998.27 (N.A.) {998.27}	347.53	45.52
		947	IMPROVEMENT OF EXISTING ALIGNMENT OF PANDHARPUR TOWN PART BYPASSED SECTION FROM WAKHARI TO LORD VITT (NHAI) (N24002072)	7-2022	10/2025 (N.A.) {10/2025}	150.21 (150.21) {150.21}	31.57	6.00
		948	STRENGTHENING OF 6-LANE PIMPALGAON- NASHIK-GONDE (KM. 380 - KM. 440) SECTION OF NH-3 IN MAHARASHTRA U (NHAI) (N24002137)	2-2024	3/2025 (N.A.) {3/2025}	175.00 (206.49) {206.49}	198.54	100.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		949	REHABILITATION/UPGRADATION OF EXISTING HIGHWAY TO 2L+PS/4 LANE OF DHAWALI TO RAJOLI FROM DESIGN KM.1 (MoRTH) (N24002169)	3-2022	9/2025 (N.A.) {9/2025}	316.44 (N.A.) {316.44}	0.00	N.A.
		950	REHABILITATION/ UPGRADATION OF EXISTING HIGHWAY TO FOUR LANE STANDARDS IN KURKHEDA TOWN FROM (KM.413 (MoRTH) (N24002170)	3-2022	5/2025 (N.A.) {5/2025}	163.86 (N.A.) {163.86}	0.00	N.A.
		951	REHABILITATION AND UP-GRADATION FOR TALERE A?? GAGANBAWDAA?? KOLHAPUR ROAD (NH-166G) STRETCHES START (MoRTH) (N24002171)	2-2023	4/2025 (N.A.) {4/2025}	249.13 (N.A.) {249.13}	0.00	N.A.
		952	UP-GRADATION TO 4 LANE CONFIGURATION FOR THE WORK OF PETH NAKA TO SANGLI ROAD, NH-166H, FROM KM 0+00 (MoRTH) (N24002172)	2-2023	12/2025 (N.A.) {12/2025}	856.82 (N.A.) {856.82}	0.00	N.A.
		953	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF MAHUD SANGOLA ROAD NH (MoRTH) (N24002173)	2-2023	4/2025 (N.A.) {4/2025}	253.78 (N.A.) {253.78}	0.00	N.A.
		954	UP-GRADATION TO FOUR LANE/ TWO LANE WITH PAVED SHOULDERS CONFIGURATION OF KALYAN - MURBAD - MALSHEJ (MoRTH) (N24002174)	2-2023	8/2026 (N.A.) {8/2026}	984.07 (N.A.) {984.07}	0.00	N.A.
		955	CONSTRUCTION OF FOUR-LANE CONCRETE ROAD FROM POLICE HEADQUARTER GONDIA CITY TO RAWANWADI VILLAGE (BI (MoRTH) (N24002175)	2-2023	8/2025 (N.A.) {8/2025}	328.11 (N.A.) {328.11}	0.00	N.A.
		956	REHABILITATION/UP GRADATION OF KARANJA ? KHERDA - MURTIZAPUR SECTION TO 4LANE+PAVED SHOULDER STANDA (MoRTH) (N24002176)	3-2023	2/2026 (N.A.) {2/2026}	594.44 (N.A.) {594.44}	0.00	N.A.

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		957	REHABILITATION / UPGRADATION TO 4 LANE WITH PAVED SHOULDER OF EXISTING SECTION IN SILLOD TOWN WITH D (MoRTH) (N24002177)	3-2023	7/2025 (N.A.) {7/2025}	153.79 (N.A.) {153.79}	0.00	N.A.
		958	REHABILITATION, UPGRADATION AND WIDENING OF EXISTING HIGHWAY TO RIGID PAVEMENT 2 LANE WITH PAVED SHO (MoRTH) (N24002178)	2-2023	7/2026 (N.A.) {7/2026}	723.13 (N.A.) {723.13}	0.00	N.A.
	URBAN DEVELOPMENT	959	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) (MMRCL) (N28000086)	7-2013	3/2020 (Jul-2025) {7/2025}	23,136.00 (N.A.) {37,276.00}	28,615.78	94.77
		960	PUNE METRO RAIL PROJECT (PHASE 1) (MMRC) (N28000121)	12-2016	11/2021 (Sep-2024) {9/2024}	11,420.00 (13,656.22) {13,656.22}	13,049.54	100.00
		961	NAGPUR METRO RAIL PROJECT PHASE II (NMRCL) (N28000155)	12-2022	12/2027 (N.A.) {12/2027}	6,708.00 (N.A.) {6,708.00}	809.32	22.68
		962	PCMC NIGDI PROJECT EXTENSION OF CORRIDOR 1 OF PUNE METRO PHASE 1 (MMRC) (N28000157)	10-2023	1/2027 (N.A.) {1/2027}	910.18 (N.A.) {910.18}	91.03	16.99
MANIPUR		963	PUNE METRO PHASE-1 EXTENSION FROM SWARGATE TO KATRAJ (MMRC) (N28000160)	9-2024	3/2029 (N.A.) {3/2029}	2,954.53 (N.A.) {2,954.53}	16.38	2.15
	CIVIL AVIATION	964	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAXI (AAI) (N04000100)	11-2021	7/2024 (Mar-2026) {3/2026}	499.00 (N.A.) {499.00}	154.47	40.36
	RAILWAYS	965	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	12/2026 (Mar-2028) {3/2028}	14,322.79 (12,274.06) {22,234.60}	15,338.76	69.00
	ROAD TRANSPORT AND HIGHWAYS	966	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (Jun-2025) {9/2025}	292.24 (N.A.) {292.24}	130.66	89.88

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		967	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (Jun-2025) {10/2025}	365.53 (N.A.) {365.53}	156.31	77.36
		968	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3-2020	6/2022 (Jan-2025) {6/2025}	167.95 (204.12) {167.95}	88.05	69.89
		969	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7-2020	8/2022 (Feb-2025) {6/2025}	177.76 (N.A.) {177.76}	89.67	80.53
		970	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (Jun-2025) {12/2025}	379.39 (N.A.) {379.39}	218.03	70.31
		971	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (Mar-2025) {12/2025}	226.32 (N.A.) {226.32}	105.78	74.48
		972	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (Jan-2025) {9/2025}	188.36 (N.A.) {188.36}	126.71	100.00
		973	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (Sep-2024) {11/2025}	234.08 (N.A.) {234.08}	139.45	92.82
		974	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (May-2025) {10/2025}	211.70 (N.A.) {211.70}	83.79	70.72
		975	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (Mar-2025) {10/2025}	467.00 (N.A.) {467.00}	193.81	77.80
		976	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (Jan-2025) {1/2025}	185.80 (N.A.) {185.80}	117.78	100.00
		977	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (Jan-2025) {12/2025}	483.87 (N.A.) {483.87}	278.89	92.94
		978	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (Feb-2025) {3/2025}	198.77 (N.A.) {198.77}	127.86	100.00
		979	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (Mar-2025) {12/2025}	673.27 (N.A.) {673.27}	382.37	79.47
		980	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (Jan-2025) {1/2026}	477.86 (N.A.) {477.86}	246.09	84.60

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		981	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (Nov-2024) {12/2025}	311.18 (N.A.) {311.18}	190.96	83.50
		982	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (Oct-2024) {2/2025}	467.41 (N.A.) {467.41}	264.83	100.00
		983	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (Jul-2025) {12/2025}	579.63 (N.A.) {579.63}	172.65	72.00
		984	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (Mar-2025) {6/2025}	310.76 (N.A.) {310.76}	129.15	96.77
		985	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (Jan-2026) {3/2026}	410.68 (N.A.) {410.68}	147.81	68.79
		986	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (Sep-2025) {12/2025}	504.76 (N.A.) {504.76}	183.15	76.52
		987	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (Feb-2025) {3/2025}	152.11 (N.A.) {152.11}	73.48	100.00
		988	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (Aug-2025) {8/2025}	315.56 (N.A.) {315.56}	137.81	88.54
		989	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (Dec-2025) {3/2026}	760.16 (N.A.) {760.16}	148.98	60.60
		990	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (Mar-2026) {3/2026}	578.98 (N.A.) {578.98}	153.92	71.25
		991	MARREM KHULLEN TO JESSAMI SECTION IMPHAL- UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	17.79	11.93
		992	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	13.14	15.90
		993	JESSAMI TO LAYNEN BRIDGE UKHRUL - JESSAMI PKG-7 (NHIDCL) (N24002227)	3-2023	6/2026 (N.A.) {6/2026}	164.89 (N.A.) {164.89}	1.46	6.50

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MEGHALAYA		994	IMPHAL-KOHIMA ROAD PKG-5A (NHIDCL) (N24002232)	9-2020	8/2026 (N.A.) {8/2026}	228.97 (N.A.) {228.97}	0.00	5.96
		995	CHOITHAR TO MARREM KHULLEN SECTION IMPHAL- UKHRUL - JESSAMI PKG-5 (NHIDCL) (N24002242)	3-2023	3/2027 (N.A.) {3/2027}	564.05 (N.A.) {564.05}	0.00	N.A.
		996	IMPHAL - KHONGSANG - JIRIBAM PKG-2 (NHIDCL) (N24002244)	3-2021	3/2026 (N.A.) {3/2026}	195.14 (N.A.) {195.14}	0.00	7.19
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	997	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (Jul-2025) {7/2025}	484.32 (429.70) {494.52}	270.55	84.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	998	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (Mar-2025) {6/2025}	553.51 (610.09) {553.51}	432.78	92.01
		999	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM ((NHIDCL) (N24001313)	11-2020	12/2023 (Oct-2025) {10/2025}	351.12 (N.A.) {351.12}	295.88	62.50
		1000	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	434.11	31.00
		1001	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	207.20	26.00
		1002	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	101.98	24.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1003	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10-2020	4/2022 (Jun-2024) {2/2025}	157.86 (146.92) {157.86}	152.95	100.00
		1004	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (N.A.) {3/2025}	302.88 (N.A.) {302.88}	228.68	96.00
		1005	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (Dec-2024) {5/2026}	359.86 (N.A.) {359.86}	233.26	87.00
		1006	RANIKOR- MAHESHKHOLA- BAGHMARA PKG- 2 (NHIDCL) (N24001541)	11-2021	6/2024 (Dec-2024) {5/2025}	283.50 (N.A.) {283.50}	257.26	100.00
		1007	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	221.86	28.00
		1008	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	292.69	25.52
		1009	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	297.79	24.00
		1010	DAINADUBI-DARUGIRI PKG-1B (NHIDCL) (N24002233)	3-2023	3/2027 (N.A.) {3/2027}	705.83 (N.A.) {705.83}	0.31	1.55
		1011	IMPROVEMENT AND WIDENING TWO LANNIG WITH PAVED SHOULDER OF NATIONAL HIGHWAY 127B FROM KM 31.500 (GOE (MoRTH) (N24002239)	12-2023	5/2027 (N.A.) {5/2027}	504.00 (N.A.) {504.00}	0.00	N.A.
		1012	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2025 (N.A.) {6/2025}	6,527.45 (5,021.45) {8,213.72}	8,001.88	97.00
MIZORAM	RAILWAYS							

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	1013	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (N.A.) {4/2025}	519.09 (N.A.) {785.65}	670.91	97.51
		1014	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (N.A.) {5/2024}	640.07 (N.A.) {1,286.35}	1,195.84	98.90
		1015	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (N.A.) {4/2025}	473.18 (N.A.) {688.25}	541.04	94.70
		1016	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (N.A.) {5/2025}	537.82 (N.A.) {789.05}	778.16	99.82
		1017	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (N.A.) {5/2025}	518.53 (N.A.) {906.76}	849.68	97.90
		1018	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (N.A.) {5/2025}	404.29 (N.A.) {750.32}	666.58	100.00
		1019	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (N.A.) {5/2025}	428.11 (N.A.) {746.39}	613.69	98.70
		1020	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (N.A.) {6/2024}	206.88 (N.A.) {219.33}	265.34	100.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1021	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (N.A.) {10/2024}	292.24 (N.A.) {331.17}	294.60	93.20
		1022	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (Apr-2024) {4/2024}	233.25 (N.A.) {233.25}	172.09	100.00
		1023	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (N.A.) {3/2026}	698.44 (N.A.) {698.45}	496.84	59.40
		1024	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (N.A.) {3/2026}	740.58 (N.A.) {740.58}	364.34	57.40
		1025	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9-2021	5/2023 (N.A.) {5/2024}	492.94 (N.A.) {492.94}	365.86	90.50
		1026	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWL RANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {12/2025}	523.78 (N.A.) {523.78}	366.81	80.51
		1027	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	263.48	68.80
		1028	ZORINPUI- HMAWNGBU-LONGMASU (NH- 502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	33.56	3.00
MULTI STATE	COAL	1029	NILJAI EXPANSION (DEEP) OC (3.5 MTY) (WCL) (N06000154)	8-2016	3/2022 (Mar-2025) {3/2025}	319.76 (319.76) {319.76}	183.67	98.00
		1030	BINA KAKRI AMALGAMATION OCP 14 MTPA (NCL) (N06000192)	8-2020	3/2024 (N.A.) {3/2027}	836.42 (N.A.) {836.42}	769.27	85.95
	DPIIT	1031	NATIONAL INDUSTRIAL CORRIDOR PROJECT (DMIC FOR DPIIT) (N40000001)	9-2011	3/2027 (Mar-2032) {3/2032}	20,084.00 (26,684.00) {26,684.00}	11,262.06	50.99
	PETROLEUM	1032	KOCHI-KOOTTANAD-BANGALORE- MANGALORE PIPELINE PHASE-II (GAIL) (N16000285)	6-2009	12/2012 (Dec-2025) {12/2025}	2,915.00 (5,909.00) {5,909.00}	4,294.80	94.00
		1033	SRIKAKULAM ANGUL PIPELINE PROJECT (GAIL) (N16000388)	9-2019	7/2022 (Jun-2025) {12/2025}	2,658.34 (N.A.) {2,658.34}	2,173.30	94.40

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1034	DHAMRA HALDIA PIPELINE PROJECT (GAIL) (N16000391)	3-2020	11/2022 (Dec-2025) {12/2025}	1,030.65 (N.A.) {1,030.65}	835.90	86.50
		1035	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT (GAIL) (N16000398)	6-2020	5/2023 (Jun-2025) {9/2025}	7,844.25 (N.A.) {7,844.25}	6,349.90	94.50
		1036	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS (IOCL) (N16000426)	6-2019	12/2029 (Mar-2030) {3/2030}	169.00 (N.A.) {169.00}	71.00	27.20
		1037	NORTH EAST GAS GRID (IGGL) (N16000439)	11-2020	3/2024 (Jul-2025) {3/2027}	9,265.00 (9,265.00) {9,265.00}	6,270.19	84.51
		1038	GURDASPUR JAMMU PIPELINE (GAIL) (N16000531)	7-2023	7/2026 (Jul-2026) {7/2026}	521.92 (521.92) {521.92}	133.30	34.90
	POWER	1039	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P (PGCIL) (N18000249)	12-2014	12/2018 (Mar-2025) {3/2027}	4,754.42 (9,129.32) {9,129.32}	7,602.44	81.50
		1040	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES (PGCIL) (N18000250)	12-2014	12/2018 (Mar-2025) {9/2025}	5,111.33 (6,700.00) {6,700.00}	5,276.39	95.90
		1041	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM (PGCIL) (N18000328)	2-2022	4/2025 (N.A.) {6/2025}	318.12 (N.A.) {318.12}	169.75	98.00
		1042	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM (PGCIL) (N18000330)	3-2022	12/2024 (N.A.) {7/2025}	288.71 (N.A.) {288.71}	149.79	48.00
		1043	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000331)	2-2022	9/2023 (N.A.) {7/2025}	359.47 (N.A.) {359.47}	319.16	90.00
		1044	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000332)	5-2022	11/2023 (N.A.) {8/2025}	1,666.00 (2,218.00) {2,218.00}	1,511.62	92.70

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1045	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B (PGCIL) (N18000337)	7-2022	6/2023 (N.A.) {9/2025}	4,546.26 (N.A.) {4,546.26}	3,969.34	92.00
		1046	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION (PGCIL) (N18000343)	10-2022	10/2025 (N.A.) {6/2025}	307.87 (N.A.) {307.87}	234.90	99.90
		1047	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B (PGCIL) (N18000352)	3-2023	11/2024 (N.A.) {8/2025}	3,546.94 (N.A.) {3,546.94}	2,759.00	97.00
		1048	ER WR TRANSMISSION LIMITED (PGCIL) (N18000353)	3-2023	3/2025 (N.A.) {6/2025}	281.16 (N.A.) {281.16}	217.88	98.80
	RAILWAYS	1049	NANGALDAM-TALWARA(NL),NR (NR) (220100188)	3-1981	12/2025 (Jan-2027) {6/2027}	2,018.00 (603.00) {2,017.96}	1,604.43	75.00
		1050	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) (WCR) (220100232)	9-1998	3/2027 (N.A.) {3/2025}	8,913.94 (63.57) {8,248.50}	2,500.34	43.00
		1051	CHHAPRA-BALLIA UP (NER) (N22000134)	3-2013	2/2025 (N.A.) {12/2025}	941.05 (954.00) {1,045.82}	1,004.58	95.50
		1052	CHOTTADEPUR-DHAR(NL) (WR) (N22000138)	4-2007	12/2026 (Dec-2027) {12/2027}	1,793.65 (1,793.63) {1,793.63}	1,626.42	59.00
		1053	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) (WR) (N22000139)	4-2007	2/2027 (Feb-2027) {2/2027}	1,942.00 (1,873.10) {2,873.11}	2,971.25	59.00
		1054	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) (NCR) (N22000148)	4-2011	3/2025 (N.A.) {12/2024}	2,912.96 (N.A.) {3,845.60}	1,024.32	N.A.
		1055	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TAMPUR-BANSI PAHARPUR (NCR) (N22000158)	4-2010	2/2019 (N.A.) {12/2026}	746.83 (N.A.) {746.83}	391.89	39.00
		1056	NEW BG LINE FROM BALURGHAT TO HILLY NFR (NFR) (N22000206)	4-2010	3/2027 (N.A.) {3/2027}	1,208.67 (N.A.) {1,181.57}	418.79	8.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1057	NEW BG LINE FROM JAGBANI TO BIRATNAGAR (NFR) (N22000207)	4-2010	3/2022 (Dec-2026) {12/2026}	401.65 (485.96) {485.96}	361.33	86.00
		1058	MURKONGSELEK-PASIGHAT NL (NFR) (N22000208)	4-2011	3/2025 (N.A.) {2/2026}	435.06 (N.A.) {1,249.35}	795.68	53.50
		1059	PIRPAINTI-JASIDIH (ER) (N22000219)	4-2013	3/2028 (Mar-2028) {3/2028}	2,555.03 (N.A.) {2,610.84}	1,129.76	45.00
		1060	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION (SCR) (N22000261)	4-2012	2/2025 (N.A.) {3/2025}	1,953.00 (N.A.) {1,952.68}	1,798.38	N.A.
		1061	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL (NR) (N22000274)	4-2007	3/2024 (N.A.) {3/2025}	1,053.23 (N.A.) {1,053.00}	588.80	99.00
		1062	RAYADURGA-TUMKUR NL (SWR) (N22000279)	4-2007	9/2015 (N.A.) {2/2028}	2,495.59 (2,495.86) {2,495.86}	1,653.85	65.00
		1063	HOTGI-KUDGI-GADAG (SWR) (N22000333)	3-2015	12/2024 (N.A.) {2/2026}	1,877.81 (1,877.81) {2,458.87}	2,539.04	89.00
		1064	KAZIPET-BALHRSHA (SCR) (N22000367)	4-2015	1/2025 (N.A.) {1/2025}	2,594.59 (N.A.) {2,909.00}	2,797.55	75.00
		1065	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT (NHSRCL) (N22000463)	12-2015	8/2027 (N.A.) {8/2027}	108,000.00 (N.A.) {108,000.00}	76,441.00	52.00
		1066	WESTERN DEDICATED FREIGHT CORRIDOR (DFCC) (N22000464)	11-2007	3/2022 (N.A.) {3/2020}	51,101.00 (51,101.00) {51,101.00}	47,476.00	83.00
		1067	CHANDIGARH-BADDI (NR) (N22000467)	4-2007	6/2025 (Dec-2026) {12/2026}	1,540.13 (1,540.14) {1,540.14}	941.19	29.00
		1068	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) (SER) (N22000506)	3-2019	12/2024 (N.A.) {6/2026}	2,400.00 (N.A.) {1,866.31}	2,048.31	60.00
	ROAD TRANSPORT AND HIGHWAYS	1069	VARANASI-AURANGABAD KM.786 TO KM.978.40 (NHAI) (N24000182)	9-2011	3/2014 (N.A.) {6/2025}	2,848.00 (N.A.) {3,241.56}	3,901.66	90.02
		1070	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 (NHAI) (N24001628)	11-2021	2/2025 (Aug-2025) {8/2025}	2,155.95 (N.A.) {2,155.95}	1,359.81	67.42

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)	
		1071	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O (NHAI) (N24001629)	4-2022	11/2024 (Jun-2025) {6/2025}	796.65 (N.A.) {796.65}	432.84	87.50	
	SHIPPING AND PORTS	1072	JAL MARG VIKAS PROJECT (IWA) (N25000072)	1-2018	3/2023 (Dec-2025) {12/2025}	5,369.18 (5,061.15) {5,061.15}	3,441.55	68.86	
	TELECOMMUN ICATIONS	1073	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (N26000114)	3-2020	6/2021 (Nov-2021) {12/2025}	461.42 (461.42) {461.42}	166.02	81.00	
		1074	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LEBEL SWITCHING (IPMPLS) NETWORK and (BSNL) (N26000115)	3-2023	3/2024 (Jul-2024) {3/2025}	239.60 (N.A.) {239.60}	179.43	100.00	
		1075	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (N26000116)	5-2023	8/2024 (Nov-2024) {6/2025}	645.13 (N.A.) {645.13}	346.69	89.15	
		1076	PLANNIN ENGINEERING SUPPLY INSTALLATION TESTING COMMISSIONING INTEGARTION and ANNUAL MAINTENANCE OF (BSNL) (N26000117)	6-2023	6/2025 (N.A.) {6/2025}	24,556.35 (24,544.55) {24,544.55}	8,087.14	94.09	
		1077	OPTICAL TRANSPORT NETWORK (OTN) PH- 4 IN BSNL (BSNL) (N26000118)	2-2024	8/2025 (N.A.) {8/2025}	810.99 (N.A.) {810.99}	635.37	100.00	
	URBAN DEVELOPMEN T	1078	DELHI GHAZIABAD MEERUT RRTS CORRIDOR (NCRTC) (N28000134)	3-2019	6/2025 (N.A.) {6/2025}	30,274.00 (N.A.) {30,274.00}	25,673.23	86.30	
	NAGALAND	PETROLEUM	1079	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	6.12	18.00
		RAILWAYS	1080	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2026 (N.A.) {12/2029}	6,663.20 (6,663.20) {6,663.20}	4,789.15	73.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	1081	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3-2016	9/2019 (Nov-2022) {5/2025}	373.07 (534.41) {534.41}	382.50	99.81
		1082	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (Sep-2025) {9/2025}	429.52 (794.74) {794.74}	321.40	91.49
		1083	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (Feb-2023) {4/2025}	387.00 (688.12) {688.12}	392.01	100.00
		1084	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (Aug-2024) {4/2025}	500.09 (698.81) {698.81}	393.53	100.00
		1085	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU- MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (Aug-2022) {8/2025}	215.79 (N.A.) {215.79}	130.20	79.58
		1086	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU- MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (Jun-2023) {9/2025}	323.98 (N.A.) {323.98}	119.94	59.68
		1087	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (Sep-2024) {6/2026}	277.44 (N.A.) {277.44}	168.88	67.81
		1088	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (Jun-2025) {12/2025}	159.85 (342.29) {159.85}	103.95	29.90

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1089	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (Apr-2023) {8/2025}	202.36 (N.A.) {202.36}	75.39	31.02
		1090	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	119.20	65.06
		1091	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3-2020	6/2022 (Oct-2022) {6/2023}	278.95 (N.A.) {278.95}	166.29	100.00
		1092	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (Nov-2025) {11/2025}	330.80 (N.A.) {330.80}	171.89	92.44
		1093	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (Nov-2026) {11/2026}	232.29 (350.88) {232.29}	70.90	14.70
		1094	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7-2021	3/2023 (Sep-2025) {9/2025}	258.52 (N.A.) {258.52}	89.46	79.70
		1095	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	62.08	67.82
		1096	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (Jun-2026) {6/2026}	252.19 (N.A.) {252.19}	14.25	17.90
		1097	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3-2021	7/2024 (Dec-2025) {12/2025}	297.24 (N.A.) {297.24}	137.76	79.47
		1098	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (Mar-2025) {3/2025}	226.44 (N.A.) {226.44}	140.24	100.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1099	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU (MoRTH) (N24001855)	2-2021	6/2025 (Sep-2025) {9/2025}	192.93 (N.A.) {192.93}	105.41	92.82
		1100	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {12/2025}	177.77 (199.02) {199.02}	46.94	61.25
		1101	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	100.51	54.28
		1102	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	50.60	26.58
		1103	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	163.84	62.02
ODISHA	COAL	1104	BASUNDHARA (WEST) OC EXTN(7.00 MTY) (MCL) (N06000112)	5-2014	3/2019 (N.A.) {3/2028}	479.15 (N.A.) {479.15}	267.20	63.04
		1105	SIARMAL OCP (40.00MTY) (MCL) (N06000113)	2-2021	3/2029 (N.A.) {3/2029}	5,194.96 (N.A.) {5,194.96}	3,436.40	51.94
		1106	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP (MCL) (N06000167)	5-2018	3/2027 (N.A.) {3/2027}	2,434.75 (N.A.) {2,434.75}	1,760.96	60.87
		1107	REORGANISATION OF BHARATPUR OCP EXPANSION (MCL) (N06000171)	11-2018	3/2029 (N.A.) {3/2029}	2,838.87 (N.A.) {2,838.87}	1,835.56	44.62
		1108	NAINI COAL MINE (SCCL) (N06000203)	3-2020	3/2024 (N.A.) {3/2027}	494.30 (N.A.) {494.30}	491.33	80.00
		1109	GOPALJI-KANIHA OCP (MCL) (N06000229)	4-2022	3/2028 (N.A.) {3/2028}	6,107.87 (N.A.) {6,107.87}	1,703.67	17.39
		1110	BALARAM EXPANSION OCP (MCL) (N06000230)	8-2020	3/2029 (N.A.) {3/2029}	3,504.21 (N.A.) {3,504.21}	1,024.91	50.17

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1111	SUBHADRA OCP (MCL) (N06000249)	5-2021	3/2029 (Mar-2029) {3/2029}	1,693.81 (N.A.) {1,693.81}	1,181.97	39.30
		1112	NLC TALABIRA THERMAL POWER PROJECT (PHASE-1: 3 X 800 MW) (NLC) (N06000270)	1-2024	5/2029 (Mar-2030) {3/2030}	27,213.00 (N.A.) {27,213.00}	1,883.39	1.55
		1113	RPR OF HINGULA EXPANSION OCP (MCL) (N06000285)	11-2022	3/2029 (N.A.) {3/2029}	1,561.85 (N.A.) {1,561.85}	49.10	3.57
		1114	BHUBANESWARI EXPANSION OCP (MCL) (N06000286)	3-2024	3/2031 (N.A.) {3/2031}	5,366.28 (N.A.) {5,366.28}	3.95	8.33
		1115	BALABHADRA OCP (MCL) (N06000288)	4-2023	3/2030 (N.A.) {3/2030}	978.44 (N.A.) {978.44}	209.50	1.86
		1116	INTEGRATED KULDA GARJANBAHAL OCP (MCL) (N06000289)	4-2023	3/2030 (N.A.) {3/2030}	3,563.50 (N.A.) {3,563.50}	496.87	3.58
	DEPARTMENT OF HIGHER EDUCATION	1117	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR (CPWD EDUCATION) (N28000126)	1-2019	3/2022 (N.A.) {10/2025}	790.79 (N.A.) {790.79}	706.39	96.00
	MINES	1118	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT (NALCO) (N10000010)	12-2014	4/2021 (Sep-2025) {9/2025}	4,103.00 (5,677.40) {5,677.40}	3,799.56	73.74
		1119	UTKAL D AND E COAL BLOCK (NALCO) (N10000011)	5-2016	1/2020 (Nov-2023) {3/2024}	534.00 (N.A.) {1,021.97}	826.94	87.50
		1120	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (NALCO) (N10000012)	12-2015	11/2020 (Sep-2025) {8/2027}	355.00 (581.00) {581.00}	163.55	12.60
		1121	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN (NALCO) (N10000013)	11-2017	4/2021 (May-2026) {5/2026}	483.00 (483.00) {495.00}	385.20	89.30
		1122	POTTANGI BAUXITE MINES (NALCO) (N10000016)	5-2018	12/2024 (N.A.) {5/2025}	1,437.00 (N.A.) {1,381.00}	650.05	51.00
		1123	CONSTRUCTION OF RED MUD POND - II AT NALCO DAMANJODI ODISHA (NALCO) (N10000017)	9-2019	3/2023 (May-2024) {5/2024}	225.79 (N.A.) {270.66}	5.00	100.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	1124	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY (IOCL) (N16000396)	7-2020	1/2024 (Apr-2025) {4/2026}	13,805.00 (N.A.) {13,805.00}	7,531.48	89.70
	POWER	1125	EASTERN REGION EXPANSION SCHEME XXIX (PGCIL) (N18000351)	3-2023	11/2025 (N.A.) {6/2025}	524.04 (N.A.) {524.04}	359.97	99.00
		1126	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) (NTPC) (N18000364)	8-2022	5/2027 (N.A.) {12/2027}	11,844.00 (N.A.) {12,539.00}	3,218.10	21.40
	RAILWAYS	1127	KHURDA ROAD-BOLANGIR(NL)ECOR (ECOR) (220100284)	4-1994	12/2026 (Dec-2026) {12/2026}	3,550.00 (3,791.66) {5,089.37}	4,840.22	85.00
		1128	TALCHER-BIMALAGARH(NL)(ECOR) (ECOR) (220100328)	4-2005	3/2025 (N.A.) {3/2026}	1,928.10 (N.A.) {1,928.07}	1,726.15	40.00
		1129	BHADRAK - NERGUNDI 3RD LINE (ECOR) (N22000316)	3-2013	11/2024 (Jan-2026) {6/2026}	1,284.39 (1,284.39) {1,284.39}	1,288.97	80.00
		1130	JAGADALPUR-KORAPUT DOUBLING (ECOR) (N22000376)	4-2015	3/2024 (N.A.) {3/2022}	1,547.38 (N.A.) {1,547.38}	1,291.30	93.60
		1131	KORAPUT - SINGAPUR ROAD DOUBLING (ECOR) (N22000379)	4-2015	12/2027 (Mar-2026) {3/2026}	2,362.00 (2,361.74) {2,361.74}	1,794.64	79.00
		1132	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE (ECOR) (N22000380)	4-2015	3/2027 (N.A.) {8/2026}	820.61 (N.A.) {810.02}	580.59	N.A.
		1133	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. (ECOR) (N22000381)	4-2015	3/2026 (Nov-2025) {11/2025}	1,172.92 (N.A.) {2,022.75}	1,949.32	80.00
		1134	VIZIANAGARAM -SAMABALPUR 3RD LINE (RVNL) (N22000409)	1-1991	12/2026 (N.A.) {12/2026}	4,803.16 (N.A.) {4,803.16}	4,691.52	N.A.
		1135	JEYPORE MALKANGIRI NEW LINE (ECOR) (N22000516)	2-2018	7/2033 (N.A.) {7/2033}	2,344.00 (N.A.) {642.69}	220.78	90.10
		1136	JEYPORE NABARANGPUR NEWLINE (ECOR) (N22000517)	7-2017	7/2028 (Dec-2029) {12/2029}	748.00 (N.A.) {747.91}	0.00	N.A.

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1137	TALCHER - ANGUL NEW LINE WITH Y CONNECTION AT TALCHER (ECOR) (N22000518)	7-2018	12/2026 (N.A.) {12/2026}	278.96 (495.00) {494.62}	29.50	N.A.
		1138	KODINGAMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (ECOR) (N22000519)	8-2022	8/2027 (N.A.) {8/2027}	190.90 (N.A.) {190.90}	10.00	N.A.
		1139	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION (ECOR) (N22000520)	9-2022	9/2027 (N.A.) {3/2028}	189.93 (N.A.) {189.93}	14.04	N.A.
		1140	BRUNDAMAL-JHARSUGUDA- FLYOVER CONNECTION FOR JOINING DN LINE (ECOR) (N22000521)	12-2009	12/2026 (N.A.) {12/2026}	296.51 (N.A.) {297.00}	171.98	10.00
		1141	BAGHUAPAL FLY OVER (20 KM) (ECOR) (N22000522)	8-2019	8/2027 (Aug-2027) {8/2027}	183.00 (257.97) {257.97}	0.83	N.A.
		1142	ROURKELA-BONDAMUNDA A-CABIN 5TH LINE (10 KM) (UMBRELLA WORK PB#57/2019- 20/NR) (SER) (N22000571)	9-2022	9/2026 (N.A.) {2/2026}	209.75 (N.A.) {244.99}	76.22	30.00
	ROAD TRANSPORT AND HIGHWAYS	1143	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S (NHAI) (N24000619)	9-2016	8/2019 (N.A.) {6/2025}	2,510.04 (N.A.) {2,510.04}	1,181.34	99.38
		1144	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO (NHAI) (N24000715)	12-2017	7/2020 (N.A.) {7/2025}	686.65 (565.00) {686.65}	574.26	97.80
		1145	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE ((NHAI) (N24000733)	1-2018	8/2022 (N.A.) {12/2025}	633.68 (492.83) {633.68}	560.38	86.00
		1146	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG (NHAI) (N24000734)	1-2018	8/2021 (N.A.) {6/2025}	614.48 (503.30) {757.12}	664.48	100.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1147	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON (NHAI) (N24000736)	1-2018	9/2020 (N.A.) {7/2025}	686.65 (504.09) {1,015.16}	488.98	97.98
		1148	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 (NHAI) (N24000738)	1-2018	9/2021 (N.A.) {7/2025}	999.00 (1,152.70) {1,152.70}	540.10	82.01
		1149	REHABILITATION AND UP-GRADATION TO 4- LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) ((NHAI) (N24000739)	1-2018	6/2021 (Jun-2025) {6/2025}	503.88 (609.03) {609.03}	536.89	98.50
		1150	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. (MoRTH) (N24000912)	8-2016	2/2017 (N.A.) {12/2025}	287.70 (N.A.) {293.66}	275.42	98.66
		1151	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA (MoRTH) (N24000914)	12-2016	8/2018 (N.A.) {9/2025}	223.50 (N.A.) {223.50}	220.50	92.00
		1152	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA (MoRTH) (N24000917)	3-2018	8/2018 (N.A.) {6/2025}	199.16 (N.A.) {199.16}	158.73	100.00
		1153	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 (NHAI) (N24001647)	8-2020	3/2022 (N.A.) {6/2025}	200.00 (154.73) {154.73}	150.38	100.00
		1154	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8 (NHAI) (N24001665)	12-2021	10/2024 (N.A.) {12/2025}	1,592.00 (1,592.00) {1,592.00}	1,083.78	78.13
		1155	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130-CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE-OD (NHAI) (N24001666)	12-2021	9/2024 (N.A.) {8/2025}	714.00 (714.00) {714.00}	580.51	94.92

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1156	6L GREENFIELD KALIAGURA ? BAUNSAGUAR SECTION OF NH-130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG (NHAI) (N24001667)	9-2021	5/2024 (N.A.) {12/2025}	1,734.00 (1,734.00) {1,734.00}	1,222.14	86.00
		1157	6L OF BADAKUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH-130- CD (PACKAGE ? OD-3) (NHAI) (N24001668)	3-2021	4/2024 (N.A.) {11/2025}	1,249.00 (N.A.) {1,249.00}	465.59	85.60
		1158	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH-130- CD (PACKAGE ? OD-1) (NHAI) (N24001669)	2-2021	3/2024 (N.A.) {6/2025}	586.00 (N.A.) {586.00}	240.33	88.90
		1159	6L OF KARKI ? KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH-130-CD (PACKAGE ? OD-4) (NHAI) (N24001670)	2-2021	3/2024 (N.A.) {6/2025}	593.00 (N.A.) {593.00}	282.15	94.46
		1160	6L OF HATIBENA - BADAKUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130- CD (PACKAGE ? OD-2) (NHAI) (N24001671)	2-2021	3/2024 (N.A.) {6/2025}	925.00 (N.A.) {925.00}	460.47	97.00
		1161	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE ? (NHAI) (N24001678)	8-2021	6/2024 (N.A.) {12/2025}	1,460.00 (1,460.00) {1,460.00}	978.88	91.00
		1162	CONSTRUCTION OF ROAD FROM KM 0/0 TO 72/0 OF NH-26 SUCH AS 4 LANE FROM KM 0/0 TO 21/0 (BARGARH TO BAR (MoRTH) (N24001857)	6-2020	12/2023 (Aug-2025) {8/2025}	414.24 (N.A.) {414.24}	307.52	98.00
		1163	WIDENING AND STRENGTHENING TO 2L+PS INCLUDING LA OF KANDARPUR-BALIKUDA FROM KM 277/500 TO 318/970 OF (MoRTH) (N24001858)	3-2022	6/2025 (N.A.) {12/2025}	499.79 (N.A.) {499.79}	285.58	45.00
		1164	CONSTRUCTION OF BYPASS ON NH-59 FROM KM 336/350 TO 349/910 (13.56 KM) NEAR BERHAMPUR TOWN INCLUDING (MoRTH) (N24001859)	3-2021	3/2024 (N.A.) {8/2025}	196.94 (N.A.) {196.94}	71.55	56.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1165	CONSTRUCTION OF BYPASS TO NAYAGARH TOWN FROM KM 235.469 TO 252.482 OF NH-57 INCLUDING LAND ACQUISITI (MoRTH) (N24001860)	1-2022	4/2025 (N.A.) {8/2025}	300.33 (N.A.) {300.33}	203.81	70.00
		1166	CONSTRUCTION OF BYPASS TO KHORDHA TOWN FROM KM 294/000 TO 300/300 ON NH-57 INCLUDING LA IN THE STATE (MoRTH) (N24001861)	2-2022	11/2024 (Aug-2025) {8/2025}	157.49 (N.A.) {157.49}	72.57	54.00
		1167	CONSTRUCTION OF BYPASS ROAD TO BALANGIR TOWN FROM KM 72/400 (DESING KM 0/0) TO KM 79/800 (DESIGN KM (MoRTH) (N24001862)	2-2022	10/2025 (Nov-2025) {11/2025}	238.78 (N.A.) {238.78}	50.39	35.00
		1168	CONSTRUCTION OF 5 HL BRIDGES AT KM 379/000 (PANGAM), KM 439/400 (POTTERU), KM 444/237 (KONGURUKONDA) (MoRTH) (N24001863)	3-2021	6/2024 (Oct-2025) {8/2025}	154.05 (N.A.) {154.05}	47.47	30.00
		1169	CONSTRUCTION OF FOUR LANE ROB AND ITS APPROACHES IN LIEU OF EXISTING LEVEL CROSSING NO. RV-71 AT KM (MoRTH) (N24001864)	11-2021	6/2025 (N.A.) {8/2025}	154.49 (N.A.) {154.49}	59.92	45.00
		1170	CONSTRUCTION OF 4 LANE ROB WITH APPROACHES IN LIEU OF LC NO. RV-172 AT KM 176.00 OF NH-201 (PRESENT (MoRTH) (N24001865)	12-2021	5/2025 (Aug-2025) {8/2025}	324.09 (N.A.) {324.09}	110.76	35.00
		1171	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM. (NHAI) (N24002078)	12-2023	12/2025 (N.A.) {12/2025}	711.00 (N.A.) {711.00}	182.54	52.30
		1172	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002079)	12-2023	12/2025 (N.A.) {12/2025}	742.25 (N.A.) {742.25}	223.42	52.89

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1173	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002080)	12-2023	12/2025 (N.A.) {12/2025}	762.75 (N.A.) {762.75}	228.86	52.78
		1174	3L MAJOR BRIDGE OVER RIVER BRAHMANI AT KM. 401.250 (DUBURI CHANDIKHOLE SECTION) OF NH 200 (NEW NH 5 (NHAI) (N24002081)	8-2022	1/2025 (N.A.) {12/2026}	153.61 (N.A.) {153.61}	14.22	34.49
		1175	WIDENING AND STRENGTHENING TO 2L+PS FROM KM 0.000 TO 40.000 (DHAUGAON- PODAMARI SECTION) OF NH 326 I (MoRTH) (N24002135)	3-2022	2/2026 (N.A.) {2/2026}	186.52 (N.A.) {186.52}	45.93	35.00
		1176	WIDENING AND STRENGTHENING TO 4L+PS/2L+PS FROM KM 0.000 TO 35.800 (KUAKHIA - MANGALPUR SECTION) OF N (MoRTH) (N24002136)	3-2022	2/2026 (N.A.) {2/2026}	636.10 (N.A.) {636.10}	264.02	36.00
		1177	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE ? PARADIP SECTION OF NH-53 (OLD NH (NHAI) (N24002219)	3-2024	10/2026 (N.A.) {10/2026}	882.45 (N.A.) {882.45}	81.90	12.73
		1178	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY (SAIL) (N12000122)	11-2020	5/2023 (Mar-2025) {3/2025}	377.18 (N.A.) {377.18}	434.90	N.A.
		1179	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP (SAIL) (N12000125)	1-2022	5/2025 (N.A.) {7/2025}	970.18 (N.A.) {970.18}	689.07	93.76
PUNJAB	DEPARTMENT OF HIGHER EDUCATION	1180	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. (CPWD EDUCATION) (N28000142)	10-2019	5/2022 (N.A.) {7/2025}	348.24 (N.A.) {348.24}	237.84	90.20

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	1181	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB (HPCL) (N16000402)	5-2020	2/2023 (Sep-2024) {12/2025}	1,421.46 (N.A.) {1,421.46}	1,156.45	95.62
		1182	BHATINDA SANGRUR PIPELINE (HPCL) (N16000440)	11-2021	5/2024 (Feb-2025) {7/2025}	367.00 (397.00) {397.00}	329.81	90.30
		1183	CGD PROJECT AT PATHANKOT DISTRICT (IOCL) (N16000488)	3-2022	3/2030 (Sep-2033) {9/2033}	151.00 (N.A.) {151.00}	8.73	2.00
	RAILWAYS	1184	235 (NR) (N22000589)	9-2020	3/2025 (N.A.) {7/2025}	235.00 (N.A.) {235.00}	5.12	98.00
		1185	FEROZPUR - PATTI (25.72 KM) (NR) (N22000614)	4-2017	3/2027 (N.A.) {3/2027}	299.74 (N.A.) {781.00}	0.00	N.A.
	ROAD TRANSPORT AND HIGHWAYS	1186	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA (MoRTH) (N24000907)	3-2018	8/2020 (N.A.) {6/2025}	293.10 (N.A.) {315.00}	318.24	99.75
		1187	JALANDHAR-HOSHIARPUR SECTION OF NH- 70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 (MoRTH) (N24000909)	10-2017	10/2019 (N.A.) {12/2025}	1,069.59 (N.A.) {1,069.59}	739.08	44.00
		1188	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 (MoRTH) (N24000910)	3-2018	11/2020 (N.A.) {6/2026}	170.57 (N.A.) {150.00}	135.00	79.00
		1189	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO (NHAI) (N24001415)	12-2020	4/2024 (Jul-2024) {7/2024}	881.00 (N.A.) {881.00}	932.64	90.64
		1190	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA- MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI (NHAI) (N24001416)	12-2020	1/2024 (Mar-2025) {3/2025}	989.66 (N.A.) {989.66}	324.77	31.08

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1191	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO (NHAI) (N24001417)	12-2020	4/2024 (Sep-2025) {9/2025}	1,234.40 (N.A.) {1,234.40}	792.35	63.09
		1192	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO (NHAI) (N24001418)	12-2020	4/2024 (Sep-2025) {9/2025}	1,094.46 (N.A.) {1,094.46}	802.93	62.99
		1193	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- (NHAI) (N24001419)	2-2021	4/2024 (Nov-2024) {11/2024}	1,269.96 (N.A.) {1,269.96}	585.86	43.45
		1194	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR- (NHAI) (N24001420)	2-2021	4/2024 (Dec-2025) {12/2025}	853.66 (N.A.) {853.66}	132.99	15.33
		1195	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA (NHAI) (N24001630)	7-2021	2/2025 (N.A.) {2/2025}	1,501.02 (N.A.) {1,501.02}	237.00	73.00
		1196	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD (NHAI) (N24001631)	3-2021	10/2024 (N.A.) {10/2024}	1,525.31 (N.A.) {1,525.31}	245.00	88.70
		1197	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM (NHAI) (N24001632)	1-2021	5/2024 (Jun-2025) {8/2025}	1,741.86 (2,281.02) {2,281.02}	1,278.00	96.00
		1198	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA ? RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR (NHAI) (N24001636)	5-2021	12/2024 (Oct-2026) {10/2026}	1,368.91 (1,368.91) {1,368.91}	163.58	15.31

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1199	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K (NHAI) (N24001637)	3-2021	1/2025 (N.A.) {1/2025}	1,754.84 (N.A.) {1,754.84}	1,082.62	35.08
		1200	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6 (NHAI) (N24001638)	11-2021	7/2024 (Aug-2025) {8/2025}	646.42 (646.42) {646.42}	481.67	96.00
		1201	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE (NHAI) (N24001639)	5-2020	12/2024 (Aug-2025) {8/2025}	864.23 (864.23) {864.23}	434.88	63.00
		1202	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N (NHAI) (N24001640)	3-2021	11/2024 (N.A.) {11/2024}	1,229.38 (N.A.) {1,229.38}	729.77	47.80
		1203	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR (NHAI) (N24001641)	3-2021	10/2024 (Dec-2025) {12/2025}	1,641.75 (N.A.) {1,641.75}	188.55	29.45
		1204	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI (NHAI) (N24001642)	2-2021	8/2024 (Dec-2025) {12/2025}	1,474.77 (N.A.) {1,474.77}	471.06	73.72
		1205	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I (NHAI) (N24001643)	12-2020	6/2024 (Jun-2025) {6/2025}	857.91 (N.A.) {857.91}	127.71	40.00
		1206	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV (NHAI) (N24001644)	12-2020	9/2023 (Sep-2025) {9/2025}	524.88 (416.58) {416.58}	157.14	73.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1207	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION OF NH-354 SECTION ARIFKES-FEROZEPUR-MUKTS (MoRTH) (N24001960)	3-2021	10/2023 (N.A.) {10/2025}	263.19 (N.A.) {220.00}	119.50	61.00
		1208	WORK OF WIDENING/UPGRADATION OF 2-LANE WITH PAVED SHOULDER OF SRI MUKTSAR SAHIB TO MALOUT ROAD FROM (MoRTH) (N24001961)	3-2022	10/2023 (N.A.) {7/2025}	152.58 (N.A.) {152.58}	97.00	85.00
		1209	6L OF JODHPUR ROMANA (BATHINDA) - MANDI DABWALI (PUNJAB HARYANA BORDER) SECTION OF NH-54 FROM KM. 0. (NHAI) (N24002075)	12-2020	8/2025 (Aug-2025) {8/2025}	757.13 (757.00) {757.00}	246.51	98.00
		1210	6L AMRITSAR-BATHINDA GREENFIELD SECTION FROM JN. WITH BHAGTA BHAI KA-BHADAUR ROAD NEAR DYALPURA BHAI (NHAI) (N24002076)	3-2021	10/2025 (Jun-2026) {6/2026}	2,029.17 (2,029.00) {2,029.00}	84.23	46.00
		1211	6L ACCESS CONTROLLED LUDHIANA-BATHINDA GREENFIELD HIGHWAY FROM JN. WITH AMRITSAR-BATHANDA GREENFIELD (NHAI) (N24002091)	6-2021	9/2025 (Mar-2026) {3/2026}	906.51 (906.51) {906.51}	134.05	49.80
		1212	6-LANE AMRITSAR-BATHINDA GREENFIELD SECTION OF NH-754A FROM JUNCTION WITH MOGA JALANDHAR ROAD (NH-70) (NHAI) (N24002092)	3-2021	10/2025 (N.A.) {10/2025}	1,801.37 (N.A.) {1,801.37}	1,074.27	44.15
		1213	6L OF AMBALA-CHANDIGARH GREENFIELD SECTION FROM KM. 0.000 TO KM. 25.000 WITH 4L SPUR TO LALRU FROM K (NHAI) (N24002098)	3-2022	10/2025 (N.A.) {10/2025}	1,641.66 (N.A.) {1,641.66}	60.00	52.00
		1214	4L OF EXISTING BEAS ? BABA BAKALA - DERA BABA NANAK SECTION FROM START OF BATALA BYPASS TILL INTERSE (NHAI) (N24002100)	10-2021	6/2025 (N.A.) {6/2025}	1,003.38 (N.A.) {1,003.38}	275.45	69.19

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
RAJASTHAN		1215	4L OF BEAS-MEHTA-BATALA-DERA BABA NANAK FROM INTERSECTION WITH JALANDHAR-AMRITSAR HIGHWAY (NH-3) NEA (NHAI) (N24002101)	8-2021	6/2025 (Dec-2025) {12/2025}	809.51 (N.A.) {809.51}	218.47	51.91
		1216	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I SPUR-I) FROM JN. WITH KAPURTHALA - SULTANPUR LODHI ROAD (NH (NHAI) (N24002102)	1-2020	4/2026 (N.A.) {4/2027}	2,165.23 (N.A.) {2,165.23}	174.63	19.60
	CIVIL AVIATION	1217	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT (AAI) (N04000101)	5-2022	11/2024 (Oct-2025) {10/2025}	480.00 (N.A.) {480.00}	246.67	70.00
		1218	UDAIPUR AIRPORT- CONSTRUCTION OF NEW INTEGRATED PASSENGER TERMINAL BUILDING (AAI) (N04000104)	6-2023	3/2026 (N.A.) {3/2026}	887.00 (N.A.) {887.00}	300.51	62.00
	COAL	1219	NLCIL 300 MW SOLAR POWER PROJECT (PART OF 510 MW CPSU SCHEME) (NLC) (N06000269)	3-2023	9/2024 (N.A.) {9/2025}	1,813.00 (N.A.) {1,813.00}	654.94	66.00
	PETROLEUM	1220	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE (IOCL) (N16000435)	12-2021	10/2024 (Dec-2025) {12/2025}	9,028.00 (N.A.) {9,028.00}	6,662.44	81.86
		1221	CGD PROJECT IN TONK, SAWAI MADHOPUR, DAUSA, KARAUJI (HPCL) (N16000496)	3-2022	3/2030 (N.A.) {3/2030}	1,751.00 (N.A.) {1,751.00}	296.16	24.70
		1222	SETTING UP OF PETROCHEMICAL EVACUATION MARKETING TERMINAL (PEMT) AT BARMER (HPCL) (N16000512)	12-2023	12/2026 (N.A.) {12/2026}	461.05 (N.A.) {461.05}	90.93	44.30
		1223	RAJASTHAN REFINERY PROJECT (HPCLRRL(JV)) (N16000513)	10-2017	10/2022 (Mar-2025) {12/2025}	43,129.00 (72,937.00) {72,937.00}	57,717.81	86.90
		1224	CGD PROJECTS AT FAZILKA (EXCEPT AREA ALREADY AUTHORIZED) GANGANAGAR AND HANUMANGARH DISTRICTS (BPCL) (N16000520)	12-2022	6/2030 (N.A.) {6/2030}	3,207.00 (N.A.) {3,207.00}	316.65	20.60
	POWER	1225	SAMBHU KI BHURJ-II SOLAR 300MW (NTPC) (N18000286)	3-2020	9/2021 (Mar-2025) {3/2025}	1,782.00 (N.A.) {1,782.00}	1,369.88	100.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1226	BHENSARA 320 MW (NTPC) (N18000293)	1-2021	7/2022 (Mar-2025) {3/2025}	1,221.73 (1,533.38) {1,533.38}	1,139.42	100.00
		1227	BHADLA-II 500MW SOLAR PV PROJECT (NTPC) (N18000347)	6-2022	3/2024 (Sep-2025) {9/2025}	2,598.92 (N.A.) {2,598.92}	1,758.06	55.00
		1228	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART (PGCIL) (N18000356)	3-2023	9/2024 (N.A.) {9/2025}	1,433.28 (N.A.) {1,433.28}	1,281.27	91.90
		1229	300 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000368)	5-2022	11/2023 (N.A.) {8/2025}	1,677.12 (N.A.) {1,677.12}	1,066.01	87.00
		1230	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE- III, PART E1 (PGCIL) (N18000373)	8-2023	2/2025 (N.A.) {9/2025}	688.74 (N.A.) {688.74}	507.00	92.00
		1231	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART H (PGCIL) (N18000374)	10-2023	4/2025 (N.A.) {8/2025}	2,211.00 (N.A.) {2,211.00}	1,551.80	60.90
		1232	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART C1 (PGCIL) (N18000375)	10-2023	4/2025 (Oct-2025) {10/2025}	1,796.00 (N.A.) {1,796.00}	1,069.00	73.60
		1233	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART B1 (PGCIL) (N18000376)	9-2023	4/2025 (N.A.) {8/2025}	2,191.00 (N.A.) {2,191.00}	1,440.66	67.90
		1234	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART J (PGCIL) (N18000378)	12-2022	3/2025 (Apr-2026) {4/2026}	331.00 (N.A.) {331.00}	8.66	26.00
		1235	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART E2 (PGCIL) (N18000379)	11-2023	6/2025 (N.A.) {9/2025}	428.00 (N.A.) {428.00}	51.42	42.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1236	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART A [BIKANER III N (PGCIL) (N18000386)	12-2023	12/2025 (N.A.) {12/2025}	2,998.00 (N.A.) {2,998.00}	1,112.98	45.30
		1237	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART D [NEEMRANA II B (PGCIL) (N18000387)	12-2023	12/2025 (N.A.) {12/2025}	2,056.00 (N.A.) {2,056.00}	1,318.23	50.70
		1238	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PH-III PART D [SIKAR KHETRI TRANSMISSI (PGCIL) (N18000389)	2-2024	8/2025 (N.A.) {8/2025}	2,000.00 (N.A.) {2,000.00}	823.00	51.00
		1239	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) PART-B (JAISALMER/BARMER COMPLEX) (PGCIL) (N18000391)	8-2024	8/2026 (N.A.) {8/2026}	3,279.00 (N.A.) {3,279.00}	293.90	16.40
		1240	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-C (PGCIL) (N18000393)	8-2024	8/2026 (N.A.) {8/2026}	2,227.00 (N.A.) {2,227.00}	292.59	16.40
		1241	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-E (PGCIL) (N18000394)	8-2024	8/2026 (N.A.) {8/2026}	3,251.00 (N.A.) {3,251.00}	426.60	13.40
		1242	ADDITIONAL TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM BHADLA-III PS AS PART OF RAJASTHAN REZ P (PGCIL) (N18000396)	8-2024	2/2026 (N.A.) {2/2026}	369.00 (N.A.) {369.00}	0.00	1.00
		1243	TRANSMISSION SYSTEM STRENGTHENING FOR INTERCONNECTIONS OF BHADLA-III AND BIKANER III COMPLEX [SPV NA (PGCIL) (N18000397)	8-2024	8/2026 (N.A.) {8/2026}	1,382.00 (N.A.) {1,382.00}	0.00	1.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1244	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BAR (PGCIL) (N18000401)	11-2024	11/2026 (N.A.) {11/2026}	2,735.00 (N.A.) {2,735.00}	0.00	0.70
		1245	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6GW)] [BIKANER COMPLEX (PGCIL) (N18000403)	11-2024	11/2026 (N.A.) {11/2026}	5,969.00 (N.A.) {5,969.00}	0.00	N.A.
		1246	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6 GW)] [BIKANER COMPLE (PGCIL) (N18000404)	11-2024	11/2026 (N.A.) {11/2026}	5,357.00 (N.A.) {5,357.00}	67.82	3.70
		1247	RAJASTHAN REZ PH-V (PART-1: 4 GW) [SIROHI/NAGAU] COMPLEX (PGCIL) (N18000414)	3-2025	3/2027 (N.A.) {3/2027}	5,028.00 (N.A.) {5,028.00}	0.00	N.A.
		1248	AUGMENTATION AT FATEHGARH-II PS, FATEHGARH-IV PS (SECTION-II) AND BARMER-I (PGCIL) (N18000415)	3-2025	12/2026 (N.A.) {12/2026}	404.00 (N.A.) {428.00}	0.00	N.A.
		1249	NOKH SOLAR PV PROJECT 735 MW (NTPC) (N18000418)	3-2022	4/2024 (Jul-2025) {7/2025}	4,189.17 (4,378.17) {4,378.17}	151.79	95.00
	RAILWAYS	1250	AGRA FORT-BANDIKUI (NCR) (N22000553)	6-2022	6/2027 (May-2026) {5/2026}	1,389.81 (N.A.) {987.83}	42.46	12.00
		1251	GUDHA THATHANA MITHRI TEST TRACK FOR RDSO (NWR) (N22000593)	4-2019	3/2025 (N.A.) {6/2025}	528.48 (N.A.) {500.85}	354.20	95.00
		1252	DEDICATED TEST TRACK FOR RDSO (PHASE II) (NWR) (N22000594)	11-2021	11/2026 (N.A.) {12/2025}	466.42 (N.A.) {466.22}	737.27	82.00
		1253	DOUBLING BETWEEN CHURU-RATANGARH (42.81 KM) (NWR) (N22000605)	2-2023	2/2028 (N.A.) {6/2025}	422.60 (N.A.) {422.60}	209.80	90.00
		1254	SAWAIMADHOPUR - BYPASS LINE (6.98 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NWR) (N22000607)	12-2022	6/2026 (N.A.) {1/2026}	304.00 (239.54) {239.54}	124.60	30.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1255	GC OF NATHDWARA - DEVGARH MADARIYA (82.5KM) (NWR) (N22000608)	1-2023	6/2028 (N.A.) {12/2026}	968.92 (N.A.) {968.92}	400.31	40.00
	ROAD TRANSPORT AND HIGHWAYS	1256	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA (NHAI) (N24000795)	2-2018	4/2021 (Jun-2025) {6/2025}	741.86 (649.00) {649.00}	663.37	99.99
		1257	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. (MoRTH) (N24001411)	12-2020	10/2023 (N.A.) {12/2025}	379.23 (N.A.) {379.23}	268.62	96.10
		1258	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR (MoRTH) (N24001527)	12-2021	5/2024 (Dec-2025) {12/2025}	411.40 (N.A.) {411.40}	219.61	71.63
		1259	WIDENING OF PACHPADRA-BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH-25 ON EPC MODE IN THE (MoRTH) (N24001528)	1-2022	12/2024 (Aug-2025) {8/2025}	194.88 (N.A.) {194.88}	105.69	83.00
		1260	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH-68) IN THE STATE OF RAJASTHAN ON EPC M (MoRTH) (N24001529)	12-2021	8/2024 (May-2025) {5/2025}	451.66 (N.A.) {451.66}	401.78	99.00
		1261	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN-LALSOT-KAROLI- DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH (MoRTH) (N24001530)	12-2021	9/2024 (N.A.) {8/2025}	150.11 (N.A.) {150.11}	82.83	88.00
		1262	4L GREENFIELD SPUR FROM DELHI- VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR (NHAI) (N24001557)	3-2022	11/2024 (Jun-2025) {6/2025}	1,636.15 (N.A.) {1,636.15}	553.96	95.26
		1263	4L OF KARWAR (KM. 281.980 OF NH-62 NAGAU ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II) (NHAI) (N24001558)	11-2021	8/2024 (Jun-2025) {6/2025}	736.75 (N.A.) {736.75}	253.43	97.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1264	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE -0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK (NHAI) (N24001559)	9-2021	6/2024 (May-2025) {5/2025}	672.35 (N.A.) {672.35}	328.24	99.50
		1265	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6) (NHAI) (N24001563)	10-2019	8/2023 (Jun-2025) {6/2025}	846.59 (N.A.) {846.59}	167.25	99.25
		1266	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-7) (NHAI) (N24001564)	10-2019	7/2023 (Jun-2025) {6/2025}	662.08 (N.A.) {662.08}	124.06	96.50
		1267	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA (NHAI) (N24001567)	11-2019	10/2022 (Jun-2025) {6/2025}	1,272.97 (N.A.) {1,272.97}	512.05	86.81
		1268	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N (NHAI) (N24001568)	11-2019	5/2023 (Jun-2025) {6/2025}	1,119.35 (N.A.) {1,119.35}	1,447.44	99.80
		1269	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M (NHAI) (N24001573)	11-2019	12/2022 (Jun-2025) {6/2025}	1,658.06 (N.A.) {1,658.06}	157.39	99.90
		1270	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH (NHAI) (N24001612)	7-2020	1/2024 (Dec-2025) {12/2025}	1,788.69 (N.A.) {1,788.69}	960.26	76.81
		1271	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FOR FATEHPUR BYPASS, MANDAWA BYPASS AND JHUNJHUNU BYPAS (MoRTH) (N24001866)	3-2022	8/2024 (N.A.) {6/2025}	186.29 (N.A.) {186.29}	142.69	90.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1272	UPGRADATION OF TWO LANE PAVED SHOULDER FROM SHAHPURA TO THANAGAZI OF NH-248A ON EPC MODE IN THE STAT (MoRTH) (N24001867)	3-2022	7/2024 (N.A.) {8/2025}	174.34 (N.A.) {174.34}	118.08	90.00
		1273	Sagwara Bypass and Garhi- Partapur Bypass of NH-927A in the State of Rajasthan. (MoRTH) (N24001868)	3-2022	8/2025 (N.A.) {8/2025}	187.65 (N.A.) {187.65}	117.57	90.00
		1274	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FROM CHARBHUJA AT DESIGN KM 0.00 (EXISTING KM 150.00) TO (MoRTH) (N24001927)	2-2022	9/2025 (N.A.) {9/2025}	838.43 (N.A.) {838.43}	455.87	99.00
		1275	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER NORTHERN BYPASS PHASE-II OF KOTA CITY FROM DESIGN CHAINAG (MoRTH) (N24001928)	3-2022	4/2025 (N.A.) {12/2025}	317.74 (N.A.) {317.74}	136.23	12.50
		1276	ADDITIONAL STRUCTURES ON 6LGURGAON- JAIPUR SECTION OF NH-48 BETWEEN KM 42.700 TO KM 273.00 (NHAI) (N24002058)	8-2022	6/2024 (Jun-2025) {6/2025}	409.64 (N.A.) {409.64}	238.22	77.10
		1277	UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF HANUMANGARH TO KENCHIYAN OF NH 54 ON EPC MODE IN THE ST (MoRTH) (N24002167)	3-2024	10/2026 (N.A.) {10/2026}	334.64 (N.A.) {334.64}	128.00	50.00
		1278	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM NEECHLI ODEN (NATHDWARA) AT DESIGN KM 88.800 TO BHATE (MoRTH) (N24002168)	3-2023	10/2026 (N.A.) {10/2026}	606.61 (N.A.) {606.61}	118.00	20.00
SIKKIM	CIVIL AVIATION	1279	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	24.99	12.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1280	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8-2020	1/2025 (N.A.) {1/2025}	314.06 (N.A.) {303.55}	157.24	80.00
	<u>POWER</u>	1281	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	4,341.50	67.67
		1282	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,486.30	88.51
	<u>RAILWAYS</u>	1283	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	5/2015 (Dec-2027) {12/2027}	7,876.92 (11,963.43) {11,963.43}	8,569.25	80.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1284	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (May-2022) {12/2023}	375.80 (N.A.) {375.80}	288.56	96.55
		1285	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11-2017	10/2020 (Aug-2023) {4/2024}	290.05 (N.A.) {290.05}	218.36	100.00
		1286	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {6/2025}	402.94 (N.A.) {402.94}	247.12	76.54
		1287	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (Nov-2024) {7/2025}	295.97 (N.A.) {295.97}	249.80	95.66
		1288	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3-2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	100.00
		1289	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {4/2025}	311.00 (N.A.) {273.78}	257.86	95.12

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1290	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (Aug-2024) {10/2025}	345.38 (395.59) {395.59}	362.61	91.24
		1291	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (Oct-2023) {12/2025}	183.31 (439.56) {439.56}	355.31	51.19
		1292	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (Aug-2024) {12/2025}	262.84 (414.20) {414.20}	221.86	47.57
		1293	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (Oct-2023) {12/2025}	292.80 (N.A.) {292.80}	202.92	60.90
		1294	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (Oct-2024) {12/2025}	230.45 (244.91) {244.91}	206.95	82.32
		1295	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (Jul-2025) {3/2026}	493.42 (478.79) {478.79}	305.20	58.28
		1296	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (Jun-2025) {12/2026}	816.79 (786.60) {786.60}	332.24	51.45
		1297	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (Apr-2025) {12/2025}	410.60 (379.30) {379.30}	234.98	74.58

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1298	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (Jan-2026) {1/2026}	385.15 (N.A.) {385.15}	170.32	81.30
TAMIL NADU	CIVIL AVIATION	1299	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI (AAI) (N04000074)	6-2018	2/2022 (Jun-2026) {6/2026}	2,467.00 (N.A.) {2,467.00}	1,601.60	71.00
		1300	DEVELOPMENT OF TUTICORIN AIRPORT (AAI) (N04000090)	6-2019	3/2022 (Apr-2025) {4/2025}	380.87 (451.74) {451.74}	361.57	100.00
	COAL	1301	JAWAHAR KHANI OPENCAST (JK OC) MINE (SCCL) (N06000259)	12-2021	3/2025 (N.A.) {3/2026}	297.88 (N.A.) {297.88}	46.37	20.00
		1302	50 MW SOLAR POWER PROJECT -NEYVELI MINED OUT AREA (NLC) (N06000279)	5-2023	6/2025 (N.A.) {9/2025}	218.03 (N.A.) {218.03}	147.99	38.00
	FINANCE	1303	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI (CPWD FOR FINANC) (N28000109)	11-2017	11/2021 (N.A.) {11/2022}	348.77 (N.A.) {348.77}	223.39	100.00
	MINES	1304	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (NALCO) (N10000014)	9-2017	6/2019 (Mar-2024) {12/2024}	166.62 (163.17) {163.17}	135.63	65.00
	PETROLEUM	1305	IRUGUR-DEVANGONTHI POL PIPELINE (BPCL) (N16000234)	11-2012	2/2017 (Oct-2025) {10/2025}	678.00 (1,732.00) {1,732.00}	615.48	59.00
		1306	CBR 9 MMTA PROJECT (CPCL) (N16000434)	1-2021	6/2025 (N.A.) {6/2025}	31,580.00 (31,580.00) {36,354.00}	1,326.17	10.20
		1307	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI (IOCL) (N16000438)	1-2022	7/2024 (Jun-2025) {12/2025}	827.00 (887.71) {887.71}	576.63	85.40
		1308	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI) (IOCL) (N16000455)	1-2022	7/2024 (May-2026) {5/2026}	829.00 (N.A.) {829.00}	257.54	59.44
		1309	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS (IOCL) (N16000486)	3-2022	3/2030 (N.A.) {12/2030}	501.00 (N.A.) {501.00}	107.21	5.30

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1310	CGD PROJECTS AT THE NILGIRIS AND ERODE DISTRICTS (BPCL) (N16000521)	12-2022	3/2030 (N.A.) {3/2030}	3,685.00 (N.A.) {3,685.00}	205.14	10.80
	POWER	1311	TRANSMISSION SYSTEM UNDER ISTS FOR EVACUATION OF POWER FROM KUDANKULAM UNIT - 3 AND 4 (2X1000 MW) (PGCIL) (N18000408)	1-2025	7/2028 (N.A.) {7/2028}	548.00 (N.A.) {548.00}	0.00	N.A.
	RAILWAYS	1312	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP (MRTF) (N22000028)	4-2006	7/2024 (May-2025) {5/2025}	734.01 (734.01) {981.83}	632.33	98.00
		1313	TIDIVANAM-NAGARI (NL) (SR) (N22000085)	9-2006	9/2016 (Mar-2028) {3/2028}	3,631.34 (3,631.34) {3,631.34}	873.31	15.00
		1314	CHENNAI BEACH-CHENNAI EGMORE (4.3 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SR) (N22000568)	3-2022	3/2026 (Feb-2025) {3/2025}	359.60 (274.20) {310.00}	302.11	95.00
		1315	MORAPPUR-DHARMAPURI (SR) (N22000618)	2-2019	3/2028 (Mar-2028) {3/2028}	358.95 (N.A.) {358.95}	40.09	1.00
		1316	KARAIKAL PERALAM(23KM)-NEW LINE PROJECT (SR) (N22000625)	1-2019	3/2026 (Mar-2025) {6/2025}	304.22 (N.A.) {373.42}	282.58	97.00
		1317	NAGAPATTINAM THIRUTURAIPUNDI (38KM)- NEW LINE PROJECT (SR) (N22000626)	7-2008	3/2026 (Mar-2027) {3/2027}	677.12 (N.A.) {788.05}	144.28	19.00
	ROAD TRANSPORT AND HIGHWAYS	1318	FOUR LANNING OF CHOLOPURAM- THANJAVUR (NHAI) (N24000697)	8-2017	9/2020 (N.A.) {6/2025}	1,176.37 (N.A.) {1,176.37}	1,325.06	99.50
		1319	4-LANNING OF STHIYATHOPU- CHOLOPURAM (NHAI) (N24000708)	9-2017	8/2020 (May-2025) {5/2025}	1,227.87 (N.A.) {1,227.87}	1,436.16	98.12
		1320	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 (NHAI) (N24000826)	3-2018	10/2022 (Jun-2025) {6/2025}	505.35 (N.A.) {837.69}	376.61	99.75

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1321	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER (NHAI) (N24001429)	3-2018	11/2021 (Jun-2025) {6/2025}	1,294.47 (1,588.40) {1,588.40}	865.95	98.72
		1322	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN (NHAI) (N24001431)	3-2018	10/2020 (Jan-2026) {1/2026}	1,872.68 (2,899.77) {2,899.77}	1,301.78	63.50
		1323	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 (MoRTH) (N24001455)	2-2022	8/2022 (N.A.) {3/2025}	191.33 (207.97) {207.97}	100.42	100.00
		1324	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH- 83) (NHAI) (N24001600)	10-2020	5/2023 (Jun-2025) {6/2025}	434.12 (N.A.) {434.12}	268.92	100.00
		1325	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 (NHAI) (N24001601)	1-2019	1/2023 (Jun-2025) {6/2025}	1,051.69 (N.A.) {1,051.69}	588.17	81.69
		1326	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001602)	1-2019	12/2022 (Nov-2025) {11/2025}	1,409.38 (N.A.) {1,409.38}	659.50	91.09
		1327	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001603)	1-2019	10/2022 (Jun-2025) {6/2025}	1,518.53 (N.A.) {1,607.54}	915.40	100.00
		1328	4-LANING OF MELUR - PILLAYARPATTI - KARAIKUDI SECTION OF NH-338, NH-36, NH- 383 (NHAI) (N24001605)	6-2018	3/2022 (N.A.) {8/2025}	1,103.86 (N.A.) {1,103.86}	568.15	84.25
		1329	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH-744A (MADURAI RING ROAD) (NHAI) (N24001606)	12-2018	3/2022 (Sep-2025) {9/2025}	854.94 (N.A.) {854.94}	400.13	77.21

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1330	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS (NHAI) (N24001692)	1-2022	9/2024 (Feb-2025) {7/2025}	467.99 (N.A.) {468.00}	71.05	80.92
		1331	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 (NHAI) (N24001693)	9-2021	10/2024 (N.A.) {10/2024}	1,751.18 (N.A.) {1,757.27}	49.69	N.A.
		1332	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM (NHAI) (N24001694)	2-2019	12/2023 (Dec-2024) {12/2024}	1,243.57 (N.A.) {1,243.57}	171.63	N.A.
		1333	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG-III) FROM KM.60+100 TO KM.94+460 (NHAI) (N24001696)	2-2019	8/2023 (Dec-2024) {12/2024}	1,291.37 (N.A.) {1,291.37}	215.02	N.A.
		1334	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM (NHAI) (N24001716)	7-2022	8/2023 (Dec-2024) {12/2024}	186.50 (242.40) {242.40}	17.15	100.00
		1335	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K (NHAI) (N24001717)	11-2020	8/2024 (N.A.) {3/2026}	1,155.49 (1,525.10) {1,525.10}	489.94	53.56
		1336	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJAHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2 (NHAI) (N24001718)	12-2020	7/2024 (N.A.) {8/2025}	843.48 (1,077.40) {1,068.60}	434.49	90.62
		1337	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEEPURAM TO SRIPERUMBUDUR SECT (NHAI) (N24001719)	2-2021	7/2024 (N.A.) {10/2025}	2,948.31 (3,605.73) {3,605.73}	813.96	76.32

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1338	BANGALORE CHENNAI EXPRESSWAY PHASE-III ? PACKAGE I (GUDIPALA TO WALAJAHPET) FROM KM 156.000 TO KM 1 (NHAI) (N24001720)	10-2020	5/2024 (N.A.) {8/2025}	1,023.91 (1,438.62) {1,438.62}	635.04	84.49
		1339	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 (NHAI) (N24001721)	2-2019	5/2024 (Aug-2025) {3/2026}	1,008.99 (1,360.53) {1,360.53}	324.81	48.10
		1340	6L OF MADURAVOYAL TO SRIPERUMBUDUR SECTION FROM KM. 13.800 TO KM. 37.000 OF NH-4 THROUGH STATE HIGH (NHAI) (N24001722)	11-2021	2/2023 (N.A.) {12/2024}	463.44 (463.07) {463.44}	334.80	99.00
		1341	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091 (NHAI) (N24001723)	10-2018	2/2021 (N.A.) {6/2025}	707.90 (766.51) {766.51}	526.39	90.06
		1342	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48 (NHAI) (N24001725)	1-2019	5/2021 (N.A.) {1/2025}	819.89 (1,314.82) {922.85}	415.60	57.32
		1343	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 ? 29/250 INCLUDING LA AND SHIFTING OF NH-234 (MoRTH) (N24001828)	1-2022	11/2024 (N.A.) {5/2025}	221.03 (243.95) {243.95}	176.50	100.00
		1344	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH-83) INCLU (MoRTH) (N24001829)	10-2022	11/2024 (N.A.) {5/2025}	172.15 (N.A.) {172.15}	157.48	100.00
		1345	CONSTRUCTION OF STRR (WEST SIDE)- NH948A-BALAGONDAPALLI (TAMIL NADU) TO KARNATAKA/TAMIL NADU BORDER F (NHAI) (N24001968)	4-2022	5/2025 (N.A.) {5/2025}	1,260.74 (N.A.) {1,260.74}	487.46	44.95
		1346	4L OF THIRUMANGALAM TO VADUGAPATTI SECTION FROM KM 0.000 TO KM 36.000 OF NH-744 (NHAI) (N24002084)	3-2022	2/2025 (N.A.) {9/2025}	1,076.97 (N.A.) {1,076.97}	540.46	87.30

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1347	CONSTRUCTION OF NEW DOUBLE TIER 4 LANE ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI (NHAI) (N24002107)	3-2023	5/2026 (N.A.) {5/2026}	1,382.00 (N.A.) {1,382.00}	0.00	N.A.
		1348	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002108)	3-2023	5/2026 (N.A.) {5/2026}	1,618.96 (N.A.) {1,618.96}	0.00	N.A.
		1349	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002109)	3-2023	5/2026 (N.A.) {5/2026}	1,301.37 (N.A.) {1,301.37}	0.00	N.A.
		1350	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002110)	3-2023	5/2026 (N.A.) {5/2026}	1,207.40 (N.A.) {1,207.40}	0.00	N.A.
		1351	FOUR LANING OF MUGAIYUR TO MARAKKANAM SECTION OF NH-332A FROM KM 31.000 TO KM 62.000 (NHAI) (N24002111)	2-2019	12/2025 (May-2026) {5/2026}	825.94 (1,116.13) {1,116.13}	327.75	38.39
		1352	SIX LANING OF TUTICORIN PORT ROAD SECTION OF NH-7A (NEW NH-138) FROM KM 0.000 TO KM 6.140 [EFFECTIVE (NHAI) (N24002112)	3-2023	7/2024 (N.A.) {6/2025}	200.30 (N.A.) {200.30}	109.38	83.35
		1353	4L OF LEFT-OVER WORKS INCLUDING ADDITIONAL STRUCTURES FROM KERALA/TAMIL NADU BORDER TO KANYAKUMARI S (NHAI) (N24002113)	3-2023	8/2025 (N.A.) {8/2025}	1,141.78 (N.A.) {1,141.78}	439.12	44.75
		1354	4L OF VADUGAPATTI TO THERKUVENGANALLUR (RAJAPALYAM) SECTION FROM KM 36.000 TO KM 71.600 OF NH744 UND (NHAI) (N24002114)	2-2022	4/2025 (N.A.) {10/2025}	1,097.59 (N.A.) {1,317.06}	689.69	96.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1355	WIDENING TO 4L/4L+PS AND STRENGTHENING IN SELECTED STRETCHES FROM KM 0/8 TO 50/570 OF NH 532 INCLUD (MoRTH) (N24002151)	3-2022	1/2024 (N.A.) {7/2025}	257.14 (294.70) {294.70}	251.25	90.00
		1356	WIDENING FROM 2L+PS TO 4L/4L+PS AND IMPROVEMENTS THE SELECTED STRETHCES FROM KM 26/5 - 81/2 INCLU (MoRTH) (N24002152)	3-2023	11/2023 (N.A.) {11/2025}	274.84 (N.A.) {274.84}	243.81	100.00
		1357	STRENGTHENING OF 2L+PS FROM KM 17/8 ? 18/2. CONSTRUCTION OF 2L+PS FROM KM 18/2 TO KM 20/0 AND CONSTR (MoRTH) (N24002153)	3-2023	2/2024 (N.A.) {8/2025}	169.68 (N.A.) {169.68}	112.18	79.00
		1358	CONSTRUCTION OF BYPASS TO MADURAI - ACHAMBATHU - VIRATIPATHU IN KM 6/850 - 10/382 OF NH 49 EXTN. (NE (MoRTH) (N24002165)	3-2022	8/2026 (N.A.) {8/2026}	238.97 (260.07) {260.07}	108.95	48.00
		1359	ACCESS CONTROLLED HIGHWAY OF 4 LANE WITH PAVED SHOULDERS FROM TIRUVALLUR (DESIGN CHAINAGE KM 17+56) (NHAI) (N24002216)	12-2024	12/2026 (N.A.) {12/2026}	1,376.10 (N.A.) {1,376.10}	0.00	7.03
TELANGANA	COAL	1360	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 (SCCL) (N06000161)	3-2017	3/2022 (N.A.) {3/2026}	413.84 (N.A.) {413.84}	397.54	85.00
		1361	GODAVARIKHANI COAL MINE (SCCL) (N06000202)	7-2019	3/2023 (N.A.) {3/2026}	438.98 (N.A.) {438.98}	171.96	70.00
		1362	VENKATESH KHANI COAL MINE (SCCL) (N06000204)	10-2020	3/2023 (N.A.) {3/2027}	484.51 (N.A.) {484.51}	318.12	55.00
		1363	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT (SCCL) (N06000210)	11-2015	3/2023 (N.A.) {3/2026}	489.62 (N.A.) {489.62}	405.54	70.00
		1364	RCE OF INDARAM OPENCAST PROJECT (SCCL) (N06000211)	8-2017	3/2021 (N.A.) {3/2025}	349.28 (N.A.) {424.81}	402.64	80.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1365	RCE OF KALYANIKHANI OPENCASE PROJECT (SCCL) (N06000213)	3-2016	3/2020 (N.A.) {3/2026}	384.32 (N.A.) {384.32}	260.96	75.00
		1366	RCE OF KAKATHIYAKHANI OC - 2 PROJECT (SCCL) (N06000214)	8-2017	3/2020 (N.A.) {3/2026}	442.42 (N.A.) {442.42}	203.00	63.00
		1367	GOLETI OPENCASE MINE (SCCL) (N06000258)	7-2021	3/2026 (N.A.) {3/2026}	345.60 (N.A.) {345.60}	68.47	20.00
	HEALTH AND FAMILY WELFARE	1368	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR (HITES) (N21000031)	12-2018	7/2024 (N.A.) {12/2025}	1,110.55 (N.A.) {1,110.55}	743.76	82.04
		1369	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD (CPWD FOR HEALTH) (N28000098)	10-2016	3/2020 (Jan-2025) {1/2025}	209.84 (281.05) {281.05}	253.13	98.50
	RAILWAYS	1370	MANOHARABAD-KOTHPALL NEW LINE(SCR) (SCR) (N22000032)	4-2006	3/2027 (N.A.) {3/2025}	1,160.00 (N.A.) {3,014.00}	1,535.65	N.A.
	ROAD TRANSPORT AND HIGHWAYS	1371	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAHAR DAM SECT (MoRTH) (N24000245)	1-2014	3/2016 (Sep-2019) {9/2019}	270.00 (N.A.) {270.00}	0.00	72.15
		1372	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR (MoRTH) (N24000247)	10-2014	2/2017 (N.A.) {2/2017}	295.47 (N.A.) {295.47}	224.42	98.15
		1373	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM (MoRTH) (N24000248)	3-2015	1/2017 (N.A.) {1/2017}	153.21 (N.A.) {153.21}	100.96	93.81
		1374	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON (MoRTH) (N24000980)	10-2016	2/2019 (N.A.) {2/2019}	298.32 (N.A.) {298.32}	178.47	98.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1375	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ (MoRTH) (N24000981)	10-2016	3/2019 (N.A.) {3/2019}	248.83 (N.A.) {248.83}	173.79	100.00
		1376	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE (MoRTH) (N24000982)	1-2017	5/2019 (N.A.) {5/2019}	244.54 (N.A.) {244.54}	174.35	100.00
		1377	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH (MoRTH) (N24000983)	1-2017	10/2019 (N.A.) {10/2019}	196.52 (N.A.) {196.52}	125.53	100.00
		1378	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI (MoRTH) (N24000984)	1-2017	12/2019 (N.A.) {12/2019}	283.00 (N.A.) {283.00}	259.15	100.00
		1379	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION (MoRTH) (N24000986)	1-2017	5/2019 (N.A.) {5/2019}	300.00 (N.A.) {300.00}	239.93	96.05
		1380	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH (MoRTH) (N24000987)	1-2018	5/2020 (N.A.) {5/2020}	283.15 (N.A.) {283.15}	270.01	92.59
		1381	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 (MoRTH) (N24000988)	1-2018	12/2019 (N.A.) {12/2019}	230.03 (N.A.) {230.03}	231.31	99.90
		1382	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 (MoRTH) (N24000989)	2-2018	6/2020 (N.A.) {6/2020}	206.13 (N.A.) {206.13}	190.94	98.36

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1383	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT (MoRTH) (N24000990)	2-2018	11/2019 (N.A.) {11/2019}	294.13 (N.A.) {294.13}	198.75	87.44
		1384	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC (MoRTH) (N24000993)	3-2018	9/2020 (N.A.) {9/2020}	322.81 (N.A.) {322.81}	315.23	98.09
		1385	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES (MoRTH) (N24000994)	3-2018	7/2020 (N.A.) {2/2026}	626.76 (N.A.) {626.76}	272.64	45.30
		1386	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR (MoRTH) (N24000996)	1-2017	10/2019 (N.A.) {10/2019}	605.08 (N.A.) {605.08}	413.37	99.84
		1387	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL ? MALLAMPALLY SECTION OF NH-365 (MoRTH) (N24000997)	3-2018	7/2019 (N.A.) {7/2019}	192.67 (N.A.) {192.67}	176.37	92.00
		1388	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR (MoRTH) (N24000998)	1-2019	(N.A.) {}	193.19 (N.A.) {249.72}	222.58	95.00
		1389	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED (GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM (NHAI) (N24001482)	8-2022	10/2024 (Aug-2022) {12/2025}	772.11 (N.A.) {772.11}	519.84	78.00
		1390	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM VILLAGE TO CHINTAGUDEM V (NHAI) (N24001483)	2-2022	9/2024 (Feb-2022) {9/2025}	637.11 (N.A.) {637.11}	415.97	84.71

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1391	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUDEM VILLAGE TO RECHERLA (NHAI) (N24001484)	9-2022	2/2024 (Sep-2022) {9/2025}	804.69 (N.A.) {804.69}	514.29	89.75
		1392	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 (NHAI) (N24001522)	1-2021	1/2024 (Jan-2021) {7/2025}	1,307.95 (N.A.) {1,307.95}	707.34	99.79
		1393	6 LANING OF EXISTING 4-LANE STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000, (NHAI) (N24001555)	3-2022	1/2025 (N.A.) {1/2025}	955.49 (N.A.) {955.49}	233.46	35.96
		1394	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44 (NHAI) (N24001556)	12-2021	7/2024 (N.A.) {7/2024}	521.53 (N.A.) {521.53}	250.70	48.76
		1395	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 (NHAI) (N24001625)	1-2022	1/2025 (N.A.) {7/2025}	1,227.57 (N.A.) {1,227.57}	288.58	44.49
		1396	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM (NHAI) (N24001626)	2-2022	1/2025 (N.A.) {1/2025}	972.06 (N.A.) {972.06}	408.48	66.81
		1397	WIDENING AND STRENGTHENING OF EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FRO (MoRTH) (N24002000)	3-2021	7/2024 (N.A.) {7/2024}	317.19 (N.A.) {317.19}	162.21	70.00
		1398	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF MEDAK - SIDDIPET SECTION FROM KM 0/0 TO KM 69/978 OF NH- (MoRTH) (N24002001)	1-2022	1/2025 (N.A.) {6/2025}	882.18 (N.A.) {882.18}	206.02	71.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1399	WIDENING AND IMPROVEMENT OF EXISTING CARRIAGE WAY TO 2 LANE WITH PAVED SHOULDERS FROM KM. 86/160 TO (MoRTH) (N24002002)	1-2022	12/2024 (N.A.) {12/2024}	423.48 (N.A.) {423.48}	149.27	71.08
		1400	REHABILITATION AND UP-GRADATION OF VALIGONDA TO THORRUR SECTION TO TWO LANE WITH PAVED SHOULDERS FRO (MoRTH) (N24002003)	1-2022	12/2024 (N.A.) {12/2024}	549.28 (N.A.) {549.28}	103.51	70.00
		1401	REHABILITATION AND UPGADATION OF LB- NAGAR TO MALKAPUR SECTION TO 6-LANE MAIN CARRIAGEWAY WITH SERVI (MoRTH) (N24002004)	3-2021	7/2024 (N.A.) {6/2025}	545.11 (N.A.) {545.11}	191.56	75.92
		1402	WIDENING TO TWO LANE WITH PAVED SHOULDERS OF 'BODHAN BASAR BHAINSA ' SECTION FROM KM 38/900 TO 95/3 (MoRTH) (N24002005)	3-2022	3/2025 (N.A.) {6/2025}	644.45 (N.A.) {644.45}	182.85	92.50
		1403	ONSTRUCTION OF 4-LANE FLYOVER AT AMBERPET-X ROAD, HYDERABAD ON NH- 202 IN THE STATE OF TELANGANA (MoRTH) (N24002006)	10-2017	6/2023 (N.A.) {6/2023}	186.71 (N.A.) {186.71}	149.64	91.50
		1404	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/000 TO KM 79/300 OF KALWAKURTHY - KOLLAPUR SECTI (MoRTH) (N24002007)	3-2022	7/2025 (N.A.) {7/2025}	886.69 (N.A.) {886.69}	90.46	59.29
		1405	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF SIDDIPET-ELKATHURTHY SECTION FROM KM 69/978 TO KM 133/6 (MoRTH) (N24002008)	1-2022	12/2024 (N.A.) {12/2024}	578.85 (N.A.) {578.85}	172.76	79.25
		1406	WIDENING AND STRENGTHENING TO 2/4 LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR ? CHINCHOLI SECTION FROM (MoRTH) (N24002009)	1-2022	1/2025 (N.A.) {7/2025}	703.68 (N.A.) {703.68}	193.39	61.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1407	WIDENING AND STRENGTHENING TO 4 LANE / 2-LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR-CHINCHOLI SECTION (MoRTH) (N24002010)	3-2022	3/2024 (N.A.) {10/2025}	631.49 (N.A.) {631.49}	7.92	25.00
		1408	IMPROVEMENT OF GEOMETRICS OF THONDUPALLY TO KOTHUR FROM KM 22.300 TO KM 34.14 OF NH-44-RCW (NHAI) (N24002082)	2-2022	9/2024 (N.A.) {1/2026}	541.58 (N.A.) {541.58}	34.89	N.A.
		1409	FOUR LANING OF KARIMNAGAR-WARANGAL SECTION OF NH-563 FROM DESIGN CH.48.860 KM NEAR SH-1 CH.170.400 K (NHAI) (N24002083)	3-2022	7/2025 (N.A.) {7/2025}	2,146.86 (2,413.00) {2,414.46}	999.41	71.83
		1410	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM-VIJAYAWADA) (NHAI) (N24002190)	3-2023	8/2026 (N.A.) {8/2026}	983.00 (N.A.) {983.00}	0.00	8.50
		1411	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM - VIJAYAWADA) (NHAI) (N24002236)	3-2023	3/2025 (N.A.) {3/2027}	832.62 (N.A.) {832.62}	0.00	N.A.
		1412	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (Sep-2025) {9/2025}	656.00 (N.A.) {656.00}	415.86	82.20
TRIPURA	PETROLEUM	1413	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (Feb-2024) {12/2024}	277.50 (302.02) {302.02}	260.38	99.94
		1414	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (Oct-2023) {11/2024}	159.13 (171.50) {171.50}	84.33	100.00
		1415	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {4/2025}	201.99 (N.A.) {287.47}	148.22	100.00
		1416	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (N.A.) {12/2025}	354.79 (N.A.) {354.79}	34.08	N.A.

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1417	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (May-2025) {5/2025}	456.88 (N.A.) {456.88}	122.23	49.88
		1418	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {12/2025}	195.95 (N.A.) {195.95}	38.10	45.30
		1419	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH- 8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	26.34	8.38
		1420	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	9.34	16.61
		1421	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	52.82	34.61
		1422	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	26.37	31.50
		1423	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	0.00	2.00
		1424	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	73.41	22.00
		1425	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM SECTION PKG-4 (NHIDCL) (N24002228)	1-2024	12/2026 (N.A.) {12/2026}	726.90 (N.A.) {726.90}	0.00	3.10
UTTAR PRADESH	CIVIL AVIATION	1426	CCS INTERNATIONAL AIRPORT , LUCKNOW (AAI) (N04000077)	6-2018	9/2021 (Oct-2026) {10/2026}	1,383.00 (1,938.00) {3,291.81}	2,645.52	80.37

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1427	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 (AAI) (N04000094)	3-2021	12/2022 (Jun-2025) {6/2025}	242.14 (328.00) {358.00}	344.58	99.90
		1428	PRAYAGRAJ AIRPORT - CONSTRUCTION OF NEW TERMINAL BUILDING, SECOND LINK TAXI TRACK, APRON EXPANSION, (AAI) (N04000102)	5-2023	11/2024 (Jul-2025) {7/2025}	185.75 (274.38) {274.38}	200.46	95.00
		1429	AGRA: DEVELOPMENT OF NEW CIVIL ENCLAVE AT AGRA AIRPORT. (AAI) (N04000113)	6-2024	7/2026 (N.A.) {7/2026}	579.00 (N.A.) {579.00}	56.17	11.50
		1430	VARANASI: DEVELOPMENT OF LAL BAHADUR SHASTRI INTERNATIONAL AIRPORT, VARANASI. (AAI) (N04000114)	7-2024	7/2027 (N.A.) {7/2027}	2,869.65 (N.A.) {2,869.65}	255.45	14.50
	COAL	1431	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW (NLC) (N06000152)	7-2016	11/2021 (Oct-2025) {10/2025}	17,237.00 (21,780.94) {21,780.94}	19,854.80	90.89
		1432	KHADIA EXPANSION OCP (NCL) (N06000208)	6-2021	3/2025 (N.A.) {3/2027}	491.67 (N.A.) {491.67}	185.60	39.73
	PETROLEUM	1433	60 KTA POLYPROPYLENE PROJECT (GAIL) (N16000429)	3-2019	4/2024 (Apr-2024) {6/2025}	910.56 (1,299.02) {1,299.02}	961.00	95.80
		1434	AUGMENTATION OF FACILITIES AT MATHURA BITUMEN PLANT (IOCL) (N16000505)	4-2022	4/2025 (Dec-2026) {12/2026}	260.12 (N.A.) {260.12}	1.03	25.00
		1435	GRASS-ROOT TERMINAL AT MIRZAPUR UTTAR PRADESH (IOCL) (N16000506)	9-2022	6/2026 (N.A.) {11/2026}	980.45 (N.A.) {980.45}	200.55	49.80
		1436	CITY GAS DISTRIBUTION PROJECTS AT LAKHIMPUR KHERI , SITAPUR, BAHRAICH, SHRAVASTI,BALRAMPUR, (BPCL) (N16000525)	12-2022	6/2030 (N.A.) {6/2030}	16,654.00 (N.A.) {16,654.00}	544.01	9.50
	POWER	1437	KHURJA SUPER THERMAL POWER PROJECT (THDCIL) (N18000272)	3-2019	9/2023 (N.A.) {7/2025}	11,089.42 (13,276.16) {13,276.16}	12,317.27	95.50
		1438	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III (2X800 MW) (NTPC) (N18000382)	3-2024	2/2030 (N.A.) {2/2030}	17,195.31 (N.A.) {17,195.31}	1,302.80	1.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1439	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-4: 3.5 GW): PART A (PGCIL) (N18000407)	12-2024	12/2026 (N.A.) {12/2026}	5,846.00 (N.A.) {5,846.00}	78.74	N.A.
		1440	TRANSMISSION SYSTEM FOR STRENGTHENING TO FACILITATE EVACUATION OF POWER FROM BHADLA/BIKANER COMPLEX (PGCIL) (N18000423)	12-2024	6/2026 (N.A.) {6/2026}	213.00 (N.A.) {213.00}	0.00	N.A.
	RAILWAYS	1441	BURHWAL - GONDA - 3RD RUNNING LINE. (NER) (N22000468)	4-2016	3/2025 (N.A.) {9/2025}	1,015.59 (N.A.) {1,250.00}	1,178.02	50.00
		1442	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU- SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. (NER) (N22000470)	4-2016	12/2024 (N.A.) {8/2025}	1,177.96 (N.A.) {2,145.00}	2,050.16	81.00
		1443	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING (NCR) (N22000495)	3-2018	3/2026 (N.A.) {3/2027}	4,329.53 (N.A.) {4,329.53}	2,008.74	50.00
		1444	JHANSI BINA DOUBLING (NCR) (N22000496)	9-2016	3/2022 (N.A.) {4/2026}	2,002.00 (N.A.) {2,001.00}	1,725.18	90.00
		1445	MATHURA-JHANSI-3RD LINE (273.80 KM) (RVNL) (N22000501)	6-2016	12/2024 (N.A.) {12/2024}	5,323.39 (N.A.) {5,190.26}	5,046.07	N.A.
		1446	SURFACE TRIANGLE LINE BETWEEN BHADURA STATION AND NEW CROSSING STN KARMA DOUBLING (ECR) (N22000525)	10-2022	10/2027 (N.A.) {10/2027}	199.96 (N.A.) {199.96}	55.09	N.A.
		1447	MUGHALSARAI - ALLAHABAD - 3RD LINE (NCR) (N22000544)	8-2019	12/2026 (N.A.) {12/2026}	2,649.44 (N.A.) {2,390.00}	83.10	55.00
		1448	ALIGARH-HARDUAGANJ FLYOVER (22 KM) (NCR) (N22000545)	4-2020	6/2026 (N.A.) {6/2026}	1,456.89 (1,244.13) {1,456.89}	10.14	8.10
		1449	LALITPUR - BIRARI WITH FLYOVER AT LALITPUR (NCR) (N22000546)	3-2017	12/2024 (N.A.) {11/2025}	356.09 (N.A.) {356.00}	196.83	65.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1450	ALIGARH-DAUD KHAN - 3RD LINE 6.9 KM AND CONSTRUCTION OF FLYOVER AT DAUD KHAN (NCR) (N22000562)	4-2019	12/2025 (N.A.) {12/2025}	451.99 (779.49) {779.49}	122.08	43.00
		1451	ALLAHABAD-BAMHRAULI - 4TH LINE (10 KM) WITH FLY-OVER AT SUBEDARGANJ (NCR) (N22000563)	4-2019	3/2026 (N.A.) {3/2026}	494.11 (N.A.) {494.11}	42.61	42.00
		1452	BHANDAI - FLYOVER FOR ETAWAH BOUND DOWN TRAINS (NCR) (N22000564)	4-2019	12/2025 (N.A.) {3/2026}	187.21 (N.A.) {250.17}	1.29	8.00
		1453	SAHJANWA - DOHRIGHAT (NER) (N22000565)	8-2019	3/2029 (N.A.) {6/2027}	371.77 (N.A.) {1,319.75}	569.15	3.00
		1454	BAHRAICH - NANPARA -NEPALGANJ (56.15 KM) (NER) (N22000566)	7-2020	12/2024 (N.A.) {6/2025}	950.00 (N.A.) {500.00}	402.22	22.00
		1455	BAHRAICH SRAVASTI BALRAMPUR (TULSIPUR) (NER) (N22000569)	10-2018	10/2030 (N.A.) {3/2028}	4,939.78 (N.A.) {4,939.78}	1,114.69	7.00
		1456	JANGHAI PRATAPGARH AMETHI DOUBLING (NR) (N22000583)	11-2017	3/2025 (N.A.) {12/2025}	721.72 (N.A.) {1,100.00}	58.98	70.00
		1457	BARABANKI MALHAUR 3RD AND 4TH LINE (32.84 KM) (NR) (N22000590)	1-2019	3/2025 (Jan-2026) {12/2025}	323.85 (N.A.) {407.00}	5.17	58.00
		1458	DOUBLING BETWEEN JAUNPUR JN- ZAFFARABAD (6.28 KM) (NR) (N22000591)	3-2023	12/2026 (N.A.) {12/2026}	177.33 (N.A.) {177.33}	0.89	10.00
		1459	JANGHAI-PHAPHAMAU - DOUBLING WITH ELECTRIFICATION (46.79 KM) (RVNL) (N22000596)	11-2018	3/2025 (N.A.) {3/2025}	357.48 (N.A.) {409.38}	362.09	N.A.
		1460	BHATNI - AUNRIHAR WITH ELECTRIFICATION (125 KM) (EXCL INDARA - MAU (116.95 KM)) (RVNL) (N22000598)	5-2018	12/2024 (N.A.) {2/2025}	2,529.46 (N.A.) {2,529.46}	1,636.33	N.A.
		1461	MATHURA - VRINDAVAN (11 KM) (NCR) (N22000612)	8-2022	6/2025 (N.A.) {6/2025}	402.88 (N.A.) {402.88}	0.00	N.A.

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1462	DOMINGARH - GORAKHPUR - GORAKHPUR CANTT - KUSUMHI - 3RD RUNNING LINE (21.15 KM) (NER) (N22000613)	11-2016	2/2025 (N.A.) {7/2025}	351.03 (N.A.) {500.37}	476.09	86.00
	ROAD TRANSPORT AND HIGHWAYS	1463	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B (MoRTH) (N24000331)	12-2019	4/2022 (N.A.) {7/2025}	282.41 (N.A.) {319.96}	276.35	88.00
		1464	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 (NHAI) (N24000564)	3-2016	7/2020 (Jul-2025) {7/2025}	1,408.00 (1,659.12) {1,659.12}	1,329.27	88.97
		1465	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA (NHAI) (N24000798)	3-2018	11/2021 (N.A.) {6/2025}	2,140.93 (N.A.) {2,140.93}	2,067.70	99.65
		1466	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN (NHAI) (N24001306)	10-2020	3/2023 (N.A.) {8/2025}	724.60 (N.A.) {724.60}	569.96	96.00
		1467	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD (MoRTH) (N24001421)	7-2018	2/2024 (N.A.) {8/2025}	1,948.25 (N.A.) {1,948.25}	1,133.21	77.00
		1468	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W (MoRTH) (N24001424)	3-2021	9/2023 (N.A.) {1/2025}	185.09 (269.81) {269.81}	266.35	100.00
		1469	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM (MoRTH) (N24001456)	4-2020	2/2024 (N.A.) {1/2025}	199.39 (212.96) {199.39}	200.01	100.00
		1470	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH-730C F (MoRTH) (N24001457)	4-2020	7/2024 (N.A.) {9/2025}	172.50 (169.56) {172.50}	106.06	73.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1471	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP (MoRTH) (N24001461)	4-2020	3/2024 (N.A.) {7/2025}	236.47 (N.A.) {236.47}	145.88	87.00
		1472	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH-92 FROM KM.30.000 TO 57.346 UNDER GNHCP (MoRTH) (N24001462)	4-2020	7/2024 (N.A.) {7/2025}	211.09 (N.A.) {211.09}	147.58	96.00
		1473	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00 (MoRTH) (N24001464)	3-2021	8/2023 (N.A.) {7/2025}	264.86 (N.A.) {264.86}	129.12	84.00
		1474	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO (MoRTH) (N24001469)	11-2021	5/2024 (N.A.) {7/2025}	307.11 (N.A.) {307.11}	199.38	91.00
		1475	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH-730C FROM KM.0.00 TO 52.770 UNDER GNHCP (MoRTH) (N24001471)	4-2020	11/2024 (N.A.) {7/2025}	325.24 (340.16) {325.24}	284.35	96.00
		1476	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR) (MoRTH) (N24001479)	3-2021	5/2024 (N.A.) {7/2025}	395.62 (392.03) {395.62}	281.93	72.00
		1477	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH-334A (PURKAJI- LAKSAR-HARIDWAR ROAD) TO TW (MoRTH) (N24001480)	10-2021	4/2024 (N.A.) {3/2025}	227.06 (N.A.) {227.06}	141.89	100.00
		1478	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO(NEAR MOHAND) OF GANESHPUR ? DEHRADUN SECTION FROM K (NHAI) (N24001523)	3-2021	10/2023 (Jun-2025) {6/2025}	836.24 (N.A.) {836.24}	792.55	98.85

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1479	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR ? DEHRADUN SECTION FROM (NHAI) (N24001524)	3-2021	10/2023 (Jun-2025) {6/2025}	990.28 (N.A.) {990.28}	997.62	98.79
		1480	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF (MoRTH) (N24001587)	3-2020	9/2024 (N.A.) {7/2025}	262.37 (343.77) {343.77}	278.92	85.00
		1481	4L SPUR OF SHAMLI-MUZAFFARNAGAR CONNECTING NH-709AD (PANIPAT-SHAMLI-MUZAFFARNAGAR) AND NH-58 (MEERUT) (NHAI) (N24001726)	1-2023	8/2024 (N.A.) {8/2024}	391.26 (N.A.) {391.26}	14.12	80.30
		1482	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF KHUTAR B (NHAI) (N24001727)	3-2022	2/2025 (N.A.) {9/2025}	762.62 (N.A.) {838.68}	561.21	94.75
		1483	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT ? SHAMLI ? MUZAFFARNAGAR) AND NH-709A (KARN) (NHAI) (N24001729)	8-2022	4/2024 (N.A.) {7/2025}	326.79 (N.A.) {329.79}	113.42	96.00
		1484	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) (NHAI) (N24001730)	12-2021	1/2025 (N.A.) {3/2025}	1,384.79 (N.A.) {1,384.79}	657.94	97.98
		1485	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 (NHAI) (N24001731)	12-2021	5/2025 (May-2025) {7/2025}	2,470.64 (N.A.) {2,335.00}	691.28	87.62
		1486	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS (NHAI) (N24001732)	12-2021	10/2024 (N.A.) {7/2025}	540.97 (N.A.) {540.97}	270.14	93.61

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1487	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.- MAVIKALAN) TO VILL.-LOHADDA FROM K (NHAI) (N24001733)	3-2022	8/2024 (N.A.) {7/2025}	1,602.48 (N.A.) {1,602.48}	444.51	92.00
		1488	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-LOHADDA TO VILL- KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. (NHAI) (N24001734)	3-2022	8/2024 (N.A.) {7/2025}	1,335.45 (N.A.) {1,335.45}	462.61	82.45
		1489	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KHYAWARI TO VILL- LATIFPUR AT SAHARANPUR BYPASS FROM KM (NHAI) (N24001735)	3-2022	8/2024 (N.A.) {7/2025}	1,428.19 (N.A.) {1,428.19}	529.71	88.46
		1490	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KARAUNDA MAHAJAN TO VILL-KHYAWARI FROM KM. 56.500 TO K (NHAI) (N24001736)	1-2022	8/2024 (N.A.) {7/2025}	1,159.96 (N.A.) {1,159.96}	515.16	98.69
		1491	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG-III (NHAI) (N24001737)	11-2021	4/2024 (N.A.) {4/2024}	923.15 (N.A.) {923.15}	455.61	100.00
		1492	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV (NHAI) (N24001738)	9-2021	10/2023 (Dec-2024) {12/2024}	300.79 (N.A.) {300.79}	122.56	76.70
		1493	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U (NHAI) (N24001739)	10-2019	11/2023 (Dec-2024) {12/2024}	1,779.83 (N.A.) {2,200.00}	1,066.00	100.00
		1494	4L OF SHAMLI BYAPSS- SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II (NHAI) (N24001744)	5-2019	11/2022 (N.A.) {7/2025}	779.17 (N.A.) {779.17}	64.10	98.27
		1495	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N (NHAI) (N24001745)	12-2021	7/2025 (Jul-2025) {7/2025}	1,972.10 (N.A.) {1,936.00}	493.67	64.31

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1496	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4-LANE ON EPC MODE IN THE STATE OF UTTAR (NHAI) (N24001746)	3-2021	4/2024 (Jun-2025) {6/2025}	364.47 (N.A.) {364.47}	208.55	91.66
		1497	4 LANING OF NAJIBABAD BYPASS OF NH-119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH-74 (NHAI) (N24001753)	2-2022	6/2024 (May-2025) {5/2025}	570.98 (578.02) {578.02}	400.10	96.06
		1498	SPUR OF MEERUT-GARH-MUKTESHWAR SECTION(NH-709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN (NHAI) (N24001754)	1-2022	10/2024 (N.A.) {10/2024}	953.79 (N.A.) {953.79}	384.66	68.59
		1499	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH (NHAI) (N24001755)	10-2019	3/2023 (Dec-2024) {12/2024}	1,936.68 (N.A.) {2,458.03}	1,380.90	100.00
		1500	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR (NHAI) (N24001772)	8-2021	3/2024 (Dec-2024) {12/2024}	1,147.26 (N.A.) {1,147.26}	81.34	60.00
		1501	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 (NHAI) (N24001826)	2-2019	2/2022 (Jun-2025) {12/2025}	927.77 (N.A.) {1,603.00}	1,202.77	91.25
		1502	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 (NHAI) (N24001830)	6-2020	11/2023 (Dec-2024) {12/2024}	2,002.79 (N.A.) {2,002.79}	1,989.85	99.00
		1503	4L FROM MATHURA BYPASS (START) AT EXISTING KM. 154.20 OF NH-44 TO GAJU VILLAGE AT KM 32.982 OF NH-53 (NHAI) (N24001851)	1-2022	3/2025 (N.A.) {3/2025}	1,738.20 (N.A.) {1,738.20}	742.13	65.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1504	6L OF AGRA BYPASS (NORTHERN) CONNECTING KM. 174.500 OF NH-2 (NEW NH-19) TO KM. 141.000 OF YAMUNA EXP (NHAI) (N24001852)	10-2021	2/2025 (N.A.) {2/2025}	957.62 (N.A.) {957.62}	832.80	86.00
		1505	CONSTRUCTION OF LEFT OUT PORTION OF AGRA INNER RING ROAD CONNECTING VILLAGE DEORI TO NH-44 VILLAGE B (NHAI) (N24001853)	10-2021	9/2024 (Mar-2025) {3/2025}	772.05 (N.A.) {772.05}	593.39	67.50
		1506	CONSTRUCTION OF 4-LANE GREEN FIELD HIGHWAY FROM KM. 35.000 TO KM. 49.155 OF NH-731A WITH PAVED SHOUL (MoRTH) (N24001929)	1-2022	10/2025 (N.A.) {10/2025}	697.66 (N.A.) {697.66}	318.82	94.00
		1507	BALANCE WORKS OF 4-LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 (NEW NH NO. 09) FROM KM. 0.000 (KM 1 (NHAI) (N24001992)	8-2022	2/2024 (Jun-2025) {6/2025}	199.31 (244.26) {244.26}	190.10	91.87
		1508	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER HIGHWAY FROM DESIGN CH.0.000 TO CH.49.200 OF NH- 731B ON (MoRTH) (N24001996)	3-2022	11/2025 (N.A.) {11/2025}	640.18 (602.76) {602.76}	479.14	80.00
		1509	CONSTRUCTION OF SHOHRATGARH BYPASS ON NH-730 UNDER EPC MODE IN THE STATE OF UTTAR PRADESH (MoRTH) (N24001997)	10-2022	5/2025 (N.A.) {2/2026}	189.31 (N.A.) {189.31}	59.91	20.00
		1510	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 90.00 TO (MoRTH) (N24002015)	11-2021	6/2025 (N.A.) {7/2025}	403.36 (328.49) {403.36}	137.71	70.00
		1511	CONSTRUCTION OF PRATAPGARH BYPASS (EXTENSION) CONNECTING NH-31 TO NH- 330 (MoRTH) (N24002016)	10-2022	6/2025 (N.A.) {8/2025}	225.17 (N.A.) {225.17}	96.21	55.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1512	WIDENING TO FOUR LANE WITH PAVED SHOULDER FROM DESIGN KM.49.200 TO KM.89.285 OF NH-731B ON EPC MODE (MoRTH) (N24002029)	3-2022	1/2026 (N.A.) {1/2026}	917.91 (956.30) {917.91}	606.74	44.00
		1513	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM EXISTING KM.0.000 TO KM.55.610 (DESIGN KM. 0.000 T (MoRTH) (N24002031)	12-2021	2/2026 (N.A.) {2/2026}	840.93 (773.58) {840.93}	499.20	40.00
		1514	CONSTRUCTION OF 4-LANE HIGHWAY WITH PAVED SHOULDERS FROM KM 49.155 TO KM 74.700 OF NH-731A ON HYBRID (MoRTH) (N24002032)	1-2022	1/2026 (N.A.) {1/2026}	1,156.72 (N.A.) {1,156.72}	407.20	62.00
		1515	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM GOGWAN JALALPUR (SHAMLI DISTRICT) TO RANIPUR (NHAI) (N24002036)	4-2022	5/2025 (N.A.) {5/2025}	1,843.59 (N.A.) {1,843.59}	843.83	49.00
		1516	GARMUKTESHWAR (KM. 83.200 OF NH-24) TO MEERUT (KM. 9.860 OF NH-235) INCLUDING CONNECTOR TO NH-119 (NHAI) (N24002073)	10-2019	10/2023 (N.A.) {6/2025}	2,068.99 (2,171.00) {2,171.00}	209.60	53.08
		1517	CONSTRUCTION OF FOUR LANE HIGHWAY FORM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002086)	10-2022	7/2025 (N.A.) {7/2025}	1,706.47 (N.A.) {1,706.47}	719.13	75.00
		1518	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002087)	10-2022	10/2025 (N.A.) {10/2025}	1,493.14 (N.A.) {1,493.14}	93.30	65.00
		1519	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002088)	10-2022	8/2025 (N.A.) {8/2025}	1,493.50 (N.A.) {1,493.50}	492.86	55.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1520	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER GREENFIELD SECTION OF N (NHAI) (N24002089)	10-2022	6/2025 (N.A.) {6/2025}	617.87 (N.A.) {617.88}	106.20	71.00
		1521	CONSTRUCTION OF FOUR-LANE ?WESTERN SIDE SPUR OF RAMPUR- RUDRAPUR SECTION CONNECTING NH-24 TO NH-87 BY (NHAI) (N24002090)	3-2021	11/2024 (Aug-2025) {8/2025}	646.27 (N.A.) {646.27}	91.95	45.61
		1522	IMPROVEMENT , UP-GRADATION OF NH-734 SECTION OF MORADABAD - THAKURDWARA - KASHIPUR: ?PACKAGE-I: MORA (NHAI) (N24002093)	10-2022	9/2025 (N.A.) {9/2025}	1,841.92 (N.A.) {1,841.92}	418.99	51.50
		1523	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 123.650 TO 175.080, FROM START OF SHA (NHAI) (N24002094)	9-2022	11/2025 (N.A.) {11/2025}	1,212.26 (N.A.) {1,212.26}	329.68	30.27
		1524	FOUR LANING OF SONAULI GORAKHPUR SECTION OF NH 29E (NEW NH 24) FROM DESIGN CH. 0.000 TO DESIGN CH. 7 (NHAI) (N24002095)	12-2021	3/2025 (N.A.) {3/2025}	2,555.50 (N.A.) {2,555.50}	966.89	60.50
		1525	CONSTRUCTION OF 4 LANE GREEN FIELD NORTHERN EAST SIDE GORAKHPUR BYPASS (26.616 KMS) STARTING FROM NH (NHAI) (N24002096)	2-2023	1/2026 (N.A.) {1/2026}	1,973.98 (N.A.) {1,973.98}	736.14	47.00
		1526	STRENGTHENING OF EXISTING 4L AYODHYA BYPASS SECTION FROM DESIGN KM.121.600 TO KM. 144.020 OF NH 28 () (NHAI) (N24002097)	2-2023	9/2025 (N.A.) {8/2025}	526.45 (N.A.) {526.45}	228.37	83.00
		1527	CONSTRUCTION OF RING ROAD AROUND KANPUR FROM KM.000 TO KM. 23.325 (CHACHENDI SACHENDI I TO MAHARAJPU (NHAI) (N24002104)	1-2023	6/2026 (N.A.) {6/2026}	1,754.00 (N.A.) {1,754.00}	343.02	34.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1528	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS (PHASE-I) FROM DESIGN KM 43+200 (AT MAHUWARI VI (NHAI) (N24002105)	8-2023	6/2026 (N.A.) {6/2026}	1,378.36 (N.A.) {739.00}	198.15	25.10
		1529	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS FROM DESIGN KM 50.860 (NABABA URF NIBI KALA UPA (NHAI) (N24002106)	8-2023	3/2025 (N.A.) {6/2025}	993.77 (N.A.) {349.48}	372.80	92.86
		1530	CONSTRUCTION OF MARIAHU BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION (KM.53.540 TO KM.59.200) (MoRTH) (N24002115)	3-2023	8/2025 (N.A.) {2/2026}	438.24 (362.39) {438.24}	211.72	36.00
		1531	REHABILITATION AND UPGRADATION FROM KM 51.600 TO KM 75.700 OF NH-321G (NUHKHAS TO ETAH SECTION) TO T (MoRTH) (N24002116)	1-2022	8/2025 (N.A.) {8/2025}	343.54 (N.A.) {343.54}	75.83	34.00
		1532	CONSTRUCTION OF JASRA BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION FROM KM. 379.670 ON NH- 76 ((MoRTH) (N24002120)	2-2023	9/2025 (N.A.) {9/2025}	274.06 (N.A.) {274.06}	129.09	84.00
		1533	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM. 420.00 (MoRTH) (N24002121)	1-2022	9/2025 (N.A.) {2/2026}	509.65 (N.A.) {509.65}	188.67	21.00
		1534	REHABILITATION AND UP-GRADATION FROM KM. 0.000 TO KM. 40.390 OF NH-730S (MAHARAJGANJ ? NICHLOUL ? TH (MoRTH) (N24002134)	3-2023	12/2025 (N.A.) {12/2025}	809.25 (N.A.) {809.25}	262.06	33.00
		1535	CONSTRUCTION OF FOUR LANE HIGHWAY WITH PAVED SHOULDER FROM KM.74.700 TO KM.112.950 OF NH-731A (I/C Y (MoRTH) (N24002138)	3-2022	6/2026 (N.A.) {6/2026}	1,141.67 (N.A.) {1,141.67}	423.37	47.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1536	CONSTRUCTION OF BALRAMPUR BYPASS WITH 2L FLEXIBLE PAVEMENT CONFIGURATION FROM KM.223.000 OF NH- 330 T (MoRTH) (N24002150)	12-2022	2/2026 (N.A.) {2/2026}	515.69 (N.A.) {515.69}	172.49	28.00
		1537	WIDENING TO 4L RIGID PAVEMENT CONFIGURATION FROM KM 90.00 TO KM 100.800 OF NH-96 (KM 42.0 TO KM 53.3 (MoRTH) (N24002199)	12-2022	11/2026 (N.A.) {11/2026}	309.63 (N.A.) {309.63}	11.05	15.00
		1538	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER/FOUR LANE CONFIGURATION FROM EXISTING K (MoRTH) (N24002201)	1-2022	5/2027 (N.A.) {5/2027}	974.19 (N.A.) {974.19}	586.68	10.00
		1539	REHABILITATION AND UPGRADATION TO FOUR LANE ROAD FROM KM 70.500 TO KM 78.600 OF NH-92 UNDER EPC MODE (MoRTH) (N24002211)	1-2022	1/2027 (N.A.) {1/2027}	296.02 (N.A.) {296.02}	27.94	N.A.
		1540	WIDENING AND STRENGTHENING FROM DESIGN KM. 67.280 TO KM. 88.622 OF NH- 727A (SALEMPUR-MAIRWA ROAD) TO (MoRTH) (N24002212)	3-2023	7/2026 (N.A.) {7/2026}	371.89 (N.A.) {371.89}	134.82	32.00
		1541	REHABILITATION and UP-GRADATION TO 2L+PS FROM KM. 0.0 TO KM. 7.80 AND KM. 35.400 TO KM. 52.345 (DESI (MoRTH) (N24002213)	3-2023	7/2026 (N.A.) {7/2026}	701.02 (N.A.) {701.02}	243.54	10.00
		1542	CONSTRUCTION OF AMETHI BYPASS (PART- II) AT KM.30.050 OF NH-931 UNDER EPC MODE IN THE STATE OF UTTAR (MoRTH) (N24002214)	12-2022	2/2027 (N.A.) {2/2027}	283.86 (N.A.) {283.86}	58.92	N.A.
		1543	WIDENING TO 4L FROM KM.108.50 TO 139.00 OF NH-135A PKG-II (JAUNPUR TO AKBARPUR SECTION) ON HAM IN TH (MoRTH) (N24002234)	3-2023	3/2027 (N.A.) {3/2027}	1,511.57 (N.A.) {1,511.57}	144.50	4.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1544	CONSTRUCTION OF RAEBARELI RING ROAD (PHASE-2) WITH FOUR LANE CONFIGURATION FOR RAEBARELI CITY IN THE (MoRTH) (N24002235)	3-2022	5/2027 (N.A.) {5/2027}	1,273.72 (N.A.) {1,273.72}	330.12	N.A.
		1545	IMPROVEMENT AND UP-GRADATION OF NH-227B (84 KOSI PARIKRAMA MARG) PACKAGE ?I, FROM KM 228.920 (JAGARN (MoRTH) (N24002240)	3-2022	11/2026 (N.A.) {11/2026}	912.50 (N.A.) {912.50}	388.50	N.A.
		1546	IMPROVEMENT AND UP-GRADATION OF NH-227B (84 KOSI PARIKRAMA MARG) PACKAGE ?III, FROM KM.47.800 (GOSAI (MoRTH) (N24002241)	3-2022	11/2026 (N.A.) {11/2026}	587.97 (N.A.) {587.97}	84.06	N.A.
	URBAN DEVELOPMENT	1547	KANPUR METRO RAIL PROJECT (LMRCL) (N28000144)	5-2019	3/2024 (N.A.) {3/2027}	11,076.48 (N.A.) {11,076.48}	8,736.58	72.50
		1548	AGRA METRO RAIL PROJECT (LMRCL) (N28000145)	5-2019	3/2024 (N.A.) {6/2027}	8,379.62 (N.A.) {8,379.62}	4,987.53	54.00
	WATER RESOURCES	1549	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH (UPJalNigam) (N30000021)	1-2019	12/2021 (Jan-2020) {3/2025}	231.79 (234.03) {234.03}	141.79	100.00
		1550	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH (UPJalNigam) (N30000024)	2-2019	6/2022 (N.A.) {12/2025}	681.78 (N.A.) {690.71}	13.34	25.00
UTTARAKHAND	CIVIL AVIATION	1551	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN (AAI) (N04000085)	7-2018	9/2020 (Sep-2024) {9/2024}	456.86 (500.00) {500.00}	483.96	100.00
	POWER	1552	TEHRI PUMPED STORAGE PLANT(1000MW) (THDCIL) (N18000010)	7-2006	7/2010 (Jun-2022) {9/2025}	1,657.00 (4,825.60) {7,877.81}	8,007.27	98.20
		1553	TAPOVAN-VISHNUGAD HEP (4X130MW) (NTPC) (N18000014)	11-2006	3/2013 (Dec-2021) {4/2029}	2,978.48 (N.A.) {10,907.00}	6,736.09	72.40
		1554	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT (THDCIL) (N18000042)	8-2008	6/2013 (N.A.) {3/2027}	2,491.58 (3,860.35) {6,823.72}	4,819.19	70.50

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1555	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW (NTPC) (N18000142)	7-2012	8/2017 (N.A.) {8/2017}	1,527.00 (N.A.) {1,527.00}	149.93	N.A.
	RAILWAYS	1556	RISHIKESH - KARNAPRAYAG NEW LINE (RVNL) (N22000406)	4-2011	12/2025 (N.A.) {3/2025}	38,953.15 (N.A.) {24,659.00}	18,820.04	N.A.
	ROAD TRANSPORT AND HIGHWAYS	1557	4-LANING OF KASHIPUR-SITARGANJ SECTION (AMR) (N24000465)	11-2012	8/2016 (N.A.) {8/2016}	605.84 (N.A.) {605.84}	0.00	N.A.
		1558	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 (NHIDCL) (N24000741)	3-2018	11/2020 (Mar-2024) {3/2024}	274.31 (N.A.) {274.31}	253.61	97.31
		1559	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI (NHIDCL) (N24000742)	3-2018	11/2020 (N.A.) {3/2024}	403.36 (N.A.) {403.36}	340.32	98.93
		1560	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA (NHIDCL) (N24000743)	3-2018	11/2020 (N.A.) {3/2024}	417.24 (N.A.) {417.24}	344.20	99.88
		1561	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000772)	12-2017	12/2019 (N.A.) {12/2019}	257.34 (N.A.) {257.34}	232.69	100.00
		1562	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000773)	12-2017	12/2019 (N.A.) {12/2019}	200.34 (253.43) {200.34}	227.98	100.00
		1563	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM KM. 235.00 (MoRTH) (N24000774)	12-2017	12/2019 (N.A.) {12/2019}	248.22 (N.A.) {248.22}	236.80	100.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1564	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000775)	6-2017	6/2019 (Mar-2023) {3/2023}	282.08 (N.A.) {282.08}	234.97	100.00
		1565	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG (MoRTH) (N24000776)	11-2017	11/2019 (N.A.) {11/2019}	232.81 (N.A.) {232.81}	201.58	100.00
		1566	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION (MoRTH) (N24000777)	11-2017	11/2019 (N.A.) {11/2019}	283.51 (N.A.) {283.51}	278.51	100.00
		1567	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000778)	11-2017	11/2019 (N.A.) {11/2019}	266.52 (N.A.) {266.52}	250.34	100.00
		1568	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR (MoRTH) (N24000779)	2-2018	2/2020 (Mar-2023) {3/2023}	418.88 (N.A.) {418.88}	339.71	94.00
		1569	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K (MoRTH) (N24000780)	2-2018	(Apr-2023) {4/2023}	293.68 (N.A.) {293.68}	244.25	100.00
		1570	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN (MoRTH) (N24000781)	5-2018	5/2020 (Dec-2023) {12/2023}	248.00 (N.A.) {248.00}	120.50	66.00
		1571	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 (MoRTH) (N24000782)	3-2018	(N.A.) {}	460.73 (N.A.) {461.00}	0.00	N.A.

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1572	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) (NHIDCL) (N24000855)	3-2018	7/2022 (N.A.) {9/2026}	1,383.78 (N.A.) {1,383.78}	709.72	63.84
		1573	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER (MoRTH) (N24001130)	8-2016	12/2017 (N.A.) {12/2017}	234.88 (273.49) {234.88}	237.19	100.00
		1574	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR ? DEHRADUN SECTION FROM KM. (NHAI) (N24001525)	3-2021	3/2024 (May-2025) {5/2025}	169.08 (N.A.) {169.08}	105.77	99.99
		1575	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH- 58) TO KM. 15.100 (KM 5.100 OF (NHAI) (N24001526)	8-2021	10/2024 (Aug-2025) {8/2025}	1,377.79 (1,384.11) {1,377.79}	678.86	56.11
		1576	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) (NHAI) (N24001553)	3-2022	2/2025 (Nov-2025) {11/2025}	1,092.90 (1,092.90) {1,092.90}	463.92	81.20
		1577	4L POANTA SAHEB?MEDNIPUR FROM KM. 435.65 TO KM. 458.65 OF NH-07(PKG-1) (NHAI) (N24001990)	6-2022	5/2025 (Oct-2025) {10/2025}	524.54 (683.26) {683.26}	91.94	74.78
		1578	ACCESS ROAD/BRIDGE CONNECTIVITY FROM NH-09 AT KM.40 NEAR JAGBUDA BRIDGE (INDIA) TO BOUNDARY PILLAR (NHAI) (N24001991)	5-2022	9/2024 (Nov-2026) {11/2026}	314.31 (N.A.) {314.31}	178.37	68.23
		1579	CONSTRUCTION FOR MITIGATION MEASURES KM 368.00-UTTARAKHAND-TO KM 433.00 ON NH-07-PKG-1 (NHIDCL) (N24002163)	12-2023	12/2025 (N.A.) {12/2025}	216.88 (N.A.) {216.88}	80.79	75.80
		1580	CONSTRUCTION FOR MITIGATION MEASURES KM 450.00-UTTARAKHAND-TO KM 468.00 ON NH-07-PKG-3 (NHIDCL) (N24002164)	12-2023	12/2025 (N.A.) {12/2025}	250.33 (N.A.) {250.33}	57.10	48.50

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1581	CONSTRUCTION FOR MITIGATION MEASURES PKG-2 (NHIDCL) (N24002206)	12-2023	6/2026 (N.A.) {6/2026}	259.64 (N.A.) {259.64}	4.16	20.23
WEST BENGAL	CIVIL AVIATION	1582	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA (AAI) (N04000080)	1-2016	3/2020 (Dec-2023) {12/2023}	458.00 (N.A.) {458.00}	251.64	100.00
		1583	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA (AAI) (N04000081)	1-2019	11/2021 (May-2023) {5/2023}	389.71 (397.00) {397.00}	396.61	100.00
		1584	NSCBI AIRPORT KOLKATA: RE- CONSTRUCTION OF RIGID POSITIONS OF SECONDARY RUNWAY, 'K' AND 'A' TAXIWAY (AAI) (N04000109)	4-2023	10/2025 (N.A.) {10/2025}	328.30 (N.A.) {328.30}	79.39	36.00
		1585	BAGDOGRA AIRPORT: DEVELOPMENT OF NEW CIVIL ENCLAVE AT BAGDOGRA AIRPORT. SUB-HEAD : CONSTRUCTION OF N (AAI) (N04000115)	8-2024	3/2027 (N.A.) {3/2027}	1,549.00 (N.A.) {1,549.00}	215.07	8.38
	COAL	1586	RANIGANJ MASTER PLAN (ECL) (N06000163)	8-2009	8/2019 (N.A.) {8/2024}	2,661.73 (N.A.) {5,146.48}	784.10	42.00
		1587	SIDULI MINE (OC AND UG) (ECL) (N06000165)	5-2018	3/2027 (N.A.) {3/2027}	535.18 (N.A.) {535.17}	4.75	14.00
		1588	NAKRAKONDA KUMARDIH B OCP (ECL) (N06000170)	8-2018	3/2029 (N.A.) {3/2029}	502.68 (N.A.) {502.67}	71.07	25.50
		1589	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT (ECL) (N06000191)	4-2020	3/2026 (Mar-2026) {3/2026}	483.65 (N.A.) {483.65}	55.23	12.00
		1590	2.0 MTPA BHOJUDIH NLW WASHERY (BCCL) (N06000195)	12-2015	9/2020 (N.A.) {7/2025}	384.57 (N.A.) {384.57}	348.66	97.00
		1591	SONEPUR BAZARI EXPANSION OC (ECL) (N06000220)	7-2021	3/2029 (N.A.) {3/2029}	5,365.88 (5,366.00) {5,365.88}	553.51	17.30
		1592	EXPANSION PR OF JHANJRA UG (5.00 MTY) (ECL) (N06000223)	4-2020	3/2029 (N.A.) {3/2029}	1,210.12 (N.A.) {1,210.12}	489.45	40.00
		1593	MOHANPUR EXPANSION OC PHASE II (ECL) (N06000236)	11-2020	3/2026 (N.A.) {3/2026}	888.99 (N.A.) {888.99}	77.94	30.25

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1594	BONJEME HARI EXPANSION OCP (ECL) (N06000244)	8-2021	3/2026 (Mar-2026) {3/2026}	570.12 (N.A.) {570.11}	81.58	16.00
		1595	ITAPARA OC (ECL) (N06000272)	12-2023	3/2030 (N.A.) {3/2030}	929.10 (N.A.) {929.10}	64.61	6.80
		1596	UCE OF TILABONI UG (ECL) (N06000276)	1-2023	3/2029 (N.A.) {3/2029}	749.07 (N.A.) {749.07}	52.09	10.30
		1597	UCE OF PARASEA BELBAID REORGANISATION UG (ECL) (N06000277)	1-2023	3/2029 (Mar-2028) {3/2028}	389.10 (N.A.) {389.10}	130.56	16.40
		1598	PARASCOLE JAMBAD OCP (ECL) (N06000281)	11-2024	3/2037 (N.A.) {3/2037}	1,193.55 (N.A.) {1,193.55}	5.91	N.A.
	DEPARTMENT OF HIGHER EDUCATION	1599	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED (CPWD EDUCATION) (N28000146)	3-2020	6/2020 (N.A.) {3/2024}	193.83 (N.A.) {193.83}	187.65	99.00
	MINES	1600	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA (CPWD) (N10000015)	4-2019	4/2022 (N.A.) {8/2026}	255.37 (N.A.) {255.37}	68.66	38.00
	PETROLEUM	1601	DURGAPUR-HALDIA PIPELINE PROJECT (GAIL) (N16000275)	3-2017	12/2020 (Dec-2025) {12/2025}	1,740.00 (2,433.15) {2,433.15}	2,185.10	89.80
		1602	CITY GAS DISTRIBUTION IN WEST BENGAL (HPCL) (N16000392)	3-2019	3/2031 (Mar-2031) {3/2031}	5,830.20 (N.A.) {5,830.20}	875.27	33.00
		1603	HALDIA PANAGARH PIPELINE PROJECT (HPCL) (N16000478)	11-2022	11/2025 (N.A.) {11/2025}	1,010.00 (N.A.) {1,010.00}	546.60	79.09
		1604	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS (IOCL) (N16000491)	3-2022	3/2030 (N.A.) {6/2031}	609.00 (N.A.) {609.00}	55.29	2.10
		1605	CGD PROJECT IN WEST BENGAL 11TH ROUND (HPCL) (N16000498)	6-2022	6/2030 (N.A.) {6/2030}	2,628.00 (N.A.) {2,628.00}	311.01	22.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1606	CITY GAS DISTRIBUTION PROJECTS AT ALIPURDUAR AND COOCH BEHAR (BPCL) (N16000522)	12-2022	3/2030 (N.A.) {3/2030}	1,017.00 (N.A.) {1,017.00}	160.80	30.60
	POWER	1607	RAMMAM-III HEPP (3X40 MW) (NTPC) (N18000178)	9-2014	9/2019 (Dec-2024) {3/2029}	1,381.84 (N.A.) {1,803.00}	1,302.76	43.68
	RAILWAYS	1608	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER (ER) (220100272)	4-2000	3/2019 (Feb-2026) {2/2026}	1,188.91 (N.A.) {2,582.49}	1,264.53	75.00
		1609	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) (KOMRCL) (N22000108)	4-2010	8/2026 (N.A.) {3/2016}	4,829.60 (N.A.) {2,397.72}	197.20	17.00
		1610	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) (RVNL) (N22000109)	4-2010	12/2026 (N.A.) {12/2025}	2,298.42 (N.A.) {2,733.86}	392.98	N.A.
		1611	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) (RVNL) (N22000110)	4-2010	12/2025 (N.A.) {3/2026}	8,964.35 (N.A.) {8,964.35}	7,387.40	N.A.
		1612	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. (RVNL) (N22000111)	4-2010	12/2026 (N.A.) {12/2026}	4,834.54 (N.A.) {4,834.54}	3,918.86	N.A.
		1613	PURULIA TO KOTSHILA DOUBLING (39.1 KM) (SER) (N22000510)	4-2018	12/2024 (N.A.) {3/2025}	393.83 (N.A.) {393.83}	318.36	100.00
		1614	NAHATI - RANAGHAT 3RD LINE (MM OF KALINARAYANPUR - KRISHNANAGAR) (ER) (N22000624)	7-2015	3/2025 (N.A.) {3/2025}	1,000.00 (N.A.) {283.54}	167.13	44.00
		1615	EAST WEST METRO CORRIDOR KOLKATA (KOMRCL) (N22000628)	2-2009	9/2016 (N.A.) {9/2016}	4,874.58 (8,575.00) {10,442.41}	0.00	N.A.
		1616	KALIPAHARI - BAKHTARNAGAR 5TH LINE (17.61 KM) (ER) (N22000630)	4-2024	6/2027 (N.A.) {6/2027}	350.46 (N.A.) {350.46}	0.00	N.A.

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1617	SITARAMPUR BYE - PASS LINE (6.59 KM) (ER) (N22000631)	2-2023	3/2027 (N.A.) {3/2027}	461.64 (N.A.) {461.64}	25.84	N.A.
	ROAD TRANSPORT AND HIGHWAYS	1618	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) (NHAI) (N24000463)	12-2015	6/2018 (May-2024) {8/2023}	1,083.00 (1,414.01) {1,414.01}	1,080.05	100.00
		1619	SIX-LANING OF BARWA ADDA-PANAGARH (NHAI) (N24000515)	4-2014	9/2016 (N.A.) {3/2025}	1,665.00 (N.A.) {4,977.49}	4,977.49	100.00
		1620	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU (NHAI) (N24000788)	3-2018	9/2022 (Dec-2022) {12/2025}	841.57 (708.30) {708.30}	11,802.22	96.13
		1621	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H (MoRTH) (N24000874)	3-2016	11/2018 (Dec-2023) {7/2025}	271.17 (291.20) {291.20}	199.72	82.47
		1622	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. (MoRTH) (N24000880)	2-2018	9/2020 (Jan-2024) {2/2025}	426.18 (426.18) {426.18}	364.92	100.00
		1623	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 (NHAI) (N24001747)	3-2020	9/2024 (N.A.) {9/2024}	2,193.23 (2,314.00) {2,314.00}	2,085.00	96.40
		1624	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA (NHAI) (N24001748)	3-2021	9/2024 (N.A.) {9/2025}	2,200.93 (N.A.) {2,621.43}	2,621.43	97.31
		1625	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE (NHAI) (N24001749)	8-2021	8/2023 (N.A.) {6/2025}	557.55 (N.A.) {567.31}	473.25	91.41

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1626	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA (NHAI) (N24001750)	8-2018	12/2021 (N.A.) {7/2025}	622.04 (N.A.) {622.04}	573.67	91.44
		1627	DEVELOPMENT TO 4/6-LANNING OF NH-31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 (MoRTH) (N24001850)	3-2022	9/2025 (Sep-2025) {9/2025}	995.04 (995.04) {995.04}	383.85	49.91
		1628	CONSTRUCTION OR 4 LANE RANIGANJ BYPASS OF LENGTH 5 261 KM ON NH 60 NEW NH 14 FROM KM 273 00 OF NH (MoRTH) (N24002184)	3-2023	3/2026 (Mar-2026) {3/2026}	410.83 (N.A.) {410.83}	152.32	34.89
		1629	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF LEVEL CROSSING NO 10 B T AT KM 307 050 OF NH 60 B (MoRTH) (N24002191)	3-2016	8/2025 (N.A.) {8/2025}	155.87 (N.A.) {155.87}	21.68	10.10
	STEEL	1630	REBUILDING OF COKE OVEN BATTERY NO.4 OF DURGAPUR STEEL PLANT (SAIL) (N12000132)	11-2023	12/2026 (N.A.) {12/2026}	916.78 (N.A.) {916.78}	98.69	9.91
		1631	INSTALLATION OF NEW BAR MILL AT DURGAPUR STEEL PLANT (SAIL) (N12000138)	9-2024	6/2027 (N.A.) {6/2027}	2,115.44 (N.A.) {2,115.44}	77.68	10.16
		1632	UP-GRADATION OF BLAST FURNACE NO. 3 AT DURGAPUR STEEL PLANT (SAIL) (N12000139)	9-2024	6/2026 (N.A.) {6/2026}	758.09 (N.A.) {758.09}	35.34	202.00
		1633	REVAMPING OF AIR POLLUTION CONTROL SYSTEMS OF SP-1 AT DURGAPUR STEEL PLANT (SAIL) (N12000140)	11-2024	5/2026 (N.A.) {5/2026}	196.40 (N.A.) {196.40}	0.19	0.90
		1634	THIRD LADLE FURNACE IN SECONDARY REFINERY UNIT AT IISCO STEEL PLANT (SAIL) (N12000141)	11-2024	7/2026 (N.A.) {7/2026}	227.96 (N.A.) {227.96}	2.58	28.26
	WATER RESOURCES	1635	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA (KMDA) (N30000032)	5-2018	2/2022 (N.A.) {8/2025}	198.43 (224.69) {286.97}	77.78	96.00

Table:-7. Project List: Ongoing Projects as of 31st May 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1636	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA (KMDA) (N30000034)	8-2017	9/2022 (Jan-2023) {12/2026}	307.12 (N.A.) {653.67}	0.00	N.A.
		1637	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH (KMDA) (N30000042)	5-2018	2/2022 (Sep-2020) {3/2025}	160.00 (154.73) {154.73}	91.87	92.00
			Total			2,719,583.76 (863,813.71) {3,012,166.88}	16,23,159.43	

Abbreviations used in the Report

AGENCY_NAME	AGENCY_NAME_SHORT
AIRPORT AUTHORITY OF INDIA LIMITED	AAI
ARTIFICIAL LIMBS MANUFACTURING CORPM. OF INDIA	ALIMCO
BHARAT ALUMINUM CORPORATION	BALCO
BHABHA ATOMIC RESEARCH CENTRE	BARC
BHARAT COKING COAL LIMITED	BCCL
BRAHMAPUTRA CRECKER & POLYMER LTD.	BCPL
BHAVINI LIMITED	BHAVNI
BHARAT HEAVY ELECTRICALS LIMITED	BHEL
BANGALORE METRO RAIL CORPORATION LIMITED	BMRCL
BOKARO STEEL PLANT	BOKARO STEEL PL
BRAHMAPUTRA BOARD	BPB
BHARAT PETROLEUM CORPORATION LIMITED	BPCL
BORDER ROAD ORGANISATION	BRO
BONGAIGAON REFINERY PETROLEUM LIMITED	BRPL
BHARAT SANCHAR NIGAM LIMITED	BSNL
Bihar Urban Infrastructure Development Corporation Ltd	BUIDCO
BRAHMAPUTRA VALLY FERTILISER CORPORATION	BVFC
CENTRE FOR DEVELOPMENT OF TELEMATICS, TELECOM, TECHNOLOGY	C-DOT
CENTRAL COAL FIELDS LIMITED	CCL
CONTAINER CORPORATION OF INDIA	CCOI
CHENAB VALLEY POWER CORPORATION LIMITED	CHENAB VALLEY P
CHENNAI METRO RAIL LTD	CMRL
CHENNAI PETROLEUM CORPORATION LIMITED	CPCL
CENTRAL PUBLIC WORKS DEPARTMENT	CPWD
CPWD OF HIGHER EDUCATION	CPWD EDUCATION
CPWD FOR DEFENCE	CPWD FOR DEFENC
CPWD FOR FINANCE	CPWD FOR FINANC
CPWD FOR HEALTH	CPWD FOR HEALTH
CPWD FOR MHA	CPWD FOR MHA
CPWD FOR POWER	CPWD FOR POWER
CPWD FOR RURAL	CPWD FOR RURAL
CPWD FOR TELECOM	CPWD FOR TELECO
CPWD FOR RENEWABLE ENERGY	CPWD R ENERGY
CENTRAL RAILWAYS	CR
COCHIN REFINERY LIMITED	CRL
COCHIN SHIPYARD LTD	CSL
CHENAB VELLEY POWER PROJECTS [P] LIMITED	CVPPPL
DUMMY AGENCY	DA
DEDICATED FREIGHT CORRIDOR CORPORATION OF INDIA LTD	DFCC
DIRECTORATE GENERAL OF CIVIL AVIATION	DGCA
Delhi Jal Board	DJB
Delhi Mumbai Industrial Corridor	DMIC
DMIC FOR DPIIT	DMIC FOR DPIIT
DELHI METRO RAIL CORPORATION	DMRC
DEPARTMENT OF TELECOMMUNICATION	DOT
Department for Promotion of Industry and Internal Trade	DPIIT
DAMODAR VALLEY CORPORATION	DVC
EASTERN COAL FIELDS LIMITED	ECL
EAST COAST RAILWAY	ECOR
EAST CENTRAL RAILWAYS	ECR

AGENCY_NAME	AGENCY_NAME_SHORT
EDCIL(India) Limited	EDCIL
ENNORE PORT LTD.	ENNORE PORT LTD
ENNORE TANK TERMINAL PVT.LTD.	ENNORE TANK
EASTERN RAILWAYS	ER
FERTILISER AND CHEMICAL TRIVANCORE	FACT
FREIGHT OPERATION INFORMATION SYSTEM	FOIS
SETTING UP FILM AND TELEVISION INSTITUTE	FTI
GAS AUTHORITY OF INDIA LIMITED	GAIL
GOA SHIPYARD LIMITED	GSL
HEALTH & FAMILY WELFARE	H&FW
HINDUSTAN AERONAUTICS LTD	HAL
HINDUSTAN COPPER LIMITED	HCL
HALDIA FERTILISER CORPORATION	HFC
HLL Infra Tech Services Limited	HITES
HYDERABAD METRO RAIL LTD	HMRL
HINDUSTAN PETROLEUM CORPORATION LIMITED	HPCL
HPCL Rajasthan Refinery Limited(JV)	HPCLRRL(JV)
HPOIL Gas Pvt. Ltd	HPOIL(JV)
HOSPITAL SERVICES CONSULTANCY CORPORATION LTD	HSCC
HINDUSTAN STEELWORK CONSTRUCTION LIMITED	HSCL
HINDUSTHAN STEELWORKS CONSTRUCTION LIMITED	HSCL
HSCL FOR DONER	HSCL FOR DONER
HSCL FOR RURAL	HSCL FOR RURAL
HSCL FOR WATER	HSCL FOR WATER
INDIAN FARMERS FERTILISER CORPORATION	IFFCO
INDIRA GANDHI CENTRE FOR ATOMIC RESEARCH	IGCAR
INDRADHANUSH GAS GRID LTD	IGGL
India International Convention and Expo Centre	IICC
IICC FOR DPIIT	IICC FOR DPIIT
INDIAN IRON STEEL COMPANY	IISCO
Indian Institute of Technology, Kharagpur	IITKGP
INDIAN OIL CORPORATION LIMITED	IOCL
INDIAN PETRO-CHEMICAL CORPORATION LIMITED	IPCL
Indian Railway Construction Company Limited	IRCON
INDIAN STRATEGIC PETROLEUM RESERVES LTD	ISPRL
INDIAN TELEPHONE INDUSTRY	ITI
Inland Waterways Authority of India	IWAI
INLAND WATER TRANSPORT	IWT
JAWAHAR LAL NEHRU NATIONAL URBAN RENEWAL MISSION	JNNURM
JWAAHARLAL NEHRU PORT TRUST	JNPT
Jharkhand Urban Infrastructure Development Company Ltd	JUIDCO
Kolkata Metropolitan Development Authority	KMDA
KOCHI METRO RAIL CORPORATION LTD	KMRCL
KOLKATA METRO RAIL CORPORATION LIMITED	KOMRCL
KAMARAJAR PORT LIMITED	KPL
KONKAN RAILWAY	KR
Rail Infrastructure Development Company	KRIDE
KOCHI REFINERIES LIMITED	KRL
Kochi Salem Pipeline Private Limited(JV)	KSPPL(JV)
LINE DOUBLING	LD
LUCKNOW METRO RAIL CORPORATION LIMITED	LMRCL
MANGALORE REFINERY AND PETROCHEMICALS LIMITED	MANGALORE REFIN

AGENCY_NAME	AGENCY_NAME_SHORT
MAHANADI COAL FIELDS LIMITED	MCL
MECON LIMITED	MECON LIMITED
AHMEDABAD METRO RAIL	MEGA
MADRAS FERTILISER LIMITED	MFL
Munitions India Limited	MIL
MAHARASTRA METRO RAIL CORPORATION LTD.	MMRC
MUMBAI METRO RAIL CORPORATION LTD	MMRCL
MINISTRY OF WATER RESOURCES	MOWR
Madhya Pradesh Metro Rail Co Limited	MPMRCL
Maharashtra Rail Infrastructure Development Corporation Limited	MRIDC
MANGALORE REFINARY LIMITED	MRL
METROPOLITAN RAPID TRANSPORT PROJECTS	MRTP
Mumbai Railway Vikas Corporation	MRVC
MAHANAGAR TELEPHONE NIGAM LIMITED	MTNL
MUMBAI PORT TRUST	MUMBAI PORT TRU
Armoured Vehicles Nigam Limited	MVNL
MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)	MoRTH
NATIONAL ALUMINUM COMPANY LIMITED (NALCO)	NALCO
NATRIIP IMPLEMENTATION SOCIETY	NATIS
NATIONAL BUILDING CONSTRUCTION CORPORATION LTD	NBCC
NBCC FOR COMMERCE	NBCC FOR COMMER
NBCC FOR HEALTH	NBCC FOR HEALTH
NORTHERN COAL FIELDS LIMITED	NCL
NORTH CENTRAL RAILWAY	NCR
NATIONAL CAPITAL REGION TRANSPORT CORP	NCRTC
NATIONAL CENTRE OF EXCELLENCE	NCoE
NORTH EAST ELECTRIC POWER CORPORATION	NEEPCO
NORTH EAST GAS GRID	NEGG
NORTH EASTERN RAILWAY	NER
National Film Archive of India	NFAI
NUCLEAR FUEL CORPORATION	NFC
NATIONAL FERTILISER LIMITED	NFL
NORTH EAST FRONTIER RAILWAY	NFR
NATIONAL HIGHWAYS AUTHORITY OF INDIA	NHAI
NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.	NHIDCL
NATIONAL HYDRO-ELECTRIC POWER CORPORATION	NHPC
National High Speed Rail Corporation Limited	NHSRCL
NEW LINE	NL
NEYVELI LIGNITE CORPORATION	NLC
NATIONAL MISSION FOR CLEAN GANGA	NMCG
NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)	NMDC
NAGPUR METRO RAIL CORPORATION LTD	NMRCL
NATIONAL PROJECTS CONSTRUCTION CORPORATION LIMITED	NPCC
NUCLEAR POWER CORPORATION OF INDIA LIMITED	NPCIL
NORTHERN RAILWAY	NR
NUMALIGARH REFINERY LIMITED	NRL
SETTING UP OF NEW RAILWAY ZONES	NRZ
NATIONAL THERMAL POWER CORPORATION	NTPC
NORTH WESTERN RAILWAY	NWR
OIL INDIA LIMITED	OIL
OIL & NATURAL GAS CORPORATION LIMITED	ONGC
PATNA METRO RAIL CORPORATION	PATNA METRO RAI

AGENCY_NAME	AGENCY_NAME_SHORT
PAWAN HANS HELICOPTERTERS LTD.	PAWAN HANS HELI
POWER GRID CORPORATION OF INDIA LIMITED	PGCIL
PORT TRUST	PORT TRUST
Polavaram Project Authority	PPA
RASHTRIYA CHEMICAL & FERTILISER LIMITED	RCF
RAILWAY ELECTRIFICATION	RE
RASTRIYA ISPAT NIGAM LIMITED	RINL
RAIL INDIA TECHNICAL AND ECONOMIC SERVICE	MITES
MITES OF HIGHER EDUCATION	MITES OF HIGHER
RAIL VIKAS NIGAM LTD.	RVNL
SIGNALLING & TELECOMMUNICATIONS	S&T
STEEL AUTHORITY OF INDIA LIMITED (SAIL)	SAIL
SINGARENI COLLIERS COMPANY LIMITED	SCCL
SOUTH CENTRAL RAILWAY	SCR
SOUTH-EASTERN COAL FIELDS LIMITED	SECL
SOUTH EAST CENTRAL RAILWAY	SECR
SOUTH EASTERN RAILWAY	SER
SER(GC) GAUGE CONVERSION	SER(GC
SHIPPING CRP. OF INDIA	SHIPP.
SATLUJ JAL VIDYUT NIGAM LIMITED	SJVN
SOUTHERN RAILWAY	SR
SOUTH WESTERN RAILWAY	SWR
Sikkim University	Sikkim Universi
THDC INDIA LIMITED	THDCIL
TUTICORIN PORT TRUST	TUTICORIN
URANIUM CORPORATION OF INDIA LIMITED	UCIL
URBAN DEVELOPMENT	UD
Uttarakhand Pey Jal Nigam	UKJalNigam
Uttar Pradesh Jal Nigam	UPJalNigam
VISAKHAPATNAM PORT TRUST	VPT
Varanasi Smart City	Varanasi Smart
WAPCOS	WAPCOS
WESTERN COAL FIELDS LIMITED	WCL
WEST CENTRAL RAILWAY	WCR
WESTERN RAILWAY	WR
WORKSHOPS & PRODUCTION UNIT	WS&PU



Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
