



Government of India
Ministry of Statistics and Programme Implementation

QUARTERLY PROJECT



IMPLEMENTATION STATUS REPORT

**COSTING
RS. 150 CRORE & ABOVE**








**Quarter-4 FY 2024-25
(January-March)**

CONTENTS


Synopsis	1-2
List of Tables	3-275
Table:-1. Overview of Ongoing Projects: Sector-wise Distribution.....	3-4
Table:-2. Overview of Ongoing Projects: State-wise Distribution.....	5-7
Table:-3. Project List: Completed during 4 th Quarter (January-March), 2024-25	8-16
Table:-4. Project List: Added during 4 th Quarter (January-March), 2024-25	17-21
Table:-5. Project List: Frozen/Deleted during 4 th Quarter (January-March), 2024-25.....	22-22
Table:-6. Project List: Ongoing Projects of North-East Region.....	23-47
Table:-7. Project List: Ongoing Projects during 4 th Quarter (January-March), 2024-25.....	48-275

SYNOPSIS

Quarterly Report - Central Sector Infrastructure Projects Costing Rs. 150 crore & above

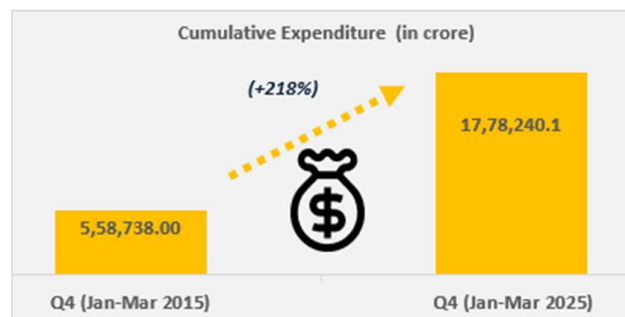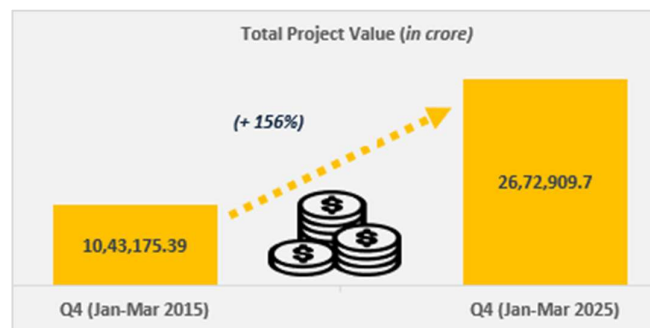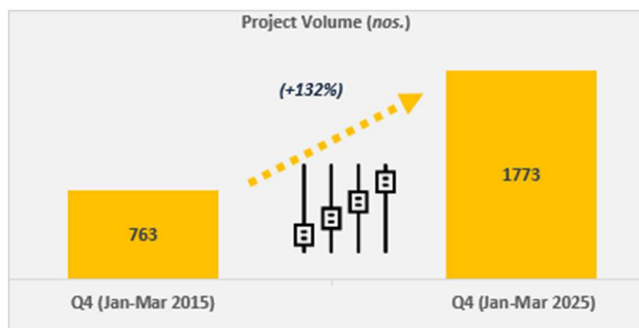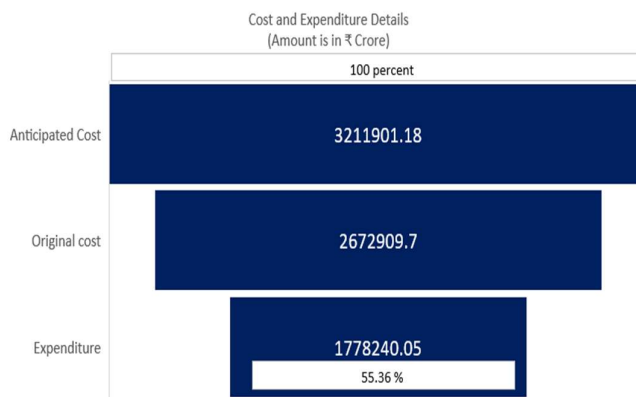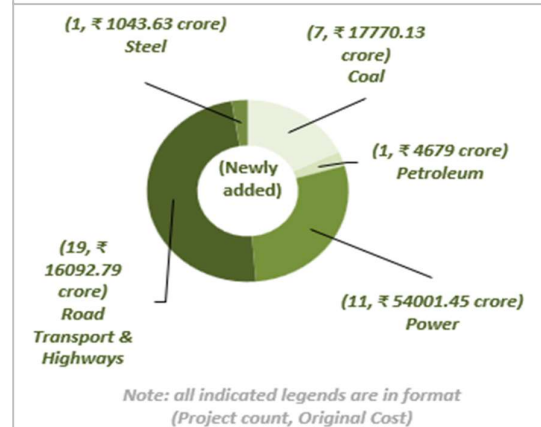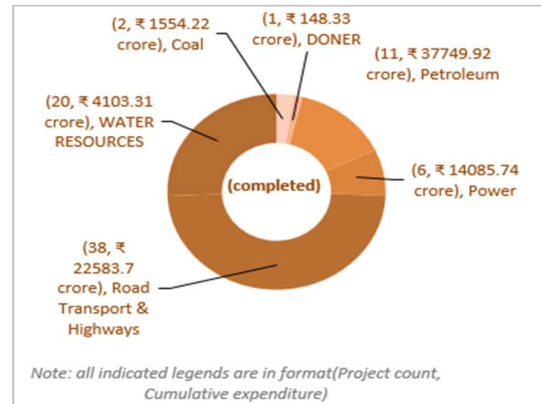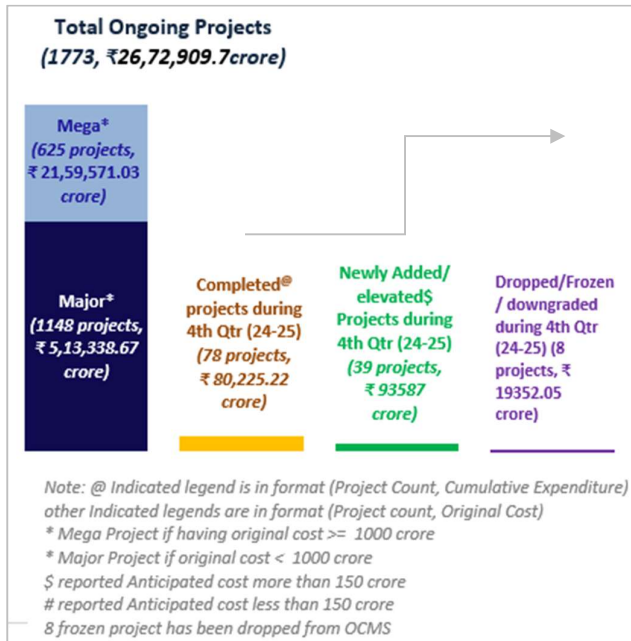


Sectoral Comparison : Major Sectors (as per count)
 [Outer Ring: Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

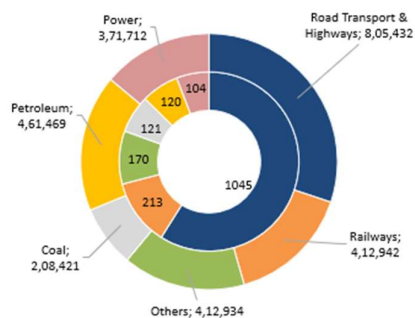


*Others include Water Resources, Civil Aviation, Urban Development, Department of Higher Education, Steel, Health & Family welfare, Mines, Telecommunications, Atomic energy, Home Affairs, Finance, DPIIT, DCINER, Renewable Energy, Shipping & Ports, and Social Justice

Sectoral Distribution of total 755 projects with reported Physical Progress between 80-100%

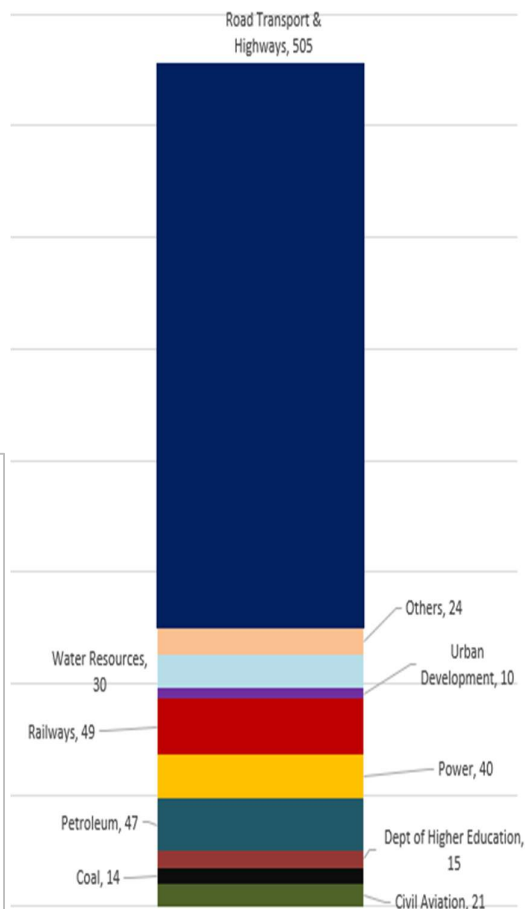

State Comparison : Major States (as per count)
 [Outer Ring: Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

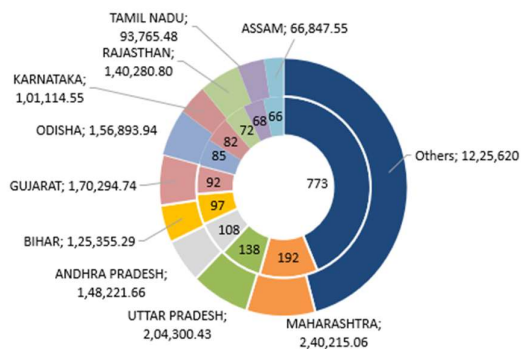

*Others include Madhya Pradesh, Jharkhand, Delhi, Chhattisgarh, Haryana, Jammu & Kashmir, West Bengal, Kerala, Arunachal Pradesh, Punjab, Telangana, Uttarakhand, Himachal Pradesh, Manipur, Sikkim, Nagaland, Mizoram, Meghalaya, Tripura, Goa, A&N Island, Ladakh and Multistate

LIST OF TABLES

**Table:-1. Overview of Ongoing Projects: Sector-wise Distribution during 4th Quarter
(January-March),2024-25**

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	CIVIL AVIATION	41	28,200.17 (29,343.52) {32,097.25}	18,637.74
2	COAL	121	208,420.76 (212,921.45) {218,842.29}	76,381.85
3	DEPARTMENT OF HIGHER EDUCATION	20	9,680.92 (10,072.78) {10,127.07}	7,619.19
4	DONER	1	151.33 (151.33) {151.33}	148.33
5	DPIIT	2	24,857.00 (31,457.00) {32,085.00}	16,191.57
6	FINANCE	2	577.27 (577.27) {569.04}	399.67
7	HEALTH AND FAMILY WELFARE	8	7,301.27 (7,358.40) {7,356.19}	5,008.24
8	HOME AFFAIRS	5	2,025.73 (2,949.25) {2,949.25}	2,466.60
9	MINES	8	7,559.78 (9,356.73) {9,845.57}	5,942.89
10	PETROLEUM	120	461,468.84 (520,312.57) {530,927.43}	2,77,185.67
11	POWER	104	371,711.68 (390,731.54) {455,417.51}	2,39,377.36
12	RAILWAYS	213	412,942.26 (532,871.94) {657,653.93}	4,43,485.55
13	ROAD TRANSPORT AND HIGHWAYS	1045	805,431.81 (838,005.47) {850,316.63}	4,32,686.76
14	SHIPPING AND PORTS	1	5,369.18 (5,061.15) {5,061.15}	3,397.03
15	SOCIAL JUSTICE	1	170.99 (170.99) {170.99}	73.80
16	STEEL	13	12,381.62 (16,313.15) {16,313.15}	7,335.71

**Table:-1. Overview of Ongoing Projects: Sector-wise Distribution during 4th Quarter
(January-March),2024-25**

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
17	TELECOMMUNICATIONS	6	26,961.69 (26,949.89) {26,949.89}	9,132.74
18	URBAN DEVELOPMENT	27	265,881.46 (272,720.33) {286,578.30}	2,01,259.87
19	WATER RESOURCES	35	21,815.94 (21,770.16) {68,489.21}	31,509.48
	Total	1773	2672909.7 (2929094.92) {3211901.18}	1778240.05

***Either Revised or Original Cost**

**Table:-2. Overview of Ongoing Projects: State-wise Distribution during 4th Quarter
(January-March),2024-25**

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	ANDAMAN AND NICOBAR ISLANDS	10	2,956.02 (3,029.18) {3,010.04}	1,801.96
2	ANDHRA PRADESH	108	148,221.66 (158,401.99) {211,663.70}	1,30,080.10
3	ARUNACHAL PRADESH	23	48,922.12 (48,985.65) {68,835.80}	32,613.79
4	ASSAM	66	66,847.55 (67,246.06) {76,566.33}	49,338.28
5	BIHAR	97	125,355.29 (143,047.81) {153,836.30}	1,00,154.55
6	CHHATTISGARH	54	82,550.77 (86,607.54) {89,442.73}	40,064.23
7	DELHI	25	92,085.93 (97,627.29) {96,636.97}	77,174.56
8	GOA	4	1,526.58 (1,526.58) {1,613.08}	781.97
9	GUJARAT	92	170,294.74 (177,161.83) {179,718.76}	87,701.22
10	HARYANA	30	70,631.20 (81,427.11) {82,176.81}	42,021.82
11	HIMACHAL PRADESH	31	31,474.58 (32,504.26) {49,326.03}	32,821.49
12	JAMMU AND KASHMIR	55	78,132.65 (113,703.22) {127,004.74}	78,614.38
13	JHARKHAND	63	109,062.32 (115,608.25) {117,040.71}	65,156.91
14	KARNATAKA	82	101,114.55 (103,540.88) {105,197.86}	49,630.97
15	KERALA	32	64,106.75 (69,889.93) {70,321.90}	35,167.38
16	LADAKH	6	2,474.97 (2,474.97) {2,634.64}	1,396.10

**Table:-2. Overview of Ongoing Projects: State-wise Distribution during 4th Quarter
(January-March),2024-25**

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
17	MADHYA PRADESH	64	108,150.99 (114,357.67) {124,349.77}	43,146.30
18	MAHARASHTRA	192	240,215.06 (244,750.37) {277,179.38}	1,50,047.54
19	MANIPUR	33	15,746.25 (23,602.31) {33,526.68}	19,646.09
20	MEGHALAYA	15	6,028.77 (6,019.79) {5,974.15}	3,775.18
21	MIZORAM	20	11,677.77 (14,305.75) {20,243.12}	16,992.15
22	MULTI STATE	53	284,355.68 (336,830.20) {355,484.57}	2,45,685.77
23	NAGALAND	32	11,633.24 (17,318.60) {17,017.57}	9,121.96
24	ODISHA	85	156,893.94 (160,042.71) {168,631.97}	70,472.11
25	PUNJAB	39	37,885.48 (38,367.95) {38,937.45}	15,182.71
26	RAJASTHAN	72	140,280.80 (168,460.75) {169,501.67}	94,712.04
27	SIKKIM	22	14,500.36 (25,520.47) {26,380.76}	18,222.60
28	TAMIL NADU	68	93,765.48 (103,331.82) {108,747.44}	29,851.98
29	TELANGANA	53	39,244.93 (39,582.28) {41,968.34}	26,050.00
30	TRIPURA	14	7,910.17 (7,947.06) {8,032.54}	1,205.32
31	UTTAR PRADESH	138	204,300.43 (211,191.06) {226,166.30}	1,16,254.86
32	UTTARAKHAND	33	36,921.91 (42,189.16) {64,285.39}	45,098.10

**Table:-2. Overview of Ongoing Projects: State-wise Distribution during 4th Quarter
(January-March), 2024-25**

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
33	WEST BENGAL	62	67,640.76 (72,494.42) {90,447.68}	48,255.63
	Total	1773	2672909.7 (2929094.92) {3211901.18}	1778240.05

***Either Revised or Original Cost**

Table:-3. Project List: Completed during 4th Quarter (January-March),2024-25

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
COAL					
	1	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) (NCL) (N06000162) (MADHYA PRADESH)	1255.17	03-2022	1254.21
	2	MADHUBAND NLW WASHERY (BCCL) (N06000126) (JHARKHAND)	289.45	05-2014	300.01
DONER					
	3	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR (HSCL FOR DONER) (N12000103) (MEGHALAYA)	151.33	09-2017	148.33
PETROLEUM					
	4	CGD PROJECT AT JHUNJHUNU, SIKAR AND NAGAU DISTRICTS (IOCL) (N16000489) (RAJASTHAN)	575	03-2030	124.37
	5	UPGRADING IPSHEM TO WORLD CLASS FACILITY OF ONGC, GOA (ONGC) (N16000502) (GOA)	325.53	06-2024	304.19
	6	CGD PROJECT AT MADURAI, THENI AND VIRUDHNAGAR DISTRICTS (IOCL) (N16000490) (TAMIL NADU)	1328	03-2030	149.21
	7	PIPELINE REPLACEMENT PROJECT - VII (ONGC) (N16000436) (MAHARASHTRA)	3183.58	05-2024	3417
	8	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI (IOCL) (N16000405) (TAMIL NADU)	1398	12-2023	1303.66
	9	VISAKH REFINERY MODERNISATION PROJECT (HPCL) (N16000235) (ANDHRA PRADESH)	20928	07-2020	28002
	10	Fuel Quality Upgradation Project at Paradip Refinery (IOCL) (N16000362) (ODISHA)	3361	08-2021	2727.6

Table:-3. Project List: Completed during 4th Quarter (January-March),2024-25

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	11	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY (IOCL) (N16000368) (ODISHA)	427.1	09-2022	312.13
	12	CGD PROJECT AT KANYAKUMARI, TUTICORIN, TIRUNVELI KATTABO AND TENKASI DISTRICTS (IOCL) (N16000492) (TAMIL NADU)	1295	03-2030	145.61
	13	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK (ONGC) (N16000239) (JHARKHAND)	823.27	03-2023	1067.89
	14	SWRO II WITH LLPH FACILITIES (HPCL) (N16000378) (ANDHRA PRADESH)	196.26	07-2020	196.26
POWER					
	15	TELANGANA SUPER THERMAL POWER PROJECT PHASE I (NTPC) (N18000212) (TELANGANA)	10598.98	11-2020	10437.71
	16	CHHATTARGARH 150 MW (NTPC) (N18000294) (RAJASTHAN)	599.99	07-2022	599.99
	17	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN (PGCIL) (N18000264) (MULTI STATE)	1931.39	02-2020	1972.44
	18	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PHASE-IV PART-I (BIKANER COMPLEX) PAR (PGCIL) (N18000372) (RAJASTHAN)	202.39	01-2025	20.04
	19	ANTA SOLAR 90 MW (NTPC) (N18000292) (RAJASTHAN)	382.22	03-2022	497.17
	20	DURGAPUR PP-III (2X20 MW) - NSPCL (NTPC) (N18000277) (WEST BENGAL)	529.68	11-2018	558.39
ROAD TRANSPORT AND RAILWAYS					

Table:-3. Project List: Completed during 4th Quarter (January-March),2024-25

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
HIGHWAYS	21	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON (NHAI) (N24001569) (RAJASTHAN)	1425.02	03-2023	1420.03
	22	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756) (NAGALAND)	285.68	09-2022	193.9
	23	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH- 248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P (NHAI) (N24000835) (HARYANA)	1484.3	12-2020	1376.15
	24	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH- 415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374) (ARUNACHAL PRADESH)	437.6	03-2027	366.59
	25	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372) (ARUNACHAL PRADESH)	588.09	03-2024	497.36
	26	PATAS-VASUNDE PHATA - BARAMATI BYPASS (NHAI) (N24001501) (MAHARASHTRA)	531.86	09-2023	520.71
	27	DEVELOPMENT OF 4L UER II [PACKAGE - V] (SPUR TO BAHADURGARH BYPASS) (NH-10) FROM KM. 0.00 TO KM.7.30 (NHAI) (N24001778) (DELHI)	801.46	10-2023	473.76
	28	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001378) (MAHARASHTRA)	362.46	01-2022	352.01
	29	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001377) (MAHARASHTRA)	731.89	01-2022	692.21

Table:-3. Project List: Completed during 4th Quarter (January-March),2024-25

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	30	4L OF SUHAGADI TO BARDIYA AMRA FROM KM. 89.200 TO KM. 135.351 OF NH-752D (PKG-III) (NHAI) (N24001758) (MADHYA PRADESH)	823.05	10-2024	402.85
	31	IMPHAL ? MOREH PACKAGE- 3 (NHIDCL) (N24001352) (MANIPUR)	259.31	12-2022	144.94
	32	2L+PS OF THIKRI ANJAD SECTION OF NH-347B (MoRTH) (N24000892) (MADHYA PRADESH)	249.05	07-2018	221.19
	33	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 (NHAI) (N24000556) (UTTAR PRADESH)	899	04-2019	1143.5
	34	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D (NHAI) (N24001756) (MADHYA PRADESH)	1352.56	10-2024	843.65
	35	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAUER SECTION BY EXECUTING BALANCE WORK FRO (MoRTH) (N24001241) (RAJASTHAN)	255.23	10-2022	256
	36	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-8) (NHAI) (N24001561) (RAJASTHAN)	839.63	10-2023	839.63
	37	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE) (MoRTH) (N24001291) (ARUNACHAL PRADESH)	421.48	03-2027	365.83
	38	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 (NHAI) (N24000559) (UTTARAKHAND)	720	10-2019	672.33

Table:-3. Project List: Completed during 4th Quarter (January-March),2024-25

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	39	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND (MoRTH) (N24000885) (WEST BENGAL)	160.27	09-2023	174.36
	40	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685) (ARUNACHAL PRADESH)	167.28	04-2022	145.2
	41	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292) (ARUNACHAL PRADESH)	543.05	03-2027	588.85
	42	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-13) (CH. 359.170 TO CH. 388.420) [JUNCTION WITH S (NHAI) (N24001571) (RAJASTHAN)	1341.36	12-2023	1089.73
	43	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N (MoRTH) (N24000887) (WEST BENGAL)	236.78	09-2021	232.54
	44	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH ? 14 (NHAI) (N24001185) (UTTAR PRADESH)	2159	07-2021	3110.5
	45	REMAINING WORK OF 2L+PS OF TRICHY - KARAIKUDI SECTION OF NH-210, INCLUDING TRICHY BYPASS (NHAI) (N24001604) (TAMIL NADU)	166.9	03-2021	121.94
	46	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-11) (CH. 319.400 TO CH. 331.030) [HARDEOGANJ VILL (NHAI) (N24001566) (RAJASTHAN)	1640.1	05-2023	1248.59

Table:-3. Project List: Completed during 4th Quarter (January-March),2024-25

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	47	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 (NHAI) (N24001432) (ASSAM)	300	08-2024	439.65
	48	DWARKA EXPRESSWAY PKG-III (DELHI/HR BORDER TO START OF ROB GURUGRAM) (NHAI) (N24001780) (HARYANA)	2228	11-2020	1628.6
	49	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 (NHIDCL) (N24001248) (ASSAM)	208.84	04-2022	193.59
	50	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (MoRTH) (N24001293) (ARUNACHAL PRADESH)	486.7	03-2027	480.44
	51	4L OF HARDA - BETUL (PKG-II) FROM KM. 30.00 TO KM.81.00 [TEMAGAON TO CHICHOLI] (NHAI) (N24001761) (MADHYA PRADESH)	520.28	02-2025	392.86
	52	DULTE- KWALKULH - CHAMPAI PKG.1 (NHIDCL) (N24001355) (MIZORAM)	374.39	12-2022	286.49
	53	ALLAHGANJ TO MIRANPUR KATRA SECTION OF NH-730C FROM KM.52.770 TO 114.00 (MoRTH) (N24001463) (UTTAR PRADESH)	294.84	07-2024	303.27
	54	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001379) (MAHARASHTRA)	594.75	01-2022	585.2
	55	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 (NHIDCL) (N24001342) (JAMMU AND KASHMIR)	260.4	12-2022	191.88

Table:-3. Project List: Completed during 4th Quarter (January-March),2024-25

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	56	MULAKALACHERUVU TO MADANAPALLE SECTION OF NH42 FROM KM 202.050 TO KM 245.640 EXCLUDING RETAINED STRE (MoRTH) (N24001933) (ANDHRA PRADESH)	480.1	12-2024	443.87
	57	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST (NHAI) (N24000655) (MAHARASHTRA)	247.02	03-2020	93.29
WATER RESOURCES					
	58	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR (BUIDCO) (N30000037) (BIHAR)	225.77	03-2020	363.79
	59	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH (KMDA) (N30000045) (WEST BENGAL)	185.22	12-2021	49.99
	60	I AND D AND STP AT CHAPPRA (BUIDCO) (N30000028) (BIHAR)	236.15	12-2020	150.75
	61	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S (DJB) (N30000016) (DELHI)	239.11	02-2022	268.13
	62	FARRUKHABAD I AND D AND STP WORKS HAM (UP JalNigam) (N30000008) (UTTAR PRADESH)	213.62	03-2022	177.62
	63	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 (DJB) (N30000015) (DELHI)	211.79	12-2021	208.71
	64	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI (KMDA) (N30000048) (WEST BENGAL)	172.1	12-2021	47.2
	65	INTERCEPTION AND DIVERSION WITH STP AT BALLY (KMDA) (N30000049) (WEST BENGAL)	164.93	12-2021	45.45

Table:-3. Project List: Completed during 4th Quarter (January-March),2024-25

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	66	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH (UPJalNigam) (N30000025) (UTTAR PRADESH)	298.12	07-2021	103.24
	67	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR (KMDA) (N30000046) (WEST BENGAL)	274.76	12-2019	278.33
	68	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH (UPJalNigam) (N30000013) (UTTAR PRADESH)	271.39	08-2021	182.26
	69	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI (DJB) (N30000017) (DELHI)	515.07	01-2021	388.08
	70	SEWERAGE SCHEME AT PAHARI ZONE V PATNA (BUIDCO) (N30000040) (BIHAR)	356.37	04-2021	312.3
	71	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH (UKJalNigam) (N30000004) (UTTARAKHAND)	158	11-2019	107.86
	72	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA (UPJalNigam) (N30000006) (UTTAR PRADESH)	767.59	09-2021	276.97
	73	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS (UPJalNigam) (N30000010) (UTTAR PRADESH)	967.23	09-2021	254.98
	74	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE (KMDA) (N30000047) (WEST BENGAL)	272.32	04-2020	307.73
	75	SEWERAGE TREATMENT PLANT AT PAHARI PATNA (BUIDCO) (N30000043) (BIHAR)	191.62	11-2020	124.4

Table:-3. Project List: Completed during 4th Quarter (January-March),2024-25

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	76	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH (UPJalNigam) (N30000022) (UTTAR PRADESH)	206.05	10-2021	140.22
	77	MATHURA SEWERAGE SCHEME (UPJalNigam) (N30000019) (UTTAR PRADESH)	460.45	12-2020	315.3
		Total	81,046.73		80,175.01

**Table:-4. Project List: Added during 4th Quarter
(January-March),2024-25**

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
COAL	1	RPR OF HINGULA EXPANSION OCP (MCL) (N06000285) (ODISHA)	11-2022	1,561.85 (1,561.85) {1,561.85}	3/2029 (N.A.) {3/2029}
	2	BHUBANESWARI EXPANSION OCP (MCL) (N06000286) (ODISHA)	3-2024	5,366.28 (5,366.28) {5,366.28}	3/2031 (N.A.) {3/2031}
	3	BLOCK-E OCP (15 MTY) (BCCL) (N06000287) (JHARKHAND)	3-2024	5,850.83 (5,850.83) {5,850.83}	3/2029 (N.A.) {3/2029}
	4	BALABHADRA OCP (MCL) (N06000288) (ODISHA)	4-2023	978.44 (978.44) {978.44}	3/2030 (N.A.) {3/2030}
	5	INTEGRATED KULDA GARJANBAHAL OCP (MCL) (N06000289) (ODISHA)	4-2023	3,563.50 (3,563.50) {3,563.50}	3/2030 (N.A.) {3/2030}
	6	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290) (ASSAM)	7-2022	159.77 (159.77) {159.77}	11/2030 (N.A.) {11/2030}
	7	TIRAP OCP (CIL) (N06000291) (ASSAM)	11-2022	289.46 (289.46) {289.46}	11/2027 (N.A.) {11/2027}
PETROLEUM	8	LUBE MODERNIZATION AND BOTTOM UPGRADATION PROJECT (HPCL) (N16000540) (MAHARASHTRA)	12-2024	4,679.00 (4,679.00) {4,679.00}	3/2028 (N.A.) {3/2028}
POWER	9	ADDITIONAL TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM BHADLA-III PS AS PART OF RAJASTHAN REZ P (PGCIL) (N18000396) (RAJASTHAN)	8-2024	369.00 (369.00) {369.00}	2/2026 (N.A.) {2/2026}

**Table:-4. Project List: Added during 4th Quarter
(January-March),2024-25**

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	10	TRANSMISSION SYSTEM STRENGTHENING FOR INTERCONNECTIONS OF BHADLA-III AND BIKANER III COMPLEX [SPV NA (PGCIL) (N18000397) (RAJASTHAN)	8-2024	1,382.00 (1,382.00) {1,382.00}	8/2026 (N.A.) {8/2026}
	11	AUGMENTATION OF TRANSFORMATION CAPACITY AT JAM KHAMBHALIYA PS [GIS] [SPV NAME POWERGRID JAM KHAMBHAL (PGCIL) (N18000398) (GUJARAT)	10-2024	329.00 (329.00) {329.00}	7/2026 (N.A.) {7/2026}
	12	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-2 5.5GW] [JAISALMER/BARME (PGCIL) (N18000399) (MADHYA PRADESH)	10-2024	3,674.00 (3,674.00) {3,674.00}	10/2026 (N.A.) {10/2026}
	13	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000400) (GUJARAT)	10-2024	4,766.00 (4,766.00) {4,766.00}	10/2026 (N.A.) {10/2026}
	14	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BAR (PGCIL) (N18000401) (RAJASTHAN)	11-2024	2,735.00 (2,735.00) {2,735.00}	11/2026 (N.A.) {11/2026}
	15	PROVISION OF DYNAMIC REACTIVE COMPENSATION AT KHAVDA POOLING STATION 1 [KPS1] AND KHAVDA POOLING STA (PGCIL) (N18000402) (GUJARAT)	11-2024	501.00 (501.00) {501.00}	11/2026 (N.A.) {11/2026}
	16	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6GW)] [BIKANER COMPLEX (PGCIL) (N18000403) (RAJASTHAN)	11-2024	5,969.00 (5,969.00) {5,969.00}	11/2026 (N.A.) {11/2026}
	17	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6 GW)] [BIKANER COMPLE (PGCIL) (N18000404) (RAJASTHAN)	11-2024	5,357.00 (5,357.00) {5,357.00}	11/2026 (N.A.) {11/2026}

**Table:-4. Project List: Added during 4th Quarter
(January-March),2024-25**

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	18	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000405) (GUJARAT)	11-2024	24,819.00 (24,819.00) {24,819.00}	5/2029 (N.A.) {5/2029}
	19	600 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000406) (GUJARAT)	4-2022	4,100.45 (4,100.45) {4,100.45}	3/2026 (N.A.) {3/2026}
ROAD TRANSPORT AND HIGHWAYS	20	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS (NHAI) (N24000176) (TAMIL NADU)	5-2010	374.00 (374.00) {166.90}	5/2013 (N.A.) {5/2013}
	21	WIDENING AND STRENGTHENING OF RAFIABAD-KUPWARA-CHOWKIBAL-TANGDHAR-CHAMKOT (NH-701) ROAD FROM DESIGN (BRO) (N24002210) (JAMMU AND KASHMIR)	3-2024	1,404.94 (1,404.94) {1,404.94}	5/2027 (N.A.) {5/2027}
	22	REHABILITATION AND UPGRADATION TO FOUR LANE ROAD FROM KM 70.500 TO KM 78.600 OF NH-92 UNDER EPC MODE (MoRTH) (N24002211) (UTTAR PRADESH)	1-2022	296.02 (296.02) {296.02}	1/2027 (N.A.) {1/2027}
	23	WIDENING AND STRENGTHENING FROM DESIGN KM. 67.280 TO KM. 88.622 OF NH-727A (SALEMPUR-MAIRWA ROAD) TO (MoRTH) (N24002212) (UTTAR PRADESH)	3-2023	371.89 (371.89) {371.89}	7/2026 (N.A.) {7/2026}
	24	REHABILITATION and UP-GRADATION TO 2L+PS FROM KM. 0.0 TO KM. 7.80 AND KM. 35.400 TO KM. 52.345 (DESI (MoRTH) (N24002213) (UTTAR PRADESH)	3-2023	701.02 (701.02) {701.02}	7/2026 (N.A.) {7/2026}
	25	CONSTRUCTION OF AMETHI BYPASS (PART-II) AT KM.30.050 OF NH-931 UNDER EPC MODE IN THE STATE OF UTTAR (MoRTH) (N24002214) (UTTAR PRADESH)	12-2022	283.86 (283.86) {283.86}	2/2027 (N.A.) {2/2027}

**Table:-4. Project List: Added during 4th Quarter
(January-March),2024-25**

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	26	DEVELOPMENT OF SIX LANE ACCESS CONTROLLED GREEN FIELD HIGHWAY FROM KAVULAKUNTALA (KM.196+000) TO NARA (NHAI) (N24002215) (ANDHRA PRADESH)	2-2023	1,092.18 (1,092.18) {1,092.18}	2/2027 (N.A.) {2/2027}
	27	ACCESS CONTROLLED HIGHWAY OF 4 LANE WITH PAVED SHOULDERS FROM TIRUVALLUR (DESIGN CHAINAGE KM 17+56) (NHAI) (N24002216) (TAMIL NADU)	12-2024	1,376.10 (1,376.10) {1,376.10}	12/2026 (N.A.) {12/2026}
	28	ACCESS CONTROLLED HIGHWAY OF 4 LANE WITH PAVED SHOULDERS FROM TN/AP BORDER (DESIGN CHAINAGE KM 61+51) (NHAI) (N24002217) (ANDHRA PRADESH)	12-2024	1,346.82 (1,346.82) {1,346.82}	12/2026 (N.A.) {12/2026}
	29	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE ? PARADIP SECTION OF NH-53 (OLD NH) (NHAI) (N24002219) (ODISHA)	3-2024	882.45 (882.45) {882.45}	10/2026 (N.A.) {10/2026}
	30	PERMANENT RECTIFICATION OF 4 NOS. OF BLACKSPOTS ON NH 27 OF KOTWA MEHSI MUZAFFARPUR SECTION FROM (NHAI) (N24002220) (BIHAR)	12-2022	410.75 (410.75) {410.75}	11/2026 (N.A.) {11/2026}
	31	4L OF GREENFIELD ALIGNMENT FROM KM. 47.000 TO KM. 89.210 OF BALBHADARPUR TO BELA NAWDA SECTION OF NH (NHAI) (N24002221) (BIHAR)	2-2022	2,185.75 (2,185.75) {2,185.75}	3/2026 (N.A.) {3/2026}
	32	HUNLI TO HAYULIANG PKG-1 (NHIDCL) (N24002222) (ARUNACHAL PRADESH)	2-2024	1,262.43 (1,262.43) {1,262.43}	2/2028 (N.A.) {2/2028}
	33	HUNLI TO ITHUN BRIDGE SECTION (NHIDCL) (N24002223) (ARUNACHAL PRADESH)	2-2024	275.50 (275.50) {275.50}	1/2027 (N.A.) {1/2027}

**Table:-4. Project List: Added during 4th Quarter
(January-March),2024-25**

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	34	PANGO TO JORGING ROAD PKG-1 (NHIDCL) (N24002224) (ARUNACHAL PRADESH)	1-2024	898.19 (898.19) {898.19}	7/2027 (N.A.) {7/2027}
	35	BILASIPURA- GUWAHATI ROAD PKG-1 (NHIDCL) (N24002225) (ASSAM)	2-2024	1,081.15 (1,081.15) {1,081.15}	8/2027 (N.A.) {8/2027}
	36	SILCHAR-JIRIBAM PKG-1 (NHIDCL) (N24002226) (ASSAM)	1-2024	957.95 (957.95) {957.95}	1/2028 (N.A.) {1/2028}
	37	JESSAMI TO LAYNEN BRIDGE UKHRUL - JESSAMI PKG-7 (NHIDCL) (N24002227) (MANIPUR)	3-2023	164.89 (164.89) {164.89}	6/2026 (N.A.) {6/2026}
	38	KHOWAI ?TELIAMURA-AMARPUR-HARINA-SABROOM SECTION PKG-4 (NHIDCL) (N24002228) (TRIPURA)	1-2024	726.90 (726.90) {726.90}	12/2026 (N.A.) {12/2026}
STEEL	39	SCREENING PLANT-II, DONIMALAI (NMDC) (N12000136) (KARNATAKA)	9-2023	1,043.63 (1,043.63) {1,043.63}	8/2026 (N.A.) {8/2026}
Grand Total				93587 (93587) {93379.9}	

Table:-5. Project List: Frozen/Deleted during 4th Quarter (January-March),2024-25

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
COAL					
	1	GARJANBAHAL OCP (ODISHA) (N06000117) (MCL)	1,375.38	03/2021	849.48
	2	BHUBANESWARI EXPANSION OCP (ODISHA) (N06000227) (MCL)	6,321.73	03/2031	1,354.15
	3	KUMUNDA EXPN.OCP(SECL)(15-50)MTY (CHHATTISGARH) (N06000008) (SECL)	7,612.33	03/2023	4,647.14
	4	RPR OF HINGULA -II EXPANSION PH-III (ODISHA) (N06000261) (MCL)	2,264.68	03/2029	1,054.83
	5	KULDA EXPANSION OCP- 15 MTY (ODISHA) (N06000248) (MCL)	348.16	03/2018	207.75
ROAD TRANSPORT AND HIGHWAYS	6	MUNGOLI NIRGUDA EXTENSION (DEEP) OC (MAHARASHTRA) (N06000231) (WCL)	826.80	03/2026	518.85
	7	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS (TAMIL NADU) (N24000176) (NHAI)	374.00	05/2013	374.00
	8	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (MANIPUR) (N24001276) (NHIDCL)	228.97	04/2022	-
		Total	19352.05		9006.2

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ARUNACHAL PRADESH	CIVIL AVIATION	1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (5/2025) {5/2025}	645.63 (N.A.) {712.15}	688.31	99.43
	POWER	2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	23,753.28	96.1
		3	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	3,182.93	14.47
	ROAD TRANSPORT AND HIGHWAYS	4	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (3/2024) {3/2025}	180.57 (244.10) {180.57}	160.46	96.62
		5	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685)	2-2017	4/2022 (11/2023) {11/2023}	167.28 (N.A.) {167.28}	145.20	100
		6	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (6/2025) {6/2025}	1,718.59 (1,718.59) {1,718.59}	728.21	73.1
		7	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9-2016	12/2019 (8/2024) {9/2024}	568.92 (568.92) {568.92}	508.65	100
		8	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (5/2023) {3/2025}	256.66 (N.A.) {256.66}	-	63.59
		9	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (2/2025) {2/2025}	301.06 (N.A.) {301.06}	191.34	76.98

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		10	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO (NHIDCL) (N24001245)	9-2020	5/2022 (10/2022) {3/2024}	353.90 (N.A.) {353.90}	41.82	25.38
		11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE (MoRTH) (N24001291)	3-2019	3/2027 (N.A.) {3/2027}	421.48 (N.A.) {421.48}	365.83	100
		12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292)	3-2019	3/2027 (N.A.) {3/2027}	543.05 (N.A.) {600.00}	588.85	100
		13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE (MoRTH) (N24001293)	3-2019	3/2027 (N.A.) {3/2027}	486.70 (N.A.) {486.70}	480.44	100
		14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	389.68	95.26
		15	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372)	2-2021	3/2024 (12/2024) {12/2024}	588.09 (N.A.) {588.09}	497.36	100
		16	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374)	6-2020	3/2027 (N.A.) {3/2027}	437.60 (N.A.) {437.60}	366.59	100
		17	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	179.53	40.57

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		18	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (8/2024) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		19	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8-2020	4/2022 (2/2024) {9/2024}	294.04 (N.A.) {294.04}	147.13	100
		20	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (2/2024) {3/2025}	184.88 (N.A.) {184.88}	99.32	97.42
		21	HUNLI TO HAYULIANG PKG-1 (NHIDCL) (N24002222)	2-2024	2/2028 (N.A.) {2/2028}	1,262.43 (N.A.) {1,262.43}	-	0.03
		22	HUNLI TO ITHUN BRIDGE SECTION (NHIDCL) (N24002223)	2-2024	1/2027 (N.A.) {1/2027}	275.50 (N.A.) {275.50}	-	0.07
		23	PANGO TO JORGING ROAD PKG-1 (NHIDCL) (N24002224)	1-2024	7/2027 (N.A.) {7/2027}	898.19 (N.A.) {898.19}	-	0
		24	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (8/2025) {8/2025}	1,142.00 (N.A.) {2,333.00}	1,750.24	83.87
ASSAM	CIVIL AVIATION	25	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290)	7-2022	11/2030 (N.A.) {11/2030}	159.77 (N.A.) {159.77}	81.45	0
	COAL	26	TIRAP OCP (CIL) (N06000291)	11-2022	11/2027 (N.A.) {11/2027}	289.46 (N.A.) {289.46}	105.55	0
	HEALTH AND FAMILY WELFARE	27	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (4/2023) {11/2024}	875.00 (873.92) {860.00}	787.90	99.35

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	28	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	99.50	14.98
		29	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	97.22	89
		30	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	250.17	55.2
		31	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	169.86	42.8
		32	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (12/2024) {6/2025}	543.91 (726.93) {726.93}	491.56	93.89
		33	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	15,390.82	71.88
		34	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	9,212.58	83.81
		35	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (2/2025) {5/2026}	412.00 (509.84) {509.84}	379.60	82.04
		36	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (9/2026) {9/2026}	277.00 (N.A.) {277.00}	175.69	65.11

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		37	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (4/2025) {4/2025}	860.00 (N.A.) {860.00}	535.46	95
		38	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (3/2024) {6/2025}	430.76 (N.A.) {430.76}	307.70	81.97
		39	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	80.15	29
		40	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (7/2027) {7/2027}	156.36 (156.36) {156.36}	36.52	26.5
		41	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (7/2027) {7/2027}	384.04 (N.A.) {384.04}	81.21	26.2
	RAILWAYS	42	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2022 (N.A.) {3/2027}	2,232.32 (N.A.) {4,983.94}	3,606.19	92.3
	ROAD TRANSPORT AND HIGHWAYS	43	BILASIPURA- GUWAHATI ROAD PKG-1 (NHIDCL) (N24002225)	2-2024	8/2027 (N.A.) {8/2027}	1,081.15 (N.A.) {1,081.15}	-	0
		44	SILCHAR-JIRIBAM PKG-1 (NHIDCL) (N24002226)	1-2024	1/2028 (N.A.) {1/2028}	957.95 (N.A.) {957.95}	-	0
		45	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	391.08	60.55

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		46	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	365.45	59.3
		47	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	417.14	56.45
		48	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	293.04	89.98
		49	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	275.46	90.4
		50	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {5/2025}	204.10 (N.A.) {204.10}	142.31	93.26
		51	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	517.67	41.82
		52	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	303.94	22.75
		53	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	395.28	22.3
		54	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	234.60	69.48

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		55	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	125.69	12.64
		56	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3-2023	12/2025 (N.A.) {12/2026}	643.42 (N.A.) {643.42}	69.47	8.89
		57	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	279.86	39.87
		58	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY) (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	149.79	26.7
		59	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.87	100
		60	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	499.58	32.68
		61	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	983.58	61.75
		62	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	280.91	49.51
		63	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	377.55	60.42

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		64	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (1,019.17) {925.47}	192.50	30.65
		65	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 (NHAI) (N24001432)	12-2021	8/2024 (3/2024) {8/2024}	300.00 (N.A.) {300.00}	439.65	100
		66	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	328.49	65.29
		67	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.76	100
		68	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	137.01	71.71
		69	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {5/2025}	625.64 (N.A.) {625.64}	550.60	100
		70	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3-2022	7/2024 (N.A.) {10/2024}	215.27 (N.A.) {215.27}	151.29	100
		71	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {6/2025}	909.02 (N.A.) {909.02}	509.89	94.64
		72	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (9/2024) {6/2024}	175.00 (N.A.) {175.00}	200.80	100

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		73	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	567.75	72.3
		74	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {3/2025}	457.72 (N.A.) {457.72}	365.99	100
		75	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	110.74	35.13
		76	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {5/2025}	458.59 (N.A.) {458.59}	196.33	59.99
		77	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	73.25	31.23
		78	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,382.39	59.88
		79	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (5/2025) {5/2025}	261.13 (N.A.) {261.13}	68.75	57.42
		80	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (4/2025) {4/2025}	217.50 (N.A.) {217.50}	88.99	68.03
		81	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	217.06	97.76

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		82	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 (NHIDCL) (N24001248)	8-2020	4/2022 (N.A.) {7/2024}	208.84 (N.A.) {208.84}	193.59	100
		83	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (1/2025) {6/2025}	216.49 (241.52) {216.49}	111.59	82.79
		84	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {4/2025}	437.39 (N.A.) {437.39}	541.08	94.36
		85	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	478.05	73.48
		86	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1-1991	6/2019 (6/2019) {6/2025}	520.01 (N.A.) {520.01}	305.03	96.71
		87	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (7/2021) {6/2025}	289.99 (N.A.) {289.99}	233.23	87.62
		88	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {4/2025}	294.17 (N.A.) {294.17}	380.19	96.25
		89	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {4/2025}	252.00 (N.A.) {330.30}	215.64	85.81
MANIPUR	CIVIL AVIATION	90	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (3/2026) {3/2026}	499.00 (N.A.) {499.00}	154.47	38.36

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	91	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	3/2011 (3/2028) {12/2028}	4,454.17 (12,274.06) {22,234.60}	15,218.35	68.5
	ROAD TRANSPORT AND HIGHWAYS	92	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (1/2025) {9/2025}	292.24 (N.A.) {292.24}	130.66	89.72
		93	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (1/2025) {10/2025}	365.53 (N.A.) {365.53}	156.31	77.36
		94	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3-2020	6/2022 (1/2025) {5/2025}	167.95 (204.12) {167.95}	88.05	69.89
		95	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7-2020	8/2022 (2/2025) {5/2025}	177.76 (N.A.) {177.76}	89.67	80.53
		96	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (6/2025) {6/2025}	379.39 (N.A.) {379.39}	214.93	63.76
		97	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276)	8-2020	4/2022 (N.A.) {3/2025}	228.97 (N.A.) {228.97}	-	0
		98	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (3/2025) {5/2025}	226.32 (N.A.) {226.32}	104.95	73.82
		99	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (10/2024) {2/2025}	188.36 (N.A.) {188.36}	126.71	100
		100	IMPHAL ? MOREH PACKAGE- 3 (NHIDCL) (N24001352)	3-2021	12/2022 (N.A.) {6/2024}	259.31 (N.A.) {259.31}	144.94	100

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		101	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3-2021	12/2022 (3/2025) {3/2026}	195.14 (N.A.) {195.14}	61.81	50.79
		102	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (9/2024) {5/2025}	234.08 (N.A.) {234.08}	139.45	91.04
		103	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (7/2025) {12/2025}	579.63 (N.A.) {579.63}	172.65	67.02
		104	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (3/2025) {5/2025}	310.76 (N.A.) {310.76}	129.15	96.77
		105	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (10/2024) {2/2025}	467.41 (N.A.) {467.41}	264.83	100
		106	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (1/2025) {6/2025}	477.86 (N.A.) {477.86}	243.46	83.92
		107	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (11/2024) {4/2025}	311.18 (N.A.) {311.18}	186.15	81.21
		108	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (5/2025) {5/2025}	211.70 (N.A.) {211.70}	83.79	65.02
		109	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (3/2025) {10/2025}	467.00 (N.A.) {467.00}	193.81	77.59
		110	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (1/2025) {1/2025}	185.80 (N.A.) {185.80}	117.78	100

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		111	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (8/2024) {5/2025}	483.87 (N.A.) {483.87}	278.89	92.73
		112	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (2/2025) {3/2025}	198.77 (N.A.) {198.77}	125.11	100
		113	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (3/2025) {5/2025}	673.27 (N.A.) {673.27}	377.12	78.46
		114	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (3/2026) {3/2026}	578.98 (N.A.) {578.98}	145.62	67.93
		115	MARREM KHULLEN TO JESSAMI SECTION IMPHAL - UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	11.64	9.21
		116	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	10.88	11.5
		117	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (2/2025) {3/2026}	410.68 (N.A.) {410.68}	147.81	65.85
		118	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (9/2025) {12/2025}	504.76 (N.A.) {504.76}	183.15	73.23
		119	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (2/2025) {3/2025}	152.11 (N.A.) {152.11}	73.48	100
		120	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (1/2025) {9/2025}	315.56 (N.A.) {315.56}	121.49	79.2

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MEGHALAYA		121	JESSAMI TO LAYNEN BRIDGE UKHRUL - JESSAMI PKG-7 (NHIDCL) (N24002227)	3-2023	6/2026 (N.A.) {6/2026}	164.89 (N.A.) {164.89}	-	0
		122	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (12/2025) {3/2026}	760.16 (N.A.) {760.16}	148.98	57.37
	DEPARTMENT OF HIGHER EDUCATION	123	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (7/2025) {7/2025}	484.32 (429.70) {429.70}	294.55	82.5
	DONER	124	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR (HSCL FOR DONER) (N12000103)	4-2014	9/2017 (N.A.) {9/2017}	151.33 (N.A.) {151.33}	148.33	100
	ROAD TRANSPORT AND HIGHWAYS	125	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10-2020	4/2022 (6/2024) {2/2025}	157.86 (146.92) {157.86}	152.90	100
		126	RANIKOR- MAHESHKHOLA- BAGHMARA PKG- 2 (NHIDCL) (N24001541)	11-2021	6/2024 (12/2024) {4/2025}	283.50 (N.A.) {283.50}	256.07	96.06
		127	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	210.58	24.5
		128	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	281.90	21.5
		129	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	292.43	21.5

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		130	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (12/2024) {12/2025}	359.86 (N.A.) {359.86}	232.55	87
		131	REHABILITATION AND UPGADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (3/2025) {3/2025}	302.88 (N.A.) {302.88}	224.39	95
		132	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3-2021	12/2022 (6/2024) {2/2025}	260.21 (N.A.) {260.21}	239.10	100
		133	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	206.15	23.5
		134	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	100.93	20.5
		135	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM ((NHIDCL) (N24001313)	11-2020	12/2023 (10/2025) {10/2025}	351.12 (N.A.) {351.12}	295.87	59.2
		136	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	425.39	28
		137	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (4/2025) {4/2025}	553.51 (610.09) {553.51}	414.04	82.32
MIZORAM	RAILWAYS	138	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2014 (N.A.) {7/2025}	2,393.47 (5,021.45) {8,213.72}	7,906.29	94.6

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	139	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (N.A.) {3/2025}	519.09 (N.A.) {785.65}	667.78	95.75
		140	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (N.A.) {7/2023}	640.07 (N.A.) {1,286.35}	1,192.26	98.9
		141	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4-2017	6/2023 (N.A.) {3/2024}	642.96 (N.A.) {988.23}	721.12	99.55
		142	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (N.A.) {3/2025}	473.18 (N.A.) {688.25}	539.93	92.01
		143	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (N.A.) {3/2025}	537.82 (N.A.) {789.05}	768.85	95.4
		144	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (N.A.) {3/2025}	518.53 (N.A.) {906.76}	847.17	97.01
		145	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (N.A.) {3/2025}	404.29 (N.A.) {750.32}	654.75	97.51
		146	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (N.A.) {3/2025}	428.11 (N.A.) {746.39}	605.09	97.46

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		147	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL- TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9-2020	10/2022 (N.A.) {4/2025}	275.02 (N.A.) {247.25}	265.18	99.74
		148	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (N.A.) {6/2024}	206.88 (N.A.) {219.33}	265.18	100
		149	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (N.A.) {6/2025}	292.24 (N.A.) {331.17}	291.20	93.15
		150	DULTE- KWALKULH - CHAMPAI PKG.1 (NHIDCL) (N24001355)	3-2021	12/2022 (3/2024) {3/2024}	374.39 (N.A.) {318.92}	286.49	100
		151	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (4/2024) {12/2025}	233.25 (N.A.) {233.25}	172.09	100
		152	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (N.A.) {3/2026}	698.44 (N.A.) {698.45}	481.12	52.84
		153	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (N.A.) {3/2026}	740.58 (N.A.) {740.58}	353.73	50.6
		154	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9-2021	5/2023 (N.A.) {5/2024}	492.94 (N.A.) {492.94}	353.09	100
		155	ZORINPUI- HMAWNGBU-LONGMASU (NH- 502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	67.12	0.5
		156	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	250.46	65.1

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		157	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWL RANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {12/2025}	523.78 (N.A.) {523.78}	303.25	61
NAGALAND	PETROLEUM	158	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	4.10	17
	RAILWAYS	159	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2015 (N.A.) {12/2029}	2,326.52 (6,663.20) {6,663.20}	4,531.38	66
	ROAD TRANSPORT AND HIGHWAYS	160	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	92.24	49.15
		161	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	39.97	20.46
		162	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	159.36	58.7
		163	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	62.08	59
		164	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7-2021	3/2023 (9/2025) {9/2025}	258.52 (N.A.) {258.52}	83.96	75.64
		165	PEREN-DIMAPUR PKG-5 (NHIDCL) (N24001407)	2-2021	3/2023 (N.A.) {3/2023}	207.33 (N.A.) {207.33}	-	0

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		166	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3-2022	12/2024 (N.A.) {1/2025}	605.36 (N.A.) {605.36}	273.21	100
		167	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (6/2026) {6/2026}	252.19 (N.A.) {252.19}	11.80	13.85
		168	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3-2021	7/2024 (6/2025) {6/2025}	297.24 (N.A.) {297.24}	137.57	74.45
		169	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (3/2025) {3/2025}	226.44 (N.A.) {226.44}	140.24	100
		170	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (6/2025) {6/2025}	192.93 (N.A.) {192.93}	96.19	87.5
		171	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {12/2025}	177.77 (199.02) {199.02}	43.33	56.47
		172	CHANGTONGYA TO LONGLENG ROAD PKG- 2 (NHIDCL) (N24001389)	3-2020	6/2022 (9/2022) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.4
		173	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	109.24	62.7
		174	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3-2020	6/2022 (10/2022) {6/2023}	278.95 (N.A.) {278.95}	166.29	100

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		175	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (11/2025) {11/2025}	330.80 (N.A.) {330.80}	168.02	87.53
		176	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (11/2026) {11/2026}	232.29 (350.88) {232.29}	69.98	13.46
		177	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (9/2024) {6/2026}	277.44 (N.A.) {277.44}	168.88	66.12
		178	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (6/2025) {6/2025}	159.85 (342.29) {159.85}	101.93	28.57
		179	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (4/2023) {8/2025}	202.36 (N.A.) {202.36}	75.17	30.33
		180	UPGRADATION OF EXISTING ROAD TO 2- LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9-2020	4/2022 (5/2024) {12/2025}	315.63 (N.A.) {315.63}	116.70	74.23
		181	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3-2017	11/2020 (2/2023) {2/2023}	217.35 (N.A.) {217.35}	214.18	100
		182	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3-2019	12/2022 (1/2023) {1/2023}	237.51 (N.A.) {237.51}	215.47	100

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		183	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3-2016	9/2019 (11/2022) {4/2025}	373.07 (534.41) {534.41}	382.50	99.81
		184	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (9/2025) {9/2025}	429.52 (794.74) {794.74}	321.40	90.38
		185	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (2/2023) {4/2025}	387.00 (688.12) {688.12}	389.81	99.72
		186	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (8/2024) {4/2025}	500.09 (698.81) {698.81}	393.53	98.88
		187	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756)	3-2018	9/2022 (1/2023) {7/2024}	285.68 (N.A.) {285.68}	193.90	100
		188	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU- MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (8/2022) {8/2025}	215.79 (N.A.) {215.79}	127.85	68.29
		189	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU- MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (6/2023) {9/2025}	323.98 (N.A.) {323.98}	112.43	51.23
SIKKIM	CIVIL AVIATION	190	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	24.80	9.75

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	DEPARTMENT OF HIGHER EDUCATION	191	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (<i>Sikkim Universi</i>) (<i>N44000002</i>)	8-2020	1/2025 (N.A.) {12/2024}	314.06 (N.A.) {303.55}	157.24	54
	POWER	192	TEESTA VI HE PROJECT (<i>NHPC</i>) (<i>N18000325</i>)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	4,141.77	66.31
		193	RANGIT IV HE PROJECT (<i>NHPC</i>) (<i>N18000326</i>)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,431.82	85.82
	RAILWAYS	194	SEVOK RANGPO, NEFR (<i>NFR</i>) (<i>N22000102</i>)	4-2008	12/2015 (12/2027) {12/2027}	1,339.48 (11,963.43) {11,963.43}	8,437.92	73.5
	ROAD TRANSPORT AND HIGHWAYS	195	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (<i>NHIDCL</i>) (<i>N24000767</i>)	3-2017	4/2022 (5/2022) {12/2023}	375.80 (N.A.) {375.80}	288.32	96.55
		196	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (<i>NHIDCL</i>) (<i>N24000768</i>)	11-2017	10/2020 (8/2023) {4/2024}	290.05 (N.A.) {290.05}	218.36	100
		197	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (<i>NHIDCL</i>) (<i>N24001261</i>)	8-2020	4/2023 (N.A.) {4/2025}	311.00 (N.A.) {273.78}	257.86	94.79
		198	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (<i>NHIDCL</i>) (<i>N24001262</i>)	7-2020	4/2023 (8/2024) {4/2025}	345.38 (395.59) {395.59}	362.61	90.44
		199	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (<i>NHIDCL</i>) (<i>N24001251</i>)	3-2019	4/2022 (N.A.) {3/2025}	402.94 (N.A.) {402.94}	247.12	76.54

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		200	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (11/2024) {3/2025}	295.97 (N.A.) {295.97}	248.39	94.74
		201	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3-2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	0
		202	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (10/2024) {12/2025}	230.45 (244.91) {244.91}	206.95	81.86
		203	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (7/2025) {7/2025}	493.42 (478.79) {478.79}	302.83	49.71
		204	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (6/2025) {12/2025}	816.79 (786.60) {786.60}	326.82	50.11
		205	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (10/2023) {12/2025}	292.80 (N.A.) {292.80}	195.98	59.65
		206	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (10/2023) {12/2025}	183.31 (439.56) {439.56}	355.31	51.85
		207	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (8/2024) {12/2025}	262.84 (414.20) {414.20}	221.86	47.56

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		208	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1-2021	9/2023 (4/2025) {12/2025}	332.20 (N.A.) {348.92}	149.38	41.04
		209	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (4/2025) {6/2025}	410.60 (379.30) {379.30}	230.03	69.98
		210	SPECIAL PROTECTION WORK ON REHABILITATION AND RESTORATION OF SLIDING AND SINKING ZONE FROM RANGPO TO (NHIDCL) (N24001913)	3-2017	6/2022 (N.A.) {6/2022}	165.56 (N.A.) {165.56}	-	71.74
		211	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (1/2026) {1/2026}	385.15 (N.A.) {385.15}	170.32	80.5
TRIPURA	PETROLEUM	212	GRASS ROOT RAIL FED DEPOT AT SEKEREKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (9/2025) {9/2025}	656.00 (N.A.) {656.00}	383.51	80.12
	ROAD TRANSPORT AND HIGHWAYS	213	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM SECTION PKG-4 (NHIDCL) (N24002228)	1-2024	12/2026 (N.A.) {12/2026}	726.90 (N.A.) {726.90}	-	0
		214	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (5/2025) {5/2025}	456.88 (N.A.) {456.88}	117.39	48.94
		215	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	63.55	18.2
		216	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH- 8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	18.44	6.12

**Table:-6. Project List: Ongoing Projects of North-East Region during 4th Quarter
(January-March),2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		217	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	7.56	15.6
		218	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	46.60	21.84
		219	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	8.31	5
		220	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	-	0
		221	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {9/2025}	195.95 (N.A.) {195.95}	37.10	38.44
		222	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (3/2024) {12/2025}	354.79 (N.A.) {354.79}	34.08	59
		223	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {3/2025}	201.99 (N.A.) {287.47}	144.07	98
		224	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (10/2023) {11/2024}	159.13 (171.50) {171.50}	84.33	100
		225	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (2/2024) {12/2024}	277.50 (302.02) {302.02}	260.38	99.94
			Total			183266.23 (-) {256576.95}	150915.37	

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ANDAMAN AND NICOBAR ISLANDS	<u>CIVIL AVIATION</u>	1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR (AAI) (N04000073)	10-2013	9/2018 (6/2023) {6/2023}	417.23 (707.73) {707.73}	698.80	100
	<u>RAILWAYS</u>	2	LUDHIANA KILA RAIPUR (19 KMS) WITH FREIGHT LINE AT GILL STATION ON LDH-JHL SECTION (NR) (N22000584)	3-2019	3/2025 (N.A.) {10/2025}	235.72 (N.A.) {235.72}	49.11	53
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	3	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N (NHIDCL) (N24000745)	3-2017	12/2019 (3/2023) {9/2024}	409.85 (N.A.) {409.85}	214.23	94.59
		4	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O (NHIDCL) (N24000749)	3-2018	9/2020 (11/2022) {12/2024}	234.27 (N.A.) {234.27}	126.50	80.26
		5	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 (MoRTH) (N24000820)	11-2017	11/2019 (N.A.) {11/2019}	237.80 (N.A.) {238.00}	222.13	98.23
		6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000821)	11-2017	11/2019 (N.A.) {11/2019}	257.34 (N.A.) {238.00}	214.90	100
		7	AJANTHA TO BULDHANA (MoRTH) (N24001008)	2-2017	7/2019 (N.A.) {12/2023}	401.00 (401.00) {401.00}	260.08	97
		8	MAJOR BRIDGE OVER MIDDLE STRAIT CREEK (NHIDCL) (N24002207)	12-2024	2/2026 (N.A.) {2/2026}	371.80 (207.99) {207.99}	-	1.3

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ANDHRA PRADESH		9	PACKAGE-3A (NHIDCL) (N24002208)	2-2018	9/2025 (3/2024) {9/2025}	207.54 (154.01) {154.01}	16.21	32.38
		10	PACKAGE-3B (NHIDCL) (N24002209)	2-2018	11/2025 (N.A.) {11/2025}	183.47 (N.A.) {183.47}	-	0
	CIVIL AVIATION	11	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT (AAI) (N04000089)	8-2017	2/2020 (12/2021) {1/2024}	177.10 (N.A.) {177.10}	143.08	100
		12	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT (AAI) (N04000091)	4-2020	3/2023 (6/2025) {6/2025}	611.80 (N.A.) {611.80}	426.46	70
		13	RAJAHMUNDRY AIRPORT: CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUD (AAI) (N04000103)	12-2022	8/2025 (N.A.) {8/2025}	347.15 (347.15) {347.15}	67.86	41
		14	KADAPPA AIRPORT- CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUDING MA (AAI) (N04000106)	3-2023	1/2026 (N.A.) {1/2026}	265.91 (N.A.) {265.91}	39.49	25
	DEPARTMENT OF HIGHER EDUCATION	15	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE (CPWD EDUCATION) (N42000005)	2-2019	6/2020 (N.A.) {6/2020}	655.34 (N.A.) {655.34}	366.21	95

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		16	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT (CPWD EDUCATION) (N42000007)	9-2019	9/2022 (N.A.) {6/2024}	588.72 (656.39) {656.39}	666.18	100
	PETROLEUM	17	VISAKH REFINERY MODERNISATION PROJECT (HPCL) (N16000235)	7-2016	7/2020 (10/2024) {12/2024}	20,928.00 (30,609.00) {30,609.00}	28,002.00	100
		18	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT (ONGC) (N16000247)	3-2016	6/2020 (3/2025) {6/2025}	34,012.00 (N.A.) {34,012.00}	32,565.18	96.1
		19	REVAMPING OF FACILITIES AT VIZAG TERMINAL (IOCL) (N16000343)	4-2018	4/2022 (3/2025) {3/2025}	355.00 (N.A.) {355.00}	249.36	100
		20	SWRO II WITH LLPH FACILITIES (HPCL) (N16000378)	9-2019	7/2020 (N.A.) {3/2025}	196.26 (196.26) {196.26}	196.26	100
		21	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY (HPCL) (N16000432)	9-2021	6/2024 (3/2026) {3/2026}	160.00 (220.00) {220.00}	50.04	54.9
		22	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS (IOCL) (N16000485)	3-2022	3/2030 (N.A.) {3/2030}	1,420.00 (N.A.) {1,420.00}	143.26	6.1
		23	MULTI-PRODUCT PIPELINE FROM KRISHNAPATNAM COASTAL INSTALLATION TO THE PROPOSED INSTALLATION AT HYDER (BPCL) (N16000499)	9-2019	3/2025 (N.A.) {10/2025}	1,932.00 (N.A.) {1,932.00}	1,491.63	82.4

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		24	HP TRIJET UNIT IN VR (HPCL) (N16000535)	7-2024	7/2027 (N.A.) {7/2027}	193.00 (N.A.) {193.00}	0.38	16
		25	CONSTRUCTION OF AVIATION FUEL FARM FACILITIES AT BHOGAPURAM AIRPORT (HPCL) (N16000538)	8-2024	3/2026 (N.A.) {3/2026}	240.00 (N.A.) {240.00}	10.01	20.2
		26	VISAKHA RAIPUR PIPELINE PROJECT (HPCL) (N16000539)	9-2024	9/2027 (N.A.) {9/2027}	2,212.00 (N.A.) {2,212.00}	2.18	2.45
	POWER	27	TRANSMISSION SCHEME FOR SOLAR ENERGY ZONE IN ANANTHPURAM (2500MW) AND KURNOOL (1000MW) (PGCIL) (N18000380)	9-2023	3/2025 (N.A.) {9/2025}	1,249.00 (N.A.) {1,249.00}	340.81	52
		28	AUGMENTATION OF 1500MVA 3RD 765/400KV TRANSFORMATION CAPACITY AT KURNOOL NEW SUBSTATION (PGCIL) (N18000395)	5-2023	9/2025 (N.A.) {9/2025}	164.00 (N.A.) {164.00}	66.00	15
	RAILWAYS	29	KOTLPALLI-NARASAPUR (NL) (SCR) (SCR) (220100265)	12-2001	3/2009 (N.A.) {3/2027}	1,045.20 (N.A.) {2,500.98}	1,150.84	0
		30	NADIKUDE-SRI KALAHASTI (SCR) (N22000286)	4-2011	3/2021 (N.A.) {5/2027}	2,288.70 (N.A.) {3,122.35}	1,919.57	0
		31	GUNTUR-GUNTAKAL (SCR) (N22000368)	4-2016	3/2022 (N.A.) {12/2025}	3,631.00 (N.A.) {3,887.48}	3,449.46	0
		32	VIJAYAWADA-GUDUR (RVNL) (N22000369)	4-2015	12/2023 (N.A.) {12/2024}	3,246.26 (N.A.) {6,238.67}	5,883.89	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		33	KOTTAVALSA - KORAPUT DOUBLING (ECOR) (N22000377)	4-2015	3/2022 (N.A.) {3/2022}	2,499.71 (N.A.) {2,499.71}	1,900.38	69.5
		34	PENUKONDA-DHARMAVARAM, EXCL. DHARMAVARAM (41.5 KM) (SWR) (N22000555)	4-2019	3/2026 (N.A.) {12/2025}	294.67 (307.66) {307.66}	197.19	41
		35	MALUGUR-PALASAMUDRAM (17.98 KM) (PB#29/NR/2022-23) (SWR) (N22000556)	9-2022	12/2025 (N.A.) {12/2026}	323.14 (342.41) {342.41}	46.89	12
		36	DOUBLING BETWEEN GOOTY- PENDAKALLU (29.225) (SCR) (N22000585)	3-2023	3/2027 (N.A.) {3/2027}	351.83 (N.A.) {351.83}	-	0
		37	VIJAYAWADA KAZIPET BYEPASS LINE (SCR) (N22000586)	4-2016	12/2025 (N.A.) {12/2025}	226.72 (N.A.) {226.72}	228.06	0
		38	RENIGUNTA WADI GOOTY - BYPASS (SCR) (N22000587)	4-2016	12/2025 (N.A.) {12/2025}	302.00 (N.A.) {302.00}	203.77	50
	ROAD TRANSPORT AND HIGHWAYS	39	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES (MoRTH) (N24000301)	3-2015	10/2015 (5/2021) {5/2021}	271.45 (N.A.) {271.45}	238.23	100
		40	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 (NHAI) (N24000811)	3-2018	12/2020 (12/2022) {12/2024}	314.43 (N.A.) {348.72}	85.61	67.72
		41	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 (MoRTH) (N24000931)	11-2016	5/2017 (N.A.) {11/2024}	290.15 (N.A.) {236.16}	205.02	90

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		42	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG (MoRTH) (N24000937)	3-2018	8/2018 (N.A.) {11/2024}	289.67 (290.00) {285.29}	254.19	98.5
		43	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH- 214(NH216)(KAKINAD (MoRTH) (N24000964)	8-2016	1/2017 (N.A.) {5/2025}	350.61 (N.A.) {411.18}	457.55	98.2
		44	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 (MoRTH) (N24000969)	1-2017	9/2017 (N.A.) {6/2025}	263.45 (N.A.) {263.45}	261.15	85
		45	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) (NHAI) (N24001301)	11-2019	1/2024 (N.A.) {7/2024}	1,601.10 (N.A.) {1,601.10}	1,341.86	85.86
		46	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU- GONDIGUDA SECT (MoRTH) (N24001386)	8-2020	3/2021 (N.A.) {6/2025}	222.61 (N.A.) {222.61}	173.53	95
		47	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI (NHAI) (N24001476)	9-2021	9/2022 (9/2024) {6/2025}	517.05 (N.A.) {655.06}	486.82	85.13
		48	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP (NHAI) (N24001477)	9-2021	9/2022 (9/2024) {6/2025}	622.00 (N.A.) {817.91}	505.64	71.28

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		49	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16 (NHAI) (N24001817)	2-2019	3/2023 (10/2024) {10/2024}	757.45 (N.A.) {757.45}	606.20	97.82
		50	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) (NHAI) (N24001818)	2-2021	1/2025 (N.A.) {1/2025}	818.73 (N.A.) {1,105.00}	548.69	23.73
		51	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) (NHAI) (N24001819)	3-2021	1/2025 (N.A.) {1/2025}	1,102.63 (N.A.) {1,303.00}	1,072.39	90.8
		52	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) (NHAI) (N24001820)	2-2021	12/2024 (N.A.) {12/2024}	1,484.83 (N.A.) {1,768.00}	1,476.55	86.82
		53	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP (NHAI) (N24001821)	11-2020	10/2024 (N.A.) {10/2024}	1,137.74 (N.A.) {1,289.00}	1,256.44	93.73
		54	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE (NHAI) (N24001822)	12-2020	10/2024 (N.A.) {10/2024}	1,075.27 (N.A.) {1,307.00}	1,068.78	79.68
		55	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A (NHAI) (N24001823)	1-2022	1/2025 (1/2023) {1/2025}	1,852.12 (N.A.) {1,787.00}	774.62	82.75
		56	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP (NHAI) (N24001824)	3-2020	1/2024 (12/2024) {12/2024}	1,863.09 (N.A.) {2,238.00}	1,227.61	98.45

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		57	6L KANTAKAPALLE ? SABBAVARAM SECTION OF NH-130CD ROAD FROM KM 445.100 TO KM 464.662 (PKG-4) (NHAI) (N24001836)	2-2021	10/2024 (N.A.) {12/2025}	824.29 (N.A.) {924.00}	393.10	70
		58	6L JAKKUVA ? KORLAM SECTION OF NH-130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) (NHAI) (N24001837)	2-2021	3/2024 (7/2024) {6/2025}	663.60 (N.A.) {768.00}	345.23	97.74
		59	6L ALURU - JAKKUVA SECTION OF NH- 130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) (NHAI) (N24001838)	2-2021	3/2024 (N.A.) {6/2025}	922.50 (N.A.) {1,128.68}	473.69	80
		60	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA (NHAI) (N24001841)	12-2022	9/2025 (N.A.) {2/2026}	912.94 (N.A.) {912.94}	238.59	51.72
		61	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 (NHAI) (N24001842)	12-2022	11/2025 (N.A.) {11/2025}	750.81 (N.A.) {750.81}	145.15	41.78
		62	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH (NHAI) (N24001843)	12-2022	11/2025 (N.A.) {11/2025}	992.89 (N.A.) {992.89}	163.04	37.4
		63	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. (NHAI) (N24001844)	12-2022	10/2025 (N.A.) {10/2025}	1,058.90 (N.A.) {1,058.90}	249.75	40.86

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		64	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 (NHAI) (N24001845)	2-2023	10/2025 (N.A.) {10/2025}	1,253.24 (N.A.) {1,253.24}	154.53	14.25
		65	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. (NHAI) (N24001846)	2-2023	10/2025 (N.A.) {10/2025}	1,200.42 (N.A.) {1,200.42}	57.89	4.5
		66	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA (NHAI) (N24001847)	1-2023	11/2025 (N.A.) {11/2025}	956.14 (N.A.) {956.14}	176.19	35.14
		67	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTALA 196.000 KM. PACK (NHAI) (N24001848)	2-2023	10/2025 (N.A.) {10/2025}	909.02 (N.A.) {909.02}	96.80	11.05
		68	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 (NHAI) (N24001849)	5-2022	7/2025 (N.A.) {9/2025}	1,063.72 (N.A.) {1,063.72}	423.17	66.57
		69	CONSTRUCTION OF 4-LANE HIGHWAY FROM SAMARLAKOTA TO ACHAMPETA JUNCTION (FROM KM. 0.000 TO KM. 12.250 (NHAI) (N24001856)	5-2023	8/2025 (N.A.) {8/2025}	648.75 (N.A.) {648.75}	191.08	54.13
		70	4 LANING OF BATHALAPALLI TO MUDIGUBBA SECTION (DESIGN CHAINAGE KM. 96.300 TO 129.300) INCLUDING BATH (MoRTH) (N24001931)	3-2022	2/2025 (N.A.) {2/2025}	536.00 (N.A.) {536.00}	393.81	98

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		71	2L+PS FROM KM. 0+000 TO KM. 32+000 (MUDIGUBBA TO PUTTAPARTHI) OF NH-342 (MoRTH) (N24001932)	3-2022	9/2024 (N.A.) {6/2025}	401.72 (N.A.) {401.72}	189.74	80
		72	MULAKALACHERUVU TO MADANAPALLE SECTION OF NH42 FROM KM 202.050 TO KM 245.640 EXCLUDING RETAINED STRE (MoRTH) (N24001933)	12-2021	12/2024 (N.A.) {12/2024}	480.10 (N.A.) {480.10}	443.87	100
		73	NH440 RAYACHOTY TOVEMPALLI 2LPS (MoRTH) (N24001934)	12-2021	5/2024 (N.A.) {7/2025}	439.82 (N.A.) {439.82}	193.63	27
		74	4 LANE WITH PAVED SHOULDER FROM KM 0.000 TO KM 51.119 OF TADIPATRI TO MUDDANUR OF NH67 (MoRTH) (N24001935)	3-2022	8/2025 (N.A.) {8/2025}	724.17 (N.A.) {724.17}	464.48	97.38
		75	NH165 FROM KM 0.000 TO KM 64.020 PAMARRU TO AKIVEEDU SECTION TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001939)	3-2020	9/2023 (N.A.) {12/2025}	529.24 (N.A.) {529.24}	312.17	52
		76	2LPS FROM KM36.400 TO KM. 107.224 OF NH167BG FROM DUTTALUR TO KAVALI SECTION (MoRTH) (N24001942)	3-2021	7/2024 (N.A.) {3/2025}	423.67 (N.A.) {423.67}	228.15	61
		77	NH167B FROM KM 99.103 CS PURAM TO KM 143.320 MALAKONDA TO 2LPS (MoRTH) (N24001949)	12-2021	3/2024 (N.A.) {1/2025}	277.30 (N.A.) {277.30}	195.88	98
		78	NH167B FROM KM.143.320 MALAKONDA TO 189.050 SINGARAYAKONDA ON NH 16 TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001950)	3-2021	2/2025 (N.A.) {2/2025}	369.81 (N.A.) {369.81}	303.78	98.2

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		79	NH167AD FROM MACHERLA TO DACHEPALLI FROM KM.0.000 TO 43.659 TO 2LPS (MoRTH) (N24001951)	1-2022	1/2025 (N.A.) {1/2025}	403.22 (N.A.) {403.22}	291.77	97
		80	NH 167 B KADAPA NELLORE BORDER TO CSPURAM I.E. FROM KM 58.635 TO KM 99.409 (MoRTH) (N24001952)	3-2022	8/2025 (N.A.) {8/2025}	285.50 (N.A.) {285.50}	195.59	95
		81	NH-30-BHADRACHALAM TO KONTA SECTION 2LPS (MoRTH) (N24001953)	12-2021	9/2024 (N.A.) {3/2025}	388.71 (N.A.) {388.71}	222.15	80
		82	WIDENING TO 2LPS OF RAMPACHODAVARAM - KOYYURU SECTION OF NH516E FROM KM.43.700 TO KM 113.820 (MoRTH) (N24001954)	3-2022	1/2025 (N.A.) {1/2025}	568.12 (N.A.) {568.12}	341.83	91
		83	GUDIWADA TOWN 2 LANE ROB AND ROAD IMPROVEMENT OF NH165 IN REPLACEMENT OF LC NO 3ESPL3 AT KM 231.700 (MoRTH) (N24001955)	3-2022	5/2025 (N.A.) {5/2025}	317.22 (N.A.) {317.22}	184.83	80
		84	2LPS FROM GONDIGUDA TO ARAKU BHALLAGUDA KM 27.480 TO KM 51.772 SECTION OF NH 516E (MoRTH) (N24001956)	8-2020	9/2023 (N.A.) {12/2024}	296.66 (N.A.) {296.66}	217.41	87.49
		85	2LPS OF KOYYURU TO CHAPRATHIPALEM SECTION OF NH 516E (MoRTH) (N24001957)	8-2020	7/2024 (N.A.) {6/2025}	349.29 (N.A.) {349.29}	208.04	76
		86	2LPS OF CHAPRATHIPALEM TO LAMBASINGI SECTION OF NH 516E (MoRTH) (N24001958)	8-2020	10/2024 (N.A.) {6/2025}	311.22 (N.A.) {311.22}	148.54	72

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		87	4 LANE FROM KM 56.400 TO KM 120.300 FROM B.KOTHAPALLI JUNCTION TO GORANTLA OF NH 716G (MoRTH) (N24001959)	3-2022	9/2025 (N.A.) {9/2025}	839.98 (N.A.) {839.98}	372.51	67
		88	4L GREENFIELD ROAD CONNECTING NORTH AND SOUTH INDUSTRIAL CLUSTER OF KHANDALERU CREEK NEAR KRISHNAPAT (NHAI) (N24001979)	8-2022	9/2025 (N.A.) {9/2025}	609.43 (N.A.) {609.43}	25.24	47.1
		89	4 LANING OF NH 544D FROM EXISTING KM 346.300 OF NH 44 (DESIGN CHAINAGE KM 0.000) TO KM 39.380 (DESIG (NHAI) (N24001980)	10-2022	7/2025 (N.A.) {7/2025}	907.76 (N.A.) {907.76}	381.66	80.52
		90	CONSTRUCTION OF SIX LANING OF NAIDUPETA JUNCTION - TURPUKANUPUR SECTION FROM KM.57+046 TO KM.91+927 (NHAI) (N24001981)	7-2022	10/2025 (N.A.) {10/2025}	1,398.84 (N.A.) {1,398.84}	58.68	11.22
		91	4L PS FROM KURNOOL (EXISTING KM. 5.400 OF NH-40/DESIGN KM.0.000) TO MANDLEM (EXISTING KM.38.000/DESI (NHAI) (N24001982)	3-2023	10/2025 (N.A.) {10/2025}	827.39 (N.A.) {827.39}	331.84	99.15
		92	4 LANING FROM EXISTING KM 39.380 (DESIGN CH. 37.000) TO KM 74.450 (DESIGN CH. 69.000) OF MUCHUKOTA ? (NHAI) (N24001983)	10-2022	8/2025 (N.A.) {8/2025}	972.63 (N.A.) {1,055.23}	309.39	50.16
		93	4L PS FROM MANDLEM (EXISTING KM. 38.000/DESIGN KM.30.600) TO ATMAKUR (EXISTING KM.73.000/DESIGN KM 6 (NHAI) (N24001984)	3-2023	10/2025 (N.A.) {10/2025}	887.28 (N.A.) {887.28}	233.90	68.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		94	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-II) FROM KM.96.000 TO KM 127.000 (BAIREDDYPALLE TO BANGAR (NHAI) (N24001985)	3-2021	6/2025 (N.A.) {6/2025}	1,942.94 (2,171.00) {2,171.00}	1,546.07	60.15
		95	4L OF PILERU TO KALUR SECTION FROM KM 55.900 TO KM 92.800 AND KM 94.500 TO KM 95.717 (NHAI) (N24001986)	10-2023	4/2025 (N.A.) {4/2025}	1,047.32 (N.A.) {1,047.32}	301.20	82.5
		96	CONSTRUCTION OF 1 NOS ROB, 2 NOS VUPS, SERVICE ROADS, PROVISION OF LIGHTING AND CONSTRUCTION OF OTHE (NHAI) (N24001987)	6-2023	12/2024 (N.A.) {12/2024}	152.05 (N.A.) {152.05}	133.08	76.61
		97	6L OF CHITTOOR TO THATCHUR FROM KUMARAJAPET TO VEERA KAVERI RAJA PURAM FROM KM 43.800 TO KM 61.380 O (NHAI) (N24001988)	2-2021	10/2025 (N.A.) {10/2025}	591.99 (703.00) {703.00}	496.65	56.95
		98	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED HIGHWAY FROM CHILLAKURU CROSS ROAD TO TURPUKANUPUR KM 0+000 (NHAI) (N24002033)	7-2022	12/2025 (N.A.) {12/2025}	909.47 (N.A.) {909.47}	97.03	24.84
		99	COMPLETION OF BALANCE WORKS PENDING IN BIT AND PIECES (INCOMPLETE STRETCH AT 7 LOCATIONS) AND LISTED (NHAI) (N24002103)	9-2022	1/2025 (N.A.) {4/2025}	166.52 (N.A.) {166.52}	49.12	82
		100	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NARAYANMPET (CH. 203+500) TO CHANDRASEKHARPURAM (CH. 22 (NHAI) (N24002122)	2-2024	2/2026 (N.A.) {2/2026}	813.66 (N.A.) {813.66}	91.45	20.1

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		101	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM CHANDRASEKHARAPURAM (CH. 228+000) TO POLAVARAM (CH. 260 (NHAI) (N24002123)	2-2024	2/2026 (N.A.) {2/2026}	1,292.65 (N.A.) {1,292.65}	134.57	11.6
		102	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM POLAVARAM (CH. 260+000) TO MARRIPUDI (CH. 285+500) OF [(NHAI) (N24002124)	2-2024	2/2026 (N.A.) {2/2026}	747.29 (N.A.) {747.29}	118.29	21.3
		103	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MARRIPUDI (CH. 285+500) TO SOMAVARAPPADU (CH. 314+600) (NHAI) (N24002125)	2-2024	2/2026 (N.A.) {2/2026}	976.40 (N.A.) {976.40}	196.90	35.18
		104	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM SOMAVARAPPADU (CH.314.600) TO MUPPAVARAM (CH.343+240) O (NHAI) (N24002126)	2-2024	2/2026 (N.A.) {2/2026}	1,103.89 (N.A.) {1,103.89}	91.99	8.9
		105	4-LANE WITH PAVED SHOULDERS FROM KM 32/0 TO KM 79/650 (DESIGN CHAINAGE KM 32+000 TO KM 78+760) PUTTA (MoRTH) (N24002139)	3-2023	12/2025 (N.A.) {11/2025}	1,318.57 (N.A.) {1,318.57}	377.10	56
		106	SOMAYAJULAPALLI ? DHONE SECTION OF NH ? 340B FROM KM.0/0 TO 56/200 [DESIGN CH. KM 0/00 TO KM 53/33] (MoRTH) (N24002140)	4-2023	12/2025 (N.A.) {12/2025}	629.73 (N.A.) {629.73}	302.57	62
		107	2 LANE WITH PAVED SHOULDER CONFIGURATION FROM SEETHARAMAPURAM TO DUTTALURU SECTION OF NH-167 BG FROM (MoRTH) (N24002141)	6-2023	7/2025 (N.A.) {7/2025}	364.07 (N.A.) {364.07}	227.21	98

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		108	2-LANE WITH PAVED SHOULDER CONFIGURATION OF LAMBASINGI TO PADERU SECTION (KM 205+000 TO KM 253+974) (MoRTH) (N24002142)	8-2023	11/2025 (N.A.) {11/2025}	361.24 (N.A.) {361.24}	57.28	26
		109	BYPASS ROAD TO ADONI TOWN CONNECTING NH-167 (HAGARI - JADCHARLA ROAD) FROM KM.62/700 TO 71/400 IN KU (MoRTH) (N24002143)	8-2023	2/2026 (N.A.) {2/2026}	361.24 (N.A.) {361.24}	97.95	52
		110	VODAREVU-CHILAKALURIPET SECTION (DESIGN CHAINAGE 0+00 TO 47+000) OF NH-167A (PACKAGE-I) (MoRTH) (N24002144)	8-2023	2/2026 (N.A.) {2/2026}	1,064.24 (N.A.) {1,064.24}	470.13	60
		111	TADIPATRI BYPASS (KM 0+000 TO KM 6+285) OF 4-LANE ON NH-67 IN ANANTAPURAMU (MoRTH) (N24002145)	11-2023	3/2026 (N.A.) {3/2026}	159.66 (N.A.) {159.66}	60.76	63.5
		112	KURNOOL/KADAPA BORDER- JAMMALAMADUGU SECTION OF NH- 167K I.E. DESIGN CH. KM 248+010 TO KM 269+900 (MoRTH) (N24002146)	11-2023	11/2025 (N.A.) {11/2025}	292.63 (N.A.) {292.63}	35.36	17
		113	DORNALA TO KUNTA JUNCTION FROM DESIGN CHAINAGE KM 244+000 TO 267+990 SECTION OF NH-765 (PACKAGE-2) (MoRTH) (N24002147)	12-2022	1/2024 (N.A.) {3/2026}	244.83 (N.A.) {244.83}	96.32	70
		114	PADERU BYPASS (KM 0+000 TO KM 13+000) OF 2- LANE WITH PAVED SHOULDER ON NH-516E (MoRTH) (N24002148)	3-2023	3/2024 (N.A.) {2/2026}	244.43 (N.A.) {244.43}	22.77	0
		115	DAVUALAPALLY TO MALLAPALEM SECTION {DESIGN CH. KM 133+922 TO KM 154+216 (EXISTING CH. KM 133+922 TO (MoRTH) (N24002149)	1-2024	2/2024 (N.A.) {2/2026}	393.61 (N.A.) {393.61}	96.06	24

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
<u>ARUNACHAL PRADESH</u>		116	DEVELOPMENT OF SIX LANE ACCESS CONTROLLED GREEN FIELD HIGHWAY FROM KAVULAKUNTALA (KM.196+000) TO NARA (NHAI) (N24002215)	2-2023	2/2027 (N.A.) {2/2027}	1,092.18 (N.A.) {1,092.18}	0.14	0
		117	ACCESS CONTROLLED HIGHWAY OF 4 LANE WITH PAVED SHOULDERS FROM TN/AP BORDER (DESIGN CHAINAGE KM 61+51 (NHAI) (N24002217)	12-2024	12/2026 (N.A.) {12/2026}	1,346.82 (N.A.) {1,346.82}	-	3.71
	<u>WATER RESOURCES</u>	118	POLAVARAM IRRIGATION PROJECT (PPA) (N30000002)	2-2009	3/2020 (3/2024) {3/2026}	10,151.04 (N.A.) {55,548.87}	23,775.68	72.86
	<u>CIVIL AVIATION</u>	119	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (5/2025) {5/2025}	645.63 (N.A.) {712.15}	688.31	99.43
	<u>POWER</u>	120	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	23,753.28	96.1
		121	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	3,182.93	14.47
		122	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (3/2024) {3/2025}	180.57 (244.10) {180.57}	160.46	96.62
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	123	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685)	2-2017	4/2022 (11/2023) {11/2023}	167.28 (N.A.) {167.28}	145.20	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		124	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (6/2025) {6/2025}	1,718.59 (1,718.59) {1,718.59}	728.21	73.1
		125	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9-2016	12/2019 (8/2024) {9/2024}	568.92 (568.92) {568.92}	508.65	100
		126	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (5/2023) {3/2025}	256.66 (N.A.) {256.66}	-	63.59
		127	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (2/2025) {2/2025}	301.06 (N.A.) {301.06}	191.34	76.98
		128	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO (NHIDCL) (N24001245)	9-2020	5/2022 (10/2022) {3/2024}	353.90 (N.A.) {353.90}	41.82	25.38
		129	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE (MoRTH) (N24001291)	3-2019	3/2027 (N.A.) {3/2027}	421.48 (N.A.) {421.48}	365.83	100
		130	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292)	3-2019	3/2027 (N.A.) {3/2027}	543.05 (N.A.) {600.00}	588.85	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		131	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE (MoRTH) (N24001293)	3-2019	3/2027 (N.A.) {3/2027}	486.70 (N.A.) {486.70}	480.44	100
		132	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	389.68	95.26
		133	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH- 215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372)	2-2021	3/2024 (12/2024) {12/2024}	588.09 (N.A.) {588.09}	497.36	100
		134	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374)	6-2020	3/2027 (N.A.) {3/2027}	437.60 (N.A.) {437.60}	366.59	100
		135	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	179.53	40.57
		136	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (8/2024) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		137	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8-2020	4/2022 (2/2024) {9/2024}	294.04 (N.A.) {294.04}	147.13	100
		138	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (2/2024) {3/2025}	184.88 (N.A.) {184.88}	99.32	97.42

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		139	HUNLI TO HAYULIANG PKG-1 (NHIDCL) (N24002222)	2-2024	2/2028 (N.A.) {2/2028}	1,262.43 (N.A.) {1,262.43}	-	0.03
		140	HUNLI TO ITHUN BRIDGE SECTION (NHIDCL) (N24002223)	2-2024	1/2027 (N.A.) {1/2027}	275.50 (N.A.) {275.50}	-	0.07
		141	PANGO TO JORGING ROAD PKG-1 (NHIDCL) (N24002224)	1-2024	7/2027 (N.A.) {7/2027}	898.19 (N.A.) {898.19}	-	0
ASSAM	CIVIL AVIATION	142	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (8/2025) {8/2025}	1,142.00 (N.A.) {2,333.00}	1,750.24	83.87
	COAL	143	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290)	7-2022	11/2030 (N.A.) {11/2030}	159.77 (N.A.) {159.77}	81.45	0
		144	TIRAP OCP (CIL) (N06000291)	11-2022	11/2027 (N.A.) {11/2027}	289.46 (N.A.) {289.46}	105.55	0
	HEALTH AND FAMILY WELFARE	145	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (4/2023) {11/2024}	875.00 (873.92) {860.00}	787.90	99.35
	PETROLEUM	146	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (12/2024) {6/2025}	543.91 (726.93) {726.93}	491.56	93.89

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		147	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	15,390.82	71.88
		148	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	9,212.58	83.81
		149	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (2/2025) {5/2026}	412.00 (509.84) {509.84}	379.60	82.04
		150	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (9/2026) {9/2026}	277.00 (N.A.) {277.00}	175.69	65.11
		151	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (4/2025) {4/2025}	860.00 (N.A.) {860.00}	535.46	95
		152	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (3/2024) {6/2025}	430.76 (N.A.) {430.76}	307.70	81.97
		153	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	80.15	29

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		154	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (7/2027) {7/2027}	156.36 (156.36) {156.36}	36.52	26.5
		155	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (7/2027) {7/2027}	384.04 (N.A.) {384.04}	81.21	26.2
		156	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	97.22	89
		157	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	250.17	55.2
		158	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	169.86	42.8
		159	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	99.50	14.98
	RAILWAYS	160	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2022 (N.A.) {3/2027}	2,232.32 (N.A.) {4,983.94}	3,606.19	92.3
	ROAD TRANSPORT AND HIGHWAYS	161	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {4/2025}	437.39 (N.A.) {437.39}	541.08	94.36
		162	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	478.05	73.48

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		163	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1-1991	6/2019 (6/2019) {6/2025}	520.01 (N.A.) {520.01}	305.03	96.71
		164	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (7/2021) {6/2025}	289.99 (N.A.) {289.99}	233.23	87.62
		165	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {4/2025}	294.17 (N.A.) {294.17}	380.19	96.25
		166	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {4/2025}	252.00 (N.A.) {330.30}	215.64	85.81
		167	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	217.06	97.76
		168	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 (NHIDCL) (N24001248)	8-2020	4/2022 (N.A.) {7/2024}	208.84 (N.A.) {208.84}	193.59	100
		169	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (1/2025) {6/2025}	216.49 (241.52) {216.49}	111.59	82.79
		170	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,382.39	59.88

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		171	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (5/2025) {5/2025}	261.13 (N.A.) {261.13}	68.75	57.42
		172	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (4/2025) {4/2025}	217.50 (N.A.) {217.50}	88.99	68.03
		173	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.76	100
		174	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	137.01	71.71
		175	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (1,019.17) {925.47}	192.50	30.65
		176	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 (NHAI) (N24001432)	12-2021	8/2024 (3/2024) {8/2024}	300.00 (N.A.) {300.00}	439.65	100
		177	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	328.49	65.29
		178	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {5/2025}	625.64 (N.A.) {625.64}	550.60	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		179	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3-2022	7/2024 (N.A.) {10/2024}	215.27 (N.A.) {215.27}	151.29	100
		180	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {5/2025}	204.10 (N.A.) {204.10}	142.31	93.26
		181	FOUR LANING OF SRIRAMPUR- DHUBRI PKG-2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {6/2025}	909.02 (N.A.) {909.02}	509.89	94.64
		182	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (9/2024) {6/2024}	175.00 (N.A.) {175.00}	200.80	100
		183	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	567.75	72.3
		184	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {3/2025}	457.72 (N.A.) {457.72}	365.99	100
		185	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	110.74	35.13
		186	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {5/2025}	458.59 (N.A.) {458.59}	196.33	59.99

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		187	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	73.25	31.23
		188	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	391.08	60.55
		189	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	365.45	59.3
		190	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	417.14	56.45
		191	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	293.04	89.98
		192	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	275.46	90.4
		193	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	517.67	41.82

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		194	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	303.94	22.75
		195	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	395.28	22.3
		196	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	234.60	69.48
		197	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	125.69	12.64
		198	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3-2023	12/2025 (N.A.) {12/2026}	643.42 (N.A.) {643.42}	69.47	8.89
		199	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.87	100
		200	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	499.58	32.68
		201	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	983.58	61.75

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		202	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	280.91	49.51
		203	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	377.55	60.42
		204	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	279.86	39.87
		205	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	149.79	26.7
		206	BILASIPURA- GUWAHATI ROAD PKG-1 (NHIDCL) (N24002225)	2-2024	8/2027 (N.A.) {8/2027}	1,081.15 (N.A.) {1,081.15}	-	0
		207	SILCHAR-JIRIBAM PKG-1 (NHIDCL) (N24002226)	1-2024	1/2028 (N.A.) {1/2028}	957.95 (N.A.) {957.95}	-	0
BIHAR	CIVIL AVIATION	208	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II (AAI) (N04000082)	5-2018	10/2022 (6/2025) {6/2025}	1,216.90 (N.A.) {1,216.90}	962.08	87.64
		209	DARBHANGA:DEVELOPMENT OF NEW CIVIL ENCLAVE AT DARBHANGA, BIHAR. SH- CONSTRUCTION OF NEW TERMINAL BUI (AAI) (N04000112)	7-2024	7/2026 (N.A.) {7/2026}	911.66 (N.A.) {911.66}	68.14	12.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	DEPARTMENT OF HIGHER EDUCATION	210	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA (CPWD EDUCATION) (N28000100)	2-2016	6/2017 (N.A.) {1/2024}	496.18 (496.00) {460.00}	436.15	100
		211	PERMANENT CAMPUS FOR IIM BODH GAYA (CPWD EDUCATION) (N42000009)	9-2018	9/2020 (N.A.) {3/2025}	375.00 (N.A.) {375.00}	333.45	99.6
	PETROLEUM	212	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA (IOCL) (N16000386)	1-2020	4/2023 (12/2024) {8/2026}	14,810.00 (N.A.) {14,810.00}	10,482.63	84.4
		213	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA (IOCL) (N16000423)	6-2019	12/2029 (3/2030) {3/2030}	163.00 (N.A.) {163.00}	96.62	40.1
		214	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI (IOCL) (N16000453)	1-2022	4/2025 (N.A.) {5/2026}	389.00 (N.A.) {389.00}	32.60	28.6
		215	CITY GAS DISTRIBUTION PROJECTS AT GOPALGANJ SIWAN WEST CHAMPARAN EAST CHAMPARAN AND DEORIA DISTRICTS (BPCL) (N16000523)	12-2022	6/2030 (N.A.) {6/2030}	3,919.00 (N.A.) {3,919.00}	356.41	12.9
		216	CITY GAS DISTRIBUTION PROJECTS AT DARBHANGA, MADHUBANI, SUPAUL, SITAMARHI AND SHEOHAR DISTRICTS (BPCL) (N16000524)	12-2022	3/2030 (N.A.) {3/2030}	3,638.00 (N.A.) {3,638.00}	356.28	18.2
	POWER	217	BARH STPP(3X660MW) NTPC (NTPC) (180100242)	2-2005	10/2011 (7/2023) {3/2025}	8,692.97 (21,312.11) {21,312.11}	22,199.16	95

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		218	BUXAR THERMAL POWER PLANT (1320 MW) (SJVN) (N18000194)	3-2019	1/2024 (N.A.) {9/2025}	10,439.09 (N.A.) {12,999.36}	11,328.77	87.45
	RAILWAYS	219	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) (ECR) (220100257)	4-1997	(N.A.) {3/2027}	162.87 (614.45) {614.45}	465.66	51
		220	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR (ECR) (220100303)	4-2003	(N.A.) {12/2026}	528.65 (2,087.36) {2,087.36}	2,273.50	73
		221	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR (NFR) (N22000087)	9-2006	3/2019 (N.A.) {9/2025}	532.87 (2,132.03) {4,412.25}	3,730.67	87
		222	SAKRI-HASANPUR ROAD (NL) (ECR) (N22000171)	4-1999	(N.A.) {3/2027}	325.00 (735.20) {735.20}	594.78	78
		223	ARARIA-SUPAUL (NL) (ECR) (N22000177)	4-2008	(N.A.) {5/2025}	1,605.17 (1,605.17) {1,605.17}	1,614.26	32
		224	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA- BARDIBAS(NEPAL) GC (ECR) (N22000181)	4-2009	3/2020 (N.A.) {3/2026}	548.00 (548.00) {783.83}	544.31	75
		225	SAMASTIPUR-DARBANGHA (ECR) (N22000329)	5-2015	(N.A.) {10/2025}	380.00 (519.33) {519.33}	626.16	70
		226	KIUL - GAYA DOUBLING PROJECT (ECR) (N22000349)	12-2015	3/2020 (N.A.) {2/2025}	1,200.20 (1,200.20) {1,771.07}	1,800.43	99

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		227	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE (ECR) (N22000350)	12-2015	3/2020 (N.A.) {12/2025}	1,491.47 (1,491.47) {1,600.00}	1,680.42	77
		228	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM (ECR) (N22000472)	4-2016	3/2021 (N.A.) {6/2025}	744.04 (1,215.54) {1,215.54}	1,533.70	90
		229	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM (ECR) (N22000473)	4-2016	3/2021 (N.A.) {5/2025}	731.64 (1,185.73) {1,300.00}	1,463.21	96
		230	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, (ECR) (N22000476)	4-1991	(N.A.) {5/2025}	329.39 (803.09) {2,722.16}	2,752.37	90
		231	DARBHANGA - BYPASS LINE CONNECTING SHISHO HALT AND KAKARGHATI EXCL DARBHANGA YARD (7.64 KM) (ECR) (N22000523)	6-2019	6/2025 (N.A.) {10/2024}	983.62 (253.23) {415.00}	417.57	100
		232	BARAUNI- BACHWARA 3RD AND 4TH LINE (ECR) (N22000524)	7-2022	7/2027 (N.A.) {12/2025}	486.00 (N.A.) {486.00}	123.91	33
		233	JHAJHA - BATIA (UMBRELLA WORK PB#23/2018-19/NR) (ECR) (N22000526)	2-2019	6/2028 (N.A.) {12/2026}	496.47 (N.A.) {496.47}	2.53	0
		234	SONENAGAR BYE PASS LINE FROM CHIRALAPOTHU TO BAGHA BISHUNPUR (ECR) (N22000528)	10-2022	10/2027 (N.A.) {12/2026}	234.00 (223.69) {223.69}	22.57	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		235	KATIHAR-KUMEDPUR & KATIHAR-MUKURIA (64.5 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NFR) (N22000570)	8-2022	8/2027 (N.A.) {8/2027}	745.00 (N.A.) {745.00}	-	0
	ROAD TRANSPORT AND HIGHWAYS	236	PATNA-MUZZAFFARPUR (NHAI) (N24000165)	8-2010	2/2013 (N.A.) {12/2024}	671.30 (N.A.) {671.30}	1,830.13	97.78
		237	4-LANNING OF CHAPRA-HAJIPUR (NHAI) (N24000187)	1-2011	7/2013 (6/2025) {6/2025}	575.00 (N.A.) {575.00}	573.48	89.81
		238	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR (MoRTH) (N24000382)	1-2014	10/2019 (4/2025) {4/2025}	675.00 (N.A.) {780.77}	764.69	96.13
		239	FOUR LANING OF PATNA TO KOILWAR (NHAI) (N24000473)	8-2015	(N.A.) {}	556.07 (N.A.) {556.07}	-	0
		240	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 (NHAI) (N24000480)	12-2015	4/2019 (3/2025) {7/2025}	1,041.10 (567.00) {639.58}	553.73	97.57
		241	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 (NHAI) (N24000507)	12-2015	12/2019 (N.A.) {12/2024}	1,167.45 (N.A.) {1,182.94}	735.99	96
		242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 (MoRTH) (N24000531)	2-2016	11/2018 (N.A.) {5/2025}	319.68 (N.A.) {503.28}	453.00	98.8

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		243	CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-I-KM 40.00 TO KM 65.400 AND K (MoRTH) (N24000576)	2-2016	5/2016 (N.A.) {5/2025}	178.85 (N.A.) {278.54}	232.61	98.35
		244	PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-III-KM 156.5 (MoRTH) (N24000578)	2-2016	5/2016 (N.A.) {3/2025}	553.30 (N.A.) {706.39}	712.38	98
		245	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR (MoRTH) (N24000579)	1-2014	10/2016 (6/2025) {6/2025}	1,408.85 (N.A.) {2,138.16}	1,738.55	96.9
		246	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN (NHAI) (N24000665)	3-2017	3/2020 (12/2025) {12/2025}	672.89 (736.01) {830.31}	678.03	84.08
		247	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 (NHAI) (N24000696)	8-2017	2/2022 (10/2024) {5/2025}	950.64 (1,161.00) {1,168.33}	1,126.17	97
		248	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 (NHAI) (N24000714)	12-2017	10/2024 (4/2025) {12/2026}	2,598.00 (N.A.) {1,978.01}	1,381.14	75.04
		249	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I (NHAI) (N24000723)	1-2018	12/2021 (12/2024) {8/2025}	573.70 (644.50) {726.99}	492.33	81.22

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		250	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION (NHAI) (N24000724)	1-2018	4/2024 (N.A.) {}	895.39 (N.A.) {895.39}	1,632.71	0
		251	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER (NHAI) (N24000813)	3-2018	11/2021 (12/2024) {5/2025}	496.20 (470.18) {470.18}	399.41	97.4
		252	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND (MoRTH) (N24000943)	9-2018	6/2024 (5/2026) {5/2026}	1,478.40 (N.A.) {1,478.40}	894.55	67.3
		253	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 (MoRTH) (N24001201)	2-2019	9/2024 (N.A.) {9/2026}	2,926.42 (N.A.) {2,926.42}	1,274.37	54.64
		254	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT (NHAI) (N24001303)	10-2013	12/2020 (12/2024) {12/2024}	649.90 (N.A.) {750.00}	711.53	98.3
		255	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE (NHAI) (N24001304)	10-2013	11/2020 (12/2024) {12/2024}	446.97 (598.48) {740.50}	638.80	96.3
		256	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA (NHAI) (N24001305)	10-2013	11/2020 (12/2024) {12/2024}	464.09 (605.53) {765.12}	698.25	97.3

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		257	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N (NHAI) (N24001371)	10-2019	8/2023 (12/2025) {12/2025}	1,101.99 (N.A.) {1,101.99}	839.40	74.46
		258	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH-119D (PKG-III) (NHAI) (N24001697)	2-2023	2/2025 (N.A.) {12/2025}	1,358.00 (N.A.) {1,358.00}	183.47	13.51
		259	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH (NHAI) (N24001698)	8-2022	8/2024 (9/2025) {9/2025}	1,198.02 (N.A.) {1,198.02}	2.27	0
		260	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT- GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH-3 (NHAI) (N24001699)	3-2022	12/2024 (N.A.) {7/2025}	312.58 (N.A.) {312.58}	182.44	75.04
		261	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO (NHAI) (N24001700)	12-2021	3/2024 (12/2024) {12/2024}	552.55 (553.00) {553.00}	414.79	74.39
		262	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU (NHAI) (N24001701)	4-2022	4/2024 (9/2025) {9/2025}	1,769.50 (N.A.) {1,769.50}	3.12	0
		263	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT-GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH: (NHAI) (N24001702)	12-2021	9/2024 (N.A.) {5/2025}	184.90 (185.00) {185.00}	163.01	95.6

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		264	6 L OF AURANGABAD TO BIHAR- JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N (NHAI) (N24001703)	2-2022	5/2025 (N.A.) {5/2025}	786.81 (787.00) {787.00}	-	0
		265	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI (NHAI) (N24001704)	3-2021	3/2024 (9/2025) {9/2025}	1,020.84 (N.A.) {1,020.84}	89.52	0
		266	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C (NHAI) (N24001705)	3-2022	3/2024 (12/2025) {12/2025}	1,485.66 (N.A.) {1,485.66}	-	0
		267	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20 (NHAI) (N24001708)	9-2020	6/2024 (N.A.) {12/2024}	2,156.22 (N.A.) {2,156.22}	2,134.67	98.23
		268	BAKHTIYARPUR RAJAULI PKG-II FROM KM 54.405 TO KM 101.630 NH20 (NHAI) (N24001709)	9-2020	4/2023 (12/2024) {12/2024}	897.45 (N.A.) {1,090.00}	1,037.63	97.85
		269	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G (NHAI) (N24001711)	9-2020	3/2023 (12/2024) {12/2024}	939.43 (N.A.) {939.43}	370.62	100
		270	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO (NHAI) (N24001712)	8-2020	7/2023 (5/2025) {5/2025}	690.00 (N.A.) {690.00}	770.73	98.8
		271	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI?MOTIHARI- RAXAUL SECTION OF NH-28A FRO (NHAI) (N24001715)	12-2018	10/2020 (N.A.) {1/2024}	333.60 (466.59) {461.41}	460.38	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		272	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH 122B FROM KM 29.730 TO KM 72.348 IN STATE OF BIH (MoRTH) (N24001870)	2-2022	11/2024 (N.A.) {11/2025}	624.43 (N.A.) {624.43}	280.98	80
		273	WIDENING AND STRENGTHENING FROM KM 70.15 TO KM 121.025 OF NH- 80 (MoRTH) (N24001875)	3-2021	1/2025 (N.A.) {5/2025}	477.54 (N.A.) {477.54}	331.57	85.04
		274	WIDENING and STRENGTHENING FROM KM132.895 TO KM 190.15 NH-80 (MoRTH) (N24001876)	3-2021	3/2024 (N.A.) {9/2025}	566.15 (N.A.) {566.15}	239.20	54.2
		275	CONSTRUCTION OF NEW 4-LANE BRIDGE (PARALLEL TO EXISTING VIKRAMASHILA SETU)FROM KM 8+920 TO KM 13+375 (MoRTH) (N24001877)	7-2020	5/2027 (N.A.) {5/2027}	1,110.23 (N.A.) {1,110.23}	425.19	37.8
		276	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH-319A FROM KM 0 TO KM 45 IN STATE OF BIHAR UNDER (MoRTH) (N24001878)	2-2022	12/2024 (N.A.) {4/2025}	427.29 (N.A.) {427.29}	193.44	72
		277	CONSTRUCTION OF PROPOSED 4_LANE REVELGUNJ BYPASS NH-19 IN THE STATE OF BIHAR ON EPC MODE CONNECTING (MoRTH) (N24001879)	3-2022	7/2025 (N.A.) {7/2025}	295.24 (N.A.) {295.24}	77.05	45.15
		278	CONSTRUCTION OF 6- LANE BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD (NH- (NHAI) (N24002062)	3-2023	9/2027 (N.A.) {9/2027}	3,012.27 (N.A.) {3,012.27}	183.74	6.1
		279	BALANCE WORK - WB-10 (GANDAK BRIDGE) KM 402.00 TO KM 440.00 (DEVANPUR - KOTWA) (NHAI) (N24002063)	12-2021	1/2024 (N.A.) {6/2025}	210.05 (N.A.) {210.05}	103.33	68.58

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		280	PERMANENT RECTIFICATION OF 3 NOS. OF BLACK SPOTS IN PROJECT HIGHWAY NH-27 OF U.P BORDER - DEWAPUR - (NHAI) (N24002064)	12-2022	12/2025 (N.A.) {12/2025}	381.80 (N.A.) {381.80}	77.78	40.1
		281	4L GREENFIELD ALIGNMENT OF AMAS TO SHIVRAMPUR FROM 0.000 KM. TO 55.002 KM. OF NH 119 D (PKG-I) (NHAI) (N24002065)	2-2022	3/2025 (N.A.) {3/2025}	1,390.92 (N.A.) {1,390.92}	150.71	15
		282	4L GREENFIELD ALIGNMENT OF SHIVRAMPUR TO RAMNAGAR FROM KM. 55.002 TO KM. 109.300 OF NH 119 D (PKG-I) (NHAI) (N24002066)	2-2022	7/2025 (N.A.) {7/2025}	1,494.31 (N.A.) {1,494.31}	38.28	4.59
		283	IMPROVEMENT OF 2 LANE WITH PAVED SHOULDER OF STRETCH FROM BIKRAMGANJ DAWATH MELAYABAGH NAWANAGR -DUM (MoRTH) (N24002133)	3-2021	3/2025 (N.A.) {6/2025}	178.63 (N.A.) {178.63}	113.61	83.86
		284	CONSTRUCTION OF 4 LANE ROB AND ITS APPROACHES AT THE LEVEL OF CROSSING (L C NO. 29-B) OF KM 29 (EKAN (MoRTH) (N24002193)	3-2023	7/2026 (N.A.) {7/2026}	201.08 (N.A.) {201.08}	23.73	22.5
		285	CONSTRUCTION OF 6-LANE ELEVATED / EXTRA DOSE CABLE BRIDGE ON RIVER GANGA PARALLEL TO AND WESTERN SID (MoRTH) (N24002194)	1-2024	11/2027 (N.A.) {11/2027}	3,064.45 (N.A.) {3,064.45}	68.06	1.5
		286	ESTIMATE FOR IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM RAMNAGAR TO ROSEDA FROM (KM 3.500 TO 4 (MoRTH) (N24002195)	1-2022	4/2026 (N.A.) {4/2026}	495.16 (N.A.) {495.16}	129.17	9

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		287	CONSTRUCTION OF BHABHUA BYPASS FROM CH. 10+800(DESIGN CH. 10+800) TO CH. 19+860 (DESIGN CH. 18+150) (MoRTH) (N24002196)	2-2022	3/2026 (N.A.) {3/2026}	179.86 (N.A.) {179.86}	24.56	0.03
		288	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM JUNCTION OF NH-22 NEAR HAJIPUR TO JUNCTION OF NH-12 (MoRTH) (N24002197)	2-2024	2/2026 (N.A.) {2/2026}	226.15 (N.A.) {226.15}	9.77	11
		289	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF BH/WBBORDER-AMDABAD-MANIHARI SECTION FROM DESIGN KM (MoRTH) (N24002198)	1-2022	3/2026 (N.A.) {3/2026}	353.27 (N.A.) {353.27}	25.33	0
		290	PERMANENT RECTIFICATION OF 4 NOS. OF BLACKSPOTS ON NH 27 OF KOTWA MEHSI MUZAFFARPUR SECTION FROM (NHAI) (N24002220)	12-2022	11/2026 (N.A.) {11/2026}	410.75 (N.A.) {410.75}	34.83	17.71
		291	4L OF GREENFIELD ALIGNMENT FROM KM. 47.000 TO KM. 89.210 OF BALBHADARPUR TO BELA NAWDA SECTION OF NH (NHAI) (N24002221)	2-2022	3/2026 (N.A.) {3/2026}	2,185.75 (N.A.) {2,185.75}	513.47	10.34
	URBAN DEVELOPMENT	292	PATNA METRO RAIL CORPORATION LIMITED (PATNA METRO RAI) (N28000148)	2-2019	6/2024 (N.A.) {9/2024}	13,365.77 (N.A.) {13,925.50}	3,157.64	43.28
	WATER RESOURCES	293	SEWER NETWORK SPS AND STP BEGUSARAI (BUIDCO) (N30000026)	3-2018	7/2021 (12/2019) {4/2025}	230.06 (N.A.) {230.06}	255.06	96
		294	I AND D AND STP WORKS FOR BHAGALPUR (BUIDCO) (N30000027)	10-2017	9/2020 (11/2020) {4/2025}	254.13 (413.29) {413.29}	120.95	89

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		295	I AND D AND STP AT CHAPPRA (BUIDCO) (N30000028)	11-2018	12/2020 (N.A.) {2/2024}	236.15 (N.A.) {236.15}	150.75	100
		296	SEWER NETWORKS SPS AND STP HAJIPUR (BUIDCO) (N30000035)	3-2018	8/2021 (3/2018) {6/2025}	305.19 (N.A.) {305.19}	340.94	95
		297	SEWER NETWORKS, SPS AND STP, MUNGER (BUIDCO) (N30000036)	3-2018	10/2021 (3/2018) {6/2024}	294.02 (350.79) {522.85}	425.62	100
		298	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR (BUIDCO) (N30000037)	12-2014	3/2020 (N.A.) {6/2022}	225.77 (N.A.) {398.90}	363.79	100
		299	SAIDPUR SEWER NETWORK PATNA (BUIDCO) (N30000039)	4-2015	1/2021 (N.A.) {6/2022}	268.63 (N.A.) {493.85}	490.63	100
		300	SEWERAGE SCHEME AT PAHARI ZONE V PATNA (BUIDCO) (N30000040)	5-2017	4/2021 (5/2017) {2/2023}	356.37 (364.00) {356.37}	312.30	100
		301	SEWERAGE TREATMENT PLANT AT PAHARI PATNA (BUIDCO) (N30000043)	5-2017	11/2020 (5/2017) {5/2022}	191.62 (N.A.) {191.62}	124.40	100
		302	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK (BUIDCO) (N30000044)	3-2017	5/2021 (3/2017) {2/2023}	277.42 (253.98) {277.42}	355.31	100
		303	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA (BUIDCO) (N30000050)	8-2017	6/2022 (N.A.) {12/2025}	578.89 (453.83) {578.89}	161.74	52

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		304	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA (BUIDCO) (N30000051)	8-2017	6/2022 (N.A.) {12/2025}	824.00 (734.09) {824.00}	379.38	54
CHHATTISGARH	COAL	305	GEVRA EXPANSION OCP (SECL) (35- 70) MTY (SECL) (060100093)	6-2010	3/2023 (3/2026) {3/2026}	11,816.40 (N.A.) {11,816.40}	6,547.79	77.2
		306	KUSMUNDA EXPN.OCP(SECL)(15- 50)MTY (SECL) (N06000008)	8-2013	3/2023 (N.A.) {3/2030}	7,612.33 (N.A.) {8,547.98}	4,647.14	0
		307	PELMA OCP(15.00MTY) (SECL) (N06000045)	10-2022	3/2023 (N.A.) {3/2033}	1,624.59 (N.A.) {1,725.04}	14.95	17
		308	CHHAL OC SEAM -III (6.00 MTY) (SECL) (N06000104)	12-2013	3/2022 (6/2025) {6/2025}	610.63 (N.A.) {610.63}	574.62	85
		309	AMERA OC RCE (SECL) (N06000123)	2-2015	3/2018 (3/2026) {3/2026}	335.97 (N.A.) {335.97}	86.98	42
		310	AMGAON OPENCAST PROJECT RCE (SECL) (N06000135)	7-2015	3/2020 (3/2026) {3/2026}	316.10 (N.A.) {316.10}	188.33	65
		311	MAHAMAYA OPENCAST PROJECT (SECL) (N06000164)	5-2018	3/2026 (N.A.) {3/2026}	410.26 (N.A.) {410.26}	179.95	38
		312	JHIRIA WEST OPENCAST PROJECT (SECL) (N06000166)	1-2024	3/2029 (N.A.) {3/2029}	366.94 (N.A.) {366.94}	32.74	41

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		313	BAROUD OC EXPANSION (3-10 MTY) (SECL) (N06000197)	8-2020	3/2029 (N.A.) {3/2029}	2,309.80 (N.A.) {2,309.80}	901.40	41
		314	JAMPALI OCP RCE (SECL) (N06000198)	5-2020	3/2024 (3/2025) {3/2025}	278.64 (N.A.) {278.64}	208.41	73
		315	PORDA CHINTAPANI OCP (10 MTY) (SECL) (N06000199)	12-2020	3/2029 (N.A.) {3/2029}	2,310.12 (N.A.) {2,310.12}	46.54	10
		316	DIPKA OC EXPANSION 40 MTY (SECL) (N06000200)	12-2020	3/2029 (N.A.) {3/2029}	5,241.40 (N.A.) {5,241.40}	2,754.95	37.3
		317	JAGANNATHPUR OC RCE (3.0 MTY) (SECL) (N06000232)	7-2016	3/2020 (3/2026) {3/2026}	459.49 (N.A.) {459.49}	263.56	92
		318	KATKONA RO UG PROJECT (1.74 MTY) (SECL) (N06000274)	1-2023	3/2029 (N.A.) {3/2029}	329.22 (N.A.) {329.22}	60.34	2
	DEPARTMENT OF HIGHER EDUCATION	319	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. (CPWD EDUCATION) (N28000141)	3-2020	7/2022 (2/2024) {3/2024}	808.62 (879.22) {808.62}	879.22	100
	PETROLEUM	320	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT (HPCL) (N16000413)	3-2021	3/2024 (3/2025) {3/2025}	456.00 (N.A.) {456.00}	382.48	100
	POWER	321	WESTERN REGION EXPANSION SCHEME XXV (PGCIL) (N18000350)	2-2023	11/2023 (N.A.) {5/2025}	385.84 (N.A.) {385.84}	252.71	89

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		322	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME XXVII (PGCIL) (N18000354)	3-2023	9/2024 (N.A.) {3/2025}	271.69 (N.A.) {271.69}	186.03	100
		323	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME-XXVIII AND XXIX (PGCIL) (N18000355)	3-2023	3/2025 (N.A.) {3/2025}	260.30 (N.A.) {260.30}	187.79	100
		324	LARA SUPER THERMAL POWER PROJECT, STAGE-II (2X800 MW) (NTPC) (N18000381)	8-2023	6/2028 (N.A.) {6/2028}	15,530.00 (N.A.) {15,530.00}	1,634.35	6.5
	RAILWAYS	325	KIRANDUL - JAGDALPUR DOUBLING (ECOR) (N22000318)	12-2012	3/2020 (N.A.) {3/2024}	1,160.00 (N.A.) {1,553.11}	1,503.11	94
		326	JHARSUGUDA-BILASPUR 4TH LINE (SECR) (N22000484)	4-2015	3/2021 (12/2023) {12/2025}	1,973.00 (2,135.34) {2,135.34}	2,222.51	88
		327	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I (IRCON) (N22000489)	4-2013	9/2018 (N.A.) {12/2025}	3,055.00 (N.A.) {3,438.39}	3,112.06	92.6
		328	Gauge conversion of Raipur(Kendri)- Dhamtari and Abhanpur-Rajim branch (67.20 km) (SECR) (N22000572)	7-2011	10/2024 (N.A.) {6/2025}	1,171.30 (N.A.) {1,171.30}	560.45	80
		329	NIPANIA-BHATAPRA (14.4 KM) 4TH LINE (PB#72/NR/2022-23) (SECR) (N22000573)	9-2022	12/2026 (N.A.) {12/2026}	170.49 (N.A.) {170.49}	0.12	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		330	4TH LINE - BHATAPARA-HATHBAND (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000574)	12-2022	12/2026 (N.A.) {12/2026}	177.03 (N.A.) {177.03}	0.21	0
		331	4TH LINE - BHILAI-BHILAI NAGAR (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000575)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {177.34}	1.17	0
		332	4TH LINE - DADHAPARA-BELHA (9.2 KM) (PB#72/NR/2022-23) (SECR) (N22000576)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {169.06}	2.05	20
		333	4TH LINE - RAJNANDGAON- DONGARHGARH (31.2 KM) (PB#72/NR/2022-23) (SECR) (N22000577)	9-2022	9/2026 (N.A.) {9/2026}	328.34 (N.A.) {328.34}	12.79	15
		334	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (N22000579)	9-2022	9/2026 (N.A.) {9/2026}	167.64 (N.A.) {167.64}	-	0
		335	DOUBLING OF BORIDAND - AMBIKAPUR (SURAJPUR) (SECR) (N22000580)	6-2022	6/2030 (N.A.) {3/2027}	1,376.20 (1,242.94) {1,242.94}	154.63	10
		336	DALLIRAJHARA - ROWGHAT (95 KM) {PART OF DALLIRAJHARA- JAGDALPUR (235 KM)} (RVNL) (N22000602)	3-2008	6/2025 (N.A.) {6/2025}	631.78 (N.A.) {1,627.56}	1,349.09	0
		337	CHIRIMIRI-NAGPUR HALT (SECR) (N22000616)	10-2018	6/2030 (N.A.) {6/2030}	241.00 (N.A.) {241.00}	-	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	338	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 (MoRTH) (N24001217)	1-2016	8/2016 (N.A.) {3/2025}	497.14 (572.66) {572.66}	379.80	60.41
		339	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION (MoRTH) (N24001221)	1-2016	10/2016 (N.A.) {3/2025}	624.98 (N.A.) {731.50}	620.52	99
		340	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI (MoRTH) (N24001222)	3-2016	7/2016 (N.A.) {6/2025}	452.94 (N.A.) {435.61}	318.15	68.92
		341	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION (MoRTH) (N24001226)	12-2014	3/2015 (N.A.) {3/2015}	496.02 (N.A.) {496.02}	240.11	0
		342	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. (MoRTH) (N24001227)	3-2018	1/2019 (N.A.) {5/2025}	349.03 (N.A.) {349.03}	316.52	97.9
		343	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH- 130A (MoRTH) (N24001228)	11-2017	5/2019 (N.A.) {5/2025}	188.80 (N.A.) {188.80}	136.81	97
		344	DEVELOPMENT OF SIX LANE SARGI- BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA (NHAI) (N24001588)	12-2021	1/2025 (N.A.) {9/2025}	1,470.73 (N.A.) {1,470.73}	646.79	73.53

Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		345	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA (NHAI) (N24001593)	11-2021	9/2024 (N.A.) {6/2025}	1,368.19 (N.A.) {1,368.19}	866.26	94.3
		346	4 LANE OF BILASPUR TO URGAL PROJECT (KM 0.00 TO KM 70.2) OF NH- 130A (NHAI) (N24001611)	4-2020	3/2024 (N.A.) {9/2025}	1,855.59 (2,523.86) {2,523.86}	592.92	88.94
		347	UP GRADATION OF NH 930 SHERPAR TO KOHKA FROM KM 67.880 TO KM 114.860 TO TWO LANE WITH PAVED SHOULDER (MoRTH) (N24001917)	3-2020	5/2024 (N.A.) {5/2025}	278.97 (N.A.) {278.97}	206.59	86.18
		348	UP GRADATION OF NH 130C ABHANPUR TO PAUND FROM NK KM 0.000 TO KM. 40.380 TO TWO LANE WITH PAVED SHOU (MoRTH) (N24001919)	12-2020	9/2023 (2/2025) {5/2025}	193.16 (N.A.) {193.16}	102.75	80.71
		349	UPGRADATION OF NH 130A MUNGELI TO PONDRI FROM NH KM. 51.600 TO KM. 77.870 KM. 80.970 TO 96.970 TO 2 (MoRTH) (N24001920)	3-2021	9/2024 (N.A.) {5/2025}	218.57 (N.A.) {218.57}	136.26	81.42
		350	DEVELOPMENT OF SIX LANE BASANWAHI-MARANGPURI OF NH 130 CD FROM KM.99+500 TO 124+661 UNDER RAIPUR VIS (NHAI) (N24002017)	3-2022	10/2025 (N.A.) {9/2026}	1,307.16 (N.A.) {1,307.16}	199.32	25.7
		351	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 1 SECTION OF NH 53 FROM CH 0.000 TO CH 44.50 (NHAI) (N24002045)	6-2022	7/2025 (N.A.) {7/2025}	1,828.00 (N.A.) {1,828.00}	499.83	33.6
		352	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 2 SECTION OF NH 53 FROM CH 44+500 TO CH.92+230 I (NHAI) (N24002046)	6-2022	5/2025 (N.A.) {5/2025}	1,958.94 (1,959.00) {1,958.94}	659.49	32.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	STEEL	353	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 (NMDC) (N12000124)	11-2015	6/2023 (7/2024) {12/2025}	2,907.00 (5,427.06) {5,427.06}	2,855.31	73.8
		354	SCREENING PLANT-III AT KIRANDUL (NMDC) (N12000127)	3-2021	8/2024 (N.A.) {1/2026}	2,092.97 (2,718.84) {2,718.84}	1,472.47	69.93
		355	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (NMDC) (N12000130)	7-2021	11/2024 (N.A.) {12/2025}	282.44 (349.75) {349.75}	205.10	74
		356	REPLACEMENT OF CONVERTER VESSELS, TRUNNION RINGS, SUPPORT SYSTEM AND INSTALLATION OF SECONDARY EMISS (SAIL) (N12000131)	10-2023	6/2026 (N.A.) {6/2026}	471.83 (N.A.) {471.83}	58.27	13.2
		357	REBUILDING OF COKE OVEN BATTERY NO.7 AND 8 OF BHILAI STEEL PLANT (SAIL) (N12000134)	11-2023	10/2025 (N.A.) {10/2025}	884.10 (N.A.) {884.10}	330.44	63.7
	URBAN DEVELOPMENT	358	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI (CPWD) (N28000149)	5-2019	9/2020 (10/2024) {10/2024}	299.97 (299.97) {299.97}	272.05	89
DELHI	CIVIL AVIATION	359	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR (AAI) (N04000076)	11-2016	4/2020 (4/2024) {4/2024}	303.80 (374.98) {351.21}	344.49	100
	DPIIT	360	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE (IICC FOR DPIIT) (N40000002)	11-2017	12/2019 (4/2025) {4/2025}	4,773.00 (N.A.) {5,401.00}	4,929.51	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	FINANCE	361	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA (NPCC) (N07000001)	7-2018	4/2022 (N.A.) {4/2022}	228.50 (N.A.) {220.27}	176.28	85
	HOME AFFAIRS	362	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI (CPWD FOR MHA) (N28000071)	10-2013	10/2019 (N.A.) {9/2024}	1,219.21 (2,091.53) {2,091.53}	1,947.12	100
		363	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI (CPWD FOR MHA) (N45000002)	6-2019	7/2022 (N.A.) {9/2025}	277.35 (N.A.) {277.35}	107.00	62
	RAILWAYS	364	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE (NR) (N22000281)	4-2012	(N.A.) {6/2026}	295.68 (N.A.) {699.00}	169.99	45
	ROAD TRANSPORT AND HIGHWAYS	365	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR (NHAI) (N24001771)	6-2020	12/2024 (N.A.) {12/2024}	1,479.22 (N.A.) {1,479.22}	1,491.26	99
		366	6L ACCESS CONTROLLED HIGHWAY FROM DND MAHARANI BAGH JN. WITH JAIPUR PUSHTA ROAD OF NH 148NA FROM (NHAI) (N24001773)	5-2020	7/2024 (N.A.) {9/2025}	1,467.44 (N.A.) {1,942.89}	1,113.43	86.3
		367	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (N.A.)0.70 (NHAI) (N24001777)	7-2020	10/2023 (N.A.) {6/2025}	2,171.80 (N.A.) {2,171.80}	958.13	99.99

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		368	DEVELOPMENT OF 4L UER II (PACKAGE - V] (SPUR TO BAHADURGARH BYPASS) (NH-10) FROM KM. 0.00 TO KM.7.30 (NHAI) (N24001778)	7-2020	10/2023 (N.A.) {12/2024}	801.46 (N.A.) {801.46}	473.76	99.33
		369	DWARKA EXPRESSWAY FROM KM - 0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) (NHAI) (N24001779)	3-2018	9/2022 (N.A.) {6/2025}	2,507.00 (N.A.) {3,030.73}	1,155.70	94
		370	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21- DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O (NHAI) (N24001781)	1-2018	10/2021 (N.A.) {3/2025}	2,067.67 (N.A.) {2,160.00}	1,496.49	99.2
		371	DEVELOPMENT OF 6L UER II (PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM (NHAI) (N24001825)	7-2020	10/2023 (N.A.) {6/2025}	1,894.96 (N.A.) {1,894.96}	741.88	92.61
	TELECOMMUNICATIONS	372	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT (CPWD FOR TELECO) (N28000115)	10-2014	3/2018 (N.A.) {3/2025}	248.20 (N.A.) {248.20}	236.27	98
	URBAN DEVELOPMENT	373	DELHI MRTS PHASE-III (DMRC) (N28000056)	9-2011	3/2016 (8/2021) {8/2021}	38,585.00 (43,095.35) {40,180.91}	40,600.65	100
		374	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR (NBCC) (N28000105)	7-2016	(N.A.) {10/2024}	2,694.00 (N.A.) {2,694.00}	2,402.68	98
		375	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I (CPWD) (N28000128)	10-2016	7/2021 (N.A.) {6/2024}	1,180.00 (N.A.) {1,100.80}	36.69	2

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		376	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I (CPWD) (N28000129)	10-2016	3/2022 (N.A.) {6/2024}	1,128.00 (N.A.) {1,128.00}	709.96	60
		377	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS (DMRC) (N28000135)	7-2019	3/2025 (N.A.) {3/2026}	24,948.65 (N.A.) {24,948.65}	15,494.03	63.28
		378	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI (CPWD) (N28000153)	1-2022	11/2024 (5/2025) {5/2025}	646.52 (N.A.) {646.52}	473.63	89
		379	REDEVELOPMENT OF GPRA AT NETAJI NAGAR NEW DELHI PACKAGE 2 (NBCC) (N28000156)	10-2016	3/2024 (3/2025) {3/2025}	1,536.72 (N.A.) {1,536.72}	468.18	0
	WATER RESOURCES	380	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD ? 10MG/L (DJB) (N30000014)	3-2017	12/2022 (N.A.) {12/2024}	665.78 (N.A.) {665.78}	782.51	96
		381	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 (DJB) (N30000015)	5-2016	12/2021 (N.A.) {2/2024}	211.79 (223.70) {211.79}	208.71	100
		382	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S (DJB) (N30000016)	5-2016	2/2022 (9/2023) {7/2023}	239.11 (314.71) {239.11}	268.13	100
		383	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI (DJB) (N30000017)	12-2018	1/2021 (N.A.) {3/2022}	515.07 (N.A.) {515.07}	388.08	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
<u>GOA</u>	<u>CIVIL AVIATION</u>	384	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. (AAI) (N04000095)	11-2017	9/2021 (6/2025) {6/2025}	255.69 (N.A.) {255.69}	113.78	82
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	385	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. (CPWD EDUCATION) (N42000002)	5-2019	8/2021 (N.A.) {12/2024}	303.90 (N.A.) {390.40}	364.00	99.3
	<u>PETROLEUM</u>	386	UPGRADING IPSHEM TO WORLD CLASS FACILITY OF ONGC, GOA (ONGC) (N16000502)	3-2023	6/2024 (N.A.) {2/2025}	325.53 (N.A.) {325.53}	304.19	100
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	387	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM. 508.000 TO KM. 513.150 INCLUDING APPROACHES ON N (MoRTH) (N24002181)	4-2023	4/2026 (N.A.) {4/2026}	641.46 (N.A.) {641.46}	-	0
<u>GUJARAT</u>	<u>CIVIL AVIATION</u>	388	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT (AAI) (N04000088)	1-2018	8/2022 (12/2024) {12/2024}	1,405.00 (N.A.) {1,405.00}	1,304.38	100
		389	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. (AAI) (N04000093)	8-2018	2/2021 (3/2025) {3/2025}	353.25 (N.A.) {353.25}	347.63	100
		390	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1. (AAI) (N04000099)	6-2022	12/2025 (N.A.) {12/2025}	1,305.00 (1,143.95) {1,143.95}	505.54	50
	<u>PETROLEUM</u>	391	REDEVELOPMENT OF SANTHAL FIELD (ONGC) (N16000279)	2-2017	3/2026 (N.A.) {3/2026}	1,162.56 (N.A.) {1,162.56}	1,155.42	93.6

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		392	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY (IOCL) (N16000382)	11-2019	5/2023 (3/2024) {4/2025}	5,251.00 (5,894.00) {5,894.00}	4,567.72	99.45
		393	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY (IOCL) (N16000409)	9-2020	8/2024 (12/2025) {12/2025}	18,936.00 (N.A.) {18,936.00}	10,530.28	80.3
		394	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM (IOCL) (N16000411)	10-2020	8/2023 (6/2025) {6/2025}	1,614.00 (N.A.) {1,614.00}	1,081.03	94.48
		395	REDEVELOPMENT OF LINCH FIELD (ONGC) (N16000428)	4-2021	3/2025 (N.A.) {7/2025}	631.03 (860.04) {860.04}	384.82	65.6
		396	REDEVELOPMENT OF SOBHASAN COMPLEX (ONGC) (N16000431)	8-2021	2/2026 (N.A.) {2/2026}	885.63 (1,286.67) {1,286.67}	546.77	66
		397	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD (ONGC) (N16000444)	1-2022	11/2024 (N.A.) {11/2025}	621.40 (N.A.) {621.40}	130.20	21.4
		398	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT (IOCL) (N16000454)	1-2022	9/2024 (N.A.) {5/2025}	328.00 (N.A.) {328.00}	57.21	40
		399	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT (ONGC) (N16000477)	5-2022	2/2025 (N.A.) {9/2025}	249.43 (N.A.) {249.43}	208.68	91.1

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		400	KALOL REDEVELOPMENT PROJECT (ONGC) (N16000481)	8-2022	3/2027 (N.A.) {3/2027}	1,487.41 (N.A.) {1,487.41}	918.00	59
		401	OLD PIPE LINE REPLACEMENT (OPRP) GROUP-A (ONGC) (N16000483)	7-2021	7/2025 (N.A.) {7/2025}	173.03 (N.A.) {169.84}	137.99	83.3
		402	REVAMPING OF SV STATIONS, GAS TERMINAL AND KRIBHCO TERMINAL (ONGC) (N16000514)	11-2022	8/2026 (N.A.) {8/2026}	837.34 (N.A.) {837.34}	147.68	39.5
	POWER	403	GUJARAT 200 MW (GUVNL TENDER) (NTPC) (N18000295)	1-2021	7/2022 (N.A.) {9/2025}	842.27 (N.A.) {842.27}	767.91	30
		404	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) (NTPC) (N18000296)	5-2021	9/2022 (N.A.) {4/2025}	674.92 (N.A.) {674.92}	572.44	91
		405	Bagodara Solar Power Project (SJVN) (N18000297)	5-2021	10/2022 (N.A.) {12/2025}	339.35 (N.A.) {339.35}	317.31	51.22
		406	DAYAPAR WIND ENERGY PROJECT 150MW (NTPC) (N18000319)	11-2021	5/2023 (N.A.) {5/2025}	937.80 (N.A.) {937.80}	787.28	98
		407	DAYAPAR WIND ENERGY PROJECT 200MW (NTPC) (N18000345)	7-2022	3/2025 (N.A.) {3/2026}	1,316.02 (N.A.) {1,316.02}	324.05	23
		408	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK) (NTPC) (N18000346)	9-2022	9/2024 (N.A.) {6/2025}	7,179.54 (N.A.) {7,179.54}	4,462.12	61

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		409	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) (NTPC) (N18000349)	11-2022	3/2024 (N.A.) {1/2026}	1,442.60 (N.A.) {1,442.60}	792.36	2
		410	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK (PGCIL) (N18000357)	3-2023	12/2024 (N.A.) {5/2025}	922.30 (N.A.) {922.30}	587.67	88
		411	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT (PGCIL) (N18000358)	3-2023	3/2025 (N.A.) {4/2025}	815.12 (N.A.) {815.12}	10.99	83
		412	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK (PGCIL) (N18000359)	3-2023	12/2024 (N.A.) {5/2025}	966.79 (N.A.) {966.79}	548.22	90
		413	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000360)	3-2023	3/2025 (N.A.) {6/2025}	1,167.55 (N.A.) {1,167.55}	677.14	69
		414	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000361)	3-2023	3/2025 (N.A.) {6/2025}	2,820.99 (N.A.) {2,820.99}	2,304.46	68
		415	KHAVDA 1200MW (4X300MW) IN KHAVDA RE PARK (NTPC) (N18000365)	6-2023	12/2024 (N.A.) {2/2026}	6,283.81 (N.A.) {6,283.81}	1,667.94	16
		416	DAYAPAR WIND- III (HYBRID TRANCHE-V) (NTPC) (N18000366)	5-2023	1/2025 (N.A.) {12/2025}	1,095.01 (N.A.) {1,095.01}	341.83	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		417	TS FOR EVACUATION OF POWER FROM POTENTIAL RE ZONE IN KHAVDA AREA OF GUJARAT UNDER PH-IV PART E3 (PGCIL) (N18000383)	7-2023	7/2025 (N.A.) {7/2025}	334.00 (N.A.) {334.00}	-	12
		418	TS FOR EVACUATION OF ADDITIONAL 7GW RE POWER FROM KHAVDA RE PARK UNDER PHASE-III PART B [VATAMAN TRA (PGCIL) (N18000384)	12-2023	12/2025 (N.A.) {12/2025}	3,752.00 (N.A.) {3,752.00}	617.02	9
		419	TS FOR EVACUATION OF POWER FROM 7GW REZ IN KHAVDA AREA UNDER PHASE-IV PART E2 (PGCIL) (N18000390)	5-2024	5/2026 (N.A.) {5/2026}	679.00 (N.A.) {679.00}	-	9
		420	AUGMENTATION OF TRANSFORMATION CAPACITY AT JAM KHAMBHALIYA PS [GIS] [SPV NAME POWERGRID JAM KHAMBHAL (PGCIL) (N18000398)	10-2024	7/2026 (N.A.) {7/2026}	329.00 (N.A.) {329.00}	-	1
		421	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000400)	10-2024	10/2026 (N.A.) {10/2026}	4,766.00 (N.A.) {4,766.00}	110.00	1
		422	PROVISION OF DYNAMIC REACTIVE COMPENSATION AT KHAVDA POOLING STATION 1 [KPS1] AND KHAVDA POOLING STA (PGCIL) (N18000402)	11-2024	11/2026 (N.A.) {11/2026}	501.00 (N.A.) {501.00}	-	1
		423	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000405)	11-2024	5/2029 (N.A.) {5/2029}	24,819.00 (N.A.) {24,819.00}	1,340.00	1

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		424	600 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000406)	4-2022	3/2026 (N.A.) {3/2026}	4,100.45 (N.A.) {4,100.45}	0.70	9
	RAILWAYS	425	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) (WR) (N22000142)	4-2011	(10/2026) {10/2026}	844.10 (844.10) {844.10}	593.17	41
		426	ANAND GODHRA DOUBLING PROJECT 79 KMS (WR) (N22000504)	4-2017	3/2020 (2/2025) {2/2025}	692.25 (692.26) {692.26}	669.82	97
		427	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS (WR) (N22000505)	4-2018	3/2024 (10/2024) {10/2024}	537.31 (537.31) {688.74}	844.55	100
		428	4TH LINE BETWEEN BAREJADI NANDEJ (GERATPUR)- SANAND (38.20 KM) (AHMEDABAD BYPASS). (WR) (N22000532)	2-2023	3/2027 (2/2027) {2/2027}	961.67 (961.67) {961.67}	107.56	2.5
		429	QUADRUPLING BETWEEN GANDHIDHAM - ADIPUR WITH Y CONNECTION AT ADIPUR FOR PROVIDING DIRECT ENTRY TOWAR (WR) (N22000533)	2-2023	12/2025 (10/2025) {10/2025}	152.44 (152.44) {152.44}	60.81	20
		430	RAJKOT-KANALUS (111.20 KM) (WR) (N22000535)	10-2021	10/2026 (3/2026) {3/2026}	1,011.72 (1,080.58) {1,080.58}	1,331.54	65
		431	HIMMATNAGAR-KHEDBRAHMA (54.83 KM) (WR) (N22000537)	6-2022	2/2030 (6/2025) {6/2025}	354.99 (482.42) {482.42}	813.37	84

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		432	PETLAD-BHADRAN (22.5 KM) (WR) (N22000538)	5-2022	5/2030 (12/2025) {12/2025}	202.50 (307.12) {307.12}	80.48	8
		433	NADIAD-PETLAD (37.26 KM) (WR) (N22000539)	5-2022	6/2030 (N.A.) {12/2025}	335.34 (461.91) {461.91}	73.23	7
		434	SAMLAYA-TIMBA ROAD (53.53 KM) (WR) (N22000540)	2-2023	3/2030 (7/2026) {7/2026}	401.48 (670.17) {670.17}	81.42	12
		435	SAMNI-JAMBUSAR (24.08 KM) (WR) (N22000541)	5-2022	3/2030 (12/2025) {12/2025}	216.72 (349.93) {349.93}	83.66	25
		436	VIJAPUR-AMBLIYASAN (41.53 KM) (WR) (N22000547)	5-2022	3/2030 (6/2025) {6/2025}	309.81 (415.38) {415.38}	557.55	75
		437	ADRAJ MOTI-VIAJAPUR (39.75 KM) (WR) (N22000548)	5-2022	5/2030 (7/2025) {5/2030}	296.54 (N.A.) {296.54}	19.57	55
		438	NEW BG LINE BETWEEN NALIYA- JAKHAU PORT (WR) (N22000550)	2-2023	1/2028 (9/2026) {9/2026}	410.46 (410.46) {410.46}	33.63	2
		439	NEW BG LINE INTERSECTION (5 NOS) BETWEEN GERATPUR-SANAND AND BOTAD-AHMEDABAD (16.51 KM) (PB29/NR/20) (WR) (N22000551)	10-2022	10/2027 (2/2027) {10/2027}	437.21 (N.A.) {437.21}	0.10	0
		440	TARANGA HILL ABU ROAD VIA AMBAJI NEW LINE (NWR) (N22000592)	7-2022	7/2030 (N.A.) {12/2026}	1,695.82 (N.A.) {2,798.16}	990.84	10

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		441	JUNAGARH -VISAADAR (42.28) KM (RVNL) (N22000600)	6-2022	12/2026 (N.A.) {12/2026}	492.83 (N.A.) {492.83}	-	0
		442	MODASA- SHAMLAJI NEW LINE (MM OF AHMEDABAD-HIMMATNAGAR- UDAIPUR (299.2 KM)) (WR) (N22000622)	9-2012	3/2027 (2/2026) {2/2026}	261.68 (261.68) {261.68}	648.40	45
	ROAD TRANSPORT AND HIGHWAYS	443	FOUR LANING OF BHAVNAGAR- TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. (NHAI) (N24000567)	5-2016	8/2019 (N.A.) {6/2024}	998.18 (N.A.) {998.18}	802.34	100
		444	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST (NHAI) (N24000569)	5-2016	9/2019 (5/2024) {5/2025}	723.64 (N.A.) {723.64}	561.37	96.35
		445	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU (NHAI) (N24000570)	5-2016	8/2019 (N.A.) {3/2025}	763.08 (N.A.) {763.08}	518.95	99.43
		446	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 (NHAI) (N24000592)	7-2016	7/2020 (N.A.) {3/2025}	829.97 (N.A.) {829.97}	484.03	95.19
		447	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. (NHAI) (N24000649)	1-2017	12/2020 (6/2025) {6/2025}	1,251.11 (1,527.75) {1,527.75}	684.13	83.84
		448	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR (NHAI) (N24000834)	3-2018	10/2021 (5/2025) {5/2025}	1,161.39 (1,738.03) {1,404.00}	519.40	76.99

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		449	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA (MoRTH) (N24000925)	10-2018	11/2020 (9/2024) {9/2024}	400.76 (394.44) {394.44}	287.39	87
		450	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT (MoRTH) (N24001427)	6-2020	4/2023 (9/2024) {9/2024}	166.21 (N.A.) {166.21}	98.65	93
		451	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 (NHAI) (N24001443)	5-2020	3/2024 (11/2024) {1/2025}	690.30 (929.95) {929.95}	1,193.08	86.4
		452	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION (NHAI) (N24001444)	5-2020	1/2024 (11/2024) {1/2025}	882.00 (N.A.) {882.00}	1,256.69	93.05
		453	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB (NHAI) (N24001445)	5-2020	7/2023 (11/2024) {1/2025}	691.52 (903.85) {903.85}	909.80	93.05
		454	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG (NHAI) (N24001446)	5-2020	12/2023 (11/2024) {1/2025}	894.00 (1,210.06) {1,210.06}	1,025.93	88.84
		455	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 (NHAI) (N24001515)	9-2020	2/2024 (N.A.) {11/2025}	1,542.02 (N.A.) {1,542.02}	954.48	67.85

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		456	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 (NHAI) (N24001516)	9-2020	2/2024 (4/2025) {4/2025}	1,185.69 (N.A.) {1,185.69}	948.23	92.7
		457	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 (NHAI) (N24001518)	11-2019	9/2023 (N.A.) {4/2025}	1,669.56 (N.A.) {1,669.56}	1,066.35	95.77
		458	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 (NHAI) (N24001519)	9-2020	11/2023 (N.A.) {4/2025}	1,198.55 (N.A.) {1,198.55}	895.39	95.7
		459	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 (NHAI) (N24001520)	11-2019	5/2024 (N.A.) {6/2025}	1,604.06 (N.A.) {1,604.06}	1,235.25	95.73
		460	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT (NHAI) (N24001785)	3-2022	6/2025 (N.A.) {6/2025}	1,373.06 (1,085.00) {1,373.06}	538.63	77.71
		461	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU (NHAI) (N24001786)	3-2021	3/2024 (N.A.) {12/2025}	1,259.00 (2,652.24) {1,910.00}	278.29	34.08
		462	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU (NHAI) (N24001788)	7-2020	12/2023 (N.A.) {4/2025}	2,271.86 (3,372.97) {3,916.00}	1,099.57	98.1

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		463	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA (NHAI) (N24001789)	7-2020	8/2023 (N.A.) {4/2025}	1,710.30 (2,665.08) {1,927.00}	709.63	90.56
		464	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH-754K (AJ-RGBS-PACKAGE-3) (NHAI) (N24001790)	2-2020	8/2023 (12/2024) {12/2024}	752.30 (N.A.) {766.20}	452.13	98.14
		465	SANCHORE - SANTALPUR FROM KM 4.888 - KM 35.000 OF NH-754K (AJ-RGBS-PACKAGE-1) (NHAI) (N24001791)	2-2020	6/2023 (3/2024) {5/2024}	606.51 (N.A.) {657.00}	453.89	98.99
		466	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II) (NHAI) (N24001792)	3-2021	9/2022 (N.A.) {1/2025}	536.03 (N.A.) {536.03}	480.77	99.48
		467	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) (NHAI) (N24001793)	3-2021	9/2022 (N.A.) {4/2025}	485.75 (N.A.) {485.75}	391.55	98.17
		468	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH-754K (AJ-RGBS-PACKAGE-4) (NHAI) (N24001794)	2-2020	3/2023 (12/2024) {12/2024}	778.15 (N.A.) {785.67}	547.22	99.7
		469	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE) (NHAI) (N24001827)	3-2022	3/2023 (N.A.) {3/2025}	162.73 (N.A.) {162.73}	131.79	95.3

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		470	UPGRADATION AND STRENGTHENING TO 2 LANE PS FROM KM 95/500 TO KM 129/775 OF NH 168 G IDAR BHILODA SA (MoRTH) (N24002014)	9-2022	12/2023 (12/2025) {12/2025}	237.28 (N.A.) {237.28}	0.59	0
		471	UPGRADATION TO 4L PS DIVIDED CARRIAGEWAY FROM PATAN (NEAR RAJPUR) TO GOJARIYA FROM KM 52.000 TO KM 1 (NHAI) (N24002034)	12-2021	3/2025 (N.A.) {3/2025}	1,181.34 (1,181.00) {1,181.34}	487.49	69.17
		472	WIDENING TO 6L OF EXISTING 4L JETPUR - GONDAL - RAJKOT SECTION FROM KM. 117.600 TO KM. 185.00 ON NH- (NHAI) (N24002035)	9-2023	9/2025 (N.A.) {9/2025}	2,070.44 (N.A.) {2,070.44}	312.19	20.77
		473	UPGRADATION OF DHORAJI JAMKANDORNA KALAVAD SECTION OF NH 927D FROM DESIGN CHAINAGE KM 00 TO KM 58.11 (MoRTH) (N24002117)	10-2022	2/2024 (2/2026) {2/2026}	246.60 (291.00) {291.00}	29.33	15
		474	UPGRADATION TO TWO LANE WITH PAVED SHULDER CONFIGURATION FROM KM 00 TO 47 OF NH 351 MAHUVA TO BADHA (MoRTH) (N24002118)	12-2022	2/2024 (8/2025) {8/2025}	173.06 (N.A.) {219.00}	0.15	0
		475	WORK OF DEVELOPMENT AND CONSTRUCTION OF ELEVATED CORRIDOR FROM KM 38/660 TO KM 42/690 (ISCON JUNCTION) (MoRTH) (N24002182)	3-2023	3/2026 (N.A.) {3/2026}	530.20 (N.A.) {530.20}	-	0
		476	WIDENING 2 LANE TO 4-LANE FROM KM 92/320 TO KM 115/320 (VAV CHOKDI-SATLASANA TO TO VRUNDAVAN CHOKDI, (MoRTH) (N24002183)	3-2022	3/2026 (N.A.) {3/2026}	151.13 (N.A.) {171.00}	-	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	URBAN DEVELOPMENT	477	AHMEDABAD METRO RAIL PROJECT PHASE 1 (AMR) (N28000122)	11-2014	12/2018 (N.A.) {8/2025}	10,773.00 (N.A.) {12,924.55}	12,462.07	99.88
		478	AHMEDABAD METRO RAIL PROJECT PHASE II (AMR) (N28000137)	3-2019	3/2024 (N.A.) {12/2025}	5,384.17 (N.A.) {5,384.17}	3,979.29	84.26
		479	SURAT METRO RAIL PROJECT (AMR) (N28000138)	3-2019	3/2024 (N.A.) {6/2026}	12,020.32 (N.A.) {12,020.32}	6,662.69	63.98
HARYANA	HEALTH AND FAMILY WELFARE	480	ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT MANETHI, HARYANA. (HITES) (N21000032)	3-2019	3/2023 (3/2026) {3/2026}	1,294.34 (1,294.34) {1,294.34}	244.20	14.92
	HOME AFFAIRS	481	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" (CPWD FOR MHA) (N28000147)	1-2020	10/2023 (3/2025) {6/2025}	166.98 (170.23) {170.23}	132.08	95
	PETROLEUM	482	R and D CAMPUS II AT FARIDABAD (IOCL) (N16000375)	6-2019	12/2022 (7/2025) {7/2025}	2,281.94 (3,219.94) {3,219.94}	1,689.98	62.5
		483	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA (IOCL) (N16000412)	2-2021	9/2024 (12/2025) {12/2025}	34,627.00 (38,231.00) {38,231.00}	19,053.36	83.9
		484	POLY BUTADIENE RUBBER PLANT AT PANIPAT (IOCL) (N16000458)	3-2022	3/2025 (6/2026) {6/2026}	1,459.00 (2,948.62) {2,948.62}	875.48	60.1
	RAILWAYS	485	DOUBLING BETWEEN BHIWANI-DOBH BAHALI (NWR) (N22000604)	2-2023	2/2028 (N.A.) {12/2025}	471.06 (N.A.) {471.06}	77.96	40

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		486	DOUBLING BETWEEN REWARI-KATHUWAS (27.73 KM) (NWR) (N22000606)	2-2023	6/2027 (N.A.) {12/2025}	352.41 (N.A.) {352.41}	142.38	31
	ROAD TRANSPORT AND HIGHWAYS	487	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P (NHAI) (N24000835)	3-2018	12/2020 (12/2024) {3/2024}	1,484.30 (N.A.) {2,182.41}	1,376.15	100
		488	CONSTRUCTION OF 4-LANE NH-344P-PACKAGE-4 (FROM KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA (NHAI) (N24001532)	11-2021	11/2023 (1/2024) {8/2024}	694.00 (1,918.00) {1,500.00}	1,682.82	100
		489	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP (NHAI) (N24001533)	11-2020	12/2023 (N.A.) {3/2025}	1,690.23 (N.A.) {2,010.17}	1,368.33	98.5
		490	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP (NHAI) (N24001534)	12-2020	1/2024 (4/2024) {3/2025}	1,334.04 (N.A.) {1,334.00}	997.01	99
		491	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 (NHAI) (N24001535)	7-2020	7/2022 (5/2024) {4/2025}	899.00 (1,882.46) {1,882.46}	1,123.98	93.1
		492	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI (NHAI) (N24001536)	7-2020	7/2022 (N.A.) {3/2025}	817.00 (1,605.00) {1,605.00}	1,025.56	99.1
		493	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F (NHAI) (N24001633)	12-2020	12/2023 (3/2024) {3/2025}	1,430.88 (1,813.91) {1,813.91}	1,122.45	99.9

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		494	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO (NHAI) (N24001634)	1-2021	12/2023 (3/2024) {4/2025}	1,306.95 (1,564.14) {1,564.14}	942.66	99
		495	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O (NHAI) (N24001635)	3-2022	2/2025 (N.A.) {2/2025}	1,269.50 (N.A.) {1,269.50}	223.00	50
		496	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K (NHAI) (N24001673)	3-2020	3/2023 (11/2024) {3/2025}	510.97 (N.A.) {510.97}	529.00	94.2
		497	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH- 352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU (NHAI) (N24001774)	12-2020	11/2023 (N.A.) {6/2024}	1,524.03 (N.A.) {1,524.03}	1,092.89	62.55
		498	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH-11 AS A FEEDER ROUTE IN THE STATE (NHAI) (N24001775)	2-2020	1/2023 (12/2024) {12/2024}	808.31 (N.A.) {958.00}	881.78	100
		499	DWARKA EXPRESSWAY PKG-III (DELHI/HR BORDER TO START OF ROB GURUGRAM) (NHAI) (N24001780)	1-2018	11/2020 (12/2024) {3/2024}	2,228.00 (N.A.) {2,228.00}	1,628.60	100
		500	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN (NHAI) (N24001783)	11-2018	9/2021 (N.A.) {4/2025}	2,252.75 (N.A.) {2,252.75}	1,223.07	99.95

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		501	UPGRADATION OF EXISTING 4 LANE ISMAILABAD-AMBALA SECTION (KM. 0+000 TO KM 42+500) (PART OF AMBALA-KO (NHAI) (N24002037)	1-2023	12/2025 (N.A.) {3/2026}	609.32 (609.00) {609.00}	180.20	41.5
		502	CONSTRUCTION OF 6-LANE GREENFIELD KARNAL RING ROAD STARTING FROM NH-44 NEAR VILLAGE SHAMGARH (DESIGN (NHAI) (N24002038)	11-2022	8/2025 (N.A.) {8/2025}	1,691.45 (1,998.00) {1,998.00}	640.26	57.5
		503	CONSTRUCTION OF 6-LANE GREENFIELD AMBALA RING ROAD STARTING FROM JUNCTION WITH SHAMLI-AMBALA SECTION (NHAI) (N24002039)	2-2023	10/2025 (N.A.) {10/2025}	1,088.64 (1,178.00) {1,178.00}	391.10	45
		504	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM RANIPUR BARS (SAHARANPUR DISTRICT) TO ADHOYA (NHAI) (N24002040)	4-2022	5/2025 (N.A.) {5/2028}	1,554.21 (N.A.) {1,554.21}	515.64	52.5
		505	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM ADHOYA MUSALMANA (AMBALA DISTRICT) TO SADOPUR (NHAI) (N24002041)	4-2022	5/2025 (N.A.) {5/2025}	1,491.71 (N.A.) {1,491.71}	706.26	49.7
		506	CONSTRUCTION OF 4-LANING OF BHIWANI HANSI ROAD SECTION OF NH 148B (DESIGN LENGTH 42.934 KM) UNDER BH (NHAI) (N24002042)	11-2022	12/2025 (N.A.) {12/2025}	1,322.13 (N.A.) {1,322.13}	315.33	73.13
		507	CONSTRUCTION OF 4-LANE GREENFIELD JALBEHRA - SHAHBAD SECTION OF NH ? 152G FROM KM 0+000 TO KM 22+850 (NHAI) (N24002043)	3-2022	6/2025 (N.A.) {6/2025}	927.22 (1,173.66) {1,173.66}	458.86	65.35

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
HIMACHAL PRADESH		508	4L AMBALA - KALAAMB FROM KM. - 0.800 TO KM. 33.015 OF OLD NH-72 (NHAI) (N24002044)	6-2023	6/2025 (N.A.) {6/2025}	629.16 (N.A.) {629.16}	191.00	85
		509	CONSTRUCTION OF GREENFIELD CONNECTIVITY TO JEWAR INTERNATIONAL AIRPORT FROM DND FARIDABAD BALLABHGAR (NHAI) (N24002048)	7-2022	6/2025 (N.A.) {3/2026}	2,414.67 (2,898.00) {2,898.00}	1,190.43	43.86
	DEPARTMENT OF HIGHER EDUCATION	510	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR (CPWD EDUCATION) (N42000008)	9-2018	6/2022 (12/2024) {8/2025}	392.51 (N.A.) {446.43}	316.10	91.5
		511	CONSTRUCTION OF PERMANENT CAMPUSES OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND DHARAMSHAL (CPWD) (N42000011)	3-2021	11/2024 (7/2025) {7/2025}	512.37 (300.45) {300.45}	144.32	68
	POWER	512	PARBATI HEP (4X200 MW) (NHPC) II (NHPC) (180100210)	9-2002	9/2009 (N.A.) {4/2025}	3,919.59 (N.A.) {12,899.00}	12,827.69	99.23
		513	LUHRI HYDROELECTRIC PROJECT (STAGE1) (SJVN) (N18000279)	11-2020	1/2026 (N.A.) {12/2028}	1,810.56 (N.A.) {3,060.71}	1,693.09	51.32
		514	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) (SJVN) (N18000291)	10-2020	11/2025 (N.A.) {3/2027}	687.97 (N.A.) {1,426.00}	835.47	65.44
		515	SUNNI DAM HYDRO ELECTRIC PROJECT (SJVN) (N18000344)	1-2023	4/2028 (N.A.) {12/2028}	2,614.51 (N.A.) {3,605.30}	928.75	28.25

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	516	BHANUPALI-BILASPUR BERI NL (RVNL) (N22000273)	4-2008	12/2026 (N.A.) {3/2025}	2,966.99 (N.A.) {6,753.42}	5,369.57	0
	ROAD TRANSPORT AND HIGHWAYS	517	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) (NHAI) (N24000232)	11-2013	11/2016 (N.A.) {}	1,916.79 (N.A.) {1,916.79}	1,660.92	0
		518	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS (NHAI) (N24000606)	8-2016	9/2020 (N.A.) {}	1,583.18 (N.A.) {1,583.18}	-	0
		519	FOUR LANNING OF NERCHOWK- PANDOH BYPASS SECTION OF NH- 21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH (NHAI) (N24000613)	9-2016	7/2020 (N.A.) {3/2025}	1,273.71 (N.A.) {1,478.61}	1,439.49	96.31
		520	FOUR LANING OF SOLAN- KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M (NHAI) (N24000852)	3-2018	5/2021 (12/2024) {12/2024}	478.74 (N.A.) {1,514.46}	1,349.59	83
		521	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA (MoRTH) (N24001381)	8-2020	4/2021 (N.A.) {4/2021}	272.98 (N.A.) {272.98}	140.69	100
		522	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. (MoRTH) (N24001382)	8-2020	3/2021 (N.A.) {7/2024}	242.80 (N.A.) {242.80}	96.76	87

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		523	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI- GUMMA SECTION (KM 75 (MoRTH) (N24001383)	8-2020	4/2021 (N.A.) {4/2021}	349.20 (N.A.) {349.20}	239.34	100
		524	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K (MoRTH) (N24001422)	2-2021	9/2021 (N.A.) {7/2024}	345.89 (N.A.) {345.89}	152.01	84
		525	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR-KARNOHAL SECTION (KM 141.000 TO K (MoRTH) (N24001447)	8-2020	12/2024 (N.A.) {12/2024}	371.93 (N.A.) {371.93}	205.67	0
		526	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF KALWAHAN-MANDI SECTION (KM 208.950 TO KM 2 (MoRTH) (N24001470)	8-2020	4/2025 (N.A.) {4/2025}	314.32 (N.A.) {314.32}	93.70	0
		527	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF (NHAI) (N24001808)	3-2021	12/2024 (12/2024) {12/2024}	1,322.95 (1,442.47) {1,442.47}	886.89	96.61
		528	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU (NHAI) (N24001809)	5-2022	3/2024 (12/2024) {12/2024}	469.95 (N.A.) {280.00}	302.91	97.16
		529	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP (NHAI) (N24001810)	2-2022	6/2024 (N.A.) {6/2024}	190.60 (N.A.) {163.00}	103.48	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		530	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH-20 (NEW NH- 154) (PACKAGE-IB) (NHAI) (N24001811)	4-2021	6/2024 (N.A.) {5/2025}	583.93 (770.00) {770.00}	171.66	98.6
		531	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) (NHAI) (N24001812)	3-2021	5/2024 (N.A.) {12/2025}	1,002.11 (1,361.79) {1,361.76}	189.82	45.29
		532	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A (NHAI) (N24001813)	7-2021	9/2024 (N.A.) {9/2024}	1,692.05 (N.A.) {1,692.05}	942.14	21.6
		533	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS-5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001915)	3-2021	6/2026 (N.A.) {6/2026}	230.54 (N.A.) {230.54}	20.16	20.16
		534	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS 5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001916)	3-2021	5/2026 (N.A.) {5/2026}	314.67 (N.A.) {314.67}	76.05	44
		535	PKG NAME: 4L OF KATHLIGHAT TO SHAKRAL VILLAGE FROM KM 128.835 TO KM 146.300 OF NH- 5 (SHIMLA BYPASS (NHAI) (N24002049)	3-2022	4/2026 (N.A.) {4/2026}	1,703.48 (2,278.00) {2,278.00}	651.98	14.5
		536	REHABILITATION AND UPGRADATION TO 4L CONFIGURATION and STRENGTHENING OF SIHUNI TO RAJOL FROM KM 51.0 (NHAI) (N24002050)	2-2022	9/2025 (N.A.) {9/2025}	696.65 (698.46) {698.46}	367.51	55.2

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		537	CONSTRUCTION OF NEW 2 LANE WITH PAVED SHOULDER OF HAMIRPUR BYPASS (PACKAGE IVA) OF NH-88 (NEW NH-103 (NHAI) (N24002051)	7-2022	10/2025 (N.A.) {10/2025}	739.39 (N.A.) {739.39}	328.43	74.14
		538	REHABILITATION AND UP-GRADATION OF EXISTING ROAD TO 2L PS FROM END OF HAMIRPUR BYPASS (NEAR CHILBAHA (NHAI) (N24002052)	2-2022	4/2025 (N.A.) {4/2025}	1,146.19 (N.A.) {1,146.19}	918.33	62.15
		539	REHABILITATION AND UP-GRADATION TO 4L CONFIGURATION AND STRENGTHENING OF THANPURI TO PAROR SECTION F (NHAI) (N24002192)	6-2022	12/2025 (N.A.) {12/2025}	815.69 (815.69) {815.69}	368.97	25.86
	<u>URBAN DEVELOPMENT</u>	540	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D (CPWD) (N28000154)	4-2022	11/2024 (N.A.) {11/2024}	512.34 (N.A.) {512.34}	-	0
<u>JAMMU AND KASHMIR</u>	<u>CIVIL AVIATION</u>	541	JAMMU - CONSTRUCTION OF NEW CIVIL ENCLAVE (AAI) (N04000107)	7-2022	6/2026 (N.A.) {6/2026}	861.37 (N.A.) {861.37}	132.41	27
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	542	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) (CPWD EDUCATION) (N28000130)	3-2019	7/2022 (1/2025) {1/2025}	424.93 (N.A.) {500.91}	473.74	96
		543	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) (CPWD EDUCATION) (N28000131)	1-2018	4/2023 (4/2025) {4/2025}	676.00 (1,144.68) {1,144.68}	64.75	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	HEALTH AND FAMILY WELFARE	544	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR (CPWD FOR HEALTH) (N21000029)	3-2019	9/2023 (4/2025) {4/2025}	1,404.00 (1,642.00) {1,642.00}	1,461.68	99.9
		545	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR (CPWD FOR HEALTH) (N28000150)	3-2019	9/2025 (1/2025) {11/2025}	1,828.00 (1,577.00) {1,577.00}	1,276.63	63.5
	PETROLEUM	546	SETTING UP A COMMON USER PETROLEUM TERMINAL AT JAMMU FOR RE-SITEMENT OF EXISTING DEPOTS OF PSU OMCS (BPCL) (N16000500)	4-2021	3/2025 (N.A.) {3/2025}	676.89 (N.A.) {676.89}	467.15	71
		547	CGD PROJECT AT JAMMU DISTRICTS (IOCL) (N16000527)	3-2022	3/2032 (9/2034) {9/2034}	538.00 (N.A.) {538.00}	3.87	0.6
	POWER	548	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) (CVPPPL) (N18000172)	10-2014	4/2020 (7/2025) {9/2026}	8,112.12 (N.A.) {12,727.76}	6,081.91	67.4
		549	KIRU HYDRO ELECTRIC PROJECT (CVPPPL) (N18000278)	3-2019	8/2024 (N.A.) {9/2026}	4,287.59 (N.A.) {5,409.00}	2,435.44	57.46
		550	RATLE HE PROJECT (NHPC) (N18000324)	2-2021	2/2026 (N.A.) {11/2028}	5,281.94 (N.A.) {5,281.94}	915.50	21.29
		551	KWAR HE PROJECT (CVPPPL) (N18000363)	5-2022	11/2026 (N.A.) {12/2027}	4,526.12 (N.A.) {4,526.12}	982.65	19.75
	RAILWAYS	552	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR (NR) (220100133)	3-1995	11/2002 (12/2024) {12/2024}	2,500.00 (37,012.26) {43,780.00}	42,312.02	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	553	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A (NHAI) (N24000471)	12-2015	6/2019 (N.A.) {}	2,168.66 (N.A.) {2,168.66}	-	0
		554	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A (NHAI) (N24000488)	12-2015	12/2018 (4/2025) {4/2025}	2,136.97 (2,644.00) {2,644.00}	2,386.23	99.5
		555	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE (NHAI) (N24000717)	12-2017	7/2021 (3/2025) {3/2025}	1,471.75 (1,471.75) {1,903.98}	1,662.19	98.44
		556	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU- AKHNOOR ROAD SECTION OF NH- 144A FROM GANESH VIHA (NHIDCL) (N24000868)	3-2018	7/2021 (8/2023) {10/2025}	253.44 (N.A.) {253.44}	187.74	81.56
		557	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D (NHIDCL) (N24001256)	8-2020	9/2026 (N.A.) {9/2026}	6,808.69 (N.A.) {6,808.69}	3,013.84	49.92
		558	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL (NHIDCL) (N24001264)	7-2020	4/2022 (10/2024) {10/2026}	228.39 (N.A.) {228.39}	67.60	87.38
		559	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K (NHIDCL) (N24001266)	7-2020	4/2022 (11/2023) {5/2025}	210.79 (N.A.) {210.79}	71.00	89.92
		560	KHELLANI-KHANABAL PKG-1 (NHIDCL) (N24001323)	3-2021	9/2022 (10/2024) {10/2024}	486.45 (N.A.) {486.45}	126.73	96.58

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		561	KHELLANI-KHANABAL PKG-3 (NHIDCL) (N24001341)	3-2021	12/2022 (10/2024) {4/2025}	398.51 (N.A.) {398.51}	80.64	95.38
		562	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 (NHIDCL) (N24001342)	3-2021	12/2022 (N.A.) {7/2024}	260.40 (N.A.) {260.40}	191.88	100
		563	KHELLANI-KHANABAL PKG-2 (NHIDCL) (N24001394)	7-2021	2/2023 (6/2025) {6/2026}	512.43 (N.A.) {512.43}	71.65	50.91
		564	KHELLANI-KHANABAL PKG-4 (NHIDCL) (N24001395)	7-2021	8/2023 (12/2025) {6/2026}	859.67 (N.A.) {859.67}	190.91	44.02
		565	KHELLANI-KHANABAL PKG-5 (NHIDCL) (N24001396)	7-2021	2/2023 (3/2025) {6/2025}	497.09 (N.A.) {497.09}	172.85	86.05
		566	GOHA-KHELLANI PKG-3 (NHIDCL) (N24001397)	2-2021	3/2023 (10/2024) {3/2025}	431.28 (N.A.) {431.28}	365.12	99.84
		567	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA (NHAI) (N24001472)	9-2021	12/2023 (6/2024) {6/2024}	811.19 (N.A.) {811.19}	848.57	99
		568	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY (NHAI) (N24001511)	3-2021	2/2024 (4/2025) {10/2025}	2,919.96 (N.A.) {2,919.96}	2,281.47	66.5
		569	FOUR LANING OF JAMMU-AKHNOOR PKG-1 (NHIDCL) (N24001543)	7-2022	1/2025 (N.A.) {10/2025}	245.34 (N.A.) {245.34}	57.03	38.47

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		570	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)- KUNJWANI SECTION OF NH-4 (NHAI) (N24001550)	9-2021	9/2024 (9/2025) {9/2025}	1,821.72 (1,917.32) {1,917.32}	910.08	78.6
		571	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT- GURDASPUR ROAD (NH-5 (NHAI) (N24001551)	10-2021	9/2024 (7/2025) {7/2025}	3,044.02 (3,044.02) {3,044.02}	1,483.20	64.04
		572	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B (NHAI) (N24001552)	10-2021	9/2024 (9/2025) {9/2025}	2,714.95 (2,714.95) {2,714.95}	1,626.47	79.97
		573	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH- (NHAI) (N24001619)	8-2022	6/2024 (6/2025) {6/2025}	200.05 (200.05) {208.92}	125.20	54.42
		574	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SLIP ZONES AT KM 130.550 TO KM.130.750; KM. (NHAI) (N24001620)	9-2021	10/2023 (12/2025) {12/2025}	442.14 (N.A.) {442.14}	328.36	19.88
		575	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL. (NHAI) (N24001621)	7-2021	8/2024 (6/2025) {6/2025}	614.48 (N.A.) {614.48}	185.83	7
		576	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX (NHAI) (N24001622)	7-2021	6/2024 (6/2025) {6/2025}	1,401.87 (N.A.) {1,401.87}	686.33	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		577	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM. 187.00 TO KM. 189.350 (NHAI) (N24001623)	1-2020	1/2024 (4/2025) {4/2025}	336.01 (N.A.) {336.01}	222.92	34
		578	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI (NHAI) (N24001624)	7-2019	10/2020 (4/2023) {9/2024}	157.05 (N.A.) {157.05}	139.54	100
		579	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K (NHAI) (N24001627)	7-2021	2/2025 (5/2026) {5/2026}	1,912.17 (N.A.) {1,912.17}	129.05	0
		580	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B (NHIDCL) (N24001833)	7-2022	3/2025 (N.A.) {8/2025}	198.28 (N.A.) {198.28}	80.80	67.29
		581	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 102 TO KM 13 (BRO) (N24001897)	3-2021	7/2024 (3/2025) {3/2024}	642.24 (N.A.) {642.24}	498.80	95
		582	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 30.000 TO K (BRO) (N24001898)	7-2020	11/2024 (N.A.) {11/2024}	272.49 (N.A.) {272.49}	180.48	87.24
		583	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 134.95 TO KM (BRO) (N24001899)	2-2021	7/2024 (N.A.) {3/2025}	395.25 (N.A.) {395.25}	211.75	64

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		584	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 49.150 TO KM (BRO) (N24001900)	3-2020	8/2024 (N.A.) {3/2025}	796.97 (N.A.) {796.97}	468.35	79
		585	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 64.535 TO K (BRO) (N24001901)	3-2020	9/2023 (N.A.) {3/2025}	152.93 (N.A.) {152.93}	103.81	78.27
		586	CONSTRUCTION OF TWIN TUBE TUNNELS ON JAMMU KASHMIR RING ROAD (NH-244A) BETWEEN DESIGN CH. 50+600 TO (NHAI) (N24001926)	3-2023	6/2025 (N.A.) {6/2025}	939.86 (N.A.) {939.86}	367.18	60.25
		587	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER FROM (DESIGN CH. 14+200 TO 24+400), (DESIGN CH. 35+300 TO (BRO) (N24001998)	6-2022	8/2025 (N.A.) {8/2025}	832.46 (N.A.) {823.46}	362.09	46
		588	2L NH-1 FROM KM 8.660 TO KM 33.775 (SUMBAL TO WAYUL) TO 4L DUAL CARRIAGEWAY NH STANDARD AS PART OF S (NHAI) (N24002059)	9-2022	6/2026 (6/2026) {12/2026}	1,183.60 (N.A.) {1,183.60}	168.02	9.87
		589	DELHI AMRITSAR KATRA EXPRESSWAY (PHASE-II PKG XVIII) DEVELOPMENT AND UPGRADATION OF FOUR LANE ACCESS (NHAI) (N24002060)	3-2023	11/2025 (N.A.) {11/2025}	1,107.00 (N.A.) {975.38}	274.78	31.5
		590	4/6L ACCESS CONTROL EXPRESSWAY FROM DESIGN CHAINAGE KM 515.000 TO 528.300 (KUNJWANI TO SIDHRA SECTIO (NHAI) (N24002061)	8-2022	6/2025 (N.A.) {8/2025}	2,474.47 (N.A.) {2,894.74}	921.13	32

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		591	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM 162.800 TO KM (BRO) (N24002119)	10-2022	1/2026 (N.A.) {1/2026}	562.45 (N.A.) {562.45}	99.06	25
		592	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER (PATTAN BYPASS) GREENFIELD BYPASS FROM EXISTING CH. KM 24 (BRO) (N24002179)	3-2023	7/2026 (N.A.) {7/2026}	980.21 (N.A.) {980.21}	300.02	8
		593	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 166.100 TO KM (BRO) (N24002180)	9-2021	7/2026 (N.A.) {7/2026}	734.64 (N.A.) {734.64}	19.60	8
		594	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDERS (BARAMULLA BYPASS) GREENFIELD BYPASS FROM EXISTING CH. K (BRO) (N24002185)	3-2023	9/2026 (N.A.) {9/2026}	992.43 (N.A.) {992.43}	338.33	0
		595	WIDENING AND STRENGTHENING OF RAFIABAD-KUPWARA-CHOWKIBAL- TANGDHAR-CHAMKOT (NH-701) ROAD FROM DESIGN (BRO) (N24002210)	3-2024	5/2027 (N.A.) {5/2027}	1,404.94 (N.A.) {1,404.94}	-	0
JHARKHAND	COAL	596	RAJRAPPA RCE OCP (3.0 MTY) (CCL) (N06000087)	12-2009	3/2016 (N.A.) {3/2027}	510.85 (N.A.) {510.85}	488.57	75
		597	MURAIIDH UG TURN-KEY PROJECT (BCCL) (N06000096)	2-2011	4/2014 (N.A.) {1/2026}	339.88 (N.A.) {339.88}	190.48	70

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		598	MOONIDIH XV SEAM UG (BCCL) (N06000098)	8-2011	3/2019 (N.A.) {2/2026}	1,230.27 (N.A.) {1,230.27}	602.16	80.3
		599	MADHUBAND NLW WASHERY (BCCL) (N06000126)	5-2010	5/2014 (N.A.) {11/2023}	289.45 (N.A.) {302.00}	300.01	100
		600	CHITRA EAST (RCE) OCP (ECL) (N06000169)	8-2018	3/2026 (3/2026) {3/2026}	513.98 (N.A.) {513.98}	224.02	51
		601	TETARIAKHAR EXPANSION OCP (CCL) (N06000186)	11-2019	3/2023 (N.A.) {3/2027}	243.52 (N.A.) {243.52}	44.39	24
		602	PACHWARA SOUTH COAL BLOCK (NLC) (N06000193)	7-2013	9/2028 (N.A.) {9/2028}	2,242.92 (2,242.90) {2,242.90}	540.80	44
		603	PATHERDIH 2.5 NLW COAL WASHERY (BCCL) (N06000194)	10-2015	4/2018 (N.A.) {3/2026}	334.27 (N.A.) {334.27}	132.74	44
		604	REVISED PROJECT REPORT MAGADH EXPANSION OCP (CCL) (N06000216)	8-2020	3/2028 (N.A.) {3/2028}	7,254.37 (N.A.) {7,254.37}	1,493.62	29
		605	EXPANSION PROJECT AMRAPALI OCP (CCL) (N06000217)	8-2020	3/2028 (N.A.) {3/2028}	5,136.15 (N.A.) {5,136.15}	1,054.89	40
		606	UCE OF EPR OF NORTH URIMARI OCP (CCL) (N06000218)	7-2021	3/2029 (N.A.) {3/2026}	778.80 (N.A.) {778.80}	694.11	75

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		607	KOTRE BASANTPUR PACHMO OCP (CCL) (N06000237)	8-2020	3/2032 (N.A.) {3/2032}	625.40 (625.40) {625.40}	441.00	41
		608	CHANDRAGUPT OCP (CCL) (N06000238)	8-2020	3/2032 (N.A.) {3/2032}	973.50 (N.A.) {973.50}	339.32	12.4
		609	SIRKA OCP (CCL) (N06000239)	5-2020	3/2028 (N.A.) {3/2025}	222.82 (N.A.) {222.82}	139.31	60
		610	JHARKHAND LAIYO OCP (CCL) (N06000240)	8-2020	3/2031 (N.A.) {3/2031}	764.57 (N.A.) {764.57}	145.80	21
		611	EPR TAPIN SOUTH OCP (CCL) (N06000241)	11-2020	3/2028 (N.A.) {3/2025}	230.41 (N.A.) {230.41}	20.29	18.3
		612	EPR PUNDI OCP (CCL) (N06000242)	11-2020	3/2027 (N.A.) {3/2027}	713.35 (N.A.) {713.35}	236.57	21
		613	EPR ROHINI KARKATA OCP (CCL) (N06000243)	1-2021	3/2028 (N.A.) {3/2028}	1,020.42 (N.A.) {1,020.42}	83.44	11.7
		614	EXPANSION OF KONAR OCP (CCL) (N06000245)	1-2022	3/2032 (N.A.) {3/2032}	799.34 (N.A.) {799.34}	405.16	32
		615	EXPANSION OF KARO OCP (CCL) (N06000246)	1-2022	3/2029 (N.A.) {3/2026}	908.47 (N.A.) {908.47}	181.79	20

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		616	EXPANSION OF ASHOK OCP (CCL) (N06000247)	5-2021	3/2028 (N.A.) {3/2028}	2,898.28 (N.A.) {2,898.28}	175.10	20
		617	AMALGAMATED NTST KUJAMA OCP 8.5 MTY (BCCL) (N06000273)	1-2023	3/2030 (N.A.) {3/2030}	4,011.85 (N.A.) {4,011.85}	397.65	25
		618	HURA C OC (ECL) (N06000275)	8-2022	3/2029 (N.A.) {3/2029}	859.41 (N.A.) {859.41}	440.20	62
		619	CHUPERBHITA- SIMLONG OCP (ECL) (N06000280)	12-2023	3/2037 (3/2037) {3/2037}	979.08 (N.A.) {979.08}	-	0
		620	BLOCK-E OCP (15 MTY) (BCCL) (N06000287)	3-2024	3/2029 (N.A.) {3/2029}	5,850.83 (N.A.) {5,850.83}	5.36	1.63
	DEPARTMENT OF HIGHER EDUCATION	621	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD (CPWD EDUCATION) (N28000067)	9-2012	3/2016 (N.A.) {3/2016}	171.86 (N.A.) {171.86}	176.08	0
	PETROLEUM	622	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK (ONGC) (N16000239)	12-2015	3/2023 (3/2024) {6/2025}	823.27 (1,137.79) {1,137.79}	1,067.89	100
		623	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) (ONGC) (N16000445)	11-2019	1/2024 (3/2025) {6/2025}	431.00 (N.A.) {431.00}	184.68	57.8
		624	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI (IOCL) (N16000480)	3-2023	2/2026 (N.A.) {2/2026}	202.07 (N.A.) {202.07}	48.24	40.57

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		625	CGD PROJECT IN BIHAR JHARKHAND (HPCL) (N16000497)	6-2022	6/2030 (N.A.) {6/2030}	1,377.00 (N.A.) {1,377.00}	238.55	21.5
	POWER	626	NORTH KARANPURA STPP (3X660 MW) (NTPC) (N18000177)	2-2014	6/2019 (10/2022) {3/2025}	16,242.90 (N.A.) {16,242.90}	16,664.81	98
		627	PATRATU STPP-I (3X800MW) (NTPC) (N18000275)	11-2017	3/2023 (N.A.) {3/2026}	17,112.00 (N.A.) {17,112.00}	16,287.00	81
		628	BADAM COAL MINING PROJECT (NTPC) (N18000367)	2-2019	10/2024 (N.A.) {4/2027}	501.79 (784.39) {501.79}	301.98	59.79
		629	KERANDARI COAL MINING PROJECT (NTPC) (N18000370)	9-2015	11/2019 (3/2025) {3/2025}	1,553.00 (2,896.64) {2,896.64}	2,002.35	64
	RAILWAYS	630	KODERMA-TILAIYA (NL), ECR (ECR) (220100305)	4-2002	(N.A.) {12/2025}	459.91 (1,625.87) {1,700.00}	1,958.27	80
		631	BONDAMUNDA RANCHI DOUBLING (SER) (N22000396)	3-2016	3/2021 (N.A.) {6/2026}	1,724.20 (3,029.04) {3,029.04}	2,326.90	83
		632	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) (SER) (N22000508)	4-2018	6/2022 (N.A.) {6/2026}	428.65 (N.A.) {472.50}	275.56	2
		633	DOUBLING OF PRADHANKHUNTA JN - PATHERDIH BAZAR-BHOJUDIH (ECR) (N22000529)	11-2022	11/2027 (N.A.) {3/2026}	202.00 (349.22) {349.22}	55.43	2

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		634	KHARAGPUR-ADITYAPUR - 3RD LINE (132 KM) (RVNL) (N22000595)	12-2015	3/2025 (N.A.) {3/2025}	1,116.00 (N.A.) {3,270.07}	2,899.45	0
		635	3RD LINE BETWEEN DHANBAD SONNAGAR (RVNL) (N22000599)	11-2016	3/2026 (N.A.) {3/2026}	8,975.00 (N.A.) {7,906.38}	4,705.38	0
		636	GARHWA ROAD - RAIL OVER RAIL (ECR) (N22000610)	3-2017	3/2024 (N.A.) {2/2026}	262.71 (N.A.) {262.71}	203.10	80
		637	GOMOH - FLYOVER FOR DOWN TRAINS (ECR) (N22000611)	1-2018	12/2025 (N.A.) {3/2026}	487.73 (N.A.) {487.73}	375.64	45
	ROAD TRANSPORT AND HIGHWAYS	638	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION (NHAI) (N24000726)	1-2018	11/2021 (6/2025) {6/2025}	1,155.16 (N.A.) {950.49}	644.97	70
		639	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I (MoRTH) (N24001216)	12-2016	9/2021 (N.A.) {12/2024}	196.00 (N.A.) {196.00}	164.21	90.1
		640	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 (NHAI) (N24001589)	9-2020	3/2024 (12/2024) {4/2025}	755.26 (N.A.) {1,039.00}	620.38	85.1
		641	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH-75 [REHLA / GARHWA BYPASS] (NHAI) (N24001590)	9-2020	10/2023 (12/2024) {1/2025}	748.99 (N.A.) {903.00}	828.41	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		642	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM (NHAI) (N24001594)	2-2022	1/2025 (3/2025) {3/2025}	534.73 (N.A.) {534.73}	125.31	90
		643	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH (NHAI) (N24001595)	8-2020	3/2024 (6/2025) {6/2025}	1,034.00 (1,879.55) {1,879.55}	41.50	95.69
		644	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF (NHAI) (N24001596)	11-2021	7/2023 (6/2025) {6/2025}	1,302.72 (1,504.80) {1,504.80}	865.35	74.51
		645	FOUR LANING WITH PAVED SHOULDER OF SECTION FROM KM 53.600 (GOLA ON NH-320) TO KM 81.446 (ORMANJHI ON (NHAI) (N24001854)	6-2023	6/2025 (N.A.) {6/2025}	1,214.93 (1,324.95) {1,324.95}	702.00	65
		646	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM 0.00 TO 44.00 (KURU-GHAGHRA SECTION) OF NH-143A INCLU (MoRTH) (N24001922)	2-2020	8/2023 (N.A.) {12/2024}	153.01 (N.A.) {153.01}	83.63	96.23
		647	WIDENING AND STRENGTHENING OF EXISTING PAVEEMNT TO TWO LANE WITH PAVED SHOULDERS FROM KM 116.00 TO K (MoRTH) (N24001923)	1-2022	7/2024 (N.A.) {12/2024}	315.21 (N.A.) {315.21}	117.26	80
		648	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDER/TWO LANE+ PAVED SHOULDER WITH SERVICE ROA (MoRTH) (N24001924)	3-2022	8/2025 (N.A.) {8/2025}	514.22 (N.A.) {514.22}	15.19	6.1

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		649	WIDENING AND STRENGTHENING/RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDER/ TWO LANE WITH PAVED SHOUL (MoRTH) (N24001925)	3-2022	8/2025 (N.A.) {8/2025}	423.18 (N.A.) {423.18}	0.11	0
		650	FOUR LANING OF KHAJURI TO WYNDHAMGANJ FROM KM 219.600 TO KM 260.483 ON NH-75 PKG SEC-V ON HAM (NHAI) (N24002053)	4-2022	9/2025 (N.A.) {9/2025}	1,232.00 (1,343.00) {1,400.00}	606.60	75
		651	FOUR LANING OF BHOGU TO SANKHA FROM KM 147.450 TO KM 196.870 ON NH-75 PKG SEC-III (NHAI) (N24002054)	10-2022	11/2025 (N.A.) {11/2025}	1,390.77 (1,391.00) {1,600.00}	296.46	62.81
		652	FOUR LANING OF BASUKINATH- DEOGHAR SECTION OF NH-114A FROM KM 85.081 TO KM 130.240 UNDER NHDP PHASE-I (NHAI) (N24002055)	3-2023	12/2025 (N.A.) {12/2025}	1,444.94 (N.A.) {1,444.94}	-	0
		653	BHARATMALA PARIYOJANA OF BOKARO JAINA MORE - GOLA SECTION OF NH-320 FROM KM. 21.110 TO KM. 53.600 IN (NHAI) (N24002056)	6-2020	6/2025 (N.A.) {6/2025}	964.64 (N.A.) {964.64}	406.82	51.02
		654	FOUR LANING OF MEHGAMA HANSDIHA SECTION OF NH-33 FROM EXISTING KM 41.900 TO 93.000 IN THE STATE OF J (NHAI) (N24002057)	12-2022	5/2025 (N.A.) {5/2025}	1,443.77 (N.A.) {1,443.77}	-	0
	STEEL	655	NEW SINTER PLANT AT BOKARO STEEL PLANT (SAIL) (N12000095)	3-2015	10/2017 (11/2026) {11/2026}	1,034.01 (1,752.30) {1,752.30}	874.25	51.75
		656	REVAMPING OF OLD SUB SYSTEM OF BLAST FURNACE 3 AT BOKARO STEEL PLANT (SAIL) (N12000129)	9-2023	7/2025 (N.A.) {7/2025}	513.82 (N.A.) {513.82}	121.69	60

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
KARNATAKA		657	REBUILDING OF COKE OVEN BATTERY NO.6 OF BOKARO STEEL PLANT (SAIL) (N12000133)	11-2023	11/2026 (N.A.) {11/2026}	627.31 (N.A.) {627.31}	75.15	29
		658	REPLACEMENT OF REMAINING 04 NOS. OF BATTERY CYCLONES WITH 04 NOS. OF ESPS IN SINTER PLANT-1 AT BSL (SAIL) (N12000135)	3-2024	6/2026 (N.A.) {6/2026}	260.37 (N.A.) {260.37}	19.53	9
	CIVIL AVIATION	659	BELAGAVI AIRPORT- EXPANSION OF TERMINAL BUILDING AND ASSOCIATED WORKS (AAI) (N04000105)	6-2023	2/2026 (N.A.) {2/2026}	322.45 (N.A.) {322.45}	77.36	35
		660	HUBBALI AIRPORT - CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS (AAI) (N04000108)	6-2023	2/2026 (N.A.) {2/2026}	320.47 (N.A.) {320.47}	49.67	25
	DEPARTMENT OF HIGHER EDUCATION	661	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) (CPWD EDUCATION) (N42000006)	7-2019	3/2022 (N.A.) {3/2023}	851.00 (851.00) {851.00}	888.66	98.75
		662	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL (CPWD) (N42000010)	8-2021	2/2024 (11/2024) {11/2024}	316.25 (N.A.) {316.25}	333.42	94
	PETROLEUM	663	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE (HPCL) (N16000369)	12-2018	12/2022 (8/2025) {8/2025}	854.00 (854.00) {854.00}	681.05	94.95

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		664	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE (IOCL) (N16000437)	1-2022	7/2025 (12/2025) {12/2025}	463.00 (500.62) {500.62}	232.76	70.14
		665	POWER SYSTEM UPGRADATION PROJECT (MANGALORE REFIN) (N16000509)	10-2023	2/2026 (N.A.) {2/2026}	385.00 (N.A.) {385.00}	119.40	45.37
		666	DEMO PLANT FOR PRODUCTION OF BIO-ATF (MANGALORE REFIN) (N16000536)	3-2024	3/2027 (N.A.) {3/2027}	364.00 (N.A.) {364.00}	9.72	2.2
	POWER	667	TS FOR INTRGRATION OF RE ZONE (PHASE II) IN KOPPAL II (PHASE A and B) AND GADAG II (PHASE A) IN KARN (PGCIL) (N18000385)	12-2023	12/2025 (N.A.) {12/2025}	2,889.00 (N.A.) {2,889.00}	413.00	20
		668	TS FOR SOLAR ENERGY ZONE IN BIDAR (2500MW), KARNATAKA [BIDAR TRANSMISSION LTD] (PGCIL) (N18000388)	2-2024	2/2026 (N.A.) {2/2026}	2,148.00 (N.A.) {2,148.00}	436.00	36
	RAILWAYS	669	TUMKUR-CHITRADURGA-DAVENGERE NL (SWR) (N22000256)	4-2011	(N.A.) {12/2027}	1,801.01 (N.A.) {1,801.01}	488.99	12
		670	BAGALKOT-KUDACHI NL (SWR) (N22000258)	4-2010	3/2016 (N.A.) {3/2027}	986.30 (1,378.00) {1,378.00}	601.72	34
		671	HOSPET-HUBLI-LONDA- VASCODAGAMA DL (RVNL) (N22000297)	4-2010	3/2023 (N.A.) {12/2026}	2,127.00 (N.A.) {3,692.60}	3,505.49	0
		672	GADAG-WADI NL (SWR) (N22000299)	4-2013	12/2018 (N.A.) {12/2027}	2,841.84 (N.A.) {2,841.84}	1,275.81	28

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		673	MARIKUPPAM - KUPPAM (SWR) (N22000308)	4-2012	3/2016 (N.A.) {12/2027}	279.54 (296.72) {296.72}	120.58	14
		674	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) (SWR) (N22000486)	3-1996	3/2017 (N.A.) {3/2026}	644.78 (825.31) {825.31}	681.97	66
		675	BAIYYAPPANAHALLI-HOSUR (48 KM) (NCRTC) (N22000542)	4-2019	3/2026 (N.A.) {3/2026}	375.67 (N.A.) {375.67}	-	0
		676	YESHVANTHPUR-CHANNASANDRA (21.7 KM) (NCRTC) (N22000543)	4-2019	3/2026 (N.A.) {3/2026}	169.65 (N.A.) {169.65}	71.75	0
		677	BELGAUM-DHARWAD VIA KITTUR (73.10 KM) (UMBRELLA WORK PB#22/2019-20/NR) (SWR) (N22000557)	9-2020	3/2026 (N.A.) {12/2027}	1,590.80 (927.42) {927.42}	0.69	0
		678	HASSAN (ALUR) - BELUR (32 KM) (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000558)	6-2019	4/2028 (N.A.) {3/2028}	663.03 (748.85) {748.85}	0.88	1
		679	SHIMOGA-SHIKARIPURA- RANEBENNUR (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000559)	9-2019	12/2027 (N.A.) {12/2027}	1,453.73 (994.47) {994.47}	70.81	7
		680	BANGALORE-WHITEFIELD- BANGALORE CITY- KRISHNARAJAPURAM QUADRUPLING (SWR) (N22000621)	3-2018	3/2025 (N.A.) {6/2025}	492.87 (N.A.) {492.87}	230.66	75

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	681	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP (MoRTH) (N24000334)	3-2015	11/2015 (8/2024) {8/2024}	165.67 (N.A.) {165.67}	126.47	99
		682	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION (NHAI) (N24000462)	7-2012	8/2016 (1/2020) {6/2025}	1,655.01 (1,990.38) {1,990.38}	1,815.01	97.8
		683	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY (NHAI) (N24000552)	3-2016	3/2019 (12/2023) {6/2025}	701.40 (591.86) {701.40}	526.83	88
		684	HOSPET-BELLARY-KARNATAKA AP BORDER (NHAI) (N24000603)	8-2016	3/2019 (5/2025) {5/2025}	1,167.42 (N.A.) {1,224.01}	988.03	84.1
		685	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS ? PA (MoRTH) (N24001156)	1-2017	9/2017 (5/2023) {5/2023}	166.67 (N.A.) {264.34}	192.08	100
		686	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH (MoRTH) (N24001157)	8-2016	2/2017 (7/2024) {7/2024}	175.50 (N.A.) {241.60}	189.72	90
		687	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 (MoRTH) (N24001158)	3-2018	6/2019 (12/2023) {12/2023}	159.97 (N.A.) {242.61}	113.15	100
		688	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHA SECTION (MoRTH) (N24001159)	1-2018	7/2018 (N.A.) {3/2022}	159.70 (N.A.) {159.70}	142.88	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		689	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA- HULIYAR (MoRTH) (N24001160)	9-2017	10/2018 (4/2022) {4/2022}	191.60 (N.A.) {191.60}	112.03	100
		690	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- (MoRTH) (N24001161)	12-2017	1/2019 (4/2022) {4/2022}	297.30 (N.A.) {318.28}	280.25	100
		691	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN (MoRTH) (N24001162)	3-2018	10/2018 (11/2022) {11/2022}	325.86 (N.A.) {386.41}	356.78	100
		692	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH- 50 UNDER EPC MODE IN THE STATE OF KARN (MoRTH) (N24001164)	10-2016	3/2017 (7/2022) {7/2022}	396.96 (N.A.) {396.96}	329.58	100
		693	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT (MoRTH) (N24001165)	11-2016	3/2017 (10/2021) {10/2021}	314.90 (N.A.) {314.90}	233.95	100
		694	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014- 15-775) (MoRTH) (N24001166)	3-2015	1/2016 (N.A.) {7/2024}	159.12 (N.A.) {159.12}	127.72	98
		695	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT (MoRTH) (N24001168)	5-2018	5/2018 (12/2023) {12/2023}	171.60 (N.A.) {171.60}	134.81	100
		696	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U (MoRTH) (N24001172)	1-2017	8/2017 (N.A.) {6/2022}	291.49 (N.A.) {291.49}	238.77	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		697	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI ? JADERCELA SECTION (MoRTH) (N24001173)	2-2017	5/2019 (N.A.) {10/2025}	157.32 (188.00) {187.61}	62.31	60
		698	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT (MoRTH) (N24001387)	1-2017	9/2017 (5/2023) {5/2023}	264.34 (N.A.) {264.34}	201.07	100
		699	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA (MoRTH) (N24001388)	3-2019	12/2019 (11/2024) {11/2024}	423.15 (N.A.) {423.15}	284.58	82
		700	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN (NHAI) (N24001425)	3-2021	11/2021 (8/2025) {8/2025}	1,100.88 (1,687.31) {1,687.31}	1,097.77	76.78
		701	4L OF ADDAHOLE TO BANTWAL CROSS SECTION (NHAI) (N24001426)	3-2021	10/2021 (4/2025) {4/2025}	317.90 (572.01) {572.01}	362.23	97.42
		702	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) (NHAI) (N24001598)	1-2022	4/2025 (4/2025) {4/2025}	1,388.70 (1,388.70) {1,388.70}	438.61	60.25
		703	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. (NHAI) (N24001599)	3-2018	12/2022 (12/2022) {11/2025}	440.16 (N.A.) {440.16}	348.59	67.03
		704	BANGALORE/TN BORDER TO HOSKOTE (NHAI) (N24001674)	2-2023	2/2025 (8/2025) {8/2025}	1,240.60 (N.A.) {1,240.60}	927.79	78.3

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		705	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 (NHAI) (N24001675)	11-2022	5/2025 (N.A.) {5/2025}	1,732.73 (N.A.) {1,732.73}	540.35	97.95
		706	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 (NHAI) (N24001676)	12-2022	6/2025 (3/2026) {6/2025}	2,718.46 (N.A.) {2,718.46}	438.90	50.88
		707	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12 (NHAI) (N24001677)	11-2022	5/2024 (5/2024) {5/2024}	226.76 (226.76) {226.76}	80.26	66.07
		708	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 (NHAI) (N24001679)	10-2022	4/2025 (4/2025) {4/2025}	1,479.30 (1,479.30) {1,479.30}	580.74	76.5
		709	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE (NHAI) (N24001680)	3-2021	10/2024 (12/2025) {12/2025}	1,409.68 (1,808.12) {1,808.12}	969.92	55.35
		710	TUMKUR - NELAMANGALA(6L) (NHAI) (N24001681)	8-2022	8/2025 (3/2027) {3/2027}	2,032.15 (2,032.15) {2,032.15}	177.48	46.91
		711	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA (NHAI) (N24001682)	11-2021	3/2024 (3/2024) {5/2026}	294.62 (309.90) {309.90}	50.21	14.17
		712	AURAD - BIDAR KM 0.00 TO KM 45.878 (NHAI) (N24001683)	9-2021	4/2023 (12/2024) {12/2024}	912.37 (N.A.) {424.16}	330.84	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		713	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION (NHAI) (N24001684)	9-2020	1/2023 (9/2020) {5/2025}	688.00 (602.09) {688.00}	514.23	80.02
		714	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 (NHAI) (N24001686)	3-2021	3/2023 (12/2025) {12/2025}	1,065.06 (1,444.50) {1,444.50}	188.48	93.5
		715	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 (NHAI) (N24001687)	10-2021	10/2023 (12/2025) {12/2025}	1,331.77 (2,082.98) {2,082.98}	463.54	75.72
		716	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN (NHAI) (N24001691)	10-2019	10/2021 (12/2025) {12/2025}	1,225.24 (1,505.85) {1,505.85}	130.38	96.85
		717	BALANCE WORK OF CONTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM. 54.370 TO KM. 101.400 (BI (MoRTH) (N24001936)	3-2021	3/2023 (7/2024) {7/2024}	344.79 (N.A.) {344.79}	10.00	90
		718	BALANCE WORK OF REHABILITATION AND UPGRADING TO 2LANE/2LANE WITH PAVED SHOULDER CONFIGURATION AND ST (MoRTH) (N24001937)	2-2023	2/2024 (2/2025) {2/2025}	398.48 (N.A.) {398.48}	5.00	50
		719	CONSTRUCTION OF ELEVATED CORRIDOR FROM KM. 135.650 TO 136.300 ON 63, FROM KM. 249 TO KM. 250.050 ON (MoRTH) (N24001938)	6-2021	6/2024 (6/2025) {6/2025}	298.00 (N.A.) {298.00}	10.70	52

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		720	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24001940)	1-2023	1/2026 (9/2025) {9/2025}	166.58 (N.A.) {166.58}	3.54	0
		721	WIDENING TO 4 LANE FROM KM. 133.00 TO 158.04 (DESIGN CHAINAGE KM. 130.88 TO 155.145) (SHIRUR CROSS T (MoRTH) (N24001941)	1-2023	1/2025 (1/2025) {1/2025}	350.69 (N.A.) {350.69}	10.00	56
		722	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM. 33.13 TO KM. 40.23 AND KM. 52.00 TO KM. 71.00 (EX (MoRTH) (N24001943)	9-2022	3/2024 (1/2025) {1/2025}	172.98 (N.A.) {172.98}	6.48	65
		723	WIDENING TO INTERMEDIATE/TWO LANE TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHANAGES KM 112.750 TO (MoRTH) (N24001944)	1-2023	6/2024 (7/2024) {7/2024}	255.88 (N.A.) {255.88}	60.99	78
		724	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 116.800 TO 149.070(DESIGN CHANGES) ON HOSADURGA HOL (MoRTH) (N24001945)	8-2022	2/2024 (12/2024) {12/2024}	170.34 (N.A.) {170.34}	4.25	72
		725	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM 24.400 TO 27.270, 40.500 TO 41.900, 84.300 TO 88.20 (MoRTH) (N24001946)	11-2022	11/2024 (11/2024) {11/2024}	218.93 (N.A.) {218.93}	10.00	95
		726	WIDENING TO EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FROM DESIGN KM 153.00 (MoRTH) (N24001947)	2-2023	2/2025 (2/2025) {2/2025}	177.94 (N.A.) {177.94}	6.66	47

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		727	WIDENING TO 4 LANE FROM KM 51.60 TO 76.20 (HEBRI TO PARKALA) AND FROM KM 85.20 TO 88.90 (KARAVALI JU) (MoRTH) (N24001948)	10-2022	10/2024 (12/2024) {12/2024}	355.72 (N.A.) {355.72}	11.32	60
		728	FOUR LANING OF LEFT OVER WORKS OF HOSPET BELLARY KARNATAKA/ AP BORDER FROM KM.280.080 TO KM. 375.450 (NHAI) (N24001989)	3-2023	5/2025 (N.A.) {5/2025}	830.28 (N.A.) {830.28}	594.40	69.24
		729	DEVELOPMENT OF 6 LANE ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KM. 97.000 TO KM. 162.500 MARADGI S (NHAI) (N24001993)	12-2022	10/2025 (N.A.) {10/2025}	1,589.00 (N.A.) {1,589.00}	483.76	58.55
		730	4/6L OF BANGALORE - PUNE SECTION OF BYPASS CONNECTING DHARWAD - HUBLI FROM KM. 403.80 TO KM. 433.20 (NHAI) (N24001994)	5-2022	3/2023 (N.A.) {9/2025}	1,135.39 (N.A.) {1,135.39}	339.37	63.75
		731	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM 422.000 TO 523.600 (CHITR) (MoRTH) (N24002011)	12-2021	6/2024 (12/2024) {12/2024}	516.96 (N.A.) {516.96}	19.93	70
		732	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40.00 TO KM 75.00 (EXISTING CHAINAGES) OF MANGALOR (MoRTH) (N24002012)	3-2023	3/2025 (3/2025) {3/2025}	718.52 (N.A.) {718.52}	24.81	23
		733	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM KM.0 TO KM. 80 ON NH 548B (VIJAYAPURA-SANKESWAR SE) (MoRTH) (N24002013)	3-2021	2/2022 (10/2024) {10/2024}	766.64 (N.A.) {766.64}	13.55	75

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		734	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24002186)	3-2024	9/2025 (N.A.) {9/2025}	166.58 (N.A.) {166.58}	3.62	0
		735	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM 55.6 TO KM 90.7 (EXISTING CHAINAGES) OF NH-766C ((MoRTH) (N24002187)	2-2024	2/2026 (N.A.) {2/2026}	313.56 (N.A.) {313.56}	53.65	0
		736	WIDENING TO 2L+PS FROM KM 71.00 TO 104.00 (EXISTING CHAINAGES) (SARJAPUR TO PATTADKALLU) ON BHANAPUR (MoRTH) (N24002188)	3-2024	3/2026 (N.A.) {3/2026}	445.62 (N.A.) {445.62}	33.24	0
		737	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0.00 (DESIGN CHAINAGE 0.00) TO KM 23.338 (DESIGN C (MoRTH) (N24002189)	9-2024	3/2026 (N.A.) {3/2026}	196.05 (N.A.) {196.05}	2.34	0
	STEEL	738	SCREENING PLANT-II, DONIMALAI (NMDC) (N12000136)	9-2023	8/2026 (N.A.) {8/2026}	1,043.63 (N.A.) {1,043.63}	176.30	9.43
	URBAN DEVELOPMENT	739	BANGALORE METRO RAIL PROJECT PHASE-2 (BMRCL) (N28000058)	2-2014	2/2021 (N.A.) {3/2025}	26,405.14 (N.A.) {26,405.14}	20,936.29	89
		740	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B (BMRCL) (N28000151)	6-2021	6/2026 (N.A.) {6/2026}	14,788.10 (N.A.) {14,788.10}	2,424.04	30
KERALA	CIVIL AVIATION	741	CALICUT AIRPORT - DEVELOPMENT OF ADDITIONAL RESA ON EITHER END ON RUNWAY 10-28 AT CALICUT AIRPORT (AAI) (N04000111)	6-2023	9/2025 (9/2025) {9/2025}	484.57 (N.A.) {323.98}	53.47	15

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	742	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA (CPWD EDUCATION) (N28000140)	7-2019	3/2021 (N.A.) {11/2025}	753.63 (N.A.) {753.63}	412.37	66
	<u>HEALTH AND FAMILY WELFARE</u>	743	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST (CPWD FOR HEALTH) (N28000112)	9-2017	3/2020 (5/2024) {11/2024}	150.29 (N.A.) {162.00}	159.03	100
	<u>PETROLEUM</u>	744	REPLACEMENT AND EXTENSION OF JETTY PIPELINES AT KOCHI REFINERY (BPCL) (N16000508)	3-2023	3/2026 (N.A.) {3/2026}	621.87 (N.A.) {621.87}	153.92	77.1
		745	SETTING UP POLYPROPYLENE UNIT AT KOCHI REFINERY (BPCL) (N16000530)	12-2023	10/2027 (N.A.) {10/2027}	4,460.00 (N.A.) {4,460.00}	126.40	8.7
	<u>RAILWAYS</u>	746	TRIVANDRUM-KANYAKUMARI DOUBLING (SR) (N22000399)	2-2015	(N.A.) {12/2027}	1,431.90 (N.A.) {3,785.45}	3,184.42	42.1
		747	ERNAKULAM-KUMBALAM - PATCH DOUBLING (7.71 KM) (SR) (N22000619)	12-2010	3/2028 (N.A.) {12/2026}	600.82 (N.A.) {595.39}	272.90	8
		748	KUMBALAM-THURAVUR - PATCH DOUBLING (15.59 KM) (SR) (N22000620)	12-2011	8/2023 (N.A.) {12/2026}	812.85 (N.A.) {802.80}	260.62	7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	749	4-LANNING OF THALSERRY -MAHE BYPASS (NHA) (N24000704)	9-2017	5/2020 (11/2023) {2/2024}	1,124.11 (1,573.18) {1,573.18}	1,525.61	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		750	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH (NHAI) (N24000784)	2-2018	2/2023 (12/2024) {5/2025}	1,424.77 (2,065.95) {2,065.95}	901.09	92.04
		751	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK (MoRTH) (N24001369)	2-2017	8/2017 (3/2022) {8/2024}	294.28 (296.53) {296.53}	286.80	98
		752	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) (MoRTH) (N24001370)	2-2017	9/2017 (1/2023) {8/2024}	380.76 (372.87) {372.87}	347.04	100
		753	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE (NHAI) (N24001648)	8-2022	1/2026 (N.A.) {1/2026}	2,429.52 (N.A.) {2,429.52}	1,022.58	53.8
		754	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 (NHAI) (N24001649)	12-2021	2/2025 (2/2025) {1/2026}	3,273.61 (N.A.) {3,273.61}	686.68	57.64
		755	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTTAM SECTION OF NH-66(OLD NH-47) FROM KM. 517+250 TO KM.54 (NHAI) (N24001650)	12-2021	1/2025 (8/2025) {8/2025}	3,635.64 (N.A.) {3,635.64}	280.92	37.75
		756	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O (NHAI) (N24001651)	9-2021	9/2024 (3/2026) {9/2024}	2,878.97 (N.A.) {2,878.97}	510.93	37.75

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		757	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR (NHAI) (N24001652)	3-2020	6/2022 (2/2024) {6/2024}	210.37 (216.94) {216.94}	198.10	100
		758	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH ?66 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 ((NHAI) (N24001653)	11-2021	4/2025 (N.A.) {4/2025}	3,565.82 (N.A.) {3,064.11}	1,997.05	57.61
		759	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 (NHAI) (N24001654)	6-2021	3/2025 (12/2025) {12/2025}	2,641.37 (N.A.) {2,641.37}	607.07	73.8
		760	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX (NHAI) (N24001655)	6-2021	2/2025 (N.A.) {11/2025}	3,606.00 (3,946.56) {3,946.56}	3,120.23	66.96
		761	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. (NHAI) (N24001656)	6-2021	3/2025 (N.A.) {12/2025}	2,595.00 (N.A.) {4,009.57}	3,044.77	60.2
		762	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC (NHAI) (N24001657)	6-2021	10/2024 (12/2025) {12/2025}	2,842.14 (N.A.) {2,842.14}	477.69	70.03
		763	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM (NHAI) (N24001658)	1-2021	7/2024 (3/2025) {3/2025}	4,265.42 (N.A.) {4,728.40}	3,474.04	98.7

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		764	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH (NHAI) (N24001659)	2-2021	7/2024 (3/2025) {3/2025}	3,375.31 (3,824.07) {3,824.07}	2,351.01	98
		765	SIX LANING OF THALIPARAMBHA-MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH (NHAI) (N24001660)	8-2020	2/2024 (11/2021) {12/2025}	2,714.60 (3,557.65) {2,714.60}	1,898.57	70.3
		766	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 (NHAI) (N24001661)	10-2020	4/2024 (5/2025) {3/2026}	3,219.47 (3,898.46) {3,896.46}	2,295.03	55.66
		767	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH (NHAI) (N24001662)	5-2020	5/2024 (11/2021) {5/2025}	1,981.07 (2,651.79) {1,981.07}	1,540.36	93.08
		768	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ (NHAI) (N24001663)	6-2020	4/2024 (10/2021) {12/2025}	3,041.65 (3,867.66) {3,041.65}	2,387.38	76.97
		769	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ (NHAI) (N24001664)	6-2020	4/2024 (10/2021) {11/2025}	1,746.45 (2,538.06) {1,746.45}	1,250.34	77.05
		770	WIDENING/DEVELOPMENT OF EXISTING NH-85 FROM KM 0.000 TO KM 124.636 SECTION TO 2L/@L+PS SECTION IN TH (NHAI) (N24002074)	8-2022	6/2025 (N.A.) {6/2025}	1,231.74 (N.A.) {1,231.74}	336.51	39.95
	URBAN DEVELOPMENT	771	KOCHI METRO RAIL PROJECT PHASE II FROM JLN STADIUM TO INFOPARK VIA KAKKANAD (KMRCL) (N28000158)	7-2018	11/2026 (N.A.) {11/2026}	1,957.05 (N.A.) {1,957.05}	2.81	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		772	KOCHI METRO RAIL PROJECT PHASE IB SECTION FROM S N JUNCTION TO THRIPUNITHURA (KMRCL) (N28000159)	6-2019	9/2023 (N.A.) {9/2023}	355.70 (448.00) {448.33}	1.64	0
LADAKH	CIVIL AVIATION	773	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT (AAI) (N04000078)	7-2018	9/2021 (10/2025) {10/2025}	480.33 (N.A.) {640.00}	407.93	62.62
	ROAD TRANSPORT AND HIGHWAYS	774	KARGIL-ZANSKR PACKAGE-1 (NHIDCL) (N24001343)	3-2021	1/2023 (12/2024) {11/2025}	384.23 (N.A.) {384.23}	162.54	60.4
		775	KARGIL-ZANSKR PACKAGE-2 (NHIDCL) (N24001344)	3-2021	1/2023 (2/2025) {11/2025}	404.89 (N.A.) {404.89}	244.21	64.36
		776	KARGIL-ZANSKR PACKAGE-3 (NHIDCL) (N24001345)	8-2020	1/2023 (8/2025) {8/2025}	381.01 (N.A.) {381.01}	230.28	74.11
		777	KARGIL-ZANSKR PACKAGE-8 (NHIDCL) (N24001348)	3-2021	1/2023 (8/2025) {8/2025}	398.37 (N.A.) {398.37}	274.39	82.28
		778	CONSTRUCTION OF REALIGNMENT BETWEEN PANDRASS- PASHKYUN (TOTAL LENGTH 27.10 KM) ON ROAD ZOZILA-KARGIL (BRO) (N24001999)	11-2021	6/2025 (N.A.) {6/2025}	426.14 (N.A.) {426.14}	76.75	37
MADHYA PRADESH	CIVIL AVIATION	779	UPGRADATION OF JABALPUR AIRPORT (AAI) (N04000087)	6-2016	6/2021 (7/2024) {7/2024}	412.24 (N.A.) {412.24}	402.81	100
		780	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 (AAI) (N04000098)	10-2021	8/2023 (8/2024) {8/2024}	446.12 (455.00) {455.00}	451.41	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>COAL</u>	781	KANCHAN OC EXPANSION (SECL) (N06000125)	12-2014	3/2021 (3/2026) {3/2026}	371.04 (N.A.) {371.04}	136.74	47
		782	AMADAND OPENCAST EXPANSION PROJECT (SECL) (N06000148)	3-2016	3/2021 (3/2027) {3/2027}	869.44 (N.A.) {869.44}	271.16	72
		783	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) (NCL) (N06000162)	11-2017	3/2022 (N.A.) {8/2024}	1,255.17 (N.A.) {1,398.56}	1,254.21	100
		784	GANDHIGRAM UG MINE (WCL) (N06000183)	8-2019	3/2026 (N.A.) {3/2026}	414.16 (N.A.) {414.16}	11.75	28
		785	BLOCK-B EXPANSION OPENCAST PROJECT (NCL) (N06000184)	7-2019	3/2023 (N.A.) {3/2027}	998.71 (N.A.) {998.71}	429.25	28.89
		786	NIGAH EXPANSION OCP (15 TO 25 MTPA) (NCL) (N06000196)	11-2020	3/2025 (N.A.) {3/2028}	1,729.68 (N.A.) {1,729.68}	749.61	42.75
		787	RAMPUR BATURA OC (4.0 MTY) (SECL) (N06000233)	7-2019	3/2026 (N.A.) {3/2026}	1,248.93 (N.A.) {1,248.93}	484.67	44
		788	TAWA III UG MINE (WCL) (N06000250)	12-2021	3/2027 (N.A.) {3/2027}	314.09 (N.A.) {324.25}	0.56	9
		789	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY) (WCL) (N06000257)	9-2022	3/2027 (N.A.) {3/2027}	399.20 (N.A.) {497.01}	64.13	42

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		790	VISHNUPURI UG TO OC (WCL) (N06000260)	11-2022	3/2029 (N.A.) {3/2029}	220.62 (N.A.) {227.65}	-	7
		791	URDHAN OC (WCL) (N06000265)	1-2023	3/2031 (N.A.) {3/2031}	206.88 (N.A.) {228.42}	22.12	9
		792	SHARDA UG (WCL) (N06000266)	9-2023	3/2028 (N.A.) {3/2028}	166.25 (N.A.) {200.16}	1.69	11
	PETROLEUM	793	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF (BPCL) (N16000518)	5-2023	5/2028 (N.A.) {5/2028}	43,367.00 (N.A.) {43,367.00}	1,543.00	11
	POWER	794	SHAJAPUR 325MW SOLAR PV PROJECT (NTPC) (N18000348)	6-2022	3/2024 (N.A.) {6/2025}	1,530.49 (N.A.) {1,530.49}	1,197.33	70
		795	TS FOR EVACUATION POWER RAJASTHAN REZ PH-IV (PART- 2:5.5GW) (JAISALMER/BARMER COMPLEX): PART-C (PGCIL) (N18000392)	8-2024	8/2026 (N.A.) {8/2026}	2,708.00 (N.A.) {2,708.00}	45.00	15
		796	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-2 5.5GW] [JAISALMER/BARME (PGCIL) (N18000399)	10-2024	10/2026 (N.A.) {10/2026}	3,674.00 (N.A.) {3,674.00}	74.00	1
	RAILWAYS	797	RAMGANJMUNDI-BHOPAL (NL),WCR (WCR) (220100314)	4-2001	3/2021 (12/2025) {6/2026}	424.60 (3,032.46) {5,125.16}	3,387.65	69
		798	RATLAM-MHOW-KHANDWA-AKOLA (GC) (WR) (N22000120)	4-2008	3/2022 (2/2027) {2/2027}	3,503.69 (5,677.80) {6,203.51}	4,243.31	80

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		799	KATNI - SINGRAULI DOUBLING PROJECT (WCR) (N22000351)	12-2015	3/2020 (12/2027) {12/2027}	1,763.93 (2,445.30) {4,353.50}	3,066.17	88
		800	KATNI GRADE SEPARATOR/BYE PASS (WCR) (N22000416)	8-2016	3/2022 (6/2025) {9/2024}	582.13 (1,247.64) {2,300.00}	1,375.23	89
		801	ANUPPUR-KATNI (SECR) (N22000485)	4-2015	12/2021 (12/2023) {3/2025}	1,370.00 (1,680.00) {2,311.02}	1,863.51	76
		802	NIMACH BADI SADRI NEW LINE PROJECT (WR) (N22000503)	4-2017	3/2022 (N.A.) {3/2026}	495.18 (N.A.) {495.18}	265.81	18
		803	NIMACH-RATLAM (133 KM) (WR) (N22000536)	10-2021	10/2027 (6/2025) {6/2025}	910.00 (1,095.88) {1,095.88}	1,001.29	72
		804	SATNA - REWA (50 KM) (WCR) (N22000554)	11-2015	3/2026 (N.A.) {3/2026}	500.00 (40.00) {500.00}	1.41	80
		805	INDORE BUDNI (INDORE JABALPUR) (RVNL) (N22000601)	9-2018	9/2030 (N.A.) {9/2030}	4,340.00 (N.A.) {7,393.75}	1,004.86	0
	ROAD TRANSPORT AND HIGHWAYS	806	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 (MoRTH) (N24000513)	3-2015	8/2017 (12/2023) {6/2025}	511.83 (N.A.) {511.83}	485.18	93
		807	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN (NHAI) (N24000709)	12-2017	2/2020 (12/2024) {12/2024}	950.27 (N.A.) {786.43}	642.26	99.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		808	2L+PS OF THIKRI ANJAD SECTION OF NH-347B (MoRTH) (N24000892)	11-2017	7/2018 (N.A.) {8/2021}	249.05 (N.A.) {249.05}	221.19	100
		809	4LBERKHEDI TO GODPEHRA NH-44 (NHAI) (N24001614)	2-2022	11/2024 (N.A.) {11/2024}	524.84 (N.A.) {524.84}	2,339.69	50
		810	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I) (NHAI) (N24001615)	3-2021	4/2024 (5/2024) {8/2024}	790.78 (N.A.) {790.78}	1,986.09	75
		811	2L PS OF SATNA - MAIHAR SECTION OF NH-135BG FROM KM 80.800 TO KM 120.125 (NHAI) (N24001616)	1-2021	10/2023 (N.A.) {2/2025}	428.04 (N.A.) {428.04}	351.52	100
		812	KATNI BYPASS FROM KM. 359.50 TO KM. 378.50 (NHAI) (N24001618)	9-2019	9/2022 (N.A.) {4/2025}	194.40 (235.00) {235.00}	206.66	98.84
		813	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D (NHAI) (N24001756)	10-2020	10/2024 (2/2025) {2/2025}	1,352.56 (N.A.) {1,480.94}	843.65	100
		814	4L OF SUHAGADI TO BARDIYA AMRA FROM KM. 89.200 TO KM. 135.351 OF NH-752D (PKG-III) (NHAI) (N24001758)	1-2020	10/2024 (N.A.) {2/2025}	823.05 (N.A.) {823.05}	402.85	100
		815	4L OF CHANDESARA TO KHEDAKHAJURIYA FROM KM. 0.000 TO (N.A.) 750 AND KM 0.000 TO KM 41.400 OF NH-752D (NHAI) (N24001759)	1-2020	6/2024 (6/2025) {6/2025}	909.84 (N.A.) {909.84}	495.72	96.82

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		816	4L OF HARDA - BETUL (PKG-II) FROM KM. 30.00 TO KM.81.00 [TEMAGAON TO CHICHOLI] (NHAI) (N24001761)	2-2023	2/2025 (2/2025) {2/2025}	520.28 (N.A.) {520.28}	392.86	100
		817	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] (NHAI) (N24001762)	10-2021	1/2024 (12/2024) {12/2024}	1,146.22 (N.A.) {1,146.22}	660.48	91.12
		818	ADDITIONAL WORKS (2VUPS, MR-10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE- DEWAS SECTION OF N (NHAI) (N24001765)	8-2022	7/2024 (N.A.) {12/2025}	207.77 (N.A.) {207.77}	60.52	44.15
		819	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] (NHAI) (N24001766)	1-2022	10/2024 (N.A.) {5/2025}	1,011.29 (N.A.) {1,011.29}	245.13	54.14
		820	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND (NHAI) (N24001767)	1-2021	4/2024 (N.A.) {4/2024}	1,001.69 (N.A.) {1,001.69}	510.13	82.09
		821	BALANCE WORK OF 4L OF INDORE- GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF (NHAI) (N24001768)	8-2019	4/2023 (N.A.) {11/2023}	323.51 (N.A.) {323.51}	51.96	100
		822	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69 (NHAI) (N24001770)	2-2022	3/2024 (3/2025) {4/2025}	417.51 (N.A.) {417.51}	275.82	91.07

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		823	2- LANE WITH PAVED SHOULDERS OF HINOTIYA TO MEHULWA FROM DESIGN KM 27+000 90F EXISTING SH- 19 KM 26+5 (NHAI) (N24001921)	8-2021	9/2025 (N.A.) {9/2025}	581.65 (592.03) {581.65}	169.81	35.12
		824	CONSTRUCTION OF MIHONA BYPASS, LAHAR BYPASS, DABOH BYPASS and BHANDER BYPASS (TOTAL LENGTH 20.60 KM) (MoRTH) (N24001962)	3-2022	12/2024 (N.A.) {3/2025}	179.19 (N.A.) {179.19}	109.91	96
		825	UPGRADATION OF NASRULLAGANI- REHTI-BUDHNI SCCTION TO 2-LANE WITH PAVED SHOULDER FROM KM 0+150 TO KM (MoRTH) (N24001963)	12-2021	10/2024 (N.A.) {9/2025}	305.12 (N.A.) {305.12}	122.88	34
		826	UPGRADATION and WIDENING OF JHARKHEDA- BERASIA - DHOLKHEDI FROM DESIGN KM 0+000 TO KM 87+900 (DESIGN (MoRTH) (N24001964)	3-2022	5/2025 (N.A.) {5/2025}	365.21 (N.A.) {365.21}	162.23	64
		827	REHABILITATION AND UPGRADATION OF KURWAI?MUNGAOLI?CHANDERI ROAD SECTION OF NH-346, FROM DESIGN CHAIN (MoRTH) (N24001965)	3-2022	2/2025 (N.A.) {12/2025}	386.49 (N.A.) {386.49}	119.76	49
		828	BALANCE WORK FOR REHABILITATION AND UP-GRADATION OF SIDHI-SINGRAULI FROM KM 82.400 TO KM 187.993 SEC (MoRTH) (N24001966)	12-2020	4/2023 (5/2023) {6/2025}	529.44 (N.A.) {529.44}	222.24	60
		829	4L GREENFIELD RUDHI TO DESHGAON (PKG V OF BETUL- KHANDWA/DESHGAON) - N/04015/06003/MP (NHAI) (N24001967)	11-2018	10/2025 (N.A.) {10/2025}	521.21 (N.A.) {521.21}	98.23	37.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		830	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF JIRAPUR-SUSNER-MP-RJ B (MoRTH) (N24002018)	1-2022	3/2025 (N.A.) {3/2025}	239.72 (232.22) {232.22}	203.70	100
		831	UPGRADATION OF DINDORI-SAGARTOLA-KABICHABUTRA (MP-CG BORDER) SECTION OF NH -45 FROM KM 0+00(DESIGN) (MoRTH) (N24002019)	1-2022	9/2025 (N.A.) {9/2025}	329.14 (319.09) {319.09}	167.87	50
		832	CONSTRUCTION OF KAITHI-PADARIA KALA BYPASS, PATNA-TAMOLI BYPASS, JASO BYPASS , NAGOD BYPASS (TOTAL L (MoRTH) (N24002020)	3-2022	10/2025 (N.A.) {10/2025}	158.36 (158.00) {158.36}	53.05	30
		833	BALANCE WORK OF 4L OF NAURADEHI SANCTUARY DE-SCOPED STRETCH OF HIRAN RIVER TO SINDOOR RIVER FROM KM. (NHAI) (N24002067)	1-2021	7/2023 (N.A.) {4/2025}	178.18 (N.A.) {178.18}	161.64	93.1
		834	CONSTRUCTION OF 4-LANE FROM BARELA TO MANEGAON SECTION OF NH-30 FROM DESIGN CH. 2.900 TO DESIGN CH. (NHAI) (N24002068)	12-2022	3/2025 (N.A.) {12/2025}	652.33 (N.A.) {652.33}	334.34	65.12
		835	CONSTRUCTION OF ADDITIONAL 3 LANE WITH PAVED SHOULDER (DESIGN LENGTH 8.87 KM) AS REALIGNMENT OF BAKA (NHAI) (N24002069)	7-2022	12/2024 (N.A.) {12/2024}	209.29 (N.A.) {209.29}	140.22	100
		836	INDORE - EDLABAD (PKG-II) [TEJAJINAGAR TO BALWARA] (NHAI) (N24002070)	1-2022	1/2025 (N.A.) {1/2025}	1,162.80 (N.A.) {1,162.80}	485.58	80

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		837	CONSTRUCTION OF (I) 4-LANE HIGHWAY FROM VIDISHA TO HINOTIYA FROM KM. 0.000 TO KM. 27.000 (LENGTH=27 (NHAI) (N24002077)	9-2022	12/2025 (N.A.) {12/2025}	1,000.63 (N.A.) {1,000.63}	208.47	42.94
		838	FOUR LANING OF RAGHOGARH (DESIGN CH.29.300/EXISTING CH. 29.555) TO NANASA (DESIGN CH.92.971/EXISTING (NHAI) (N24002166)	3-2024	3/2026 (3/2026) {3/2026}	799.20 (N.A.) {799.20}	244.09	26.2
		839	BALANCE WORKS OF 4 LANE DIVIDED CARRIAGEWAY OF MISSING LINK SECTION OF NH-39 (REWA BYPASS) FROM JUNC (NHAI) (N24002200)	4-2024	4/2026 (N.A.) {4/2026}	355.36 (N.A.) {355.36}	18.53	18.48
	<u>SOCIAL JUSTICE</u>	840	CENTRE FOR DISABILITY SPORTS (CPWD) (N38000001)	2-2019	3/2024 (N.A.) {3/2024}	170.99 (N.A.) {170.99}	73.80	74
	<u>URBAN DEVELOPMENT</u>	841	BHOPAL METRO RAIL (MPMRCL) (N28000124)	11-2018	2/2023 (6/2028) {6/2028}	6,941.40 (N.A.) {6,941.40}	2,899.44	39.68
		842	INDORE METRO RAIL (MPMRCL) (N28000125)	11-2018	2/2023 (12/2028) {12/2028}	7,500.80 (N.A.) {7,500.80}	3,630.12	51.3
<u>MAHARASHTRA</u>	<u>CIVIL AVIATION</u>	843	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT (AAI) (N04000079)	3-2017	4/2021 (12/2023) {12/2023}	475.39 (N.A.) {520.00}	532.88	100
		844	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM (AAI) (N04000096)	6-2017	12/2020 (N.A.) {4/2024}	255.68 (N.A.) {270.00}	267.86	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>COAL</u>	845	AMALGAMATED YEKONA-I YEKONA-II (WCL) (N06000132)	8-2015	3/2025 (N.A.) {3/2025}	727.28 (N.A.) {727.28}	530.02	86
		846	UKNI DEEP OC (WCL) (N06000179)	1-2019	3/2021 (3/2025) {3/2025}	237.06 (N.A.) {318.14}	163.86	91
		847	GHONSA EXPANSION DEEP OC (WCL) (N06000205)	3-2021	3/2028 (N.A.) {3/2029}	184.71 (N.A.) {241.72}	9.25	6
		848	SASTI EXPANSION OC (WCL) (N06000206)	8-2020	3/2026 (N.A.) {3/2026}	319.04 (N.A.) {371.59}	68.64	24
		849	DHUPTALA OC(SASTI UG TO OC) (WCL) (N06000209)	10-2021	3/2028 (N.A.) {3/2028}	711.00 (N.A.) {720.87}	159.15	33
		850	ADASA UG TO OC (1.50 MTY) (WCL) (N06000219)	11-2018	3/2024 (3/2025) {3/2025}	316.00 (N.A.) {333.43}	208.20	78
		851	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) (WCL) (N06000222)	2-2020	3/2027 (N.A.) {3/2027}	822.88 (N.A.) {1,184.33}	578.89	48
		852	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) (WCL) (N06000226)	9-2018	3/2024 (3/2025) {3/2025}	235.90 (N.A.) {313.34}	116.46	87
		853	MUNGOLI NIRGUDA EXTENSION (DEEP) OC (WCL) (N06000231)	11-2020	3/2026 (N.A.) {3/2026}	826.80 (N.A.) {826.80}	518.85	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		854	SAONER UG MINE I EXPANSION (WCL) (N06000251)	1-2022	3/2028 (N.A.) {3/2028}	228.64 (N.A.) {253.51}	118.34	27
		855	SINGHORI DEEP OC (WCL) (N06000252)	5-2022	3/2029 (N.A.) {3/2029}	335.75 (N.A.) {421.84}	22.01	16
		856	MAKARDHOKDA I EXPANSION OC (WCL) (N06000253)	6-2022	3/2026 (N.A.) {3/2026}	361.87 (N.A.) {497.06}	33.90	12
		857	BHATADI EXPANSION OC (WCL) (N06000254)	5-2022	3/2028 (N.A.) {3/2028}	580.60 (N.A.) {729.86}	61.33	17
		858	NEW MAJARI UG TO OC (3.0 MTY) (WCL) (N06000255)	9-2022	3/2027 (N.A.) {3/2027}	402.27 (N.A.) {496.38}	47.99	27
		859	BHANEKAON OC (1.15MTY) (WCL) (N06000256)	9-2022	3/2028 (N.A.) {3/2028}	405.20 (N.A.) {494.60}	10.21	7
		860	GOKUL EXPANSION OC (WCL) (N06000264)	4-2021	3/2026 (N.A.) {3/2026}	309.58 (N.A.) {456.95}	3.65	7
		861	KOLGAON EXPANSION (DEEP) OC (WCL) (N06000267)	9-2023	3/2027 (N.A.) {3/2027}	198.71 (N.A.) {206.19}	0.55	5
		862	AMALGAMATED GAURI PAUNI EXPANSION OC (WCL) (N06000271)	3-2024	3/2030 (N.A.) {3/2030}	1,225.21 (N.A.) {1,428.25}	52.83	17

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		863	GAURI CENTRAL OCM (WCL) (N06000278)	6-2024	3/2030 (N.A.) {3/2030}	973.07 (N.A.) {1,015.07}	-	0
		864	BALLARPUR NORTHWEST OC MINE (WCL) (N06000282)	12-2022	3/2029 (N.A.) {3/2029}	360.18 (N.A.) {360.18}	-	0
		865	NORTHERN EXTENSION OF MUNGOLI NIRGUDA DEEP OC (WCL) (N06000283)	6-2024	3/2029 (N.A.) {3/2029}	1,024.91 (N.A.) {1,184.44}	-	0
		866	AMALGAMATED GONDEGAON - GHATROHAN EXPANSION OCM (WCL) (N06000284)	9-2024	3/2029 (N.A.) {3/2029}	668.54 (N.A.) {871.59}	-	0
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	867	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI (CPWD EDUCATION) (N28000117)	1-2018	7/2020 (11/2023) {2/2024}	223.37 (275.00) {230.00}	141.16	100
	<u>HEALTH AND FAMILY WELFARE</u>	868	500 BEDDED HOSPITAL INCLUDING 50 SUPERSPECIALITY BEDS FOR ESIC AT PUNE (CPWD) (N21000033)	7-2022	9/2025 (N.A.) {9/2025}	429.25 (N.A.) {429.25}	99.08	0
	<u>PETROLEUM</u>	869	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS (ONGC) (N16000213)	12-2015	4/2018 (12/2023) {6/2025}	3,190.69 (3,375.90) {3,375.90}	3,002.91	88.1
		870	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV (ONGC) (N16000358)	4-2019	3/2022 (6/2024) {6/2025}	3,228.80 (3,976.67) {3,976.67}	3,969.16	99.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		871	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND (GAIL) (N16000430)	5-2019	4/2025 (10/2025) {10/2025}	8,797.00 (11,256.00) {11,256.00}	6,150.68	81.86
		872	PIPELINE REPLACEMENT PROJECT - VII (ONGC) (N16000436)	1-2022	5/2024 (1/2025) {3/2025}	3,183.58 (N.A.) {3,645.23}	3,417.00	100
		873	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL (BPCL) (N16000442)	4-2021	6/2024 (N.A.) {4/2025}	1,164.69 (N.A.) {1,164.69}	791.23	76.2
		874	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY (IOCL) (N16000446)	9-2021	10/2023 (5/2024) {5/2024}	378.00 (N.A.) {378.00}	120.07	39.08
		875	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI (BPCL) (N16000452)	5-2022	3/2024 (N.A.) {9/2024}	423.39 (N.A.) {423.39}	233.21	74.4
		876	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA) (IOCL) (N16000456)	9-2022	8/2025 (N.A.) {3/2026}	165.00 (N.A.) {165.00}	72.19	60.58
		877	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK (ONGC) (N16000470)	6-2022	10/2025 (N.A.) {2/2026}	4,144.41 (6,406.90) {6,406.90}	2,782.42	69.4

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		878	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS (IOCL) (N16000487)	3-2022	3/2030 (N.A.) {9/2031}	865.00 (N.A.) {865.00}	54.81	2.8
		879	ANDHERI RESIDENTIAL TOWERS MUMBAI (IOCL) (N16000503)	6-2017	5/2025 (6/2026) {6/2026}	281.35 (389.67) {389.67}	214.14	48
		880	CONSTRUCTION OF ADDITIONAL TANKAGES AND ALLIED FACILITIES AT JNPT TERMINAL (IOCL) (N16000504)	4-2022	10/2024 (8/2026) {8/2026}	341.43 (436.14) {436.14}	229.37	45.1
		881	INSTALLATION OF INDEPENDENT DE- AROMATIZED SOLVENTS PRODUCTION FACILITIES AT MUMBAI REFINERY (BPCL) (N16000507)	3-2023	7/2025 (N.A.) {7/2025}	405.00 (N.A.) {405.00}	170.03	70
		882	PART REPLACEMENT PIPELINE PROJECT (PRPP) (ONGC) (N16000515)	11-2022	5/2024 (12/2024) {3/2025}	1,219.48 (N.A.) {1,145.10}	678.55	77.6
		883	POL AND LOBS INSTALLATIONS WITH RECEIPT PIPELINES AT RASAYANI (BPCL) (N16000519)	5-2023	5/2026 (N.A.) {5/2026}	2,585.00 (N.A.) {2,585.00}	402.83	51
		884	MHN TCPP PGC BGC PROJECT (MTPBP) (ONGC) (N16000526)	2-2024	5/2026 (N.A.) {5/2026}	2,329.45 (N.A.) {2,354.23}	500.55	33.4
		885	PRP-VIII GROUP B (NH AND BS ASSET) (ONGC) (N16000533)	6-2024	5/2026 (N.A.) {2/2026}	2,379.84 (N.A.) {2,379.84}	259.58	35.81

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		886	HP TDAE UNIT IN MUMBAI REFINERY (HPCL) (N16000534)	6-2024	4/2026 (N.A.) {4/2026}	240.00 (N.A.) {240.00}	22.14	22.6
		887	INTEGRATED DEVELOPMENT OF 4 CONTRACT AREAS UNDER DSF2 (ONGC) (N16000537)	5-2023	4/2027 (N.A.) {4/2027}	6,183.79 (N.A.) {6,183.79}	-	10
		888	LUBE MODERNIZATION AND BOTTOM UPGRADATION PROJECT (HPCL) (N16000540)	12-2024	3/2028 (N.A.) {3/2028}	4,679.00 (N.A.) {4,679.00}	157.57	3.4
	POWER	889	BIKANER SOLAR POWER PROJECT (SJVN) (N18000335)	4-2022	5/2024 (N.A.) {9/2025}	5,491.89 (532.00) {5,491.89}	3,839.51	71.25
		890	TS FOR EVACUATION OF 7GW RE INJECTION AT KHAVDA PS UNDER PHASE-IV PART E4 (PGCIL) (N18000377)	11-2023	7/2025 (N.A.) {7/2025}	224.00 (N.A.) {224.00}	-	3
	RAILWAYS	891	AHMEDNAGAR-PARLI VAIJNATH(NL) CR (CR) (220100181)	2-1997	3/2021 (N.A.) {12/2025}	2,271.50 (N.A.) {4,957.27}	4,746.88	94
		892	MUMBAI URBAN TRANSPORT PROJECT PHASE-II (MRTP) (N22000092)	4-2008	3/2014 (N.A.) {3/2014}	5,300.00 (N.A.) {918.53}	7,304.64	0
		893	WARDHA-NANDED MAHARASHTRA (CR) (N22000231)	4-2008	3/2023 (N.A.) {3/2027}	3,168.29 (N.A.) {3,445.34}	2,990.05	47
		894	KALYAN-KASARA 3RD LINE (CR) (N22000233)	4-2011	3/2021 (N.A.) {12/2026}	792.89 (N.A.) {1,432.61}	862.37	50

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		895	WARDHA-SEWAGRAM NGP 3RD LINE (CR) (N22000250)	4-2012	3/2022 (N.A.) {2/2026}	540.02 (N.A.) {540.02}	710.67	72
		896	WARDHA-BALHARSHAH - 3RD LINE (132 KM) (CR) (N22000356)	2-2015	3/2022 (N.A.) {3/2026}	1,272.19 (N.A.) {1,384.72}	1,433.66	67
		897	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) (CR) (N22000358)	2-2015	3/2023 (N.A.) {3/2027}	2,449.91 (N.A.) {2,449.91}	1,669.03	48
		898	PUNE-MIRAJ-LONDA (467 KM) (CR) (N22000359)	2-2015	3/2024 (N.A.) {5/2025}	3,627.47 (3,627.00) {7,037.24}	4,543.81	84
		899	DAUND - MANMAD (236 KM) (CR) (N22000360)	2-2016	3/2023 (N.A.) {1/2026}	1,876.00 (N.A.) {2,081.27}	2,629.40	87
		900	MANMAD - JALGAON - 3RD LINE (160 KM) (CR) (N22000361)	2-2016	3/2022 (N.A.) {3/2026}	1,035.16 (N.A.) {1,558.75}	1,614.83	80
		901	WARDHA - NAGPUR - 4TH LINE (76 KM) (CR) (N22000362)	2-2016	3/2023 (N.A.) {5/2025}	637.95 (N.A.) {637.95}	925.35	70
		902	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) (SECR) (N22000420)	9-2016	3/2023 (N.A.) {12/2025}	1,908.51 (N.A.) {3,544.25}	3,012.85	90
		903	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (WR) (N22000434)	3-2010	(N.A.) {3/2024}	265.88 (N.A.) {311.36}	-	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		904	WADSA-GADHCHIROLI NEW LINE (52.36 KM) (SECR) (N22000480)	6-2018	12/2021 (N.A.) {12/2026}	229.00 (N.A.) {1,880.61}	674.93	23
		905	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (N22000511)	8-2022	8/2027 (N.A.) {3/2029}	955.00 (N.A.) {2,093.82}	114.22	0
		906	SOLAPUR-TULJAPUR-OSMANABAD (UMBRELLA WORK) (CR) (N22000513)	1-2019	3/2028 (N.A.) {12/2027}	904.92 (N.A.) {2,933.01}	1,130.01	7
		907	DHULE (BORVIHIR)-NARDANA (UMBRELLA WORK) (CR) (N22000514)	1-2019	3/2026 (N.A.) {3/2028}	492.76 (N.A.) {1,158.99}	197.06	5
		908	KALYAN-MURBAD VIA ULHASNAGAR (UMBRELLA WORK) (CR) (N22000515)	2-2023	3/2027 (N.A.) {3/2027}	836.12 (N.A.) {836.12}	9.23	0
		909	BARAMATI - LONAND (CR) (N22000615)	2-1999	3/2027 (N.A.) {3/2027}	736.44 (N.A.) {1,843.90}	655.85	50
		910	MUMBAI URBAN TRANSPORT PROJECT IIIA (MRVC) (N22000627)	4-2019	3/2025 (N.A.) {12/2027}	33,690.00 (N.A.) {33,690.00}	1,110.28	0
		911	NAGPUR- NAGBHIR RAILWAY LINE GAUGE CONVERSION PROJECT (MRIDC) (N22000629)	10-2019	6/2024 (N.A.) {10/2025}	1,400.00 (N.A.) {2,383.00}	1,682.86	85

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	912	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM (MoRTH) (N24000332)	1-2015	(N.A.) {}	225.81 (N.A.) {225.81}	167.96	96
		913	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN (NHAI) (N24000442)	12-2015	3/2019 (11/2023) {5/2025}	649.50 (N.A.) {649.50}	609.98	91.75
		914	NAGPUR RING ROAD PACKAGE-2 (NHAI) (N24000560)	3-2016	7/2019 (3/2024) {5/2025}	591.66 (N.A.) {591.66}	627.04	98
		915	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000584)	3-2016	(N.A.) {12/2023}	1,142.62 (1,907.03) {1,142.62}	1,056.08	95.17
		916	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000585)	3-2016	(N.A.) {}	1,101.58 (N.A.) {1,101.58}	608.53	0
		917	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST (NHAI) (N24000655)	3-2017	3/2020 (11/2024) {11/2024}	247.02 (N.A.) {157.49}	93.29	100
		918	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) (NHAI) (N24000656)	3-2017	3/2020 (7/2022) {12/2025}	744.64 (N.A.) {1,007.00}	467.65	93
		919	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) (NHAI) (N24000659)	3-2017	3/2017 (5/2021) {10/2024}	1,059.73 (1,071.00) {1,071.00}	878.19	82.04

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		920	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF (NHAI) (N24000851)	3-2018	7/2021 (N.A.) {6/2025}	1,162.92 (1,182.87) {1,182.87}	372.63	58.15
		921	SARSAM TO KOTHARI (MoRTH) (N24001002)	2-2016	7/2019 (N.A.) {12/2023}	545.64 (N.A.) {545.64}	232.64	93.68
		922	AKOLA TO AKOT (MoRTH) (N24001003)	1-2017	6/2019 (N.A.) {12/2023}	313.95 (N.A.) {313.95}	270.26	99
		923	DIGRAS DARWAH KARANJA (MoRTH) (N24001013)	1-2017	6/2019 (N.A.) {12/2023}	391.06 (391.00) {391.06}	287.60	92.76
		924	DAHEGAON TO KUHI (MoRTH) (N24001017)	1-2017	6/2019 (N.A.) {12/2023}	228.89 (229.00) {228.89}	154.82	99
		925	BHANDARA TO GHOTITOK (MoRTH) (N24001018)	1-2017	6/2019 (N.A.) {6/2019}	392.83 (393.00) {392.83}	274.75	100
		926	AMDIT TO SAONER (MoRTH) (N24001021)	1-2017	6/2019 (N.A.) {12/2023}	396.91 (397.00) {396.91}	289.79	99
		927	WADI TO ASOLA (MoRTH) (N24001022)	1-2017	9/2019 (N.A.) {12/2023}	363.82 (364.00) {363.82}	154.65	93.15
		928	SHAHPUR PATGAON SECTION I (MoRTH) (N24001027)	1-2018	12/2019 (N.A.) {3/2024}	150.79 (N.A.) {150.79}	81.14	70.66

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		929	JINTUR TO PARBHANI (MoRTH) (N24001039)	1-2017	(N.A.) {12/2023}	356.66 (N.A.) {356.66}	209.48	80.48
		930	RALEGAON TO RAMTIRTH (MoRTH) (N24001046)	1-2017	7/2019 (N.A.) {8/2023}	210.81 (N.A.) {210.81}	210.81	96.5
		931	VITA TO NAGAJ (MoRTH) (N24001050)	3-2018	12/2019 (N.A.) {12/2023}	304.58 (305.00) {304.58}	154.68	68.39
		932	KARAD PATAN CHIPLUN GUHAGAR (MoRTH) (N24001057)	2-2017	6/2019 (N.A.) {10/2023}	407.19 (407.00) {407.19}	323.02	89.97
		933	KARWANDI TO RAJURI (MoRTH) (N24001058)	3-2018	12/2019 (N.A.) {3/2024}	276.95 (277.00) {276.95}	160.94	92.06
		934	PALPHATA TO PHULAMBARI (MoRTH) (N24001060)	3-2018	12/2019 (N.A.) {12/2023}	227.19 (227.00) {227.19}	141.92	95
		935	NANDED TO JALKOT (MoRTH) (N24001069)	12-2017	9/2019 (N.A.) {9/2019}	456.93 (457.00) {456.93}	278.22	0
		936	PUNE TO MALE VILLAGE (MoRTH) (N24001078)	3-2018	12/2019 (N.A.) {12/2023}	228.31 (N.A.) {228.31}	100.97	98.83
		937	ARDHAPUR TO HIMAYATNAGAR (MoRTH) (N24001079)	12-2017	6/2020 (N.A.) {12/2023}	426.06 (426.00) {426.06}	271.40	96.25

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		938	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER (MoRTH) (N24001080)	3-2018	12/2019 (N.A.) {10/2023}	256.15 (N.A.) {256.15}	126.62	98
		939	HIMAYATNAGAR TO PHULSAWANGI (MoRTH) (N24001081)	3-2018	12/2019 (N.A.) {12/2023}	294.87 (295.00) {294.87}	183.17	89.99
		940	PUNE RAIGARH DISTRICT BORDER TO MANGAON (MoRTH) (N24001082)	3-2018	12/2019 (N.A.) {12/2023}	223.46 (N.A.) {223.46}	123.46	100
		941	KOLDE TO KHETIYA (MoRTH) (N24001090)	1-2017	7/2019 (N.A.) {12/2023}	509.18 (N.A.) {509.18}	283.13	94.81
		942	SATARA TO MHASWAD (MoRTH) (N24001092)	1-2017	7/2019 (N.A.) {12/2023}	653.46 (N.A.) {653.46}	369.62	76.76
		943	SATARA MURVAD PILLOV PANDHARPUR (MoRTH) (N24001095)	1-2017	(N.A.) {6/2024}	388.44 (N.A.) {388.44}	240.05	88.16
		944	SELDOH TO PANVAR (MoRTH) (N24001097)	7-2018	5/2020 (N.A.) {5/2020}	404.33 (404.00) {404.33}	140.65	64
		945	MHASWAD TO TEMBHURNI (MoRTH) (N24001099)	1-2017	7/2019 (N.A.) {12/2023}	488.60 (N.A.) {488.60}	279.42	76.5
		946	KURUDWADI TO PANDHARPUR (MoRTH) (N24001101)	1-2017	7/2019 (N.A.) {11/2023}	307.63 (N.A.) {307.63}	232.57	96.27

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		947	PANDHARPUR TO SANGOLA (MoRTH) (N24001102)	7-2017	7/2019 (N.A.) {12/2023}	218.38 (N.A.) {218.38}	182.63	99.78
		948	PEN TO KHOPOLI (MoRTH) (N24001106)	3-2018	3/2018 (N.A.) {1/2024}	301.39 (302.00) {301.39}	170.12	82.07
		949	PANCHARAL TO MANDANGHAR (MoRTH) (N24001107)	7-2018	5/2020 (N.A.) {5/2020}	381.08 (302.00) {381.08}	45.66	0
		950	KOLHA TO NASRATPUR (MoRTH) (N24001111)	4-2016	4/2019 (N.A.) {8/2024}	281.78 (282.00) {281.78}	77.83	87
		951	NASRATPUR TO BARASGAON (MoRTH) (N24001112)	7-2016	9/2019 (N.A.) {9/2019}	406.54 (407.00) {406.54}	274.30	0
		952	INDAPUR TO VADPALE (MoRTH) (N24001114)	1-2017	12/2019 (N.A.) {3/2024}	1,202.52 (1,656.94) {1,202.52}	1,450.82	61.42
		953	PAITHAN TO SHIRUR (MoRTH) (N24001122)	3-2017	6/2019 (N.A.) {3/2024}	341.80 (N.A.) {341.80}	226.19	78.6
		954	SHIRUR TO KHARDA (MoRTH) (N24001123)	2-2017	6/2019 (N.A.) {12/2023}	381.77 (N.A.) {381.77}	199.48	83.93
		955	AURANGABAD TO SILLOD (MoRTH) (N24001124)	2-2017	6/2019 (N.A.) {12/2023}	456.32 (541.93) {456.32}	355.54	94.07

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		956	SILLOD TO FARDAPUR (MoRTH) (N24001125)	2-2017	6/2019 (N.A.) {12/2023}	337.46 (432.98) {337.46}	335.30	91.56
		957	KUMBHARI PHTA TO DEULGAON RAJA (MoRTH) (N24001127)	2-2017	6/2019 (N.A.) {2/2024}	406.51 (N.A.) {406.51}	340.26	88
		958	BHOGAN KHURD TO KASHEDI (MoRTH) (N24001132)	9-2017	6/2021 (N.A.) {12/2023}	743.21 (743.00) {743.21}	911.64	88.69
		959	KANTE TO WAKED (MoRTH) (N24001134)	3-2016	11/2019 (N.A.) {12/2024}	1,230.02 (1,230.00) {1,230.02}	791.80	0
		960	PARLI PIMPLA DAHIGUDA (MoRTH) (N24001138)	2-2017	6/2019 (N.A.) {8/2023}	205.72 (206.00) {205.72}	85.71	100
		961	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001377)	2-2019	1/2022 (8/2023) {8/2023}	731.89 (731.99) {731.99}	692.21	100
		962	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001378)	2-2019	1/2022 (6/2023) {6/2023}	362.46 (372.46) {372.46}	352.01	100
		963	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001379)	2-2019	1/2022 (8/2023) {8/2023}	594.75 (594.75) {613.75}	585.20	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		964	UPGRADATION OF ADHALGAON-JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH (MoRTH) (N24001448)	11-2021	2/2022 (N.A.) {2/2022}	223.35 (N.A.) {223.35}	209.36	88
		965	REPANPALLI TO SIRONCHA (MoRTH) (N24001468)	3-2022	6/2022 (N.A.) {6/2024}	282.07 (N.A.) {282.07}	34.65	0
		966	TUNNEL AT KHAMBATI GHAT SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0 (NHAI) (N24001486)	2-2019	2/2022 (12/2024) {8/2025}	493.00 (N.A.) {493.00}	395.69	76.16
		967	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL-ALANDI SECTION (NHAI) (N24001488)	9-2021	9/2023 (12/2024) {5/2025}	618.45 (N.A.) {618.45}	639.23	95.5
		968	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) (NHAI) (N24001493)	12-2022	12/2024 (N.A.) {11/2025}	1,749.86 (N.A.) {1,749.86}	1,827.71	65.65
		969	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 () (NHAI) (N24001495)	11-2022	11/2024 (N.A.) {9/2025}	930.00 (N.A.) {930.00}	361.17	74.9
		970	PATAS-VASUNDE PHATA - BARAMATI BYPASS (NHAI) (N24001501)	9-2021	9/2023 (7/2023) {7/2023}	531.86 (532.41) {532.41}	520.71	100
		971	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH-965G (SAINT TUKARAM MARG) (NHAI) (N24001502)	9-2021	9/2023 (5/2025) {5/2025}	624.45 (580.15) {580.15}	420.42	2

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		972	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH- 965G (SAINT TUKARAM MARG) (NHAI) (N24001503)	9-2021	9/2023 (1/2025) {3/2025}	667.66 (666.21) {666.21}	598.65	3
		973	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) (NHAI) (N24001504)	5-2022	5/2024 (1/2025) {1/2025}	1,260.00 (N.A.) {1,260.00}	608.72	93.5
		974	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) (NHAI) (N24001505)	3-2022	3/2024 (5/2025) {5/2025}	1,549.02 (N.A.) {1,549.02}	537.10	75.4
		975	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) (NHAI) (N24001506)	2-2022	2/2024 (6/2025) {6/2025}	2,747.00 (N.A.) {2,747.00}	929.38	75
		976	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) (NHAI) (N24001507)	11-2022	5/2024 (6/2025) {6/2025}	1,124.00 (N.A.) {1,124.00}	360.76	64.1
		977	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) (NHAI) (N24001508)	11-2022	10/2024 (6/2025) {6/2025}	1,450.00 (N.A.) {1,450.00}	638.66	80.04
		978	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XV) [KM. 20.200 TO KM. 43.000 OF SPUR] (AKLOLI - AMNE) (NHAI) (N24001521)	11-2022	10/2024 (4/2025) {4/2025}	990.00 (N.A.) {990.00}	352.70	66.8
		979	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) (NHAI) (N24001546)	1-2023	1/2025 (N.A.) {1/2025}	1,025.20 (N.A.) {1,025.20}	734.54	42.71

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		980	BALANCE WORKS OF 4L PANVEL- INDAPUR SECTION OF NH-66 (OLD NH- 17) FROM KM 42.300 (KASU) TO KM 84.600 ((NHAI) (N24001607)	10-2022	5/2024 (12/2025) {12/2025}	332.00 (N.A.) {332.00}	240.77	59.64
		981	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) (NHAI) (N24001608)	9-2021	7/2025 (N.A.) {7/2025}	2,208.68 (N.A.) {2,208.68}	488.60	72.01
		982	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH- 66(OLD NH- 17) FROM KM 0.000 (PANVEL) TO (NHAI) (N24001609)	1-2023	12/2023 (6/2025) {6/2025}	151.26 (N.A.) {151.26}	153.72	86.38
		983	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL ? ALANDI S (NHAI) (N24001610)	1-2022	5/2024 (3/2025) {5/2025}	1,833.73 (N.A.) {1,833.73}	539.18	93.22
		984	FOUR LANING OF AURANGABAD- PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA . (NHAI) (N24001795)	10-2022	7/2024 (6/2025) {12/2024}	490.40 (N.A.) {289.00}	275.78	89
		985	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B (NHAI) (N24001796)	3-2022	10/2024 (4/2025) {4/2025}	1,013.33 (1,013.33) {1,111.33}	355.07	62.01
		986	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800 (NHAI) (N24001797)	10-2021	1/2024 (N.A.) {4/2025}	815.77 (N.A.) {815.77}	724.87	99.25

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		987	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH- 53 (NHAI) (N24001798)	2-2021	11/2023 (N.A.) {4/2025}	540.21 (N.A.) {540.21}	451.46	99.78
		988	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH- 353J (NHAI) (N24001799)	2-2021	10/2023 (N.A.) {9/2025}	1,166.96 (N.A.) {1,251.00}	1,078.48	80.97
		989	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794) (NHAI) (N24001804)	12-2019	9/2022 (6/2024) {6/2025}	1,654.07 (N.A.) {980.00}	835.19	95.75
		990	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH-166 (PKG ? II) (NHAI) (N24001834)	5-2023	5/2025 (N.A.) {5/2025}	839.00 (N.A.) {839.00}	435.88	50.58
		991	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH-166 (PKG?III) (NHAI) (N24001835)	5-2023	5/2025 (N.A.) {5/2025}	986.00 (N.A.) {986.00}	430.75	49.4
		992	REHABILITATION AND UP-GRADATION TO 4 LANE ROAD WITH PAVED SHOULDER CONFIGURATION OF SECTION FROM UND (MoRTH) (N24001880)	3-2022	7/2025 (N.A.) {7/2025}	778.18 (N.A.) {778.18}	135.78	27
		993	CONSTRUCTION OF NEW FOUR LANE BYPASS TO PARBHANI CITY (PARWA TO ASOLA) KM 463/265 TO KM 481/180 (DES (MoRTH) (N24001882)	3-2022	10/2024 (N.A.) {10/2024}	496.64 (N.A.) {496.64}	-	8

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		994	CONSTRUCTION OF 4 LANE FLYOVER AT NAGPUR RTO CHOWK TO NAGPUR UNIVERSITY CAMPUS FROM CH 2/250 TO 5/10 (MoRTH) (N24001883)	3-2021	3/2024 (N.A.) {4/2024}	478.83 (N.A.) {478.83}	233.48	65
		995	REHABILITATION AND UPGRADATION OF SATANA TO MANGRUL (CHANDWAD) SECTION OF NH752 G DESIGN CH: KM 64.0 (MoRTH) (N24001884)	3-2023	5/2025 (N.A.) {5/2025}	428.80 (N.A.) {428.80}	54.11	30.69
		996	REHABILITATION AND UP-GRADATION OF JINTUR- SHIRAD SHAHAPUR SECTION KM 258.300 TO KM 306.300 [DESIGN (MoRTH) (N24001885)	2-2023	12/2024 (N.A.) {12/2024}	414.81 (N.A.) {414.81}	-	0
		997	DEVELOPMENT/WIDENING OF TALEGAON ? CHAKAN ? SHIKRAPUR ? NHAVARA SECTION OF NH 548DG (NHAVARA TO CHOU (MoRTH) (N24001886)	10-2022	8/2024 (N.A.) {8/2024}	304.68 (N.A.) {304.68}	97.09	58.78
		998	REHABILITATION AND UPGRADATION OF BHOKARDAN TO KUMBHARI FATA DESIGN CH. (KM 13+500 TO 17+00) AND RAJ (MoRTH) (N24001887)	8-2022	6/2024 (N.A.) {6/2024}	291.37 (N.A.) {291.37}	102.94	78.44
		999	UP-GRADATION OF TIRORA-GONDIA, STATE HIGHWAY FROM EXISTING KM 163+213 (ON SH-335, TIRORA) TO KM 191+ (MoRTH) (N24001888)	8-2021	4/2023 (N.A.) {5/2024}	288.14 (N.A.) {288.14}	63.01	46.31
		1000	2 LANE + PS PIMPLNER TO SATANA - [DESIGN CHAINAGE KM 21.427 TO 64.00] OF NH-752G] (MoRTH) (N24001889)	9-2019	7/2021 (N.A.) {12/2023}	277.81 (N.A.) {277.81}	148.68	90

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1001	REHABILITATION AND UPGRADATION OF PARLI TO SIRSALA SECTION OF NH-361F (KM 136+700 TO 115+000) (LENGT (MoRTH) (N24001890)	2-2023	12/2024 (N.A.) {12/2024}	261.82 (N.A.) {261.82}	70.59	46
		1002	BALANCE WORK OF REHABILITATION AND UP-GRADATION TO NH-166F FROM MAHAD JUNCTION (AT KM 123/400 ON NH- (MoRTH) (N24001891)	7-2021	11/2023 (N.A.) {3/2024}	256.54 (N.A.) {256.54}	80.10	59.66
		1003	REHABILITATION AND UPGRADATION OF SHIRAPUR JUNCTION TO SHIVAJI CHOWK (DESIGN CHAINAGE KM. 130+00 TO (MoRTH) (N24001892)	2-2023	12/2024 (N.A.) {12/2024}	245.61 (N.A.) {245.61}	43.39	32.5
		1004	2 LANE + PS ASTHAMODE - TIVATYAL [DESIGN CH. KM 24.300 - 62.00] [KM 134.98-172.95 OF NH-63] (MoRTH) (N24001894)	9-2019	7/2021 (N.A.) {12/2023}	228.82 (N.A.) {228.82}	144.54	95.44
		1005	REHABILITATION AND UPGRADATION TO TWO LANES WITH PAVED SHOULDER CONFIGURATION FROM WATUR TO CHARTHANA (MoRTH) (N24001895)	11-2021	9/2023 (N.A.) {12/2023}	228.01 (N.A.) {228.01}	103.01	99
		1006	UPGRADATION AND REHABILITATION OF SECTION OF NH 361 F FROM PARLI (00/000) TO GANGAKHED (30/400) TO (MoRTH) (N24001896)	11-2021	9/2023 (N.A.) {4/2024}	224.44 (N.A.) {224.44}	75.34	45.63
		1007	REHABILITATION AND UP-GRADATION OF SABALKHED TO ASHTI SECTION FROM KM 37+900 TO KM 55+100 AND CHINCH (MoRTH) (N24001902)	12-2022	9/2024 (N.A.) {9/2024}	213.32 (N.A.) {213.32}	20.00	34

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1008	REHABILITATION AND UP-GRADATION OF MUDKHED TO NANDED SECTION FROM KM. 372+000 TO KM 388+400 OF NH 16 (MoRTH) (N24001903)	8-2022	4/2025 (N.A.) {4/2025}	206.54 (N.A.) {206.54}	21.36	0
		1009	KOPARGAON TO SAVALI VIHIR SECTION (MoRTH) (N24001904)	9-2022	7/2024 (N.A.) {7/2024}	195.38 (N.A.) {195.38}	29.59	19.76
		1010	CONSTRUCTION OF MAJOR BRIDGE ACROSS MANJRA RIVER NEAR YESGI VILLAGE @ KM, 166/500 ON NH 63 TQ BILOLI (MoRTH) (N24001905)	10-2021	8/2023 (N.A.) {12/2023}	188.69 (N.A.) {188.69}	111.26	95.8
		1011	UP-GRADATION TO 4 LANING OF DAULTABAD T-POINT TO MALIWADA [FROM DESIGN KM.0.000 TO KM 4.000] AND UPG (MoRTH) (N24001906)	8-2022	3/2024 (N.A.) {3/2024}	185.59 (N.A.) {185.59}	63.56	48
		1012	CONSTRUCTION OF SIX LANE FLYOVER AT KATRAJ JUNCTION AT KM, 3/880 OF NH 548-DD (VADGAON - KATRAJ - KO (MoRTH) (N24001907)	6-2021	2/2024 (N.A.) {3/2024}	169.15 (N.A.) {169.15}	36.94	35.96
		1013	UPGRADATION OF EXHISTING 2 LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDERS RIGID PAVEMENT FROM DESI (MoRTH) (N24001908)	12-2021	5/2024 (N.A.) {5/2024}	167.97 (N.A.) {167.97}	35.28	36.76
		1014	STRENGTHING AND WIDINING OF EXISTING CARRIAGEWAY TO 10 M IN KM, 156/160 TO 229/160 (TEMBHURNI - KUSL (MoRTH) (N24001909)	11-2021	6/2024 (N.A.) {6/2024}	157.72 (N.A.) {157.72}	55.38	91
		1015	REHABILITATION AND UPGRADATION OF JAMKHED TO SAUTADA SECTION OF NH548 D (FROM KM 195.375 TO KM 208.7 (MoRTH) (N24001910)	9-2022	7/2024 (N.A.) {7/2024}	157.62 (N.A.) {157.62}	13.86	17.03

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1016	PANGAON TO DHARMAPURI AND PARALI TO INJEGAON 2L+PS (MoRTH) (N24001911)	3-2018	7/2024 (N.A.) {12/2023}	152.03 (N.A.) {152.03}	81.35	97.57
		1017	4L OF INDORA CHOWK TO PACHPAOLI AND AGRASEN CHOWK - ASHOKA CHOWK (NHA) (N24002071)	3-2023	6/2026 (N.A.) {6/2026}	998.27 (N.A.) {998.27}	298.69	39.24
		1018	IMPROVEMENT OF EXISTING ALIGNMENT OF PANDHARPUR TOWN PART BYPASSED SECTION FROM WAKHARI TO LORD VITT (NHA) (N24002072)	7-2022	10/2025 (N.A.) {10/2025}	150.21 (150.21) {150.21}	24.66	2
		1019	STRENGTHENING OF 6-LANE PIMPALGAON-NASHIK-GONDE (KM. 380 - KM. 440) SECTION OF NH-3 IN MAHARASHTRA U (NHA) (N24002137)	2-2024	3/2025 (N.A.) {3/2025}	175.00 (206.49) {206.49}	198.54	98
		1020	REHABILITATION/UPGRADATION OF EXISTING HIGHWAY TO 2L+PS/4 LANE OF DHAWALI TO RAJOLI FROM DESIGN KM.1 (MoRTH) (N24002169)	3-2022	9/2025 (N.A.) {9/2025}	316.44 (N.A.) {316.44}	-	0
		1021	REHABILITATION/ UPGRADATION OF EXISTING HIGHWAY TO FOUR LANE STANDARDS IN KURKHEDA TOWN FROM (KM.413 (MoRTH) (N24002170)	3-2022	5/2025 (N.A.) {5/2025}	163.86 (N.A.) {163.86}	-	0
		1022	REHABILITATION & UP-GRADATION FOR TALERE A?? GAGANBAWDAA?? KOLHAPUR ROAD (NH-166G) STRETCHES START F (MoRTH) (N24002171)	2-2023	4/2025 (N.A.) {4/2025}	249.13 (N.A.) {249.13}	-	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1023	UP-GRADATION TO 4 LANE CONFIGURATION FOR THE WORK OF PETH NAKA TO SANGLI ROAD, NH- 166H, FROM KM 0+00 (MoRTH) (N24002172)	2-2023	12/2025 (N.A.) {12/2025}	856.82 (N.A.) {856.82}	-	0
		1024	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF MAHUD SANGOLA ROAD NH (MoRTH) (N24002173)	2-2023	4/2025 (N.A.) {4/2025}	253.78 (N.A.) {253.78}	-	0
		1025	UP-GRADATION TO FOUR LANE/ TWO LANE WITH PAVED SHOULDERS CONFIGURATION OF KALYAN - MURBAD - MALSHEJ (MoRTH) (N24002174)	2-2023	8/2026 (N.A.) {8/2026}	984.07 (N.A.) {984.07}	-	0
		1026	CONSTRUCTION OF FOUR-LANE CONCRETE ROAD FROM POLICE HEADQUARTER GONDIA CITY TO RAWANWADI VILLAGE (BI (MoRTH) (N24002175)	2-2023	8/2025 (N.A.) {8/2025}	328.11 (N.A.) {328.11}	-	0
		1027	REHABILITATION/UP GRADATION OF KARANJA ? KHERDA - MURTIZAPUR SECTION TO 4LANE+PAVED SHOULDER STANDA (MoRTH) (N24002176)	3-2023	2/2026 (N.A.) {2/2026}	594.44 (N.A.) {594.44}	-	0
		1028	REHABILITATION / UPGRADATION TO 4 LANE WITH PAVED SHOULDER OF EXISTING SECTION IN SILLOD TOWN WITH D (MoRTH) (N24002177)	3-2023	7/2025 (N.A.) {7/2025}	153.79 (N.A.) {153.79}	-	0
		1029	REHABILITATION, UPGRADATION & WIDENING OF EXISTING HIGHWAY TO RIGID PAVEMENT 2 LANE WITH PAVED SHOUL (MoRTH) (N24002178)	2-2023	7/2026 (N.A.) {7/2026}	723.13 (N.A.) {723.13}	-	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	URBAN DEVELOPMENT	1030	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) (MMRCL) (N28000086)	7-2013	3/2020 (7/2025) {7/2025}	23,136.00 (N.A.) {37,276.00}	32,315.32	94.77
		1031	PUNE METRO RAIL PROJECT (PHASE 1) (MMRC) (N28000121)	12-2016	11/2021 (9/2024) {9/2024}	11,420.00 (13,656.22) {13,656.22}	13,023.70	100
		1032	NAGPUR METRO RAIL PROJECT PHASE II (NMRCL) (N28000155)	12-2022	12/2027 (N.A.) {12/2027}	6,708.00 (N.A.) {6,708.00}	739.81	19.34
		1033	PCMC NIGDI PROJECT EXTENSION OF CORRIDOR 1 OF PUNE METRO PHASE 1 (MMRC) (N28000157)	10-2023	1/2027 (N.A.) {1/2027}	910.18 (N.A.) {910.18}	67.86	12.05
		1034	PUNE METRO PHASE-1 EXTENSION FROM SWARGATE TO KATRAJ (MMRC) (N28000160)	9-2024	3/2029 (N.A.) {3/2029}	2,954.53 (N.A.) {2,954.53}	14.25	1
MANIPUR	CIVIL AVIATION	1035	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (3/2026) {3/2026}	499.00 (N.A.) {499.00}	154.47	38.36
	RAILWAYS	1036	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	3/2011 (3/2028) {12/2028}	4,454.17 (12,274.06) {22,234.60}	15,218.35	68.5
	ROAD TRANSPORT AND HIGHWAYS	1037	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG-2A) (NHIDCL) (N24001270)	3-2020	6/2022 (1/2025) {9/2025}	292.24 (N.A.) {292.24}	130.66	89.72

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1038	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (1/2025) {10/2025}	365.53 (N.A.) {365.53}	156.31	77.36
		1039	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3-2020	6/2022 (1/2025) {5/2025}	167.95 (204.12) {167.95}	88.05	69.89
		1040	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7-2020	8/2022 (2/2025) {5/2025}	177.76 (N.A.) {177.76}	89.67	80.53
		1041	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (6/2025) {6/2025}	379.39 (N.A.) {379.39}	214.93	63.76
		1042	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276)	8-2020	4/2022 (N.A.) {3/2025}	228.97 (N.A.) {228.97}	-	0
		1043	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (3/2025) {5/2025}	226.32 (N.A.) {226.32}	104.95	73.82
		1044	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (10/2024) {2/2025}	188.36 (N.A.) {188.36}	126.71	100
		1045	IMPHAL ? MOREH PACKAGE- 3 (NHIDCL) (N24001352)	3-2021	12/2022 (N.A.) {6/2024}	259.31 (N.A.) {259.31}	144.94	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1046	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3-2021	12/2022 (3/2025) {3/2026}	195.14 (N.A.) {195.14}	61.81	50.79
		1047	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (9/2024) {5/2025}	234.08 (N.A.) {234.08}	139.45	91.04
		1048	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (5/2025) {5/2025}	211.70 (N.A.) {211.70}	83.79	65.02
		1049	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (3/2025) {10/2025}	467.00 (N.A.) {467.00}	193.81	77.59
		1050	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (1/2025) {1/2025}	185.80 (N.A.) {185.80}	117.78	100
		1051	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (8/2024) {5/2025}	483.87 (N.A.) {483.87}	278.89	92.73
		1052	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (2/2025) {3/2025}	198.77 (N.A.) {198.77}	125.11	100
		1053	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (3/2025) {5/2025}	673.27 (N.A.) {673.27}	377.12	78.46
		1054	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (1/2025) {6/2025}	477.86 (N.A.) {477.86}	243.46	83.92

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1055	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (11/2024) {4/2025}	311.18 (N.A.) {311.18}	186.15	81.21
		1056	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (10/2024) {2/2025}	467.41 (N.A.) {467.41}	264.83	100
		1057	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (7/2025) {12/2025}	579.63 (N.A.) {579.63}	172.65	67.02
		1058	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (3/2025) {5/2025}	310.76 (N.A.) {310.76}	129.15	96.77
		1059	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (2/2025) {3/2026}	410.68 (N.A.) {410.68}	147.81	65.85
		1060	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (9/2025) {12/2025}	504.76 (N.A.) {504.76}	183.15	73.23
		1061	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (2/2025) {3/2025}	152.11 (N.A.) {152.11}	73.48	100
		1062	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (1/2025) {9/2025}	315.56 (N.A.) {315.56}	121.49	79.2
		1063	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (12/2025) {3/2026}	760.16 (N.A.) {760.16}	148.98	57.37

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1064	UKHRUL TO LOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (3/2026) {3/2026}	578.98 (N.A.) {578.98}	145.62	67.93
		1065	MARREM KHULLEN TO JESSAMI SECTION IMPHAL - UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	11.64	9.21
		1066	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	10.88	11.5
		1067	JESSAMI TO LAYNEN BRIDGE UKHRUL - JESSAMI PKG-7 (NHIDCL) (N24002227)	3-2023	6/2026 (N.A.) {6/2026}	164.89 (N.A.) {164.89}	-	0
MEGHALAYA	DEPARTMENT OF HIGHER EDUCATION	1068	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (7/2025) {7/2025}	484.32 (429.70) {429.70}	294.55	82.5
	DONER	1069	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR (HSCL FOR DONER) (N12000103)	4-2014	9/2017 (N.A.) {9/2017}	151.33 (N.A.) {151.33}	148.33	100
	ROAD TRANSPORT AND HIGHWAYS	1070	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (4/2025) {4/2025}	553.51 (610.09) {553.51}	414.04	82.32
		1071	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4- LANING FROM ((NHIDCL) (N24001313)	11-2020	12/2023 (10/2025) {10/2025}	351.12 (N.A.) {351.12}	295.87	59.2

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1072	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	425.39	28
		1073	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	206.15	23.5
		1074	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	100.93	20.5
		1075	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI- RONGARA) (NHIDCL) (N24001339)	10-2020	4/2022 (6/2024) {2/2025}	157.86 (146.92) {157.86}	152.90	100
		1076	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3-2021	12/2022 (6/2024) {2/2025}	260.21 (N.A.) {260.21}	239.10	100
		1077	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (3/2025) {3/2025}	302.88 (N.A.) {302.88}	224.39	95
		1078	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (12/2024) {12/2025}	359.86 (N.A.) {359.86}	232.55	87
		1079	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11-2021	6/2024 (12/2024) {4/2025}	283.50 (N.A.) {283.50}	256.07	96.06

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1080	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	210.58	24.5
		1081	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	281.90	21.5
		1082	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	292.43	21.5
<u>MIZORAM</u>	<u>RAILWAYS</u>	1083	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2014 (N.A.) {7/2025}	2,393.47 (5,021.45) {8,213.72}	7,906.29	94.6
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1084	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (N.A.) {3/2025}	519.09 (N.A.) {785.65}	667.78	95.75
		1085	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (N.A.) {7/2023}	640.07 (N.A.) {1,286.35}	1,192.26	98.9
		1086	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4-2017	6/2023 (N.A.) {3/2024}	642.96 (N.A.) {988.23}	721.12	99.55

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1087	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (N.A.) {3/2025}	473.18 (N.A.) {688.25}	539.93	92.01
		1088	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (N.A.) {3/2025}	537.82 (N.A.) {789.05}	768.85	95.4
		1089	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (N.A.) {3/2025}	518.53 (N.A.) {906.76}	847.17	97.01
		1090	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (N.A.) {3/2025}	404.29 (N.A.) {750.32}	654.75	97.51
		1091	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (N.A.) {3/2025}	428.11 (N.A.) {746.39}	605.09	97.46
		1092	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9-2020	10/2022 (N.A.) {4/2025}	275.02 (N.A.) {247.25}	265.18	99.74
		1093	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (N.A.) {6/2024}	206.88 (N.A.) {219.33}	265.18	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1094	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING- DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (N.A.) {6/2025}	292.24 (N.A.) {331.17}	291.20	93.15
		1095	DULTE- KWALKULH - CHAMPAI PKG.1 (NHIDCL) (N24001355)	3-2021	12/2022 (3/2024) {3/2024}	374.39 (N.A.) {318.92}	286.49	100
		1096	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (4/2024) {12/2025}	233.25 (N.A.) {233.25}	172.09	100
		1097	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (N.A.) {3/2026}	698.44 (N.A.) {698.45}	481.12	52.84
		1098	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (N.A.) {3/2026}	740.58 (N.A.) {740.58}	353.73	50.6
		1099	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9-2021	5/2023 (N.A.) {5/2024}	492.94 (N.A.) {492.94}	353.09	100
		1100	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWLRAH SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {12/2025}	523.78 (N.A.) {523.78}	303.25	61
		1101	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	250.46	65.1
		1102	ZORINPUI- HMAWNGBU-LONGMASU (NH-502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	67.12	0.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MULTI STATE	COAL	1103	NILJAI EXPANSION (DEEP) OC (3.5 MTY) (WCL) (N06000154)	8-2016	3/2022 (3/2025) {3/2025}	319.76 (319.76) {319.76}	183.67	98
		1104	BINA KAKRI AMALGAMATION OCP 14 MTPA (NCL) (N06000192)	8-2020	3/2024 (N.A.) {3/2027}	836.42 (N.A.) {836.42}	726.61	57.18
	DPIIT	1105	NATIONAL INDUSTRIAL CORRIDOR PROJECT (DMIC FOR DPIIT) (N40000001)	9-2011	3/2027 (3/2032) {3/2032}	20,084.00 (26,684.00) {26,684.00}	11,262.06	50.99
	PETROLEUM	1106	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II (GAIL) (N16000285)	6-2009	12/2012 (2/2025) {3/2026}	2,915.00 (5,909.00) {5,909.00}	4,176.20	93.7
		1107	SRIKAKULAM ANGUL PIPELINE PROJECT (GAIL) (N16000388)	9-2019	7/2022 (6/2025) {6/2025}	2,658.34 (N.A.) {2,658.34}	2,132.70	94
		1108	DHAMRA HALDIA PIPELINE PROJECT (GAIL) (N16000391)	3-2020	11/2022 (7/2025) {12/2025}	1,030.65 (N.A.) {1,030.65}	822.90	86
		1109	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT (GAIL) (N16000398)	6-2020	5/2023 (6/2025) {6/2025}	7,844.25 (N.A.) {7,844.25}	6,224.30	93.2
		1110	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS (IOCL) (N16000426)	6-2019	12/2029 (3/2030) {3/2030}	169.00 (N.A.) {169.00}	75.02	27.2
		1111	NORTH EAST GAS GRID (IGGL) (N16000439)	11-2020	3/2024 (7/2025) {3/2027}	9,265.00 (9,265.00) {9,265.00}	6,270.19	84.4

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1112	GURDASPUR JAMMU PIPELINE (GAIL) (N16000531)	7-2023	7/2026 (7/2026) {7/2026}	521.92 (521.92) {521.92}	120.70	32
	POWER	1113	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P (PGCIL) (N18000249)	12-2014	12/2018 (3/2025) {3/2027}	4,754.42 (9,129.32) {9,129.32}	7,602.44	80
		1114	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES (PGCIL) (N18000250)	12-2014	12/2018 (3/2025) {6/2025}	5,111.33 (6,700.00) {6,700.00}	5,276.39	95.7
		1115	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME - II AC SYSTEM STRENGTHENING AT PUGALUR EN (PGCIL) (N18000264)	8-2017	2/2020 (4/2023) {9/2025}	1,931.39 (2,635.55) {2,635.55}	1,972.44	100
		1116	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM (PGCIL) (N18000328)	2-2022	4/2025 (N.A.) {4/2025}	318.12 (N.A.) {318.12}	157.75	94
		1117	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR- LEH TRANSMISSION SYSTEM (PGCIL) (N18000330)	3-2022	12/2024 (N.A.) {7/2025}	288.71 (N.A.) {288.71}	144.79	48
		1118	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000331)	2-2022	9/2023 (N.A.) {5/2025}	359.47 (N.A.) {359.47}	292.16	82

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1119	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000332)	5-2022	11/2023 (N.A.) {5/2025}	1,666.00 (N.A.) {1,666.00}	1,449.62	88
		1120	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B (PGCIL) (N18000337)	7-2022	6/2023 (N.A.) {6/2025}	4,546.26 (N.A.) {4,546.26}	2,680.35	89
		1121	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C (PGCIL) (N18000338)	7-2022	3/2025 (N.A.) {3/2025}	186.19 (N.A.) {186.19}	71.53	100
		1122	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION (PGCIL) (N18000343)	10-2022	10/2025 (N.A.) {10/2025}	307.87 (N.A.) {307.87}	184.31	89
		1123	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B (PGCIL) (N18000352)	3-2023	11/2024 (N.A.) {5/2025}	3,546.94 (N.A.) {3,546.94}	2,106.14	87
		1124	ER WR TRANSMISSION LIMITED (PGCIL) (N18000353)	3-2023	3/2025 (N.A.) {4/2025}	281.16 (N.A.) {281.16}	129.14	84
	RAILWAYS	1125	NANGALDAM-TALWARA(NL),NR (NR) (220100188)	3-1981	7/2012 (1/2027) {6/2027}	450.00 (N.A.) {2,017.96}	1,579.04	70
		1126	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) (WCR) (220100232)	9-1998	5/2008 (N.A.) {3/2025}	247.66 (63.57) {8,248.50}	2,520.04	43

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1127	CHHAPRA-BALLIA UP (NER) (N22000134)	3-2013	1/2019 (N.A.) {12/2025}	295.00 (954.00) {1,045.82}	1,001.52	95.5
		1128	CHOTTAUDEPUR-DHAR(NL) (WR) (N22000138)	4-2007	3/2022 (12/2027) {12/2027}	1,347.26 (1,793.63) {1,793.63}	1,615.35	59
		1129	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) (WR) (N22000139)	4-2007	3/2022 (2/2027) {2/2027}	1,640.04 (1,873.10) {2,873.11}	2,834.85	59
		1130	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) (NCR) (N22000148)	4-2011	3/2022 (N.A.) {12/2024}	2,912.96 (N.A.) {3,845.60}	1,024.32	0
		1131	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR- BANSI PAHARPUR (NCR) (N22000158)	4-2010	(12/2026) {12/2026}	2,030.50 (746.83) {746.83}	152.47	31
		1132	NEW BONGAIGAON-RANGIA- KAMAKGHYA DOUBLING (NFR) (N22000183)	4-2013	3/2019 (N.A.) {10/2024}	1,798.00 (N.A.) {2,832.35}	3,647.20	99.5
		1133	NEW BG LINE FROM BALURGHAT TO HILLY NFR (NFR) (N22000206)	4-2010	3/2020 (N.A.) {3/2027}	242.22 (N.A.) {1,181.57}	402.03	6
		1134	NEW BG LINE FROM JAGBANI TO BIRATNAGAR (NFR) (N22000207)	4-2010	(12/2026) {12/2026}	241.52 (485.96) {485.96}	365.61	86.21
		1135	MURKONGSELEK-PASIGHAT NL (NFR) (N22000208)	4-2011	3/2020 (N.A.) {11/2025}	414.84 (N.A.) {1,252.49}	709.39	51.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1136	PIRPAINTI-JASIDIH (ER) (N22000219)	4-2013	3/2022 (3/2028) {3/2028}	915.98 (N.A.) {2,610.84}	1,121.11	45
		1137	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION (SCR) (N22000261)	4-2012	3/2023 (N.A.) {3/2025}	1,856.95 (N.A.) {1,952.68}	1,688.42	0
		1138	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL (NR) (N22000274)	4-2007	(N.A.) {3/2025}	336.91 (N.A.) {791.39}	578.85	99
		1139	RAYADURGA-TUMKUR NL (SWR) (N22000279)	4-2007	(N.A.) {2/2028}	2,062.30 (2,495.59) {2,495.59}	1,629.58	60
		1140	HOTGI-KUDGI-GADAG (SWR) (N22000333)	3-2015	3/2019 (N.A.) {2/2026}	1,614.59 (1,877.81) {2,458.87}	2,500.63	89
		1141	KAZIPET-BALHRSHA (SCR) (N22000367)	4-2015	3/2021 (N.A.) {1/2025}	2,063.03 (N.A.) {2,909.00}	2,775.02	0
		1142	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT (NHSRCL) (N22000463)	12-2015	12/2023 (N.A.) {8/2027}	108,000.00 (N.A.) {108,000.00}	72,257.00	50
		1143	WESTERN DEDICATED FREIGHT CORRIDOR (DFCC) (N22000464)	11-2007	3/2020 (N.A.) {3/2020}	16,592.00 (51,101.00) {51,101.00}	47,476.00	83
		1144	CHANDIGARH-BADDI (NR) (N22000467)	4-2007	3/2023 (12/2026) {12/2026}	328.14 (1,540.14) {1,540.14}	936.85	25

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1145	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) (SER) (N22000506)	3-2019	5/2023 (N.A.) {6/2026}	1,866.31 (N.A.) {1,866.31}	1,928.60	58
	ROAD TRANSPORT AND HIGHWAYS	1146	VARANASI-AURANGABAD KM.786 TO KM.978.40 (NHAI) (N24000182)	9-2011	3/2014 (N.A.) {6/2025}	2,848.00 (N.A.) {3,241.56}	3,901.66	90.02
		1147	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 (NHAI) (N24001628)	11-2021	2/2025 (8/2025) {8/2025}	2,155.95 (N.A.) {2,155.95}	1,279.14	60.28
		1148	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O (NHAI) (N24001629)	4-2022	11/2024 (5/2025) {5/2025}	796.65 (N.A.) {796.65}	412.96	83.55
	SHIPPING AND PORTS	1149	JAL MARG VIKAS PROJECT (IWAI) (N25000072)	1-2018	3/2023 (12/2025) {12/2025}	5,369.18 (5,061.15) {5,061.15}	3,397.03	67.98
	TELECOMMUNIC ATIONS	1150	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (N26000114)	3-2020	6/2021 (11/2021) {6/2025}	461.42 (461.42) {461.42}	165.04	81
		1151	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LABEL SWITCHING (IPMPLS) NETWORK and (BSNL) (N26000115)	3-2023	3/2024 (7/2024) {3/2025}	239.60 (N.A.) {239.60}	174.71	100
		1152	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (N26000116)	5-2023	8/2024 (11/2024) {3/2025}	645.13 (N.A.) {645.13}	340.81	85.63

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1153	PLANNIN ENGINEERING SUPPLY INSTALLATION TESTING COMMISSIONING INTEGARTION and ANNUAL MAINTENANCE OF (BSNL) (N26000117)	6-2023	6/2025 (N.A.) {6/2025}	24,556.35 (24,544.55) {24,544.55}	7,739.52	87.36
		1154	OPTICAL TRANSPORT NETWORK (OTN) PH-4 IN BSNL (BSNL) (N26000118)	2-2024	8/2025 (N.A.) {8/2025}	810.99 (N.A.) {810.99}	476.39	98.71
	URBAN DEVELOPMENT	1155	DELHI GHAZIABAD MEERUT RRTS CORRIDOR (NCRTC) (N28000134)	3-2019	6/2025 (N.A.) {6/2025}	30,274.00 (N.A.) {30,274.00}	24,993.22	85
<u>NAGALAND</u>	<u>PETROLEUM</u>	1156	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	4.10	17
	<u>RAILWAYS</u>	1157	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2015 (N.A.) {12/2029}	2,326.52 (6,663.20) {6,663.20}	4,531.38	66
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1158	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3-2016	9/2019 (11/2022) {4/2025}	373.07 (534.41) {534.41}	382.50	99.81
		1159	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (9/2025) {9/2025}	429.52 (794.74) {794.74}	321.40	90.38
		1160	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (2/2023) {4/2025}	387.00 (688.12) {688.12}	389.81	99.72

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1161	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (8/2024) {4/2025}	500.09 (698.81) {698.81}	393.53	98.88
		1162	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA- ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756)	3-2018	9/2022 (1/2023) {7/2024}	285.68 (N.A.) {285.68}	193.90	100
		1163	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (8/2022) {8/2025}	215.79 (N.A.) {215.79}	127.85	68.29
		1164	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (6/2023) {9/2025}	323.98 (N.A.) {323.98}	112.43	51.23
		1165	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3-2017	11/2020 (2/2023) {2/2023}	217.35 (N.A.) {217.35}	214.18	100
		1166	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3-2019	12/2022 (1/2023) {1/2023}	237.51 (N.A.) {237.51}	215.47	100
		1167	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (9/2024) {6/2026}	277.44 (N.A.) {277.44}	168.88	66.12

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1168	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (6/2025) {6/2025}	159.85 (342.29) {159.85}	101.93	28.57
		1169	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (4/2023) {8/2025}	202.36 (N.A.) {202.36}	75.17	30.33
		1170	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9-2020	4/2022 (5/2024) {12/2025}	315.63 (N.A.) {315.63}	116.70	74.23
		1171	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	109.24	62.7
		1172	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3-2020	6/2022 (10/2022) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
		1173	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (11/2025) {11/2025}	330.80 (N.A.) {330.80}	168.02	87.53
		1174	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (11/2026) {11/2026}	232.29 (350.88) {232.29}	69.98	13.46
		1175	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3-2020	6/2022 (9/2022) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.4

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1176	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7-2021	3/2023 (9/2025) {9/2025}	258.52 (N.A.) {258.52}	83.96	75.64
		1177	PEREN-DIMAPUR PKG-5 (NHIDCL) (N24001407)	2-2021	3/2023 (N.A.) {3/2023}	207.33 (N.A.) {207.33}	-	0
		1178	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	62.08	59
		1179	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (6/2026) {6/2026}	252.19 (N.A.) {252.19}	11.80	13.85
		1180	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH- 61 (N (MoRTH) (N24001466)	3-2021	7/2024 (6/2025) {6/2025}	297.24 (N.A.) {297.24}	137.57	74.45
		1181	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (3/2025) {3/2025}	226.44 (N.A.) {226.44}	140.24	100
		1182	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3-2022	12/2024 (N.A.) {1/2025}	605.36 (N.A.) {605.36}	273.21	100
		1183	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (6/2025) {6/2025}	192.93 (N.A.) {192.93}	96.19	87.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1184	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {12/2025}	177.77 (199.02) {199.02}	43.33	56.47
		1185	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	92.24	49.15
		1186	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE- II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	39.97	20.46
		1187	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE- III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	159.36	58.7
ODISHA	COAL	1188	BASUNDHARA (WEST) OC EXTN(7.00 MTY) (MCL) (N06000112)	5-2014	3/2019 (N.A.) {3/2027}	479.15 (N.A.) {479.15}	267.05	63.04
		1189	SIARMAL OCP (40.00MTY) (MCL) (N06000113)	2-2021	3/2029 (N.A.) {3/2029}	5,194.96 (N.A.) {5,194.96}	3,435.86	51.07
		1190	GARJANBAHAL OCP (MCL) (N06000117)	11-2014	3/2021 (N.A.) {3/2026}	1,375.38 (N.A.) {1,375.38}	849.48	0
		1191	INTEGRATED LAKHANPUR-BELPAHAR- LILARI OCP (MCL) (N06000167)	5-2018	3/2027 (N.A.) {3/2027}	2,434.75 (N.A.) {2,434.75}	1,747.84	60.87

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1192	REORGANISATION OF BHARATPUR OCP EXPANSION (MCL) (N06000171)	11-2018	3/2029 (N.A.) {3/2029}	2,838.87 (N.A.) {2,838.87}	1,742.83	44.6
		1193	TALABIRA II AND III OCP (NLC) (N06000189)	7-2017	1/2027 (N.A.) {1/2027}	2,401.07 (N.A.) {2,401.07}	1,581.42	60.1
		1194	NAINI COAL MINE (SCCL) (N06000203)	3-2020	3/2024 (N.A.) {3/2026}	494.30 (N.A.) {494.30}	491.33	80
		1195	BHUBANESWARI EXPANSION OCP (MCL) (N06000227)	3-2024	3/2031 (N.A.) {3/2031}	6,321.73 (N.A.) {6,321.73}	1,354.15	18.2
		1196	GOPALJI-KANIHA OCP (MCL) (N06000229)	4-2022	3/2028 (N.A.) {3/2028}	6,107.87 (N.A.) {6,107.87}	1,693.77	17.39
		1197	BALARAM EXPANSION OCP (MCL) (N06000230)	8-2020	3/2029 (N.A.) {3/2029}	3,504.21 (N.A.) {3,504.21}	1,004.00	50.17
		1198	KULDA EXPANSION OCP- 15 MTY (MCL) (N06000248)	6-2014	3/2018 (N.A.) {3/2026}	348.16 (N.A.) {348.16}	207.75	0
		1199	SUBHADRA OCP (MCL) (N06000249)	5-2021	3/2029 (3/2029) {3/2029}	1,693.81 (N.A.) {1,693.81}	1,179.60	39.3
		1200	RPR OF HINGULA -II EXPANSION PH-III (MCL) (N06000261)	12-2022	3/2029 (N.A.) {3/2029}	2,264.68 (N.A.) {2,264.68}	1,054.83	39.2

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1201	NLC TALABIRA THERMAL POWER PROJECT (PHASE-1: 3 X 800 MW) (NLC) (N06000270)	1-2024	5/2029 (3/2030) {3/2030}	27,213.00 (N.A.) {27,213.00}	1,556.04	1.55
		1202	RPR OF HINGULA EXPANSION OCP (MCL) (N06000285)	11-2022	3/2029 (N.A.) {3/2029}	1,561.85 (N.A.) {1,561.85}	43.33	3.57
		1203	BHUBANESWARI EXPANSION OCP (MCL) (N06000286)	3-2024	3/2031 (N.A.) {3/2031}	5,366.28 (N.A.) {5,366.28}	0.50	3.39
		1204	BALABHADRA OCP (MCL) (N06000288)	4-2023	3/2030 (N.A.) {3/2030}	978.44 (N.A.) {978.44}	208.37	1
		1205	INTEGRATED KULDA GARJANBAHAL OCP (MCL) (N06000289)	4-2023	3/2030 (N.A.) {3/2030}	3,563.50 (N.A.) {3,563.50}	6.43	1
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1206	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR (CPWD EDUCATION) (N28000126)	1-2019	3/2022 (N.A.) {6/2025}	790.79 (N.A.) {790.79}	701.39	95
	<u>MINES</u>	1207	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT (NALCO) (N10000010)	12-2014	4/2021 (9/2025) {9/2025}	4,103.00 (5,677.40) {5,677.40}	3,711.07	72.13
		1208	UTKAL D AND E COAL BLOCK (NALCO) (N10000011)	5-2016	1/2020 (11/2023) {3/2024}	534.00 (N.A.) {1,021.97}	826.19	85.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1209	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (NALCO) (N10000012)	12-2015	11/2020 (9/2025) {8/2027}	355.00 (581.00) {581.00}	163.55	12.6
		1210	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN (NALCO) (N10000013)	11-2017	4/2021 (5/2025) {5/2025}	483.00 (483.00) {495.00}	382.83	88.6
		1211	POTTANGI BAUXITE MINES (NALCO) (N10000016)	5-2018	12/2024 (N.A.) {5/2025}	1,437.00 (N.A.) {1,381.00}	649.96	50.8
		1212	CONSTRUCTION OF RED MUD POND - II AT NALCO DAMANJODI ODISHA (NALCO) (N10000017)	9-2019	3/2023 (5/2024) {5/2024}	225.79 (N.A.) {270.66}	5.00	100
	PETROLEUM	1213	ADDITIONAL STORAGE TANKS AT PARADIP (IOCL) (N16000361)	11-2018	9/2021 (12/2024) {3/2025}	462.30 (552.44) {552.44}	493.72	98
		1214	Fuel Quality Upgradation Project at Paradip Refinery (IOCL) (N16000362)	5-2019	8/2021 (12/2024) {1/2025}	3,361.00 (N.A.) {3,361.00}	2,727.60	98.8
		1215	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY (IOCL) (N16000368)	6-2019	9/2022 (12/2024) {1/2025}	427.10 (427.10) {427.10}	312.13	95.9
		1216	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY (IOCL) (N16000396)	7-2020	1/2024 (4/2025) {4/2026}	13,805.00 (N.A.) {13,805.00}	7,155.59	88.6

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	1217	EASTERN REGION EXPANSION SCHEME XXIX (PGCIL) (N18000351)	3-2023	11/2025 (N.A.) {11/2025}	524.04 (N.A.) {524.04}	347.97	92
		1218	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) (NTPC) (N18000364)	8-2022	5/2027 (N.A.) {12/2027}	11,844.00 (N.A.) {12,539.00}	2,868.74	21.4
	RAILWAYS	1219	KHURDA ROAD-BOLANGIR(NL)ECOR (ECOR) (220100284)	4-1994	3/2009 (12/2026) {12/2026}	2,923.13 (3,791.66) {5,089.37}	4,627.52	84
		1220	TALCHER-BIMALAGARH(NL)(ECOR) (ECOR) (220100328)	4-2005	6/2021 (N.A.) {3/2026}	810.78 (N.A.) {1,928.07}	1,666.92	40
		1221	BHADRAK - NERGUNDI 3RD LINE (ECOR) (N22000316)	3-2013	10/2020 (10/2025) {10/2025}	843.04 (1,284.39) {1,284.39}	1,237.22	75
		1222	JAGADALPUR-KORAPUT DOUBLING (ECOR) (N22000376)	4-2015	3/2022 (N.A.) {3/2022}	1,547.38 (N.A.) {1,547.38}	1,262.13	93
		1223	KORAPUT - SINGAPUR ROAD DOUBLING (ECOR) (N22000379)	4-2015	3/2022 (3/2026) {3/2026}	2,361.74 (2,361.74) {2,361.74}	1,736.99	77
		1224	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE (ECOR) (N22000380)	4-2015	11/2018 (N.A.) {8/2026}	701.61 (N.A.) {810.02}	571.79	0
		1225	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. (ECOR) (N22000381)	4-2015	12/2018 (11/2025) {11/2025}	1,172.92 (N.A.) {2,022.75}	1,887.49	75

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1226	VIZIANAGARAM -SAMABALPUR 3RD LINE (RVNL) (N22000409)	1-1991	12/2024 (N.A.) {12/2026}	2,335.67 (N.A.) {4,803.16}	4,691.52	0
		1227	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL (IRCON) (N22000418)	4-2016	3/2020 (N.A.) {12/2025}	5,200.00 (N.A.) {5,200.00}	-	17.4
		1228	JEYPORE MALKANGIRI NEW LINE (ECOR) (N22000516)	2-2018	7/2033 (N.A.) {7/2033}	642.69 (N.A.) {642.69}	200.33	0.1
		1229	JEYPORE NABARANGPUR NEWLINE (ECOR) (N22000517)	7-2017	7/2028 (N.A.) {7/2028}	499.99 (N.A.) {747.91}	-	0
		1230	TALCHER - ANGUL NEW LINE WITH Y CONNECTION AT TALCHER (ECOR) (N22000518)	7-2018	12/2026 (N.A.) {12/2026}	278.96 (495.00) {494.62}	29.50	0
		1231	KODINGAMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (ECOR) (N22000519)	8-2022	8/2027 (N.A.) {8/2027}	190.90 (N.A.) {190.90}	10.00	0
		1232	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION (ECOR) (N22000520)	9-2022	9/2027 (N.A.) {3/2028}	189.93 (N.A.) {189.93}	13.76	0
		1233	BRUNDAMAL-JHARSUGUDA- FLYOVER CONNECTION FOR JOINING DN LINE (ECOR) (N22000521)	12-2009	12/2026 (N.A.) {12/2026}	48.44 (N.A.) {297.00}	302.50	10
		1234	BAGHUAPAL FLY OVER (20 KM) (ECOR) (N22000522)	8-2019	8/2027 (8/2027) {8/2027}	183.00 (257.97) {257.97}	0.60	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1235	ROURKELA-BONDAMUNDA A-CABIN 5TH LINE (10 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SER) (N22000571)	9-2022	9/2026 (N.A.) {2/2026}	209.75 (N.A.) {244.99}	55.81	10
	ROAD TRANSPORT AND HIGHWAYS	1236	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH- 55 IN THE S (NHA) (N24000619)	9-2016	8/2019 (N.A.) {5/2025}	2,510.04 (N.A.) {2,510.04}	1,181.34	99.38
		1237	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH- 42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO (NHA) (N24000715)	12-2017	7/2020 (N.A.) {6/2025}	686.65 (565.00) {686.65}	574.26	97
		1238	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE ((NHA) (N24000733)	1-2018	8/2022 (N.A.) {12/2025}	633.68 (492.83) {633.68}	560.38	85.59
		1239	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG (NHA) (N24000734)	1-2018	8/2021 (N.A.) {6/2025}	614.48 (503.30) {757.12}	664.48	99
		1240	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON (NHA) (N24000736)	1-2018	9/2020 (N.A.) {6/2025}	686.65 (504.09) {1,015.16}	435.85	95
		1241	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 (NHA) (N24000738)	1-2018	9/2021 (N.A.) {7/2025}	999.00 (1,152.70) {1,152.70}	498.82	80.25

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1242	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA- BARKOTE SECTION OF NH-23 (NEW NH NO. 143) ((NHAI) (N24000739)	1-2018	6/2021 (4/2025) {4/2025}	503.88 (609.03) {609.03}	536.89	98.09
		1243	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. (MoRTH) (N24000912)	8-2016	2/2017 (N.A.) {6/2025}	287.70 (N.A.) {293.66}	275.42	98.66
		1244	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA (MoRTH) (N24000914)	12-2016	8/2018 (N.A.) {6/2025}	223.50 (N.A.) {223.50}	220.50	92
		1245	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA (MoRTH) (N24000917)	3-2018	8/2018 (N.A.) {6/2025}	199.16 (N.A.) {199.16}	158.73	98
		1246	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 (NHAI) (N24001647)	8-2020	3/2022 (N.A.) {5/2025}	200.00 (154.73) {154.73}	150.38	99.62
		1247	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8 (NHAI) (N24001665)	12-2021	10/2024 (N.A.) {10/2025}	1,592.00 (1,592.00) {1,592.00}	1,042.87	74.7
		1248	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130-CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE-OD (NHAI) (N24001666)	12-2021	9/2024 (N.A.) {8/2025}	714.00 (714.00) {714.00}	556.84	90.09
		1249	6L GREENFIELD KALIAGURA ? BAUNSAGUAR SECTION OF NH-130- CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG (NHAI) (N24001667)	9-2021	5/2024 (N.A.) {10/2025}	1,734.00 (1,734.00) {1,734.00}	1,179.74	82.36

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1250	6L OF BADAKUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH-130-CD (PACKAGE ? OD-3) (NHAI) (N24001668)	3-2021	4/2024 (N.A.) {6/2025}	1,249.00 (N.A.) {1,249.00}	462.56	82.52
		1251	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH-130-CD (PACKAGE ? OD-1) (NHAI) (N24001669)	2-2021	3/2024 (N.A.) {6/2025}	586.00 (N.A.) {586.00}	240.33	85
		1252	6L OF KARKI ? KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH-130-CD (PACKAGE ? OD-4) (NHAI) (N24001670)	2-2021	3/2024 (N.A.) {5/2025}	593.00 (N.A.) {593.00}	282.15	93.35
		1253	6L OF HATIBENA - BADAKUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130-CD (PACKAGE ? OD- 2) (NHAI) (N24001671)	2-2021	3/2024 (N.A.) {5/2025}	925.00 (N.A.) {925.00}	460.47	97
		1254	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE ? (NHAI) (N24001678)	8-2021	6/2024 (N.A.) {8/2025}	1,460.00 (1,460.00) {1,460.00}	923.36	85.64
		1255	CONSTRUCTION OF ROAD FROM KM 0/0 TO 72/0 OF NH-26 SUCH AS 4 LANE FROM KM 0/0 TO 21/0 (BARGARH TO BAR (MoRTH) (N24001857)	6-2020	12/2023 (5/2025) {5/2025}	414.24 (N.A.) {414.24}	307.44	97
		1256	WIDENING AND STRENGTHENING TO 2L+PS INCLUDING LA OF KANDARPUR- BALIKUDA FROM KM 277/500 TO 318/970 OF (MoRTH) (N24001858)	3-2022	6/2025 (N.A.) {6/2025}	499.79 (N.A.) {499.79}	279.04	36.83
		1257	CONSTRUCTION OF BYPASS ON NH- 59 FROM KM 336/350 TO 349/910 (13.56 KM) NEAR BERHAMPUR TOWN INCLUDING (MoRTH) (N24001859)	3-2021	3/2024 (N.A.) {6/2025}	196.94 (N.A.) {196.94}	68.10	15

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1258	CONSTRUCTION OF BYPASS TO NAYAGARH TOWN FROM KM 235.469 TO 252.482 OF NH-57 INCLUDING LAND ACQUISITI (MoRTH) (N24001860)	1-2022	4/2025 (N.A.) {6/2025}	300.33 (N.A.) {300.33}	199.19	50
		1259	CONSTRUCTION OF BYPASS TO KHORDHA TOWN FROM KM 294/000 TO 300/300 ON NH-57 INCLUDING LA IN THE STATE (MoRTH) (N24001861)	2-2022	11/2024 (6/2025) {6/2025}	157.49 (N.A.) {157.49}	69.00	31.74
		1260	CONSTRUCTION OF BYPASS ROAD TO BALANGIR TOWN FROM KM 72/400 (DESING KM 0/0) TO KM 79/800 (DESIGN KM (MoRTH) (N24001862)	2-2022	10/2025 (11/2025) {11/2025}	238.78 (N.A.) {238.78}	39.26	18
		1261	CONSTRUCTION OF 5 HL BRIDGES AT KM 379/000 (PANGAM), KM 439/400 (POTTERU), KM 444/237 (KONGURUKONDA) (MoRTH) (N24001863)	3-2021	6/2024 (10/2025) {6/2025}	154.05 (N.A.) {154.05}	47.47	25
		1262	CONSTRUCTION OF FOUR LANE ROB AND ITS APPROACHES IN LIEU OF EXISTING LEVEL CROSSING NO. RV-71 AT KM (MoRTH) (N24001864)	11-2021	6/2025 (N.A.) {6/2025}	154.49 (N.A.) {154.49}	59.92	30
		1263	CONSTRUCTION OF 4 LANE ROB WITH APPROACHES IN LIEU OF LC NO. RV-172 AT KM 176.00 OF NH-201 (PRESENT (MoRTH) (N24001865)	12-2021	5/2025 (8/2025) {8/2025}	324.09 (N.A.) {324.09}	102.30	35
		1264	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM. (NHAI) (N24002078)	12-2023	12/2025 (N.A.) {12/2025}	711.00 (N.A.) {711.00}	111.90	42

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1265	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002079)	12-2023	12/2025 (N.A.) {12/2025}	742.25 (N.A.) {742.25}	186.57	40
		1266	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002080)	12-2023	12/2025 (N.A.) {12/2025}	762.75 (N.A.) {762.75}	152.76	50.15
		1267	3L MAJOR BRIDGE OVER RIVER BRAHMANI AT KM. 401.250 (DUBURI CHANDIKHOLE SECTION) OF NH 200 (NEW NH 5 (NHAI) (N24002081)	8-2022	1/2025 (N.A.) {12/2026}	153.61 (N.A.) {153.61}	14.22	21.5
		1268	WIDENING AND STRENGTHENLNG TO 2L+PS FROM KM 0.000 TO 40.000 (DHAUGAON- PODAMARI SECTION) OF NH 326 I (MoRTH) (N24002135)	3-2022	2/2026 (N.A.) {2/2026}	186.52 (N.A.) {186.52}	41.44	30
		1269	WIDENING AND STRENGTHENING TO 4L+PS/2L+PS FROM KM 0.000 TO 35.800 (KUAKHIA - MANGALPUR SECTION) OF N (MoRTH) (N24002136)	3-2022	2/2026 (N.A.) {2/2026}	636.10 (N.A.) {636.10}	256.60	22.73
		1270	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE ? PARADIP SECTION OF NH-53 (OLD NH (NHAI) (N24002219)	3-2024	10/2026 (N.A.) {10/2026}	882.45 (N.A.) {882.45}	1.70	6
	STEEL	1271	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY (SAIL) (N12000122)	11-2020	5/2023 (3/2025) {3/2025}	377.18 (N.A.) {377.18}	434.90	95.29

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1272	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP (SAIL) (N12000125)	1-2022	5/2025 (N.A.) {7/2025}	970.18 (N.A.) {970.18}	630.53	85.94
PUNJAB	DEPARTMENT OF HIGHER EDUCATION	1273	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. (CPWD EDUCATION) (N28000142)	10-2019	5/2022 (N.A.) {7/2025}	348.24 (N.A.) {348.24}	284.45	90.2
	PETROLEUM	1274	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB (HPCL) (N16000402)	5-2020	2/2023 (9/2024) {12/2025}	1,421.46 (N.A.) {1,421.46}	1,135.14	95.55
		1275	BHATINDA SANGRUR PIPELINE (HPCL) (N16000440)	11-2021	5/2024 (2/2025) {6/2025}	367.00 (397.00) {397.00}	315.52	88.4
		1276	CGD PROJECT AT PATHANKOT DISTRICT (IOCL) (N16000488)	3-2022	3/2030 (9/2033) {9/2033}	151.00 (N.A.) {151.00}	8.41	2
	RAILWAYS	1277	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI (NR) (N22000502)	6-2009	8/2016 (N.A.) {8/2025}	404.00 (N.A.) {404.00}	190.00	100
		1278	LUDHIANA MULLANPUR DOUBLING (NR) (N22000589)	9-2020	3/2025 (N.A.) {3/2025}	82.99 (N.A.) {235.00}	2.50	98
		1279	FEROZPUR - PATTI (25.72 KM) (NR) (N22000614)	4-2017	3/2027 (N.A.) {3/2027}	299.74 (N.A.) {781.00}	-	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	1280	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA (MoRTH) (N24000907)	3-2018	8/2020 (N.A.) {7/2024}	293.10 (N.A.) {315.00}	306.60	100
		1281	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 (MoRTH) (N24000909)	10-2017	10/2019 (N.A.) {12/2025}	1,069.59 (N.A.) {1,069.59}	739.08	62
		1282	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 (MoRTH) (N24000910)	3-2018	11/2020 (N.A.) {6/2024}	170.57 (192.48) {150.00}	104.98	79
		1283	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES (MoRTH) (N24000941)	3-2018	8/2020 (N.A.) {8/2020}	293.64 (N.A.) {293.64}	295.46	100
		1284	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO (NHAI) (N24001415)	12-2020	4/2024 (7/2024) {7/2024}	881.00 (N.A.) {881.00}	882.83	89.33
		1285	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH- 11) NEAR BHOGI WAL VI (NHAI) (N24001416)	12-2020	1/2024 (3/2025) {3/2025}	989.66 (N.A.) {989.66}	324.77	31.08
		1286	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO (NHAI) (N24001417)	12-2020	4/2024 (9/2025) {9/2025}	1,234.40 (N.A.) {1,234.40}	792.35	57.84

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1287	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO (NHAI) (N24001418)	12-2020	4/2024 (9/2025) {9/2025}	1,094.46 (N.A.) {1,094.46}	802.93	61.96
		1288	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- (NHAI) (N24001419)	2-2021	4/2024 (11/2024) {11/2024}	1,269.96 (N.A.) {1,269.96}	585.86	43.45
		1289	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR- MEHTA-SRIHARGOBINDPUR- (NHAI) (N24001420)	2-2021	4/2024 (12/2025) {12/2025}	853.66 (N.A.) {853.66}	132.99	15.33
		1290	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA (NHAI) (N24001630)	7-2021	2/2025 (N.A.) {2/2025}	1,501.02 (N.A.) {1,501.02}	357.00	70
		1291	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD (NHAI) (N24001631)	3-2021	10/2024 (N.A.) {10/2024}	1,525.31 (N.A.) {1,525.31}	348.00	82
		1292	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM (NHAI) (N24001632)	1-2021	5/2024 (6/2025) {6/2025}	1,741.86 (2,281.02) {2,281.02}	1,278.00	94
		1293	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA ? RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR (NHAI) (N24001636)	5-2021	12/2024 (10/2026) {10/2026}	1,368.91 (1,368.91) {1,368.91}	163.58	15.31

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1294	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K (NHAI) (N24001637)	3-2021	1/2025 (N.A.) {1/2025}	1,754.84 (N.A.) {1,754.84}	1,082.62	33.49
		1295	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6 (NHAI) (N24001638)	11-2021	7/2024 (5/2025) {5/2025}	646.42 (646.42) {646.42}	481.67	95
		1296	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE (NHAI) (N24001639)	5-2020	12/2024 (8/2025) {8/2025}	864.23 (864.23) {864.23}	434.88	55
		1297	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N (NHAI) (N24001640)	3-2021	11/2024 (N.A.) {11/2024}	1,229.38 (N.A.) {1,229.38}	729.77	40.99
		1298	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR (NHAI) (N24001641)	3-2021	10/2024 (12/2025) {12/2025}	1,641.75 (N.A.) {1,641.75}	187.88	25.5
		1299	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI (NHAI) (N24001642)	2-2021	8/2024 (12/2025) {12/2025}	1,474.77 (N.A.) {1,474.77}	441.47	73
		1300	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I (NHAI) (N24001643)	12-2020	6/2024 (6/2025) {6/2025}	857.91 (N.A.) {857.91}	127.71	38.71

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1301	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV (NHAI) (N24001644)	12-2020	9/2023 (9/2025) {9/2025}	524.88 (416.58) {416.58}	157.14	71.5
		1302	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION OF NH-354 SECTION ARIFKES- FEROZEPUR-MUKTS (MoRTH) (N24001960)	3-2021	10/2023 (N.A.) {4/2025}	263.19 (N.A.) {220.00}	94.08	42
		1303	WORK OF WIDENING/UPGRADATION OF 2-LANE WITH PAVED SHOULDER OF SRI MUKTSAR SAHIB TO MALOUT ROAD FROM (MoRTH) (N24001961)	3-2022	10/2023 (N.A.) {4/2025}	152.58 (N.A.) {152.58}	81.25	69
		1304	6L OF JODHPUR ROMANA (BATHINDA) - MANDI DABWALI (PUNJAB HARYANA BORDER) SECTION OF NH-54 FROM KM. 0. (NHAI) (N24002075)	12-2020	8/2025 (8/2025) {8/2025}	757.13 (757.00) {757.00}	246.51	95
		1305	6L AMRITSAR-BATHINDA GREENFIELD SECTION FROM JN. WITH BHAGTA BHAI KA-BHADAUR ROAD NEAR DYALPURA BHAI (NHAI) (N24002076)	3-2021	10/2025 (6/2026) {6/2026}	2,029.17 (2,029.00) {2,029.00}	84.23	41
		1306	6L ACCESS CONTROLLED LUDHIANA- BATHINDA GREENFIELD HIGHWAY FROM JN. WITH AMRITSAR- BATHANDA GREENFIELD (NHAI) (N24002091)	6-2021	9/2025 (4/2026) {4/2026}	906.51 (906.51) {906.51}	221.31	46.5
		1307	6-LANE AMRITSAR-BATHINDA GREENFIELD SECTION OF NH-754A FROM JUNCTION WITH MOGA JALANDHAR ROAD (NH-70 (NHAI) (N24002092)	3-2021	10/2025 (N.A.) {10/2025}	1,801.37 (N.A.) {1,801.37}	1,003.17	40.44

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1308	6L OF AMBALA-CHANDIGARH GREENFIELD SECTION FROM KM. 0.000 TO KM. 25.000 WITH 4L SPUR TO LALRU FROM K (NHAI) (N24002098)	3-2022	10/2025 (N.A.) {10/2025}	1,641.66 (N.A.) {1,641.66}	134.00	44
		1309	4L OF EXISTING BEAS ? BABA BAKALA - DERA BABA NANAK SECTION FROM START OF BATALA BYPASS TILL INTERSE (NHAI) (N24002100)	10-2021	6/2025 (N.A.) {6/2025}	1,003.38 (N.A.) {1,003.38}	265.84	67.37
		1310	4L OF BEAS-MEHTA-BATALA-DERA BABA NANAK FROM INTERSECTION WITH JALANDHAR-AMRITSAR HIGHWAY (NH-3) NEA (NHAI) (N24002101)	8-2021	6/2025 (12/2025) {12/2025}	809.51 (N.A.) {809.51}	199.79	47.2
		1311	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I SPUR-I) FROM JN. WITH KAPURTHALA - SULTANPUR LODHI ROAD (NH (NHAI) (N24002102)	1-2020	4/2026 (N.A.) {4/2027}	2,165.23 (N.A.) {2,165.23}	158.94	18.4
RAJASTHAN	CIVIL AVIATION	1312	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT (AAI) (N04000101)	5-2022	11/2024 (10/2025) {10/2025}	480.00 (N.A.) {480.00}	217.20	59
		1313	UDAIPUR AIRPORT- CONSTRUCTION OF NEW INTEGRATED PASSENGER TERMINAL BUILDING (AAI) (N04000104)	6-2023	3/2026 (N.A.) {3/2026}	887.00 (N.A.) {887.00}	285.97	55.9
	COAL	1314	NLCIL 300 MW SOLAR POWER PROJECT (PART OF 510 MW CPSU SCHEME) (NLC) (N06000269)	3-2023	9/2024 (N.A.) {9/2025}	1,813.00 (N.A.) {1,813.00}	579.82	63
	PETROLEUM	1315	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE (IOCL) (N16000435)	12-2021	10/2024 (12/2025) {12/2025}	9,028.00 (N.A.) {9,028.00}	6,543.60	77.53

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1316	CGD PROJECT AT JHUNJHUNU, SIKAR AND NAGAU DISTRICTS (IOCL) (N16000489)	3-2022	3/2030 (N.A.) {3/2031}	575.00 (N.A.) {575.00}	124.37	99
		1317	CGD PROJECT IN TONK, SAWAI MADHOPUR, DAUSA, KARALI (HPCL) (N16000496)	3-2022	3/2030 (N.A.) {3/2030}	1,751.00 (N.A.) {1,751.00}	281.34	23.7
		1318	SETTING UP OF PETROCHEMICAL EVACUATION MARKETING TERMINAL (PEMT) AT BARMER (HPCL) (N16000512)	12-2023	12/2026 (N.A.) {12/2026}	461.05 (N.A.) {461.05}	67.46	37.5
		1319	RAJASTHAN REFINERY PROJECT (HPCLRRL(JV)) (N16000513)	10-2017	10/2022 (3/2025) {6/2025}	43,129.00 (72,937.00) {72,937.00}	55,741.80	85.8
		1320	CGD PROJECTS AT FAZILKA (EXCEPT AREA ALREADY AUTHORIZED) GANGANAGAR AND HANUMANGARH DISTRICTS (BPCL) (N16000520)	12-2022	6/2030 (N.A.) {6/2030}	3,207.00 (N.A.) {3,207.00}	287.71	19.7
	POWER	1321	SAMBHU KI BHURJ-II SOLAR 300MW (NTPC) (N18000286)	3-2020	9/2021 (N.A.) {3/2025}	1,782.00 (12.00) {1,782.00}	1,369.88	95
		1322	ANTA SOLAR 90 MW (NTPC) (N18000292)	1-2021	3/2022 (N.A.) {3/2022}	382.22 (N.A.) {382.22}	497.17	100
		1323	BHENSARA 320 MW (NTPC) (N18000293)	1-2021	7/2022 (N.A.) {3/2025}	1,221.73 (1,521.00) {1,221.73}	1,128.14	0
		1324	CHHATTARGARH 150 MW (NTPC) (N18000294)	2-2021	7/2022 (N.A.) {3/2024}	599.99 (N.A.) {599.99}	599.99	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1325	NOKH PLOT-1 SOLAR PV PROJECT 245MW (NTPC) (N18000320)	3-2022	8/2023 (N.A.) {6/2025}	1,352.71 (N.A.) {1,352.71}	1,022.36	45
		1326	NOKH PLOT-2 SOLAR PV PROJECT 245MW (NTPC) (N18000321)	3-2022	8/2023 (N.A.) {3/2025}	1,409.52 (N.A.) {1,409.52}	1,377.89	95
		1327	NOKH PLOT-3 SOLAR PV PROJECT 245MW (NTPC) (N18000322)	3-2022	8/2023 (N.A.) {5/2025}	1,426.94 (N.A.) {1,426.94}	1,166.29	80
		1328	BHADLA-II 500MW SOLAR PV PROJECT (NTPC) (N18000347)	6-2022	3/2024 (N.A.) {9/2025}	2,598.92 (N.A.) {2,598.92}	1,705.70	12
		1329	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART (PGCIL) (N18000356)	3-2023	9/2024 (N.A.) {5/2025}	1,433.28 (N.A.) {1,433.28}	850.47	89
		1330	300 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000368)	5-2022	11/2023 (N.A.) {8/2025}	1,677.12 (N.A.) {1,677.12}	1,023.13	84
		1331	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PHASE-IV PART-I (BIKANER COMPLEX) PAR (PGCIL) (N18000372)	6-2023	1/2025 (2/2025) {2/2025}	202.39 (N.A.) {202.39}	20.04	100
		1332	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III, PART E1 (PGCIL) (N18000373)	8-2023	2/2025 (N.A.) {4/2025}	688.74 (N.A.) {688.74}	330.00	89

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1333	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART H (PGCIL) (N18000374)	10-2023	4/2025 (N.A.) {5/2025}	2,211.00 (N.A.) {2,211.00}	1,023.63	53
		1334	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART C1 (PGCIL) (N18000375)	10-2023	4/2025 (10/2025) {10/2025}	1,796.00 (N.A.) {1,796.00}	873.48	60
		1335	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART B1 (PGCIL) (N18000376)	9-2023	4/2025 (N.A.) {6/2025}	2,191.00 (N.A.) {2,191.00}	980.26	64
		1336	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART J (PGCIL) (N18000378)	12-2022	3/2025 (4/2026) {4/2026}	331.00 (N.A.) {331.00}	8.66	26
		1337	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART E2 (PGCIL) (N18000379)	11-2023	6/2025 (N.A.) {6/2025}	428.00 (N.A.) {428.00}	-	20
		1338	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART- 1) [BIKANER COMPLEX] PART A [BIKANER III N (PGCIL) (N18000386)	12-2023	12/2025 (N.A.) {12/2025}	2,998.00 (N.A.) {2,998.00}	527.98	39
		1339	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART- 1) [BIKANER COMPLEX] PART D [NEEMRANA II B (PGCIL) (N18000387)	12-2023	12/2025 (N.A.) {12/2025}	2,056.00 (N.A.) {2,056.00}	660.00	43

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1340	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PH-III PART D [SIKAR KHETRI TRANSMISSION] (PGCIL) (N18000389)	2-2024	8/2025 (N.A.) {8/2025}	2,000.00 (N.A.) {2,000.00}	683.00	47
		1341	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) PART-B (JAISALMER/BARMER COMPLEX) (PGCIL) (N18000391)	8-2024	8/2026 (N.A.) {8/2026}	3,279.00 (N.A.) {3,279.00}	61.00	7
		1342	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-C (PGCIL) (N18000393)	8-2024	8/2026 (N.A.) {8/2026}	2,227.00 (N.A.) {2,227.00}	72.00	10
		1343	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-E (PGCIL) (N18000394)	8-2024	8/2026 (N.A.) {8/2026}	3,251.00 (N.A.) {3,251.00}	139.00	9
		1344	ADDITIONAL TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM BHADLA-III PS AS PART OF RAJASTHAN REZ P (PGCIL) (N18000396)	8-2024	2/2026 (N.A.) {2/2026}	369.00 (N.A.) {369.00}	-	1
		1345	TRANSMISSION SYSTEM STRENGTHENING FOR INTERCONNECTIONS OF BHADLA-III AND BIKANER III COMPLEX [SPV NA] (PGCIL) (N18000397)	8-2024	8/2026 (N.A.) {8/2026}	1,382.00 (N.A.) {1,382.00}	-	1
		1346	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BAR] (PGCIL) (N18000401)	11-2024	11/2026 (N.A.) {11/2026}	2,735.00 (N.A.) {2,735.00}	-	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1347	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6GW)] [BIKANER COMPLEX (PGCIL) (N18000403)	11-2024	11/2026 (N.A.) {11/2026}	5,969.00 (N.A.) {5,969.00}	-	0
		1348	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6 GW)] [BIKANER COMPLE (PGCIL) (N18000404)	11-2024	11/2026 (N.A.) {11/2026}	5,357.00 (N.A.) {5,357.00}	-	0
	RAILWAYS	1349	AGRA FORT-BANDIKUI (NCR) (N22000553)	6-2022	6/2027 (5/2026) {5/2026}	1,389.81 (N.A.) {987.83}	42.46	12
		1350	GUDHA THATHANA MITHRI TEST TRACK FOR RDSO (NWR) (N22000593)	4-2019	3/2025 (N.A.) {6/2025}	528.48 (N.A.) {500.85}	348.05	75
		1351	DEDICATED TEST TRACK FOR RDSO (PHASE II) (NWR) (N22000594)	11-2021	11/2026 (N.A.) {12/2025}	466.42 (N.A.) {466.22}	702.41	76
		1352	DOUBLING BETWEEN CHURU- RATANGARH (42.81 KM) (NWR) (N22000605)	2-2023	2/2028 (N.A.) {6/2025}	422.60 (N.A.) {422.60}	179.69	72
		1353	SAWAIMADHOPUR - BYPASS LINE (6.98 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NWR) (N22000607)	12-2022	6/2026 (N.A.) {1/2026}	304.00 (239.54) {239.54}	99.82	25
		1354	GC OF NATHDWARA - DEVGARH MADARIYA (82.5KM) (NWR) (N22000608)	1-2023	6/2028 (N.A.) {12/2026}	968.92 (N.A.) {968.92}	359.08	37

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	1355	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT- RAMGARH BHADASAR-JA (NHAI) (N24000795)	2-2018	4/2021 (4/2025) {4/2025}	741.86 (649.00) {649.00}	672.53	97.32
		1356	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER- NAGOUR SECTION BY EXECUTING BALANCE WORK FRO (MoRTH) (N24001241)	3-2020	10/2022 (12/2024) {12/2024}	255.23 (N.A.) {255.23}	256.00	97
		1357	4L+PS OF NH -58 FROM BEAWAR- GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. (MoRTH) (N24001411)	12-2020	10/2023 (N.A.) {12/2025}	379.23 (N.A.) {379.23}	243.62	96.1
		1358	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR (MoRTH) (N24001527)	12-2021	5/2024 (6/2025) {6/2025}	411.40 (N.A.) {411.40}	198.61	69
		1359	WIDENING OF PACHPADRA-BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH-25 ON EPC MODE IN THE (MoRTH) (N24001528)	1-2022	12/2024 (6/2025) {6/2025}	194.88 (N.A.) {194.88}	104.69	75.46
		1360	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH- 68) IN THE STATE OF RAJASTHAN ON EPC M (MoRTH) (N24001529)	12-2021	8/2024 (5/2025) {5/2025}	451.66 (N.A.) {451.66}	401.78	99
		1361	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN-LALSOT- KAROLI-DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH (MoRTH) (N24001530)	12-2021	9/2024 (N.A.) {7/2025}	150.11 (N.A.) {150.11}	69.83	75

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1362	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR (NHAI) (N24001557)	3-2022	11/2024 (4/2025) {4/2025}	1,636.15 (N.A.) {1,636.15}	725.85	91.22
		1363	4L OF KARWAR (KM. 281.980 OF NH-62 NAGPUR ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II) (NHAI) (N24001558)	11-2021	8/2024 (4/2025) {4/2025}	736.75 (N.A.) {736.75}	246.49	93.25
		1364	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE - 0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK (NHAI) (N24001559)	9-2021	6/2024 (4/2025) {4/2025}	672.35 (N.A.) {672.35}	392.56	99.5
		1365	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-8) (NHAI) (N24001561)	10-2019	10/2023 (1/2025) {1/2025}	839.63 (N.A.) {839.63}	839.63	100
		1366	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6) (NHAI) (N24001563)	10-2019	8/2023 (4/2025) {4/2025}	846.59 (N.A.) {846.59}	161.34	98
		1367	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-7) (NHAI) (N24001564)	10-2019	7/2023 (4/2025) {4/2025}	662.08 (N.A.) {662.08}	123.90	96.5
		1368	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-11) (CH. 319.400 TO CH. 331.030) [HARDEOGANJ VILL (NHAI) (N24001566)	11-2019	5/2023 (1/2025) {1/2025}	1,640.10 (N.A.) {1,640.10}	1,248.59	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1369	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA (NHAI) (N24001567)	11-2019	10/2022 (6/2025) {6/2025}	1,272.97 (N.A.) {1,272.97}	627.42	85.5
		1370	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N (NHAI) (N24001568)	11-2019	5/2023 (4/2025) {4/2025}	1,119.35 (N.A.) {1,119.35}	1,447.42	99.8
		1371	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON (NHAI) (N24001569)	11-2019	3/2023 (5/2024) {5/2024}	1,425.02 (N.A.) {1,425.02}	1,420.03	100
		1372	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-13) (CH. 359.170 TO CH. 388.420) [JUNCTION WITH S (NHAI) (N24001571)	11-2019	12/2023 (1/2025) {1/2025}	1,341.36 (N.A.) {1,341.36}	1,089.73	99.65
		1373	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M (NHAI) (N24001573)	11-2019	12/2022 (4/2025) {4/2025}	1,658.06 (N.A.) {1,658.06}	180.53	99.9
		1374	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH (NHAI) (N24001612)	7-2020	1/2024 (12/2025) {12/2025}	1,788.69 (N.A.) {1,788.69}	927.35	73.93
		1375	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FOR FATEHPUR BYPASS, MANDAWA BYPASS AND JHUNJHUNU BYPAS (MoRTH) (N24001866)	3-2022	8/2024 (N.A.) {6/2025}	186.29 (N.A.) {186.29}	142.69	78

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1376	UPGRADATION OF TWO LANE PAVED SHOULDER FROM SHAHPURA TO THANAGAZI OF NH-248A ON EPC MODE IN THE STAT (MoRTH) (N24001867)	3-2022	7/2024 (N.A.) {6/2025}	174.34 (N.A.) {174.34}	104.08	80
		1377	Sagwara Bypass and Garhi- Partapur Bypass of NH-927A in the State of Rajasthan. (MoRTH) (N24001868)	3-2022	8/2025 (N.A.) {6/2025}	187.65 (N.A.) {187.65}	106.57	81
		1378	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF GHAGARIYA-MUNABAO SECTION FROM KM (MoRTH) (N24001869)	12-2022	8/2025 (N.A.) {8/2025}	235.15 (N.A.) {235.15}	152.69	94
		1379	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FROM CHARBHUJA AT DESIGN KM 0.00 (EXISTING KM 150.00) TO (MoRTH) (N24001927)	2-2022	9/2025 (N.A.) {9/2025}	838.43 (N.A.) {838.43}	345.87	83
		1380	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER NORTHERN BYPASS PHASE-II OF KOTA CITY FROM DESIGN CHAINAG (MoRTH) (N24001928)	3-2022	4/2025 (N.A.) {12/2025}	317.74 (N.A.) {317.74}	136.23	11
		1381	ADDITIONAL STRUCTURES ON 6LGURGAON-JAIPUR SECTION OF NH-48 BETWEEN KM 42.700 TO KM 273.00 (NHAI) (N24002058)	8-2022	6/2024 (6/2025) {6/2025}	409.64 (N.A.) {409.64}	226.16	77.1
		1382	UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF HANUMANGARH TO KENCHIYAN OF NH 54 ON EPC MODE IN THE ST (MoRTH) (N24002167)	3-2024	10/2026 (N.A.) {10/2026}	334.64 (N.A.) {334.64}	73.00	20

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1383	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM NEECHLI ODEN (NATHDWARA) AT DESIGN KM 88.800 TO BHATE (MoRTH) (N24002168)	3-2023	10/2026 (N.A.) {10/2026}	606.61 (N.A.) {606.61}	66.00	10
SIKKIM	CIVIL AVIATION	1384	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	24.80	9.75
	DEPARTMENT OF HIGHER EDUCATION	1385	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8-2020	1/2025 (N.A.) {12/2024}	314.06 (N.A.) {303.55}	157.24	54
	POWER	1386	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	4,141.77	66.31
		1387	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,431.82	85.82
	RAILWAYS	1388	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	12/2015 (12/2027) {12/2027}	1,339.48 (11,963.43) {11,963.43}	8,437.92	73.5
	ROAD TRANSPORT AND HIGHWAYS	1389	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (5/2022) {12/2023}	375.80 (N.A.) {375.80}	288.32	96.55
		1390	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11-2017	10/2020 (8/2023) {4/2024}	290.05 (N.A.) {290.05}	218.36	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1391	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {3/2025}	402.94 (N.A.) {402.94}	247.12	76.54
		1392	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (11/2024) {3/2025}	295.97 (N.A.) {295.97}	248.39	94.74
		1393	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3-2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	0
		1394	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {4/2025}	311.00 (N.A.) {273.78}	257.86	94.79
		1395	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (8/2024) {4/2025}	345.38 (395.59) {395.59}	362.61	90.44
		1396	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (10/2023) {12/2025}	183.31 (439.56) {439.56}	355.31	51.85
		1397	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (8/2024) {12/2025}	262.84 (414.20) {414.20}	221.86	47.56

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1398	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (10/2023) {12/2025}	292.80 (N.A.) {292.80}	195.98	59.65
		1399	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (10/2024) {12/2025}	230.45 (244.91) {244.91}	206.95	81.86
		1400	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (7/2025) {7/2025}	493.42 (478.79) {478.79}	302.83	49.71
		1401	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (6/2025) {12/2025}	816.79 (786.60) {786.60}	326.82	50.11
		1402	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1-2021	9/2023 (4/2025) {12/2025}	332.20 (N.A.) {348.92}	149.38	41.04
		1403	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (4/2025) {6/2025}	410.60 (379.30) {379.30}	230.03	69.98
		1404	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (1/2026) {1/2026}	385.15 (N.A.) {385.15}	170.32	80.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1405	SPECIAL PROTECTION WORK ON REHABILITATION AND RESTORATION OF SLIDING AND SINKING ZONE FROM RANGPO TO (NHIDCL) (N24001913)	3-2017	6/2022 (N.A.) {6/2022}	165.56 (N.A.) {165.56}	-	71.74
TAMIL NADU	CIVIL AVIATION	1406	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI (AAI) (N04000074)	6-2018	2/2022 (3/2026) {3/2026}	2,467.00 (N.A.) {2,467.00}	1,580.73	70
		1407	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI (AAI) (N04000075)	8-2018	10/2021 (12/2023) {12/2023}	951.28 (1,112.49) {1,112.49}	1,112.49	100
		1408	DEVELOPMENT OF TUTICORIN AIRPORT (AAI) (N04000090)	6-2019	3/2022 (4/2025) {4/2025}	380.87 (N.A.) {451.74}	356.74	98.75
	COAL	1409	JAWAHAR KHANI OPENCAST (JK OC) MINE (SCCL) (N06000259)	12-2021	3/2025 (N.A.) {3/2025}	297.88 (N.A.) {297.88}	46.37	20
		1410	50 MW SOLAR POWER PROJECT - NEYVELI MINED OUT AREA (NLC) (N06000279)	5-2023	6/2025 (N.A.) {6/2025}	218.03 (N.A.) {218.03}	137.84	37
	FINANCE	1411	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI (CPWD FOR FINANC) (N28000109)	11-2017	11/2021 (N.A.) {11/2022}	348.77 (N.A.) {348.77}	223.39	100
	MINES	1412	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (NALCO) (N10000014)	9-2017	6/2019 (3/2024) {12/2024}	166.62 (163.17) {163.17}	135.63	65

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	1413	IRUGUR-DEVANGONTHI POL PIPELINE (BPCL) (N16000234)	11-2012	2/2017 (10/2025) {10/2025}	678.00 (1,732.00) {1,732.00}	583.76	53.6
		1414	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI (IOCL) (N16000405)	10-2020	12/2023 (1/2025) {1/2025}	1,398.00 (1,587.00) {1,587.00}	1,303.66	100
		1415	CBR 9 MMTPA PROJECT (CPCL) (N16000434)	1-2021	6/2025 (N.A.) {6/2025}	31,580.00 (31,580.00) {36,354.00}	1,320.41	10.2
		1416	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI (IOCL) (N16000438)	1-2022	7/2024 (6/2025) {6/2025}	827.00 (887.71) {887.71}	560.69	84
		1417	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI) (IOCL) (N16000455)	1-2022	7/2024 (5/2026) {5/2026}	829.00 (N.A.) {829.00}	237.37	58.1
		1418	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS (IOCL) (N16000486)	3-2022	3/2030 (N.A.) {12/2030}	501.00 (N.A.) {501.00}	100.03	5.1
		1419	CGD PROJECT AT MADURAI, THENI AND VIRUDHNAGAR DISTRICTS (IOCL) (N16000490)	3-2022	3/2030 (12/2030) {12/2030}	1,328.00 (N.A.) {1,328.00}	149.21	100
		1420	CGD PROJECT AT KANYAKUMARI, TUTICORIN, TIRUNVELI KATTABO AND TENKASI DISTRICTS (IOCL) (N16000492)	3-2022	3/2030 (N.A.) {12/2030}	1,295.00 (N.A.) {1,295.00}	145.61	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1421	CGD PROJECTS AT THE NILGIRIS AND ERODE DISTRICTS (BPCL) (N16000521)	12-2022	3/2030 (N.A.) {3/2030}	3,685.00 (N.A.) {3,685.00}	188.76	10
	RAILWAYS	1422	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP (MRTP) (N22000028)	4-2006	6/2013 (5/2025) {5/2025}	495.74 (734.01) {981.83}	632.33	98
		1423	TIDIVANAM-NAGARI (NL) (SR) (N22000085)	9-2006	(3/2028) {3/2028}	582.83 (3,631.34) {3,631.34}	833.41	14
		1424	CHENNAI BEACH-CHENNAI EGMORE (4.3 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SR) (N22000568)	3-2022	3/2026 (2/2025) {3/2025}	359.60 (274.20) {274.20}	252.48	95
		1425	MORAPPUR-DHARMAPURI (SR) (N22000618)	2-2019	3/2028 (3/2027) {3/2027}	358.95 (N.A.) {358.95}	39.07	1
		1426	KARAIKAL PERALAM(23KM)-NEW LINE PROJECT (SR) (N22000625)	1-2019	3/2026 (3/2025) {6/2025}	304.22 (N.A.) {373.42}	274.24	80
		1427	NAGAPATTINAM THIRUTURAIPUNDI (38KM)- NEW LINE PROJECT (SR) (N22000626)	7-2008	3/2026 (3/2027) {3/2027}	677.12 (N.A.) {788.05}	142.44	19
	ROAD TRANSPORT AND HIGHWAYS	1428	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS (NHA) (N24000176)	5-2010	5/2013 (N.A.) {5/2013}	374.00 (N.A.) {166.90}	374.00	88.05

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1429	FOUR LANNING OF CHOLOPURAM- THANJAVUR (NHAI) (N24000697)	8-2017	9/2020 (N.A.) {4/2025}	1,176.37 (N.A.) {1,176.37}	1,325.06	99.5
		1430	4-LANNING OF STHIYATHOPU- CHOLOPURAM (NHAI) (N24000708)	9-2017	8/2020 (4/2025) {4/2025}	1,227.87 (N.A.) {1,227.87}	1,391.60	95.2
		1431	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 (NHAI) (N24000826)	3-2018	10/2022 (4/2025) {4/2025}	505.35 (N.A.) {837.69}	376.61	99.75
		1432	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH- 45A ON (NHAI) (N24001428)	3-2018	11/2021 (12/2024) {12/2024}	998.70 (1,358.32) {1,358.32}	926.75	98.31
		1433	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER (NHAI) (N24001429)	3-2018	11/2021 (12/2024) {12/2024}	1,294.47 (1,588.40) {1,588.40}	860.60	98.68
		1434	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM (NHAI) (N24001430)	3-2018	1/2022 (12/2024) {12/2024}	2,120.40 (2,565.63) {2,565.63}	1,588.17	99.8
		1435	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN (NHAI) (N24001431)	3-2018	10/2020 (8/2025) {8/2025}	1,872.68 (2,661.51) {2,756.09}	1,299.72	60.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1436	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 (MoRTH) (N24001455)	2-2022	8/2022 (N.A.) {3/2025}	191.33 (207.97) {207.97}	197.17	100
		1437	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83) (NHAI) (N24001600)	10-2020	5/2023 (4/2025) {4/2025}	434.12 (N.A.) {434.12}	258.89	99.3
		1438	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH- 209 (NHAI) (N24001601)	1-2019	1/2023 (6/2025) {6/2025}	1,051.69 (N.A.) {1,051.69}	575.28	79.9
		1439	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001602)	1-2019	12/2022 (5/2025) {5/2025}	1,409.38 (N.A.) {1,409.38}	654.93	90.46
		1440	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001603)	1-2019	10/2022 (4/2025) {4/2025}	1,518.53 (N.A.) {1,607.54}	915.40	100
		1441	REMAINING WORK OF 2L+PS OF TRICHY - KARAIKUDI SECTION OF NH- 210, INCLUDING TRICHY BYPASS (NHAI) (N24001604)	2-2019	3/2021 (N.A.) {3/2025}	166.90 (N.A.) {166.90}	121.94	100
		1442	4-LANING OF MELUR - PILLAYARPATTI - KARAIKUDI SECTION OF NH-338, NH- 36, NH-383 (NHAI) (N24001605)	6-2018	3/2022 (N.A.) {6/2025}	1,103.86 (N.A.) {1,103.86}	461.32	76.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1443	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH- 744A (MADURAI RING ROAD) (NHAI) (N24001606)	12-2018	3/2022 (8/2025) {8/2025}	854.94 (N.A.) {854.94}	371.20	71.78
		1444	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS (NHAI) (N24001692)	1-2022	9/2024 (2/2025) {6/2025}	467.99 (N.A.) {468.00}	22.57	74.45
		1445	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 (NHAI) (N24001693)	9-2021	10/2024 (N.A.) {10/2024}	1,751.18 (N.A.) {1,757.27}	49.69	0
		1446	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM (NHAI) (N24001694)	2-2019	12/2023 (12/2024) {12/2024}	1,243.57 (N.A.) {1,243.57}	171.63	0
		1447	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG-III) FROM KM.60+100 TO KM.94+460 (NHAI) (N24001696)	2-2019	8/2023 (12/2024) {12/2024}	1,291.37 (N.A.) {1,291.37}	215.02	0
		1448	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM (NHAI) (N24001716)	7-2022	8/2023 (12/2024) {12/2024}	186.50 (242.40) {242.40}	17.15	100
		1449	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K (NHAI) (N24001717)	11-2020	8/2024 (N.A.) {3/2026}	1,155.49 (1,525.10) {1,525.10}	485.62	53.3

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1450	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2 (NHAI) (N24001718)	12-2020	7/2024 (N.A.) {7/2025}	843.48 (1,068.60) {1,068.60}	431.31	90.21
		1451	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT (NHAI) (N24001719)	2-2021	7/2024 (N.A.) {10/2025}	2,948.31 (3,605.73) {3,605.73}	808.77	73.8
		1452	BANGALORE CHENNAI EXPRESSWAY PHASE-III ? PACKAGE I (GUDIPALA TO WALAJHPET) FROM KM 156.000 TO KM 1 (NHAI) (N24001720)	10-2020	5/2024 (N.A.) {6/2025}	1,023.91 (1,438.62) {1,438.62}	635.04	81.89
		1453	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 (NHAI) (N24001721)	2-2019	5/2024 (8/2025) {3/2026}	1,008.99 (1,360.53) {1,360.53}	303.48	45.01
		1454	6L OF MADURAVOYAL TO SRIPERUMBUDUR SECTION FROM KM. 13.800 TO KM. 37.000 OF NH-4 THROUGH STATE HIGH (NHAI) (N24001722)	11-2021	2/2023 (N.A.) {12/2024}	463.44 (463.07) {463.44}	334.80	99
		1455	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091 (NHAI) (N24001723)	10-2018	2/2021 (N.A.) {5/2025}	707.90 (766.51) {766.51}	526.39	88.25
		1456	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48 (NHAI) (N24001725)	1-2019	5/2021 (N.A.) {1/2025}	819.89 (1,314.82) {922.85}	415.60	57.32

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1457	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 ? 29/250 INCLUDING LA AND SHIFTING OF NH-234 (MoRTH) (N24001828)	1-2022	11/2024 (N.A.) {3/2025}	221.03 (243.95) {243.95}	176.50	80
		1458	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH-83) INCLU (MoRTH) (N24001829)	10-2022	11/2024 (N.A.) {5/2025}	172.15 (N.A.) {172.15}	152.47	98
		1459	CONSTRUCTION OF STRR (WEST SIDE)-NH948A-BALAGONDAPALLI (TAMIL NADU) TO KARNATAKA/TAMIL NADU BORDER F (NHAI) (N24001968)	4-2022	5/2025 (N.A.) {5/2025}	1,260.74 (N.A.) {1,260.74}	487.46	44.95
		1460	4L OF THIRUMANGALAM TO VADUGAPATTI SECTION FROM KM 0.000 TO KM 36.000 OF NH-744 (NHAI) (N24002084)	3-2022	2/2025 (N.A.) {6/2025}	1,076.97 (N.A.) {1,076.97}	517.10	83.3
		1461	CONSTRUCTION OF NEW DOUBLE TIER 4 LANE ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI (NHAI) (N24002107)	3-2023	5/2026 (N.A.) {5/2026}	1,382.00 (N.A.) {1,382.00}	-	0
		1462	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002108)	3-2023	5/2026 (N.A.) {5/2026}	1,618.96 (N.A.) {1,618.96}	-	0
		1463	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002109)	3-2023	5/2026 (N.A.) {5/2026}	1,301.37 (N.A.) {1,301.37}	-	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1464	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002110)	3-2023	5/2026 (N.A.) {5/2026}	1,207.40 (N.A.) {1,207.40}	-	0
		1465	FOUR LANING OF MUGAIYUR TO MARAKKANAM SECTION OF NH-332A FROM KM 31.000 TO KM 62.000 (NHAI) (N24002111)	2-2019	12/2025 (12/2025) {12/2025}	825.94 (1,116.13) {1,116.13}	272.93	35.72
		1466	SIX LANING OF TUTICORIN PORT ROAD SECTION OF NH-7A (NEW NH- 138) FROM KM 0.000 TO KM 6.140 EFFECTIVE (NHAI) (N24002112)	3-2023	7/2024 (N.A.) {6/2025}	200.30 (N.A.) {200.30}	72.69	76.2
		1467	4L OF LEFT-OVER WORKS INCLUDING ADDITIONAL STRUCTURES FROM KERALA/TAMIL NADU BORDER TO KANYAKUMARI S (NHAI) (N24002113)	3-2023	8/2025 (N.A.) {8/2025}	1,141.78 (N.A.) {1,141.78}	369.27	37.13
		1468	4L OF VADUGAPATTI TO THERKUVENGANALLUR (RAJAPALYAM) SECTION FROM KM 36.000 TO KM 71.600 OF NH744 UND (NHAI) (N24002114)	2-2022	4/2025 (N.A.) {4/2025}	1,097.59 (N.A.) {1,317.06}	670.74	93.85
		1469	WIDENING TO 4L/4L+PS AND STRENGTHENING IN SELECTED STRETCHES FROM KM 0/8 TO 50/570 OF NH 532 INCLU (MoRTH) (N24002151)	3-2022	1/2024 (N.A.) {7/2025}	257.14 (294.70) {294.70}	228.36	80
		1470	WIDENING FROM 2L+PS TO 4L/4L+PS AND IMPROVEMENTS THE SELECTED STRETHCES FROM KM 26/5 - 81/2 INCLU (MoRTH) (N24002152)	3-2023	11/2023 (N.A.) {11/2025}	274.84 (N.A.) {274.84}	243.81	98

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1471	STRENGTHENING OF 2L+PS FROM KM 17/8 ? 18/2, CONSTRUCTION OF 2L+PS FROM KM 18/2 TO KM 20/0 AND CONSTR (MoRTH) (N24002153)	3-2023	2/2024 (N.A.) {8/2025}	169.68 (N.A.) {169.68}	95.62	62
		1472	CONSTRUCTION OF BYPASS TO MADURAI - ACHAMBATHU - VIRATIPATHU IN KM 6/850 - 10/382 OF NH 49 EXTN. (NE (MoRTH) (N24002165)	3-2022	8/2026 (N.A.) {8/2026}	238.97 (260.07) {260.07}	92.66	39
		1473	ACCESS CONTROLLED HIGHWAY OF 4 LANE WITH PAVED SHOULDERS FROM TIRUVALLUR (DESIGN CHAINAGE KM 17+56) (NHAI) (N24002216)	12-2024	12/2026 (N.A.) {12/2026}	1,376.10 (N.A.) {1,376.10}	-	4.07
TELANGANA	CIVIL AVIATION	1474	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD (AAI) (N04000086)	5-2020	5/2022 (6/2023) {6/2023}	353.61 (N.A.) {353.61}	303.22	100
	COAL	1475	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 (SCCL) (N06000161)	3-2017	3/2022 (N.A.) {3/2025}	413.84 (N.A.) {413.84}	397.54	85
		1476	GODAVARIKHANI COAL MINE (SCCL) (N06000202)	7-2019	3/2023 (N.A.) {3/2025}	438.98 (N.A.) {438.98}	171.13	70
		1477	VENKATESH KHANI COAL MINE (SCCL) (N06000204)	10-2020	3/2023 (N.A.) {3/2026}	484.51 (N.A.) {484.51}	318.12	55
		1478	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT (SCCL) (N06000210)	11-2015	3/2023 (N.A.) {3/2025}	489.62 (N.A.) {489.62}	405.54	70

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1479	RCE OF INDARAM OPENCAST PROJECT (SCCL) (N06000211)	8-2017	3/2021 (N.A.) {3/2025}	349.28 (N.A.) {424.81}	402.64	80
		1480	RCE OF KALYANIKHANI OPENCAST PROJECT (SCCL) (N06000213)	3-2016	3/2020 (N.A.) {3/2025}	384.32 (N.A.) {384.32}	251.23	75
		1481	RCE OF KAKATHIYAKHANI OC - 2 PROJECT (SCCL) (N06000214)	8-2017	3/2020 (N.A.) {3/2025}	442.42 (N.A.) {442.42}	202.61	63
		1482	GOLETI OPENCAST MINE (SCCL) (N06000258)	7-2021	3/2026 (N.A.) {3/2026}	345.60 (N.A.) {345.60}	67.07	20
	HEALTH AND FAMILY WELFARE	1483	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR (HITES) (N21000031)	12-2018	7/2024 (N.A.) {7/2025}	1,110.55 (N.A.) {1,110.55}	726.59	81.29
		1484	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD (CPWD FOR HEALTH) (N28000098)	10-2016	3/2020 (1/2025) {1/2025}	209.84 (281.05) {281.05}	253.13	98.5
	POWER	1485	TELANGANA SUPER THERMAL POWER PROJECT PHASE I (NTPC) (N18000212)	1-2016	11/2020 (N.A.) {2/2024}	10,598.98 (N.A.) {10,998.00}	10,437.71	100
	RAILWAYS	1486	MANOHARABAD-KOTHPALL NEW LINE(SCR) (SCR) (N22000032)	4-2006	3/2010 (N.A.) {3/2025}	1,160.48 (N.A.) {3,014.00}	1,490.43	0
	ROAD TRANSPORT AND HIGHWAYS	1487	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT (MoRTH) (N24000245)	1-2014	3/2016 (9/2019) {9/2019}	270.00 (N.A.) {270.00}	-	72.15

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1488	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR (MoRTH) (N24000247)	10-2014	2/2017 (N.A.) {2/2017}	295.47 (N.A.) {295.47}	224.42	98.51
		1489	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM (MoRTH) (N24000248)	3-2015	1/2017 (N.A.) {1/2017}	153.21 (N.A.) {153.21}	101.15	93.81
		1490	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON (MoRTH) (N24000980)	10-2016	2/2019 (N.A.) {2/2019}	298.32 (N.A.) {298.32}	178.47	98
		1491	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ (MoRTH) (N24000981)	10-2016	3/2019 (N.A.) {3/2019}	248.83 (N.A.) {248.83}	173.82	100
		1492	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE (MoRTH) (N24000982)	1-2017	5/2019 (N.A.) {5/2019}	244.54 (N.A.) {244.54}	176.32	99.1
		1493	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH (MoRTH) (N24000983)	1-2017	10/2019 (N.A.) {10/2019}	196.52 (N.A.) {196.52}	125.53	95.7
		1494	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI (MoRTH) (N24000984)	1-2017	12/2019 (N.A.) {12/2019}	283.00 (N.A.) {283.00}	259.15	99.3

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1495	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION (MoRTH) (N24000986)	1-2017	5/2019 (N.A.) {5/2019}	300.00 (N.A.) {300.00}	243.36	96.05
		1496	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH (MoRTH) (N24000987)	1-2018	5/2020 (N.A.) {5/2020}	283.15 (N.A.) {283.15}	283.61	92.59
		1497	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 (MoRTH) (N24000988)	1-2018	12/2019 (N.A.) {12/2019}	230.03 (N.A.) {230.03}	232.00	99.9
		1498	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 (MoRTH) (N24000989)	2-2018	6/2020 (N.A.) {6/2020}	206.13 (N.A.) {206.13}	192.73	98.36
		1499	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT (MoRTH) (N24000990)	2-2018	11/2019 (N.A.) {11/2019}	294.13 (N.A.) {294.13}	203.07	87.44
		1500	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC (MoRTH) (N24000993)	3-2018	9/2020 (N.A.) {9/2020}	322.81 (N.A.) {322.81}	325.77	98.09
		1501	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES (MoRTH) (N24000994)	3-2018	7/2020 (N.A.) {2/2026}	626.76 (N.A.) {626.76}	287.56	45.3

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1502	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR (MoRTH) (N24000996)	1-2017	10/2019 (N.A.) {10/2019}	605.08 (N.A.) {605.08}	416.50	99.84
		1503	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL ? MALLAMPALLY SECTION OF NH-365 (MoRTH) (N24000997)	3-2018	7/2019 (N.A.) {7/2019}	192.67 (N.A.) {192.67}	179.25	92
		1504	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR (MoRTH) (N24000998)	1-2019	(N.A.) {}	193.19 (N.A.) {249.72}	230.79	95
		1505	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED (GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM (NHAI) (N24001482)	8-2022	10/2024 (N.A.) {10/2024}	772.11 (N.A.) {772.11}	514.73	74.3
		1506	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM VILLAGE TO CHINTAGUEM V (NHAI) (N24001483)	2-2022	9/2024 (N.A.) {9/2024}	637.11 (N.A.) {637.11}	398.77	80.63
		1507	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUEM VILLAGE TO RECHERLA (NHAI) (N24001484)	9-2022	2/2024 (12/2024) {12/2024}	804.69 (N.A.) {804.69}	509.98	84.89
		1508	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 (NHAI) (N24001522)	1-2021	1/2024 (12/2024) {12/2024}	1,307.95 (N.A.) {1,307.95}	707.25	99.79

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1509	6 LANING OF EXISTING 4-LANE STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000, (NHAI) (N24001555)	3-2022	1/2025 (N.A.) {1/2025}	955.49 (N.A.) {955.49}	226.99	35.96
		1510	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44 (NHAI) (N24001556)	12-2021	7/2024 (N.A.) {7/2024}	521.53 (N.A.) {521.53}	240.45	48.3
		1511	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 (NHAI) (N24001625)	1-2022	1/2025 (N.A.) {7/2025}	1,227.57 (N.A.) {1,227.57}	288.58	43.66
		1512	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM (NHAI) (N24001626)	2-2022	1/2025 (N.A.) {1/2025}	972.06 (N.A.) {972.06}	408.48	60.6
		1513	WIDENING AND STRENGTHENING OF EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FRO (MoRTH) (N24002000)	3-2021	7/2024 (N.A.) {7/2024}	317.19 (N.A.) {317.19}	164.85	70
		1514	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF MEDAK - SIDDIPET SECTION FROM KM 0/0 TO KM 69/978 OF NH- (MoRTH) (N24002001)	1-2022	1/2025 (N.A.) {6/2025}	882.18 (N.A.) {882.18}	323.30	71
		1515	WIDENING AND IMPROVEMENT OF EXISTING CARRIAGE WAY TO 2 LANE WITH PAVED SHOULDERS FROM KM. 86/160 TO (MoRTH) (N24002002)	1-2022	12/2024 (N.A.) {12/2024}	423.48 (N.A.) {423.48}	227.25	71.08

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1516	REHABILITATION AND UP-GRADATION OF VALIGONDA TO THORRUR SECTION TO TWO LANE WITH PAVED SHOULDERS FRO (MoRTH) (N24002003)	1-2022	12/2024 (N.A.) {12/2024}	549.28 (N.A.) {549.28}	226.47	70
		1517	REHABILITATION AND UPGRADATION OF LB-NAGAR TO MALKAPUR SECTION TO 6-LANE MAIN CARRIAGEWAY WITH SERVI (MoRTH) (N24002004)	3-2021	7/2024 (N.A.) {6/2025}	545.11 (N.A.) {545.11}	312.61	75.92
		1518	WIDENING TO TWO LANE WITH PAVED SHOULDERS OF 'BODHAN BASAR BHAINSA ' SECTION FROM KM 38/900 TO 95/3 (MoRTH) (N24002005)	3-2022	3/2025 (N.A.) {6/2025}	644.45 (N.A.) {644.45}	347.65	92.5
		1519	ONSTRUCTION OF 4-LANE FLYOVER AT AMBERPET-X ROAD, HYDERABAD ON NH-202 IN THE STATE OF TELANGANA (MoRTH) (N24002006)	10-2017	6/2023 (N.A.) {6/2023}	186.71 (N.A.) {186.71}	186.81	91.5
		1520	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/000 TO KM 79/300 OF KALWAKURTHY - KOLLAPUR SECTI (MoRTH) (N24002007)	3-2022	7/2025 (N.A.) {7/2025}	886.69 (N.A.) {886.69}	170.81	59.29
		1521	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF SIDDIPET- ELKATHURTHY SECTION FROM KM 69/978 TO KM 133/6 (MoRTH) (N24002008)	1-2022	12/2024 (N.A.) {12/2024}	578.85 (N.A.) {578.85}	202.27	79.25
		1522	WIDENING AND STRENGTHENING TO 2/4 LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR ? CHINCHOLI SECTION FROM (MoRTH) (N24002009)	1-2022	1/2025 (N.A.) {7/2025}	703.68 (N.A.) {703.68}	315.63	61

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1523	WIDENING AND STRENGTHENING TO 4 LANE / 2-LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR-CHINCHOLI SECTION (MoRTH) (N24002010)	3-2022	3/2024 (N.A.) {10/2025}	631.49 (N.A.) {631.49}	71.81	25
		1524	IMPROVEMENT OF GEOMETRICS OF THONDUPALLY TO KOTHUR FROM KM 22.300 TO KM 34.14 OF NH-44-RCW (NHAI) (N24002082)	2-2022	9/2024 (N.A.) {1/2026}	541.58 (N.A.) {541.58}	27.77	0
		1525	FOUR LANING OF KARIMNAGAR-WARANGAL SECTION OF NH-563 FROM DESIGN CH.48.860 KM NEAR SH-1 CH.170.400 K (NHAI) (N24002083)	3-2022	7/2025 (N.A.) {7/2025}	2,146.86 (2,413.00) {2,414.46}	917.08	67.56
		1526	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM-VIJAYAWADA) (NHAI) (N24002190)	3-2023	8/2026 (N.A.) {8/2026}	983.00 (N.A.) {983.00}	-	6.25
TRIPURA	PETROLEUM	1527	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (9/2025) {9/2025}	656.00 (N.A.) {656.00}	383.51	80.12
	ROAD TRANSPORT AND HIGHWAYS	1528	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (2/2024) {12/2024}	277.50 (302.02) {302.02}	260.38	99.94
		1529	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (10/2023) {11/2024}	159.13 (171.50) {171.50}	84.33	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1530	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {3/2025}	201.99 (N.A.) {287.47}	144.07	98
		1531	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (3/2024) {12/2025}	354.79 (N.A.) {354.79}	34.08	59
		1532	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (5/2025) {5/2025}	456.88 (N.A.) {456.88}	117.39	48.94
		1533	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {9/2025}	195.95 (N.A.) {195.95}	37.10	38.44
		1534	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	18.44	6.12
		1535	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	7.56	15.6
		1536	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	46.60	21.84
		1537	KHOWAI ?TELIAMURA-AMARPUR-HARINA-SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	8.31	5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1538	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	-	0
		1539	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	63.55	18.2
		1540	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM SECTION PKG-4 (NHIDCL) (N24002228)	1-2024	12/2026 (N.A.) {12/2026}	726.90 (N.A.) {726.90}	-	0
UTTAR PRADESH	CIVIL AVIATION	1541	CCS INTERNATIONAL AIRPORT , LUCKNOW (AAI) (N04000077)	6-2018	9/2021 (10/2026) {10/2026}	1,383.00 (1,938.00) {3,291.81}	2,622.42	79.66
		1542	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 (AAI) (N04000094)	3-2021	12/2022 (4/2025) {4/2025}	242.14 (328.00) {358.00}	344.58	99.9
		1543	PRAYAGRAJ AIRPORT - CONSTRUCTION OF NEW TERMINAL BUILDING, SECOND LINK TAXI TRACK, APRON EXPANSION, (AAI) (N04000102)	5-2023	11/2024 (6/2025) {6/2025}	185.75 (274.38) {274.38}	182.90	87
		1544	AGRA: DEVELOPMENT OF NEW CIVIL ENCLAVE AT AGRA AIRPORT. (AAI) (N04000113)	6-2024	7/2026 (N.A.) {7/2026}	579.00 (N.A.) {579.00}	41.93	10.4
		1545	VARANASI: DEVELOPMENT OF LAL BAHADUR SHASTRI INTERNATIONAL AIRPORT, VARANASI. (AAI) (N04000114)	7-2024	7/2027 (N.A.) {7/2027}	2,869.65 (N.A.) {2,869.65}	209.60	9

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>COAL</u>	1546	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW (NLC) (N06000152)	7-2016	11/2021 (6/2025) {10/2025}	17,237.00 (21,780.94) {21,780.94}	19,667.77	89.6
		1547	KHADIA EXPANSION OCP (NCL) (N06000208)	6-2021	3/2025 (N.A.) {3/2027}	491.67 (N.A.) {491.67}	138.70	9.21
	<u>HOME AFFAIRS</u>	1548	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI (CPWD FOR MHA) (N45000003)	5-2019	1/2022 (3/2023) {3/2023}	199.31 (N.A.) {199.31}	86.49	85
	<u>PETROLEUM</u>	1549	60 KTA POLYPROPYLENE PROJECT (GAIL) (N16000429)	3-2019	4/2024 (4/2024) {6/2025}	910.56 (1,299.02) {1,299.02}	950.40	95
		1550	AUGMENTATION OF FACILITIES AT MATHURA BITUMEN PLANT (IOCL) (N16000505)	4-2022	4/2025 (12/2026) {12/2026}	260.12 (N.A.) {260.12}	1.03	25
		1551	GRASS-ROOT TERMINAL AT MIRZAPUR UTTAR PRADESH (IOCL) (N16000506)	9-2022	6/2026 (N.A.) {11/2026}	980.45 (N.A.) {980.45}	177.07	69.4
		1552	CITY GAS DISTRIBUTION PROJECTS AT LAKHIMPUR KHERI , SITAPUR, BAHRAICH, SHRAVASTI,BALRAMPUR, (BPCL) (N16000525)	12-2022	6/2030 (N.A.) {6/2030}	16,654.00 (N.A.) {16,654.00}	477.21	9.3
	<u>POWER</u>	1553	KHURJA SUPER THERMAL POWER PROJECT (THDCIL) (N18000272)	3-2019	9/2023 (N.A.) {6/2025}	11,089.42 (N.A.) {13,276.16}	12,211.23	95
		1554	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III (2X800 MW) (NTPC) (N18000382)	3-2024	2/2030 (N.A.) {2/2030}	17,195.31 (N.A.) {17,195.31}	1,300.60	0.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	1555	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING (RVNL) (N22000401)	4-2015	3/2022 (N.A.) {12/2024}	943.60 (N.A.) {2,018.23}	1,780.22	0
		1556	RAMNA - SINGRAULI DOUBLING (ECR) (N22000417)	8-2015	3/2020 (N.A.) {1/2025}	2,436.21 (2,880.40) {2,880.40}	3,067.25	95
		1557	KARAILA ROAD - SHAKTINAGAR DOUBLING (ECR) (N22000419)	8-2015	3/2019 (N.A.) {12/2024}	528.57 (762.97) {762.97}	807.05	100
		1558	BURHWAL - GONDA - 3RD RUNNING LINE. (NER) (N22000468)	4-2016	(N.A.) {9/2025}	602.50 (N.A.) {1,117.80}	1,092.11	48
		1559	SHAHGANJ-BHATNI-PHEPHNA- INDARA, MAU-SHAHGANJ (EXCL. MAU- INDARA) PATCH DOUBLING. (NER) (N22000470)	4-2016	12/2019 (N.A.) {5/2025}	1,177.96 (N.A.) {2,050.00}	2,042.60	80.5
		1560	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING (NCR) (N22000495)	3-2018	3/2023 (N.A.) {3/2027}	4,329.53 (N.A.) {4,329.53}	1,702.93	35
		1561	JHANSI BINA DOUBLING (NCR) (N22000496)	9-2016	3/2021 (3/2027) {3/2027}	2,001.00 (N.A.) {2,001.00}	1,699.31	85
		1562	MATHURA-JHANSI-3RD LINE (273.80 KM) (RVNL) (N22000501)	6-2016	12/2023 (N.A.) {12/2024}	3,677.76 (N.A.) {5,190.26}	5,046.07	0
		1563	SURFACE TRIANGLE LINE BETWEEN BHADURA STATION AND NEW CROSSING STN KARMA DOUBLING (ECR) (N22000525)	10-2022	10/2027 (N.A.) {10/2027}	199.96 (N.A.) {199.96}	55.09	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1564	MUGHALSARAI - ALLAHABAD - 3RD LINE (NCR) (N22000544)	8-2019	12/2026 (N.A.) {12/2026}	2,390.00 (N.A.) {2,390.00}	83.10	55
		1565	ALIGARH-HARDUAGANJ FLYOVER (22 KM) (NCR) (N22000545)	4-2020	6/2026 (N.A.) {6/2026}	1,456.89 (1,244.13) {1,456.89}	10.14	8
		1566	LALITPUR - BIRARI WITH FLYOVER AT LALITPUR (NCR) (N22000546)	3-2017	12/2024 (6/2025) {6/2025}	260.00 (356.00) {356.00}	181.47	55
		1567	ALIGARH-DAUD KHAN - 3RD LINE 6.9 KM AND CONSTRUCTION OF FLYOVER AT DAUD KHAN (NCR) (N22000562)	4-2019	12/2025 (N.A.) {12/2025}	451.99 (779.49) {779.49}	99.70	38
		1568	ALLAHABAD-BAMHRAULI - 4TH LINE (10 KM) WITH FLY-OVER AT SUBEDARGANJ (NCR) (N22000563)	4-2019	3/2026 (N.A.) {3/2026}	494.11 (N.A.) {494.11}	42.61	42
		1569	BHANDAI - FLYOVER FOR ETAWAH BOUND DOWN TRAINS (NCR) (N22000564)	4-2019	12/2025 (N.A.) {3/2026}	187.21 (N.A.) {250.17}	2.72	8
		1570	SAHJANWA - DOHRIGHAT (NER) (N22000565)	8-2019	3/2029 (N.A.) {12/2027}	371.77 (N.A.) {1,319.75}	551.74	2.5
		1571	BAHRAICH - NANPARA - NEPALGANJ (56.15 KM) (NER) (N22000566)	7-2020	12/2024 (N.A.) {6/2025}	950.00 (N.A.) {341.66}	300.63	21.5
		1572	BAHRAICH SRAVASTI BALRAMPUR (TULSIPUR) (NER) (N22000569)	10-2018	10/2030 (N.A.) {3/2028}	1,600.00 (N.A.) {4,939.78}	1,079.60	5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1573	JANGHAI PRATAPGARH AMETHI DOUBLING (NR) (N22000583)	11-2017	3/2025 (N.A.) {12/2025}	701.98 (N.A.) {1,100.00}	21.80	60
		1574	BARABANKI MALHAUR 3RD AND 4TH LINE (32.84 KM) (NR) (N22000590)	1-2019	3/2025 (N.A.) {12/2025}	323.85 (N.A.) {407.00}	5.17	56
		1575	DOUBLING BETWEEN JAUNPUR JN- ZAFFARABAD (6.28 KM) (NR) (N22000591)	3-2023	12/2026 (N.A.) {12/2026}	177.33 (N.A.) {177.33}	0.32	0
		1576	JANGHAI-PHAPHAMAU - DOUBLING WITH ELECTRIFICATION (46.79 KM) (RVNL) (N22000596)	11-2018	3/2025 (N.A.) {3/2025}	357.48 (N.A.) {409.38}	362.09	0
		1577	BHATNI - AUNRIHAR WITH ELECTRIFICATION (125 KM) (EXCL INDARA - MAU (116.95 KM)) (RVNL) (N22000598)	5-2018	3/2024 (N.A.) {2/2025}	1,177.96 (N.A.) {2,529.46}	1,636.33	0
		1578	MATHURA - VRINDAVAN (11 KM) (NCR) (N22000612)	8-2022	6/2025 (N.A.) {6/2025}	402.88 (N.A.) {402.88}	-	0
		1579	DOMINGARH - GORAKHPUR - GORAKHPUR CANTT - KUSUMHI - 3RD RUNNING LINE (21.15 KM) (NER) (N22000613)	11-2016	6/2024 (N.A.) {7/2025}	186.85 (N.A.) {500.37}	464.91	86
	ROAD TRANSPORT AND HIGHWAYS	1580	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B (MoRTH) (N24000331)	12-2019	4/2022 (N.A.) {6/2025}	282.41 (N.A.) {319.96}	274.75	88

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1581	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 (NHAI) (N24000556)	3-2016	4/2019 (4/2025) {4/2025}	899.00 (1,633.98) {1,633.98}	1,143.50	97.4
		1582	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 (NHAI) (N24000564)	3-2016	7/2020 (6/2025) {6/2025}	1,408.00 (1,659.12) {1,659.12}	1,296.98	86.39
		1583	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO (NHAI) (N24000796)	3-2018	12/2021 (12/2023) {7/2024}	1,117.84 (N.A.) {1,203.92}	1,198.22	99.76
		1584	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA (NHAI) (N24000798)	3-2018	11/2021 (N.A.) {6/2025}	2,140.93 (N.A.) {2,140.93}	2,066.87	98.9
		1585	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH ? 14 (NHAI) (N24001185)	11-2017	7/2021 (12/2024) {12/2024}	2,159.00 (2,262.00) {2,262.00}	3,110.50	100
		1586	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN (NHAI) (N24001306)	10-2020	3/2023 (N.A.) {5/2024}	724.60 (N.A.) {724.60}	569.96	95.2
		1587	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD (MoRTH) (N24001421)	7-2018	2/2024 (N.A.) {8/2025}	1,948.25 (N.A.) {1,948.25}	1,073.15	76

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1588	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT (MoRTH) (N24001423)	4-2021	9/2023 (N.A.) {3/2026}	309.48 (N.A.) {309.48}	113.14	51
		1589	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W (MoRTH) (N24001424)	3-2021	9/2023 (N.A.) {1/2025}	185.09 (269.81) {269.81}	266.35	100
		1590	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM (MoRTH) (N24001456)	4-2020	2/2024 (N.A.) {1/2025}	199.39 (212.96) {199.39}	200.01	100
		1591	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH-730C F (MoRTH) (N24001457)	4-2020	7/2024 (N.A.) {9/2025}	172.50 (169.56) {172.50}	95.76	71
		1592	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP (MoRTH) (N24001461)	4-2020	3/2024 (N.A.) {7/2025}	236.47 (N.A.) {236.47}	132.97	86
		1593	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH-92 FROM KM.30.000 TO 57.346 UNDER GNHCP (MoRTH) (N24001462)	4-2020	7/2024 (N.A.) {7/2025}	211.09 (N.A.) {211.09}	147.58	95
		1594	ALLAHGANJ TO MIRANPUR KATRA SECTION OF NH-730C FROM KM.52.770 TO 114.00 (MoRTH) (N24001463)	4-2020	7/2024 (N.A.) {2/2024}	294.84 (N.A.) {294.84}	303.27	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1595	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00 (MoRTH) (N24001464)	3-2021	8/2023 (N.A.) {4/2025}	264.86 (N.A.) {264.86}	122.82	82
		1596	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO (MoRTH) (N24001469)	11-2021	5/2024 (N.A.) {7/2025}	307.11 (N.A.) {307.11}	199.38	88
		1597	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH-730C FROM KM.0.00 TO 52.770 UNDER GNHCP (MoRTH) (N24001471)	4-2020	11/2024 (N.A.) {5/2025}	325.24 (340.16) {325.24}	278.77	95
		1598	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR) (MoRTH) (N24001479)	3-2021	5/2024 (N.A.) {6/2025}	395.62 (392.03) {395.62}	273.96	71
		1599	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH- 334A (PURKAJI-LAKSAR-HARIDWAR ROAD) TO TW (MoRTH) (N24001480)	10-2021	4/2024 (N.A.) {3/2025}	227.06 (N.A.) {227.06}	141.89	100
		1600	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO(NEAR MOHAND) OF GANESHPUR ? DEHRADUN SECTION FROM K (NHAI) (N24001523)	3-2021	10/2023 (4/2025) {4/2025}	836.24 (N.A.) {836.24}	782.55	98.85
		1601	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR ? DEHRADUN SECTION FROM (NHAI) (N24001524)	3-2021	10/2023 (4/2025) {4/2025}	990.28 (N.A.) {990.28}	997.62	98.78

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1602	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF (MoRTH) (N24001587)	3-2020	9/2024 (N.A.) {5/2025}	262.37 (343.77) {343.77}	278.90	81
		1603	4L SPUR OF SHAMLI-MUZZAFARNAGAR CONNECTING NH-709AD (PANIPAT-SHAMLI-MUZAFFARNAGAR) AND NH-58 (MEERUT) (NHAI) (N24001726)	1-2023	8/2024 (N.A.) {8/2024}	391.26 (N.A.) {391.26}	14.12	80.3
		1604	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF KHUTAR B (NHAI) (N24001727)	3-2022	2/2025 (N.A.) {2/2025}	762.62 (N.A.) {762.62}	524.54	91.25
		1605	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO (NHAI) (N24001728)	12-2021	7/2025 (N.A.) {1/2025}	1,138.81 (N.A.) {1,138.81}	440.25	99.82
		1606	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT ? SHAMLI ? MUZAFFARNAGAR) AND NH-709A (KARN) (NHAI) (N24001729)	8-2022	4/2024 (N.A.) {5/2025}	326.79 (N.A.) {329.79}	109.08	96
		1607	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) (NHAI) (N24001730)	12-2021	1/2025 (N.A.) {3/2025}	1,384.79 (N.A.) {1,384.79}	657.94	97.98
		1608	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 (NHAI) (N24001731)	12-2021	5/2025 (5/2025) {5/2025}	2,470.64 (N.A.) {2,335.00}	691.28	83.37

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1609	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS (NHAI) (N24001732)	12-2021	10/2024 (N.A.) {4/2025}	540.97 (N.A.) {540.97}	263.36	79.48
		1610	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.-MAVIKALAN) TO VILL.- LOHADDA FROM K (NHAI) (N24001733)	3-2022	8/2024 (N.A.) {5/2025}	1,602.48 (N.A.) {1,602.48}	410.69	90
		1611	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-LOHADDA TO VILL- KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. (NHAI) (N24001734)	3-2022	8/2024 (N.A.) {5/2025}	1,335.45 (N.A.) {1,335.45}	420.84	77
		1612	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KHYAWARI TO VILL- LATIFPUR AT SAHARANPUR BYPASS FROM KM (NHAI) (N24001735)	3-2022	8/2024 (N.A.) {5/2025}	1,428.19 (N.A.) {1,428.19}	486.92	83
		1613	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KARAUNDA MAHAJAN TO VILL-KHYAWARI FROM KM. 56.500 TO K (NHAI) (N24001736)	1-2022	8/2024 (N.A.) {5/2025}	1,159.96 (N.A.) {1,159.96}	510.48	98.69
		1614	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG-III (NHAI) (N24001737)	11-2021	4/2024 (N.A.) {4/2024}	923.15 (N.A.) {923.15}	455.61	98.25
		1615	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV (NHAI) (N24001738)	9-2021	10/2023 (12/2024) {12/2024}	300.79 (N.A.) {300.79}	122.56	73.22

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1616	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U (NHAI) (N24001739)	10-2019	11/2023 (12/2024) {12/2024}	1,779.83 (N.A.) {2,200.00}	1,066.00	99.8
		1617	4L OF SHAMLI BYAPSS- SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II (NHAI) (N24001744)	5-2019	11/2022 (N.A.) {5/2025}	779.17 (N.A.) {779.17}	64.10	96.45
		1618	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N (NHAI) (N24001745)	12-2021	7/2025 (7/2025) {7/2025}	1,972.10 (N.A.) {1,936.00}	431.50	58.36
		1619	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4- LANE ON EPC MODE IN THE STATE OF UTTAR (NHAI) (N24001746)	3-2021	4/2024 (6/2025) {6/2025}	364.47 (N.A.) {364.47}	202.47	89.26
		1620	4 LANING OF NAJIBABAD BYPASS OF NH-119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH- 74 (NHAI) (N24001753)	2-2022	6/2024 (4/2025) {4/2025}	570.98 (578.02) {578.02}	372.94	94.11
		1621	SPUR OF MEERUT-GARH- MUKTESHWAR SECTION(NH-709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN (NHAI) (N24001754)	1-2022	10/2024 (N.A.) {10/2024}	953.79 (N.A.) {953.79}	384.66	64.85
		1622	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH (NHAI) (N24001755)	10-2019	3/2023 (12/2024) {12/2024}	1,936.68 (N.A.) {2,458.03}	1,380.90	98.8

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1623	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR (NHAI) (N24001772)	8-2021	3/2024 (12/2024) {12/2024}	1,147.26 (N.A.) {1,147.26}	81.34	55
		1624	4L BYPASSES FOR JAGATPUR, B4ABUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA (NHAI) (N24001815)	12-2022	11/2024 (N.A.) {11/2024}	1,699.00 (1,078.00) {1,699.00}	64.39	98
		1625	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 (NHAI) (N24001826)	2-2019	2/2022 (12/2024) {12/2024}	927.77 (N.A.) {1,603.00}	1,202.77	79.45
		1626	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 (NHAI) (N24001830)	6-2020	11/2023 (12/2024) {12/2024}	2,002.79 (N.A.) {2,002.79}	1,989.85	99
		1627	4L FROM MATHURA BYPASS (START) AT EXISTING KM. 154.20 OF NH-44 TO GAJU VILLAGE AT KM 32.982 OF NH-53 (NHAI) (N24001851)	1-2022	3/2025 (N.A.) {3/2025}	1,738.20 (N.A.) {1,738.20}	742.13	65
		1628	6L OF AGRA BYPASS (NORTHERN) CONNECTING KM. 174.500 OF NH-2 (NEW NH-19) TO KM. 141.000 OF YAMUNA EXP (NHAI) (N24001852)	10-2021	2/2025 (N.A.) {2/2025}	957.62 (N.A.) {957.62}	832.80	86
		1629	CONSTRUCTION OF LEFT OUT PORTION OF AGRA INNER RING ROAD CONNECTING VILLAGE DEORI TO NH- 44 VILLAGE B (NHAI) (N24001853)	10-2021	9/2024 (3/2025) {3/2025}	772.05 (N.A.) {772.05}	593.39	67.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1630	CONSTRUCTION OF 4-LANE GREEN FIELD HIGHWAY FROM KM. 35.000 TO KM. 49.155 OF NH-731A WITH PAVED SHOUL (MoRTH) (N24001929)	1-2022	10/2025 (N.A.) {10/2025}	697.66 (N.A.) {697.66}	301.72	83
		1631	BALANCE WORKS OF 4-LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 (NEW NH NO. 09) FROM KM. 0.000 (KM 1 (NHAI) (N24001992)	8-2022	2/2024 (4/2025) {4/2025}	199.31 (199.38) {199.38}	134.71	85.1
		1632	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER HIGHWAY FROM DESIGN CH.0.000 TO CH.49.200 OF NH-731B ON (MoRTH) (N24001996)	3-2022	11/2025 (N.A.) {11/2025}	640.18 (602.76) {602.76}	468.28	76
		1633	CONSTRUCTION OF SHOHRATGARH BYPASS ON NH-730 UNDER EPC MODE IN THE STATE OF UTTAR PRADESH (MoRTH) (N24001997)	10-2022	5/2025 (N.A.) {5/2025}	189.31 (N.A.) {189.31}	56.13	20
		1634	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 90.00 TO (MoRTH) (N24002015)	11-2021	6/2025 (N.A.) {6/2025}	403.36 (328.49) {403.36}	130.44	58
		1635	CONSTRUCTION OF PRATAPGARH BYPASS (EXTENSION) CONNECTING NH-31 TO NH-330 (MoRTH) (N24002016)	10-2022	6/2025 (N.A.) {6/2025}	225.17 (N.A.) {225.17}	95.68	51
		1636	WIDENING TO FOUR LANE WITH PAVED SHOULDER FROM DESIGN KM.49.200 TO KM.89.285 OF NH-731B ON EPC MODE (MoRTH) (N24002029)	3-2022	1/2026 (N.A.) {1/2026}	917.91 (956.30) {917.91}	567.63	42

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1637	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM EXISTING KM.0.000 TO KM.55.610 (DESIGN KM. 0.000 T (MoRTH) (N24002031)	12-2021	2/2026 (N.A.) {2/2026}	840.93 (773.58) {840.93}	492.26	36
		1638	CONSTRUCTION OF 4-LANE HIGHWAY WITH PAVED SHOULDERS FROM KM 49.155 TO KM 74.700 OF NH-731A ON HYBRID (MoRTH) (N24002032)	1-2022	1/2026 (N.A.) {1/2026}	1,156.72 (N.A.) {1,156.72}	365.66	51
		1639	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM GOGWAN JALALPUR (SHAMLI DISTRICT) TO RANIPUR (NHAI) (N24002036)	4-2022	5/2025 (N.A.) {5/2025}	1,843.59 (N.A.) {1,843.59}	843.83	49
		1640	GARHMUKTESHWAR (KM. 83.200 OF NH-24) TO MEERUT (KM. 9.860 OF NH- 235) INCLUDING CONNECTOR TO NH- 119 (NHAI) (N24002073)	10-2019	10/2023 (N.A.) {6/2025}	2,068.99 (2,171.00) {2,171.00}	209.60	53.08
		1641	WIDENING OF RAEBARELI TO PRAYAGRAJ SECTION FROM KM. 82.650 TO KM. 161.450 OF NH-30 AND LINK ROAD FRO (NHAI) (N24002085)	11-2023	3/2025 (N.A.) {3/2025}	1,470.93 (N.A.) {1,470.93}	69.56	99
		1642	CONSTRUCTION OF FOUR LANE HIGHWAY FORM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002086)	10-2022	7/2025 (N.A.) {7/2025}	1,706.47 (N.A.) {1,706.47}	719.13	68.1
		1643	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002087)	10-2022	10/2025 (N.A.) {10/2025}	1,493.14 (N.A.) {1,493.14}	93.30	55

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1644	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002088)	10-2022	8/2025 (N.A.) {8/2025}	1,493.50 (N.A.) {1,493.50}	492.86	48
		1645	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER GREENFIELD SECTION OF N (NHAI) (N24002089)	10-2022	6/2025 (N.A.) {6/2025}	617.87 (N.A.) {617.88}	106.20	66
		1646	CONSTRUCTION OF FOUR-LANE ?WESTERN SIDE SPUR OF RAMPUR- RUDRAPUR SECTION CONNECTING NH-24 TO NH-87 BY (NHAI) (N24002090)	3-2021	11/2024 (4/2025) {4/2025}	646.27 (N.A.) {646.27}	69.10	37.27
		1647	IMPROVEMENT , UP-GRADATION OF NH-734 SECTION OF MORADABAD - THAKURDWARA - KASHIPUR: ?PACKAGE-I: MORA (NHAI) (N24002093)	10-2022	9/2025 (N.A.) {9/2025}	1,841.92 (N.A.) {1,841.92}	382.24	44.8
		1648	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 123.650 TO 175.080, FROM START OF SHA (NHAI) (N24002094)	9-2022	11/2025 (N.A.) {11/2025}	1,212.26 (N.A.) {1,212.26}	329.52	27
		1649	FOUR LANING OF SONAULI GORAKHPUR SECTION OF NH 29E (NEW NH 24) FROM DESIGN CH. 0.000 TO DESIGN CH. 7 (NHAI) (N24002095)	12-2021	3/2025 (N.A.) {3/2025}	2,555.50 (N.A.) {2,555.50}	951.47	52.43
		1650	CONSTRUCTION OF 4 LANE GREEN FIELD NORTHERN EAST SIDE GORAKHPUR BYPASS (26.616 KMS) STARTING FROM NH (NHAI) (N24002096)	2-2023	1/2026 (N.A.) {1/2026}	1,973.98 (N.A.) {1,973.98}	736.14	38.54

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1651	STRENGTHENING OF EXISTING 4L AYODHYA BYPASS SECTION FROM DESIGN KM.121.600 TO KM. 144.020 OF NH 28 ((NHAI) (N24002097)	2-2023	9/2025 (N.A.) {8/2025}	526.45 (N.A.) {526.45}	217.96	81.85
		1652	CONSTRUCTION OF RING ROAD AROUND KANPUR FROM KM.000 TO KM. 23.325 (CHACHENDI SACHENDI I TO MAHARAJPU (NHAI) (N24002104)	1-2023	6/2026 (N.A.) {6/2026}	1,754.00 (N.A.) {1,754.00}	304.19	28
		1653	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS (PHASE-I) FROM DESIGN KM 43+200 (AT MAHUWARI VI (NHAI) (N24002105)	8-2023	6/2026 (N.A.) {6/2026}	1,378.36 (N.A.) {739.00}	182.98	24.1
		1654	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS FROM DESIGN KM 50.860 (NABABA URF NIBI KALA UPA (NHAI) (N24002106)	8-2023	3/2025 (N.A.) {6/2025}	993.77 (N.A.) {349.48}	353.59	85.2
		1655	CONSTRUCTION OF MARIAHU BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION (KM.53.540 TO KM.59.200) (MoRTH) (N24002115)	3-2023	8/2025 (N.A.) {2/2026}	438.24 (362.39) {438.24}	202.30	30
		1656	REHABILITATION AND UPGRADATION FROM KM 51.600 TO KM 75.700 OF NH- 321G (NUHKHAS TO ETAH SECTION) TO T (MoRTH) (N24002116)	1-2022	8/2025 (N.A.) {8/2025}	343.54 (N.A.) {343.54}	66.01	34
		1657	CONSTRUCTION OF JASRA BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION FROM KM. 379.670 ON NH-76 ((MoRTH) (N24002120)	2-2023	9/2025 (N.A.) {9/2025}	274.06 (N.A.) {274.06}	122.34	83

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1658	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM. 420.00 (MoRTH) (N24002121)	1-2022	9/2025 (N.A.) {9/2025}	509.65 (N.A.) {509.65}	160.68	18
		1659	REHABILITATION AND UP-GRADATION FROM KM. 0.000 TO KM. 40.390 OF NH- 730S (MAHARAJGANJ ? NICHLOUL ? TH (MoRTH) (N24002134)	3-2023	12/2025 (N.A.) {12/2025}	809.25 (N.A.) {809.25}	243.50	25
		1660	CONSTRUCTION OF FOUR LANE HIGHWAY WITH PAVED SHOULDER FROM KM.74.700 TO KM.112.950 OF NH-731A (I/C Y (MoRTH) (N24002138)	3-2022	6/2026 (N.A.) {6/2026}	1,141.67 (N.A.) {1,141.67}	386.36	33
		1661	CONSTRUCTION OF BALRAMPUR BYPASS WITH 2L FLEXIBLE PAVEMENT CONFIGURATION FROM KM.223.000 OF NH-330 T (MoRTH) (N24002150)	12-2022	2/2026 (N.A.) {2/2026}	515.69 (N.A.) {515.69}	171.64	22
		1662	WIDENING TO 4L RIGID PAVEMENT CONFIGURATION FROM KM 90.00 TO KM 100.800 OF NH-96 (KM 42.0 TO KM 53.3 (MoRTH) (N24002199)	12-2022	11/2026 (N.A.) {11/2026}	309.63 (N.A.) {309.63}	6.78	15
		1663	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER/FOUR LANE CONFIGURATION FROM EXISTING K (MoRTH) (N24002201)	1-2022	5/2027 (N.A.) {5/2027}	974.19 (N.A.) {974.19}	557.35	0
		1664	REHABILITATION AND UPGRADATION TO FOUR LANE ROAD FROM KM 70.500 TO KM 78.600 OF NH-92 UNDER EPC MODE (MoRTH) (N24002211)	1-2022	1/2027 (N.A.) {1/2027}	296.02 (N.A.) {296.02}	27.68	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1665	WIDENING AND STRENGTHENING FROM DESIGN KM. 67.280 TO KM. 88.622 OF NH-727A (SALEMPUR- MAIRWA ROAD) TO (MoRTH) (N24002212)	3-2023	7/2026 (N.A.) {7/2026}	371.89 (N.A.) {371.89}	105.34	0
		1666	REHABILITATION and UP-GRADATION TO 2L+PS FROM KM. 0.0 TO KM. 7.80 AND KM. 35.400 TO KM. 52.345 (DESI (MoRTH) (N24002213)	3-2023	7/2026 (N.A.) {7/2026}	701.02 (N.A.) {701.02}	241.58	0
		1667	CONSTRUCTION OF AMETHI BYPASS (PART-II) AT KM.30.050 OF NH-931 UNDER EPC MODE IN THE STATE OF UTTAR (MoRTH) (N24002214)	12-2022	2/2027 (N.A.) {2/2027}	283.86 (N.A.) {283.86}	58.89	0
	URBAN DEVELOPMENT	1668	KANPUR METRO RAIL PROJECT (LMRCL) (N28000144)	5-2019	3/2024 (N.A.) {12/2026}	11,076.48 (N.A.) {11,076.48}	8,639.03	71.8
		1669	AGRA METRO RAIL PROJECT (LMRCL) (N28000145)	5-2019	3/2024 (N.A.) {12/2026}	8,379.62 (N.A.) {8,379.62}	4,852.78	52
	WATER RESOURCES	1670	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA (UPJalNigam) (N30000006)	5-2017	9/2021 (N.A.) {6/2023}	767.59 (N.A.) {767.59}	276.97	100
		1671	FARRUKHABAD I AND D AND STP WORKS HAM (UPJalNigam) (N30000008)	10-2017	3/2022 (2/2021) {11/2024}	213.62 (261.12) {261.12}	177.62	100
		1672	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS (UPJalNigam) (N30000010)	3-2018	9/2021 (N.A.) {7/2023}	967.23 (708.70) {967.23}	254.98	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1673	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH (UPJalNigam) (N30000013)	3-2019	8/2021 (N.A.) {7/2024}	271.39 (N.A.) {271.39}	182.26	100
		1674	MATHURA SEWERAGE SCHEME (UPJalNigam) (N30000019)	12-2017	12/2020 (6/2018) {6/2022}	460.45 (N.A.) {460.45}	315.30	100
		1675	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH (UPJalNigam) (N30000021)	1-2019	12/2021 (1/2020) {3/2025}	231.79 (234.03) {234.03}	141.79	96
		1676	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH (UPJalNigam) (N30000022)	1-2019	10/2021 (N.A.) {7/2023}	206.05 (N.A.) {206.05}	140.22	100
		1677	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH (UPJalNigam) (N30000024)	2-2019	6/2022 (N.A.) {12/2025}	681.78 (N.A.) {690.71}	13.34	17
		1678	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH (UPJalNigam) (N30000025)	3-2019	7/2021 (5/2020) {9/2024}	298.12 (N.A.) {240.93}	103.24	100
UTTARAKHAND	CIVIL AVIATION	1679	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN (AAI) (N040000085)	7-2018	9/2020 (9/2024) {9/2024}	456.86 (500.00) {500.00}	483.86	100
	POWER	1680	TEHRI PUMPED STORAGE PLANT(1000MW) (THDCIL) (N18000010)	7-2006	7/2010 (6/2022) {8/2025}	1,657.00 (4,825.60) {7,877.81}	7,810.35	98

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1681	TAPOVAN-VISHNUGAD HEP (4X130MW) (NTPC) (N18000014)	11-2006	3/2013 (12/2021) {4/2029}	2,978.48 (N.A.) {10,907.00}	6,696.56	72.4
		1682	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT (THDCIL) (N18000042)	8-2008	6/2013 (N.A.) {12/2026}	2,491.58 (3,860.35) {6,630.60}	4,609.65	69.8
		1683	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW (NTPC) (N18000142)	7-2012	8/2017 (N.A.) {8/2017}	1,527.00 (N.A.) {1,527.00}	149.93	0
	<u>RAILWAYS</u>	1684	RISHIKESH - KARNAPRAYAG NEW LINE (RVNL) (N22000406)	4-2011	12/2024 (N.A.) {3/2025}	16,216.00 (N.A.) {24,659.00}	18,820.04	0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1685	4-LANING OF KASHIPUR-SITARGANJ SECTION (AMR) (N24000465)	11-2012	8/2016 (N.A.) {8/2016}	605.84 (N.A.) {605.84}	-	0
		1686	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 (NHA) (N24000559)	3-2016	10/2019 (4/2025) {4/2025}	720.00 (1,150.00) {1,150.00}	672.33	97.22
		1687	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 (NHIDCL) (N24000741)	3-2018	11/2020 (3/2024) {3/2024}	274.31 (N.A.) {274.31}	251.61	97
		1688	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI (NHIDCL) (N24000742)	3-2018	11/2020 (3/2024) {3/2024}	403.36 (N.A.) {403.36}	337.72	99

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1689	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA (NHIDCL) (N24000743)	3-2018	11/2020 (3/2024) {3/2024}	417.24 (N.A.) {417.24}	344.20	100
		1690	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000772)	12-2017	12/2019 (N.A.) {12/2019}	257.34 (N.A.) {257.34}	232.69	100
		1691	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000773)	12-2017	12/2019 (N.A.) {12/2019}	200.34 (253.43) {200.34}	227.98	100
		1692	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 (MoRTH) (N24000774)	12-2017	12/2019 (N.A.) {12/2019}	248.22 (N.A.) {248.22}	236.80	100
		1693	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000775)	6-2017	6/2019 (3/2023) {3/2023}	282.08 (N.A.) {282.08}	234.97	100
		1694	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG (MoRTH) (N24000776)	11-2017	11/2019 (N.A.) {11/2019}	232.81 (N.A.) {232.81}	201.58	100
		1695	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION (MoRTH) (N24000777)	11-2017	11/2019 (N.A.) {11/2019}	283.51 (N.A.) {283.51}	278.51	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1696	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000778)	11-2017	11/2019 (N.A.) {11/2019}	266.52 (N.A.) {266.52}	250.34	100
		1697	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR (MoRTH) (N24000779)	2-2018	2/2020 (3/2023) {3/2023}	418.88 (N.A.) {418.88}	339.71	94
		1698	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K (MoRTH) (N24000780)	2-2018	(4/2023) {4/2023}	293.68 (N.A.) {293.68}	244.25	100
		1699	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN (MoRTH) (N24000781)	5-2018	5/2020 (12/2023) {12/2023}	248.00 (N.A.) {248.00}	120.50	65.56
		1700	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 (MoRTH) (N24000782)	3-2018	(N.A.) {}	460.73 (N.A.) {461.00}	-	0
		1701	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) (NHIDCL) (N24000855)	3-2018	7/2022 (5/2024) {1/2026}	1,383.78 (N.A.) {1,383.78}	687.14	63
		1702	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER (MoRTH) (N24001130)	8-2016	12/2017 (N.A.) {12/2017}	234.88 (273.49) {234.88}	237.19	100

Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1703	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR ? DEHRADUN SECTION FROM KM. (NHAI) (N24001525)	3-2021	3/2024 (4/2025) {4/2025}	169.08 (N.A.) {169.08}	95.77	99.99
		1704	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF (NHAI) (N24001526)	8-2021	10/2024 (8/2025) {8/2025}	1,377.79 (1,384.11) {1,377.79}	679.10	47.31
		1705	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH- 07(PKG-2) (NHAI) (N24001553)	3-2022	2/2025 (6/2025) {6/2025}	1,092.90 (1,092.90) {1,092.90}	463.92	81.2
		1706	4L POANTA SAHEB?MEDNIPUR FROM KM. 435.65 TO KM. 458.65 OF NH- 07(PKG-1) (NHAI) (N24001990)	6-2022	5/2025 (5/2025) {5/2025}	524.54 (683.26) {683.26}	76.94	73.37
		1707	ACCESS ROAD/BRIDGE CONNECTIVITY FROM NH-09 AT KM.40 NEAR JAGBUDA BRIDGE (INDIA) TO BOUNDARY PILLAR (NHAI) (N24001991)	5-2022	9/2024 (3/2026) {3/2026}	314.31 (N.A.) {314.31}	173.10	66.57
		1708	CONSTRUCTION FOR MITIGATION MEASURES KM 368.00-UTTARAKHAND- TO KM 433.00 ON NH-07-PKG-1 (NHIDCL) (N24002163)	12-2023	12/2025 (N.A.) {12/2025}	216.88 (N.A.) {216.88}	15.09	45
		1709	CONSTRUCTION FOR MITIGATION MEASURES KM 450.00-UTTARAKHAND- TO KM 468.00 ON NH-07-PKG-3 (NHIDCL) (N24002164)	12-2023	12/2025 (N.A.) {12/2025}	250.33 (N.A.) {250.33}	18.41	43
		1710	CONSTRUCTION FOR MITIGATION MEASURES PKG-2 (NHIDCL) (N24002206)	12-2023	6/2026 (N.A.) {6/2026}	259.64 (N.A.) {259.64}	-	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>WATER RESOURCES</u>	1711	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH (UKJalNigam) (N30000004)	3-2017	11/2019 (N.A.) {2/2022}	158.00 (N.A.) {158.00}	107.86	100
<u>WEST BENGAL</u>	<u>CIVIL AVIATION</u>	1712	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA (AAI) (N04000080)	1-2016	3/2020 (12/2023) {12/2023}	458.00 (N.A.) {458.00}	251.64	100
		1713	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA (AAI) (N04000081)	1-2019	11/2021 (5/2023) {5/2023}	389.71 (N.A.) {397.00}	396.61	100
		1714	NSCBI AIRPORT KOLKATA: RE- CONSTRUCTION OF RIGID POSITIONS OF SECONDARY RUNWAY, 'K' AND 'A' TAXIWAY (AAI) (N04000109)	4-2023	10/2025 (N.A.) {10/2025}	328.30 (N.A.) {328.30}	79.39	36
		1715	BAGDOGRA AIRPORT: DEVELOPMENT OF NEW CIVIL ENCLAVE AT BAGDOGRA AIRPORT. SUB-HEAD : CONSTRUCTION OF N (AAI) (N04000115)	8-2024	3/2027 (N.A.) {3/2027}	1,549.00 (N.A.) {1,549.00}	153.11	8
	<u>COAL</u>	1716	RANIGANJ MASTER PLAN (ECL) (N06000163)	8-2009	8/2019 (N.A.) {8/2019}	2,661.73 (N.A.) {5,146.48}	777.27	42
		1717	SIDULI MINE (OC AND UG) (ECL) (N06000165)	5-2018	3/2027 (N.A.) {3/2027}	535.18 (N.A.) {535.17}	4.67	14
		1718	NAKRAKONDA KUMARDIH B OCP (ECL) (N06000170)	8-2018	3/2029 (N.A.) {3/2029}	502.68 (N.A.) {502.67}	69.26	25.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1719	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT (ECL) (N06000191)	4-2020	3/2026 (3/2026) {3/2026}	483.65 (N.A.) {483.65}	54.35	12
		1720	2.0 MTPA BHOJUDIH NLW WASHERY (BCCL) (N06000195)	12-2015	9/2020 (N.A.) {5/2025}	384.57 (341.22) {341.22}	345.54	96.6
		1721	SONEPUR BAZARI EXPANSION OC (ECL) (N06000220)	7-2021	3/2029 (N.A.) {3/2029}	5,365.88 (5,366.00) {5,365.88}	540.83	17
		1722	EXPANSION PR OF JHANJRA UG (5.00 MTY) (ECL) (N06000223)	4-2020	3/2029 (N.A.) {3/2029}	1,210.12 (N.A.) {1,210.12}	474.57	38
		1723	MOHANPUR EXPANSION OC PHASE II (ECL) (N06000236)	11-2020	3/2026 (N.A.) {3/2026}	888.99 (N.A.) {888.99}	68.85	30
		1724	BONJEMEHARI EXPANSION OCP (ECL) (N06000244)	8-2021	3/2026 (3/2026) {3/2026}	570.12 (N.A.) {570.11}	80.53	16
		1725	ITAPARA OC (ECL) (N06000272)	12-2023	3/2030 (N.A.) {3/2030}	929.10 (N.A.) {929.10}	61.09	7
		1726	UCE OF TILABONI UG (ECL) (N06000276)	1-2023	3/2029 (N.A.) {3/2029}	749.07 (N.A.) {749.07}	51.59	10
		1727	UCE OF PARASEA BELBAID REORGANISATION UG (ECL) (N06000277)	1-2023	3/2029 (3/2028) {3/2028}	389.10 (N.A.) {389.10}	130.56	16

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1728	PARASCOLE JAMBAD OCP (ECL) (N06000281)	11-2024	3/2037 (N.A.) {3/2037}	1,193.55 (N.A.) {1,193.55}	-	0
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1729	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED (CPWD EDUCATION) (N28000146)	3-2020	6/2020 (N.A.) {5/2024}	193.83 (N.A.) {193.83}	185.75	0
	<u>HOME AFFAIRS</u>	1730	NSG AT KOLKATA (CPWD FOR MHA) (N28000104)	10-2014	4/2018 (N.A.) {8/2025}	162.88 (210.83) {210.83}	193.91	92
	<u>MINES</u>	1731	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA (CPWD) (N10000015)	4-2019	4/2022 (N.A.) {8/2026}	255.37 (N.A.) {255.37}	68.66	34
	<u>PETROLEUM</u>	1732	DURGAPUR-HALDIA PIPELINE PROJECT (GAIL) (N16000275)	3-2017	12/2020 (7/2025) {12/2025}	1,740.00 (2,433.15) {2,433.15}	2,167.00	89.1
		1733	CITY GAS DISTRIBUTION IN WEST BENGAL (HPCL) (N16000392)	3-2019	3/2031 (3/2029) {3/2029}	5,830.20 (N.A.) {5,830.20}	864.03	30
		1734	HALDIA PANAGARH PIPELINE PROJECT (HPCL) (N16000478)	11-2022	11/2025 (N.A.) {11/2025}	1,010.00 (N.A.) {1,010.00}	509.19	74.78
		1735	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS (IOCL) (N16000491)	3-2022	3/2030 (N.A.) {6/2031}	609.00 (N.A.) {609.00}	59.84	2

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1736	CGD PROJECT IN WEST BENGAL 11TH ROUND (HPCL) (N16000498)	6-2022	6/2030 (N.A.) {6/2030}	2,628.00 (N.A.) {2,628.00}	219.16	21.2
		1737	CITY GAS DISTRIBUTION PROJECTS AT ALIPURDUAR AND COOCH BEHAR (BPCL) (N16000522)	12-2022	3/2030 (N.A.) {3/2030}	1,017.00 (N.A.) {1,017.00}	147.99	27.8
	POWER	1738	RAMMAM-III HEPP (3X40 MW) (NTPC) (N18000178)	9-2014	9/2019 (12/2024) {3/2029}	1,381.84 (N.A.) {1,803.00}	1,302.76	43.68
		1739	DURGAPUR PP-III (2X20 MW) - NSPCL (NTPC) (N18000277)	12-2016	11/2018 (N.A.) {3/2024}	529.68 (N.A.) {679.00}	558.39	100
	RAILWAYS	1740	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER (ER) (220100272)	4-2000	3/2019 (2/2026) {2/2026}	1,188.91 (N.A.) {2,582.49}	1,224.25	75
		1741	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA- BARASAI VIA BIMANBANDER (MTP) (KOMRCL) (N22000108)	4-2010	3/2016 (N.A.) {3/2016}	2,397.72 (N.A.) {2,397.72}	197.20	17
		1742	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) (RVNL) (N22000109)	4-2010	3/2014 (N.A.) {12/2025}	2,298.42 (N.A.) {2,733.86}	392.98	0
		1743	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) (RVNL) (N22000110)	4-2010	3/2016 (N.A.) {3/2026}	3,951.98 (N.A.) {8,964.35}	7,387.40	0

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1744	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. (RVNL) (N22000111)	4-2010	3/2016 (N.A.) {12/2026}	2,913.51 (N.A.) {4,834.54}	3,918.86	0
		1745	PURULIA TO KOTSHILA DOUBLING (39.1 KM) (SER) (N22000510)	4-2018	6/2022 (N.A.) {3/2025}	338.00 (N.A.) {393.83}	297.26	99
		1746	AZIMGANJ-MURSHIDABAD (JIYAGANJ) INCL. RLY. BRIDGE OVER RIVER BHAGIRATHI (ER) (N22000609)	10-2001	2/2024 (N.A.) {2/2024}	164.33 (N.A.) {187.05}	159.45	100
		1747	NAHATI - RANAGHAT 3RD LINE (MM OF KALINARAYANPUR - KRISHNANAGAR) (ER) (N22000624)	7-2015	3/2025 (3/2026) {3/2026}	283.54 (N.A.) {283.54}	164.95	44
		1748	EAST WEST METRO CORRIDOR KOLKATA (KOMRCL) (N22000628)	2-2009	9/2016 (N.A.) {9/2016}	4,874.58 (8,575.00) {10,442.41}	-	0
		1749	KALIPAHARI - BAKHTARNAGAR 5TH LINE (17.61 KM) (ER) (N22000630)	4-2024	6/2027 (N.A.) {6/2027}	350.46 (N.A.) {350.46}	-	0
		1750	SITARAMPUR BYE - PASS LINE (6.59 KM) (ER) (N22000631)	2-2023	3/2027 (N.A.) {3/2027}	461.64 (N.A.) {461.64}	12.44	0
	ROAD TRANSPORT AND HIGHWAYS	1751	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) (NHA) (N24000463)	12-2015	6/2018 (5/2024) {8/2023}	1,083.00 (1,414.01) {1,414.01}	1,080.05	100

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1752	SIX-LANING OF BARWA ADDA- PANAGARH (NHAI) (N24000515)	4-2014	9/2016 (N.A.) {3/2025}	1,665.00 (N.A.) {4,966.39}	4,966.39	100
		1753	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU (NHAI) (N24000788)	3-2018	9/2022 (12/2022) {12/2025}	841.57 (708.30) {708.30}	10,442.91	95.53
		1754	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H (MoRTH) (N24000874)	3-2016	11/2018 (12/2023) {7/2025}	271.17 (291.20) {291.20}	199.72	81.75
		1755	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. (MoRTH) (N24000880)	2-2018	9/2020 (1/2024) {2/2025}	426.18 (426.18) {426.18}	364.92	100
		1756	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH- 60 (PAND (MoRTH) (N24000885)	3-2016	9/2023 (N.A.) {2/2025}	160.27 (N.A.) {213.97}	174.36	100
		1757	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N (MoRTH) (N24000887)	6-2016	9/2021 (2/2024) {1/2025}	236.78 (263.26) {263.26}	232.54	100
		1758	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 (NHAI) (N24001747)	3-2020	9/2024 (N.A.) {9/2024}	2,193.23 (2,314.00) {2,314.00}	2,048.00	92.5

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1759	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA (NHAI) (N24001748)	3-2021	9/2024 (N.A.) {9/2025}	2,200.93 (N.A.) {2,621.32}	2,621.32	96.63
		1760	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE (NHAI) (N24001749)	8-2021	8/2023 (N.A.) {6/2025}	557.55 (N.A.) {567.31}	472.92	91.41
		1761	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA (NHAI) (N24001750)	8-2018	12/2021 (N.A.) {6/2025}	622.04 (N.A.) {622.04}	550.96	87.92
		1762	DEVELOPMENT TO 4/6-LANNING OF NH-31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 (MoRTH) (N24001850)	3-2022	9/2025 (9/2025) {9/2025}	995.04 (995.04) {995.04}	383.34	45
		1763	CONSTRUCTION OR 4 LANE RANIGANJ BYPASS OF LENGTH 5 261 KM ON NH 60 NEW NH 14 FROM KM 273 00 OF NH (MoRTH) (N24002184)	3-2023	3/2026 (3/2026) {3/2026}	410.83 (N.A.) {410.83}	151.50	26.45
		1764	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF LEVEL CROSSING NO 10 B T AT KM 307 050 OF NH 60 B (MoRTH) (N24002191)	3-2016	8/2025 (N.A.) {8/2025}	155.87 (N.A.) {155.87}	21.68	9.12
	STEEL	1765	REBUILDING OF COKE OVEN BATTERY NO.4 OF DURGAPUR STEEL PLANT (SAIL) (N12000132)	11-2023	12/2026 (N.A.) {12/2026}	916.78 (N.A.) {916.78}	81.77	4.82
	WATER RESOURCES	1766	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA (KMDA) (N30000032)	5-2018	2/2022 (N.A.) {3/2025}	198.43 (224.69) {286.97}	75.87	93

**Table:-7. Project List: Ongoing Projects 4th Quarter (January-March),
2024-25**

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1767	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA (KMDA) (N30000034)	8-2017	9/2022 (1/2023) {12/2026}	307.12 (N.A.) {653.67}	-	0
		1768	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH (KMDA) (N30000042)	5-2018	2/2022 (9/2020) {3/2025}	160.00 (154.73) {154.73}	87.35	89
		1769	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH (KMDA) (N30000045)	8-2017	12/2021 (2/2021) {2/2024}	185.22 (N.A.) {185.22}	49.99	100
		1770	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR (KMDA) (N30000046)	2-2014	12/2019 (N.A.) {6/2022}	274.76 (N.A.) {332.56}	278.33	100
		1771	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE (KMDA) (N30000047)	12-2014	4/2020 (N.A.) {6/2022}	272.32 (341.68) {272.32}	307.73	100
		1772	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI (KMDA) (N30000048)	1-2018	12/2021 (2/2021) {2/2024}	172.10 (N.A.) {172.10}	47.20	100
		1773	INTERCEPTION AND DIVERSION WITH STP AT BALLY (KMDA) (N30000049)	10-2017	12/2021 (2/2021) {2/2024}	164.93 (N.A.) {164.93}	45.45	100
			Total			2672909.7 (-) {3211901.18}	1778240.05	

Abbreviations used in the Report

AGENCY_NAME	AGENCY_NAME_SHORT
AIRPORT AUTHORITY OF INDIA LIMITED	AAI
ARTIFICIAL LIMBS MANUFACTURING CORPM. OF INDIA	ALIMCO
BHARAT ALUMINUM CORPORATION	BALCO
BHABHA ATOMIC RESEARCH CENTRE	BARC
BHARAT COKING COAL LIMITED	BCCL
BRAHMAPUTRA CRECKER & POLYMER LTD.	BCPL
BHAVINI LIMITED	BHAVNI
BHARAT HEAVY ELECTRICALS LIMITED	BHEL
BANGALORE METRO RAIL CORPORATION LIMITED	BMRCL
BOKARO STEEL PLANT	BOKARO STEEL PL
BRAHMAPUTRA BOARD	BPB
BHARAT PETROLEUM CORPORATION LIMITED	BPCL
BORDER ROAD ORGANISATION	BRO
BONGAIGAON REFINERY PETROLEUM LIMITED	BRPL
BHARAT SANCHAR NIGAM LIMITED	BSNL
Bihar Urban Infrastructure Development Corporation Ltd	BUIDCO
BRAHMAPUTRA VALLY FERTILISER CORPORATION	BVFC
CENTRE FOR DEVELOPMENT OF TELEMATICS, TELECOM, TECHNOLOGY	C-DOT
CENTRAL COAL FIELDS LIMITED	CCL
CONTAINER CORPORATION OF INDIA	CCOI
CHENAB VALLEY POWER CORPORATION LIMITED	CHENAB VALLEY P
CHENNAI METRO RAIL LTD	CMRL
CHENNAI PETROLEUM CORPORATION LIMITED	CPCL
CENTRAL PUBLIC WORKS DEPARTMENT	CPWD
CPWD OF HIGHER EDUCATION	CPWD EDUCATION
CPWD FOR DEFENCE	CPWD FOR DEFENC
CPWD FOR FINANCE	CPWD FOR FINANC
CPWD FOR HEALTH	CPWD FOR HEALTH
CPWD FOR MHA	CPWD FOR MHA
CPWD FOR POWER	CPWD FOR POWER
CPWD FOR RURAL	CPWD FOR RURAL
CPWD FOR TELECOM	CPWD FOR TELECO
CPWD FOR RENEWABLE ENERGY	CPWD R ENERGY
CENTRAL RAILWAYS	CR
COCHIN REFINERY LIMITED	CRL
COCHIN SHIPYARD LTD	CSL
CHENAB VELLEY POWER PROJECTS [P] LIMITED	CVPPPL
DUMMY AGENCY	DA
DEDICATED FREIGHT CORRIDOR CORPORATION OF INDIA LTD	DFCC
DIRECTORATE GENERAL OF CIVIL AVIATION	DGCA
Delhi Jal Board	DJB
Delhi Mumbai Industrial Corridor	DMIC
DMIC FOR DPIIT	DMIC FOR DPIIT
DELHI METRO RAIL CORPORATION	DMRC
DEPARTMENT OF TELECOMMUNICATION	DOT
Department for Promotion of Industry and Internal Trade	DPIIT
DAMODAR VALLEY CORPORATION	DVC
EASTERN COAL FIELDS LIMITED	ECL
EAST COAST RAILWAY	ECOR
EAST CENTRAL RAILWAYS	ECR

AGENCY_NAME	AGENCY_NAME_SHORT
EDCIL(India) Limited	EDCIL
ENNORE PORT LTD.	ENNORE PORT LTD
ENNORE TANK TERMINAL PVT.LTD.	ENNORE TANK
EASTERN RAILWAYS	ER
FERTILISER AND CHEMICAL TRIVANCORE	FACT
FREIGHT OPERATION INFORMATION SYSTEM	FOIS
SETTING UP FILM AND TELEVISION INSTITUTE	FTI
GAS AUTHORITY OF INDIA LIMITED	GAIL
GOA SHIPYARD LIMITED	GSL
HEALTH & FAMILY WELFARE	H&FW
HINDUSTAN AERONAUTICS LTD	HAL
HINDUSTAN COPPER LIMITED	HCL
HALDIA FERTILISER CORPORATION	HFC
HLL Infra Tech Services Limited	HITES
HYDERABAD METRO RAIL LTD	HMRL
HINDUSTAN PETROLEUM CORPORATION LIMITED	HPCL
HPCL Rajasthan Refinery Limited(JV)	HPCLRRL(JV)
HPOIL Gas Pvt. Ltd	HPOIL(JV)
HOSPITAL SERVICES CONSULTANCY CORPORATION LTD	HSCC
HINDUSTAN STEELWORK CONSTRUCTION LIMITED	HSCL
HINDUSTHAN STEELWORKS CONSTRUCTION LIMITED	HSCL
HSCL FOR DONER	HSCL FOR DONER
HSCL FOR RURAL	HSCL FOR RURAL
HSCL FOR WATER	HSCL FOR WATER
INDIAN FARMERS FERTILISER CORPORATION	IFFCO
INDIRA GANDHI CENTRE FOR ATOMIC RESEARCH	IGCAR
INDRADHANUSH GAS GRID LTD	IGGL
India International Convention and Expo Centre	IICC
IICC FOR DPIIT	IICC FOR DPIIT
INDIAN IRON STEEL COMPANY	IISCO
Indian Institute of Technology, Kharagpur	IITKGP
INDIAN OIL CORPORATION LIMITED	IOCL
INDIAN PETRO-CHEMICAL CORPORATION LIMITED	IPCL
Indian Railway Construction Company Limited	IRCON
INDIAN STRATEGIC PETROLEUM RESERVES LTD	ISPRL
INDIAN TELEPHONE INDUSTRY	ITI
Inland Waterways Authority of India	IWAI
INLAND WATER TRANSPORT	IWT
JAWAHAR LAL NEHRU NATIONAL URBAN RENEWAL MISSION	JNNURM
JWAAHARLAL NEHRU PORT TRUST	JNPT
Jharkhand Urban Infrastructure Development Company Ltd	JUIDCO
Kolkata Metropolitan Development Authority	KMDA
KOCHI METRO RAIL CORPORATION LTD	KMRCL
KOLKATA METRO RAIL CORPORATION LIMITED	KOMRCL
KAMARAJAR PORT LIMITED	KPL
KONKAN RAILWAY	KR
Rail Infrastructure Development Company	KRIDE
KOCHI REFINERIES LIMITED	KRL
Kochi Salem Pipeline Private Limited(JV)	KSPPL(JV)
LINE DOUBLING	LD
LUCKNOW METRO RAIL CORPORATION LIMITED	LMRCL
MANGALORE REFINERY AND PETROCHEMICALS LIMITED	MANGALORE REFIN

AGENCY_NAME	AGENCY_NAME_SHORT
MAHANADI COAL FIELDS LIMITED	MCL
MECON LIMITED	MECON LIMITED
AHMEDABAD METRO RAIL	MEGA
MADRAS FERTILISER LIMITED	MFL
Munitions India Limited	MIL
MAHARASTRA METRO RAIL CORPORATION LTD.	MMRC
MUMBAI METRO RAIL CORPORATION LTD	MMRCL
MINISTRY OF WATER RESOURCES	MOWR
Madhya Pradesh Metro Rail Co Limited	MPMRCL
Maharashtra Rail Infrastructure Development Corporation Limited	MRIDC
MANGALORE REFINARY LIMITED	MRL
METROPOLITAN RAPID TRANSPORT PROJECTS	MRTP
Mumbai Railway Vikas Corporation	MRVC
MAHANAGAR TELEPHONE NIGAM LIMITED	MTNL
MUMBAI PORT TRUST	MUMBAI PORT TRU
Armoured Vehicles Nigam Limited	MVNL
MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)	MoRTH
NATIONAL ALUMINUM COMPANY LIMITED (NALCO)	NALCO
NATRIIP IMPLEMENTATION SOCIETY	NATIS
NATIONAL BUILDING CONSTRUCTION CORPORATION LTD	NBCC
NBCC FOR COMMERCE	NBCC FOR COMMER
NBCC FOR HEALTH	NBCC FOR HEALTH
NORTHERN COAL FIELDS LIMITED	NCL
NORTH CENTRAL RAILWAY	NCR
NATIONAL CAPITAL REGION TRANSPORT CORP	NCRTC
NATIONAL CENTRE OF EXCELLENCE	NCoE
NORTH EAST ELECTRIC POWER CORPORATION	NEEPCO
NORTH EAST GAS GRID	NEGG
NORTH EASTERN RAILWAY	NER
National Film Archive of India	NFAI
NUCLEAR FUEL CORPORATION	NFC
NATIONAL FERTILISER LIMITED	NFL
NORTH EAST FRONTIER RAILWAY	NFR
NATIONAL HIGHWAYS AUTHORITY OF INDIA	NHAI
NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.	NHIDCL
NATIONAL HYDRO-ELECTRIC POWER CORPORATION	NHPC
National High Speed Rail Corporation Limited	NHSRCL
NEW LINE	NL
NEYVELI LIGNITE CORPORATION	NLC
NATIONAL MISSION FOR CLEAN GANGA	NMCG
NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)	NMDC
NAGPUR METRO RAIL CORPORATION LTD	NMRCL
NATIONAL PROJECTS CONSTRUCTION CORPORATION LIMITED	NPCC
NUCLEAR POWER CORPORATION OF INDIA LIMITED	NPCIL
NORTHERN RAILWAY	NR
NUMALIGARH REFINERY LIMITED	NRL
SETTING UP OF NEW RAILWAY ZONES	NRZ
NATIONAL THERMAL POWER CORPORATION	NTPC
NORTH WESTERN RAILWAY	NWR
OIL INDIA LIMITED	OIL
OIL & NATURAL GAS CORPORATION LIMITED	ONGC
PATNA METRO RAIL CORPORATION	PATNA METRO RAI

AGENCY_NAME	AGENCY_NAME_SHORT
PAWAN HANS HELICOPTERTERS LTD.	PAWAN HANS HELI
POWER GRID CORPORATION OF INDIA LIMITED	PGCIL
PORT TRUST	PORT TRUST
Polavaram Project Authority	PPA
RASHTRIYA CHEMICAL & FERTILISER LIMITED	RCF
RAILWAY ELECTRIFICATION	RE
RASTRIYA ISPAT NIGAM LIMITED	RINL
RAIL INDIA TECHNICAL AND ECONOMIC SERVICE	MITES
MITES OF HIGHER EDUCATION	MITES OF HIGHER
RAIL VIKAS NIGAM LTD.	RVNL
SIGNALLING & TELECOMMUNICATIONS	S&T
STEEL AUTHORITY OF INDIA LIMITED (SAIL)	SAIL
SINGARENI COLLIERS COMPANY LIMITED	SCCL
SOUTH CENTRAL RAILWAY	SCR
SOUTH-EASTERN COAL FIELDS LIMITED	SECL
SOUTH EAST CENTRAL RAILWAY	SECR
SOUTH EASTERN RAILWAY	SER
SER(GC) GAUGE CONVERSION	SER(GC
SHIPPING CRP. OF INDIA	SHIPP.
SATLUJ JAL VIDYUT NIGAM LIMITED	SJVN
SOUTHERN RAILWAY	SR
SOUTH WESTERN RAILWAY	SWR
Sikkim University	Sikkim Universi
THDC INDIA LIMITED	THDCIL
TUTICORIN PORT TRUST	TUTICORIN
URANIUM CORPORATION OF INDIA LIMITED	UCIL
URBAN DEVELOPMENT	UD
Uttarakhand Pey Jal Nigam	UKJalNigam
Uttar Pradesh Jal Nigam	UPJalNigam
VISAKHAPATNAM PORT TRUST	VPT
Varanasi Smart City	Varanasi Smart
WAPCOS	WAPCOS
WESTERN COAL FIELDS LIMITED	WCL
WEST CENTRAL RAILWAY	WCR
WESTERN RAILWAY	WR
WORKSHOPS & PRODUCTION UNIT	WS&PU



Government of India
Ministry of Statistics and Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
