



OCMS

Ministry of Statistics & Programme Implementation

Government of India
Ministry of Statistics and Programme Implementation



476th —

Flash Report on Central Sector Infrastructure Projects —

(Rs. 150 crore
& above)

June 2025




CONTENTS

Synopsis	1-2
List of Tables	3-225
Table:-1. Overview of Ongoing Projects: Sector-wise Distribution.....	3-4
Table:-2. Overview of Ongoing Projects: State-wise Distribution.....	5-6
Table:-3. Project List: Completed during June 2025.....	7-11
Table:-4. Project List: Added during June 2025.....	12-12
Table:-5. Project List: Frozen/Deleted during June 2025.....	13-13
Table:-6. Project List: Ongoing Projects of North-East Region.....	14-36
Table:-7. Project List: Ongoing Projects as of 30 th June 2025.....	37-225

SYNOPSIS

Flash Report - Central Sector Infrastructure Projects Costing Rs. 150 crore & above

Total Ongoing Projects (1595, ₹26,85,568.07 crore)

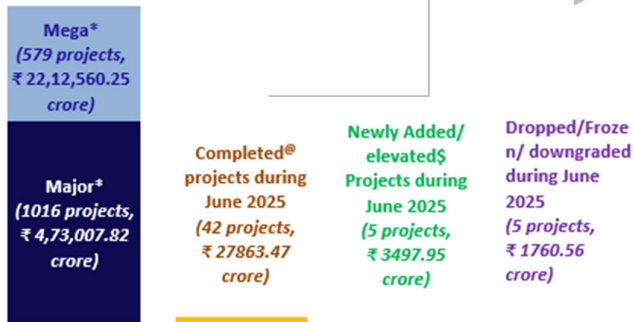








Note: @ Indicated legend is in format (Project Count, Cumulative Expenditure) other Indicated legends are in format (Project count, Original Cost)

* Mega Project if having original cost >= 1000 crore


* Major Project if original cost < 1000 crore

\$ reported Anticipated cost more than 150 crore

reported Anticipated cost less than 150 crore

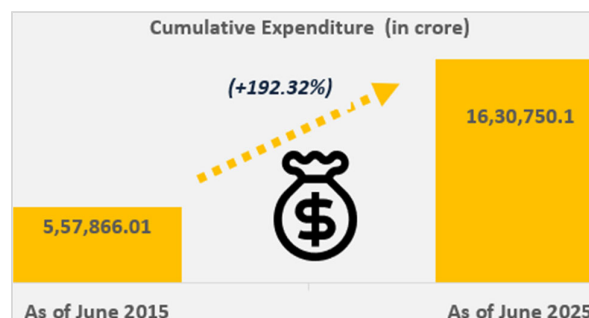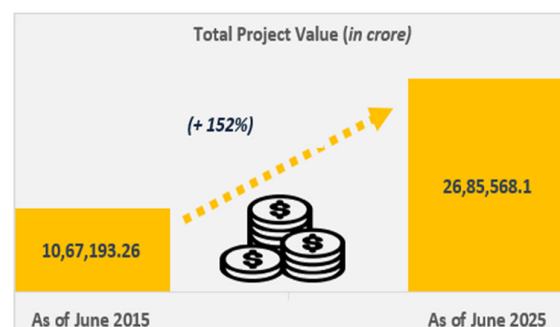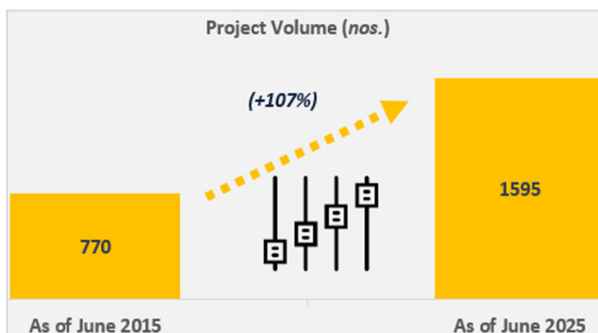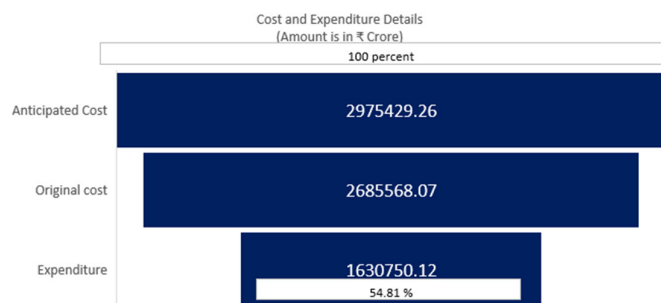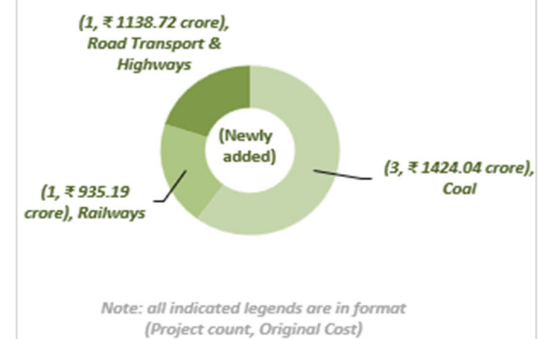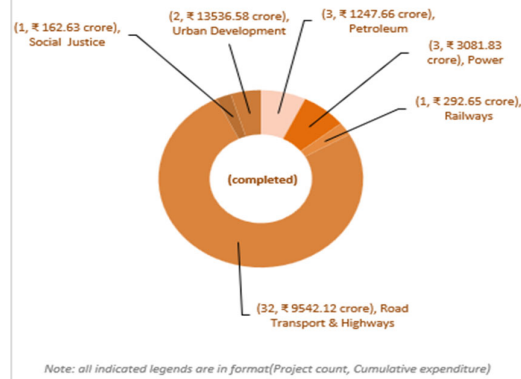


Sectoral Comparison : Major Sectors (as per count)
 [Outer Ring: Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

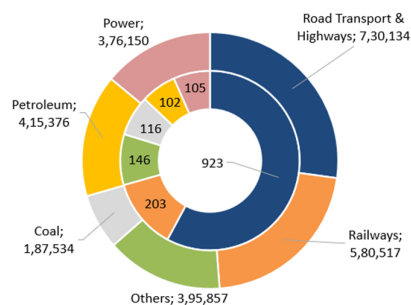


*Others include Water Resources, Civil Aviation, Urban Development, Department of Higher Education, Steel, Health & Family welfare, Mines, Telecommunications, Home Affairs, Finance, DPIIT, Shipping & Ports, and Social Justice

State Comparison : Major States (as per count)
 [Outer Ring: Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

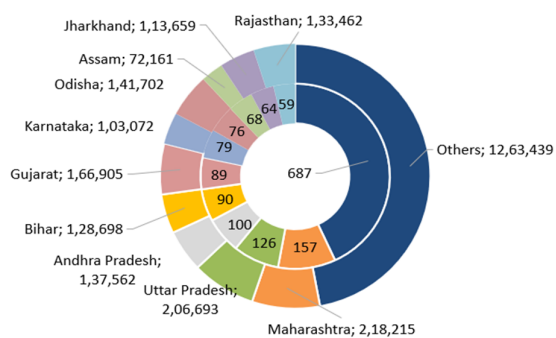

*Others include Tamilnadu, Madhya Pradesh, Delhi, Chhattisgarh, Haryana, Jammu & Kashmir, West Bengal, Kerala, Arunachal Pradesh, Punjab, Telangana, Uttarakhand, Himachal Pradesh, Manipur, Sikkim, Nagaland, Mizoram, Meghalaya, Tripura, Goa, A&N Island, Ladakh and Multistate

Sectoral Distribution of total 650 projects with reported Physical Progress between 80-100%

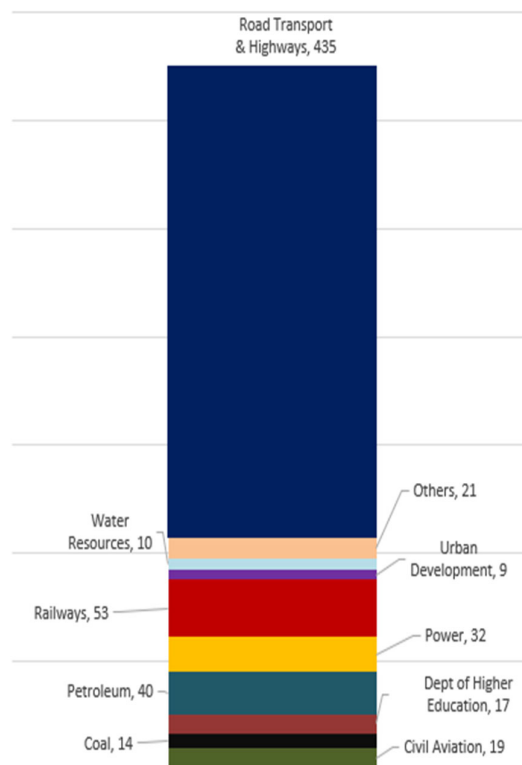

Note: This report is as of June 2025, based on the (non-exhaustive) list of projects and information as reported by Line Ministries/ implementing agencies on the OCMS (www.cspm.gov.in) portal latest by 8th July 2025.

A decorative scroll graphic with a light gray background and a dark gray border. The scroll is unrolled, with the top and bottom edges showing a dark gray inner lining. The text "LIST OF TABLES" is centered within the scroll.

LIST OF TABLES

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	CIVIL AVIATION	38	26,718.18 (27,878.25) {30,487.46}	18,038.38
2	COAL	116	187,533.87 (192,077.91) {196,907.16}	67,974.52
3	DEPARTMENT OF HIGHER EDUCATION	20	9,680.92 (10,072.78) {10,271.25}	7,214.67
4	DPIIT	2	24,857.00 (31,457.00) {32,085.00}	16,231.95
5	FINANCE	2	577.27 (577.27) {569.04}	399.67
6	HEALTH AND FAMILY WELFARE	7	7,150.98 (7,459.11) {7,194.19}	4,974.49
7	HOME AFFAIRS	3	1,663.54 (2,539.11) {2,539.11}	2,209.10
8	MINES	8	7,559.78 (9,356.73) {9,845.57}	6,076.89
9	PETROLEUM	102	415,375.80 (466,585.36) {476,738.57}	2,47,728.10
10	POWER	105	376,149.61 (399,127.37) {454,133.11}	2,30,429.15
11	RAILWAYS	203	580,517.44 (570,567.02) {600,296.37}	4,05,391.57
12	ROAD TRANSPORT AND HIGHWAYS	923	730,133.91 (757,547.67) {768,280.94}	3,87,153.65
13	SHIPPING AND PORTS	1	5,369.18 (5,061.15) {5,061.15}	3,472.54
14	STEEL	20	16,297.20 (20,228.73) {20,228.73}	8,030.85
15	TELECOMMUNICATIONS	6	26,961.69 (26,949.89) {26,949.89}	9,777.17
16	URBAN DEVELOPMENT	24	253,593.42 (258,103.77) {271,961.41}	1,88,202.04

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
17	WATER RESOURCES	15	15,428.28 (15,429.03) {61,880.31}	27,445.38
	Total	1595	2,685,568.07 (2,801,018.15) {2,975,429.26}	16,30,750.12

*Either Revised or Original Cost

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	ANDAMAN AND NICOBAR ISLANDS	9	2,555.02 (2,628.18) {2,609.04}	1,570.91
2	ANDHRA PRADESH	100	137,562.41 (138,061.74) {185,913.61}	1,03,214.40
3	ARUNACHAL PRADESH	14	45,061.06 (45,210.96) {64,937.64}	30,494.52
4	ASSAM	68	72,160.68 (72,644.55) {80,115.95}	51,124.39
5	BIHAR	90	128,697.89 (141,442.84) {153,894.78}	98,886.26
6	CHHATTISGARH	50	75,244.87 (79,134.30) {79,609.36}	36,041.06
7	DELHI	21	90,609.18 (96,063.03) {94,869.54}	76,898.76
8	GOA	3	1,201.05 (1,201.05) {1,287.55}	485.92
9	GUJARAT	89	166,904.62 (172,995.69) {173,705.16}	87,806.46
10	HARYANA	24	60,500.88 (69,284.79) {69,434.48}	35,685.89
11	HIMACHAL PRADESH	27	33,945.98 (34,975.66) {33,959.82}	18,520.60
12	JAMMU AND KASHMIR	53	73,422.59 (74,733.70) {81,014.68}	37,490.59
13	JHARKHAND	64	113,658.99 (117,419.60) {116,571.41}	67,421.35
14	KARNATAKA	79	103,071.74 (104,231.19) {103,281.26}	49,083.86
15	KERALA	29	62,476.65 (67,557.87) {68,138.39}	34,596.89
16	LADAKH	6	2,474.97 (2,634.64) {2,634.64}	1,349.63
17	MADHYA PRADESH	53	111,280.15 (110,681.55) {117,479.56}	40,730.40

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
18	MAHARASHTRA	157	218,215.39 (219,727.02) {244,735.03}	1,25,686.25
19	MANIPUR	31	25,573.90 (23,525.17) {33,485.71}	19,617.15
20	MEGHALAYA	14	6,669.20 (6,671.16) {6,679.40}	3,297.68
21	MIZORAM	16	14,026.44 (12,520.44) {18,053.36}	15,684.86
22	MULTI STATE	49	331,697.08 (337,250.07) {350,472.22}	2,53,221.50
23	NAGALAND	23	13,242.51 (14,429.85) {14,128.82}	7,970.58
24	ODISHA	76	141,702.20 (143,692.35) {146,380.41}	66,140.85
25	PUNJAB	37	37,339.85 (37,800.41) {38,239.81}	15,087.38
26	RAJASTHAN	59	133,461.98 (163,301.66) {162,895.85}	91,952.19
27	SIKKIM	18	20,007.02 (24,489.69) {25,331.78}	18,325.74
28	TAMIL NADU	58	86,711.11 (92,401.36) {97,359.99}	23,782.67
29	TELANGANA	52	29,124.48 (29,461.83) {31,449.35}	15,398.11
30	TRIPURA	14	7,910.17 (7,947.06) {8,032.54}	1,403.56
31	UTTAR PRADESH	126	206,693.32 (215,027.99) {219,300.59}	1,08,471.35
32	UTTARAKHAND	30	58,506.75 (63,252.30) {63,200.39}	45,102.40
33	WEST BENGAL	56	73,857.94 (78,618.45) {86,227.14}	48,205.96
	Total	1595	2,685,568.07 (2,801,018.15) {2,975,429.26}	16,30,750.12

***Either Revised or Original Cost**

Table:-3. Project List: Completed during June 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
PETROLEUM					
	1	CITY GAS DISTRIBUTION IN WEST BENGAL (HPCL) (N16000392) (WEST BENGAL)	5,830.20	03/2031	875.27
	2	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS (IOCL) (N16000426) (MULTI STATE)	169.00	12/2029	71.00
	3	CGD PROJECT IN TONK, SAWAI MADHOPUR, DAUSA, KARAU LI (HPCL) (N16000496) (RAJASTHAN)	1,751.00	03/2030	301.39
POWER					
	4	BHENSARA 320 MW (NTPC) (N18000293) (RAJASTHAN)	1,221.73	07/2022	1,139.42
	5	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) (NTPC) (N18000296) (GUJARAT)	674.92	09/2022	572.53
	6	SAMBHU KI BHURJ-II SOLAR 300MW (NTPC) (N18000286) (RAJASTHAN)	1,782.00	09/2021	1,369.88
RAILWAYS					
	7	KARAIKAL PERALAM(23KM)-NEW LINE PROJECT (SR) (N22000625) (TAMIL NADU)	304.22	03/2026	292.65
ROAD TRANSPORT AND HIGHWAYS					
	8	REHABILITATION AND UPGRADATION OF BHOKARDAN TO KUMBHARI FATA DESIGN CH. (KM 13+500 TO 17+00) AND RAJ (MoRTH) (N24001887) (MAHARASHTRA)	291.37	06/2024	157.59
	9	UP-GRADATION OF TIRORA-GONDIA, STATE HIGHWAY FROM EXISTING KM 163+213 (ON SH-335, TIRORA) TO KM 191+ (MoRTH) (N24001888) (MAHARASHTRA)	288.14	04/2023	72.78

Table:-3. Project List: Completed during June 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	10	2 LANE + PS PIMPLNER TO SATANA -[DESIGN CHAINAGE KM 21.427 TO 64.00] OF NH-752G] (MoRTH) (N24001889) (MAHARASHTRA)	277.81	07/2021	155.01
	11	2 LANE + PS ASTHAMODE - TIVATYAL [DESIGN CH. KM 24.300 - 62.00] [KM 134.98-172.95 OF NH-63] (MoRTH) (N24001894) (MAHARASHTRA)	228.82	07/2021	145.50
	12	REHABILITATION AND UPGRADATION TO TWO LANES WITH PAVED SHOULDER CONFIGURATION FROM WATUR TO CHARTHANA (MoRTH) (N24001895) (MAHARASHTRA)	228.01	09/2023	106.11
	13	CONSTRUCTION OF MAJOR BRIDGE ACROSS MANJRA RIVER NEAR YESGI VILLAGE @ KM, 166/500 ON NH 63 TQ BILOLI (MoRTH) (N24001905) (MAHARASHTRA)	188.69	08/2023	111.25
	14	STRENGTHING AND WIDINING OF EXISTING CARRIAGEWAY TO 10 M IN KM, 156/160 TO 229/160 (TEMBHURNI - KUSL) (MoRTH) (N24001909) (MAHARASHTRA)	157.72	06/2024	80.37
	15	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440) (MIZORAM)	492.94	05/2023	365.86
	16	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83) (NHAI) (N24001600) (TAMIL NADU)	434.12	05/2023	268.92
	17	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001603) (TAMIL NADU)	1,518.53	10/2022	915.40
	18	STRENGTHENING OF 6-LANE PIMPALGAON-NASHIK-GONDE (KM. 380 - KM. 440) SECTION OF NH-3 IN MAHARASHTRA U (NHAI) (N24002137) (MAHARASHTRA)	175.00	03/2025	201.00

Table:-3. Project List: Completed during June 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	19	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254) (SIKKIM)	242.97	06/2022	246.91
	20	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286) (NAGALAND)	278.95	06/2022	166.29
	21	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339) (MEGHALAYA)	157.86	04/2022	152.95
	22	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH (MoRTH) (N24000301) (ANDHRA PRADESH)	271.45	10/2015	240.23
	23	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM (MoRTH) (N24000332) (MAHARASHTRA)	225.81	N.A.	118.84
	24	4-LANING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) (NHAI) (N24000659) (MAHARASHTRA)	1,059.73	03/2017	928.19
	25	4-LANING OF THALSERRY -MAHE BYPASS (NHAI) (N24000704) (KERALA)	1,124.11	05/2020	1,527.28
	26	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 (NHIDCL) (N24000741) (UTTARAKHAND)	274.31	11/2020	253.61
	27	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768) (SIKKIM)	290.05	10/2020	218.36

Table:-3. Project List: Completed during June 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	28	AKOLA TO AKOT (MoRTH) (N24001003) (MAHARASHTRA)	313.95	06/2019	270.02
	29	AJANTHA TO BULDHANA (MoRTH) (N24001008) (ANDAMAN AND NICOBAR ISLANDS)	401.00	07/2019	246.39
	30	BHANDARA TO GHOTITOK (MoRTH) (N24001018) (MAHARASHTRA)	392.83	06/2019	264.35
	31	AMDHI TO SAONER (MoRTH) (N24001021) (MAHARASHTRA)	396.91	06/2019	253.59
	32	RALEGAON TO RAMTIRTH (MoRTH) (N24001046) (MAHARASHTRA)	210.81	07/2019	132.00
	33	PUNE TO MALE VILLAGE (MoRTH) (N24001078) (MAHARASHTRA)	228.31	12/2019	113.29
	34	ARDHAPUR TO HIMAYATNAGAR (MoRTH) (N24001079) (MAHARASHTRA)	426.06	06/2020	268.96
	35	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER (MoRTH) (N24001080) (MAHARASHTRA)	256.15	12/2019	115.53
	36	KOLDE TO KHETIYA (MoRTH) (N24001090) (MAHARASHTRA)	509.18	07/2019	246.83
	37	KURUDWADI TO PANDHARPUR (MoRTH) (N24001101) (MAHARASHTRA)	307.63	07/2019	208.22

Table:-3. Project List: Completed during June 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	38	PANDHARPUR TO SANGOLA (MoRTH) (N24001102) (MAHARASHTRA)	218.38	07/2019	176.99
	39	PARLI PIMPLA DAHIGUDA (MoRTH) (N24001138) (MAHARASHTRA)	205.72	06/2019	813.50
<u>SOCIAL JUSTICE</u>					
	40	CENTRE FOR DISABILITY SPORTS (CPWD) (N38000001) (MADHYA PRADESH)	170.99	03/2024	162.63
<u>URBAN DEVELOPMENT</u>					
	41	KOCHI METRO RAIL PROJECT PHASE IB SECTION FROM S N JUNCTION TO THIRUPUNITHURA (KMRCL) (N28000159) (KERALA)	355.70	09/2023	448.39
	42	PUNE METRO RAIL PROJECT (PHASE 1) (MMRC) (N28000121) (MAHARASHTRA)	11,420.00	11/2021	13,088.19
		Total	35,753.08		27,863.47

Table:-4. Project List: Added during June 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
COAL	1	WAGHODA UG (WCL) (N06000293) (MAHARASHTRA)	1-2025	379.30 (N.A.) {379.30}	3/2030 (N.A.) {3/2030}
	2	KOLARPIMPRI EXPANSION OCM (2.50 MTY) (WCL) (N06000294) (MAHARASHTRA)	2-2025	630.37 (N.A.) {630.37}	3/2030 (N.A.) {3/2030}
	3	JARANGDIH OCP (CCL) (N06000295) (JHARKHAND)	2-2020	414.37 (N.A.) {414.37}	3/2029 (N.A.) {3/2029}
RAILWAYS	4	MURARAI - BARHARWA 3RD LINE (48.90 KM) (ER) (N22000632) (WEST BENGAL)	5-2025	935.19 (N.A.) {935.19}	5/2028 (N.A.) {5/2028}
ROAD TRANSPORT AND HIGHWAYS	5	CONSTRUCTION OF BASTI RING ROAD (PHASE-I) WITH 4L CONFIGURATION FOR BASTI CITY IN THE STATE OF UTTAR (MoRTH) (N24002245) (UTTAR PRADESH)	12-2022	1,138.72 (N.A.) {1,138.72}	6/2027 (N.A.) {6/2027}
Grand Total				3,497.95 (-) {3,497.95}	

Table:-5. Project List: Frozen/Deleted during June 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore	Progress (%)
ROAD TRANSPORT AND HIGHWAYS						
	1	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686) (NAGALAND)	373.07	09/2019	382.50	99.81
	2	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH- 102B (PKG- 4A) (NHIDCL) (N24001272) (MANIPUR)	167.95	06/2022	88.05	69.89
	3	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH- 102B (PKG- 4B) (NHIDCL) (N24001273) (MANIPUR)	177.76	08/2022	89.67	80.53
	4	BALANCE WORK FOR REHABILITATION AND UP- GRADATION OF SIDHI-SINGRAULI FROM KM 82.400 TO KM 187.993 SEC (MoRTH) (N24001966) (MADHYA PRADESH)	529.44	04/2023	378.40	0
URBAN DEVELOPMENT						
	5	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D (CPWD) (N28000154) (HIMACHAL PRADESH)	512.34	11/2024	-	0
		Total	1,760.56		938.62	

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ARUNACHAL PRADESH	CIVIL AVIATION	1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (Jul-2025) {7/2025}	645.63 (732.00) {732.00}	694.26	99.89
	POWER	2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	24,484.77	96.6
		3	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	3,380.24	15.81
	ROAD TRANSPORT AND HIGHWAYS	4	HUNLI TO HAYULIANG PKG-1 (NHIDCL) (N24002222)	2-2024	2/2028 (N.A.) {2/2028}	1,262.43 (N.A.) {1,262.43}	12.12	2.76
		5	HUNLI TO ITHUN BRIDGE SECTION (NHIDCL) (N24002223)	2-2024	1/2027 (N.A.) {1/2027}	275.50 (N.A.) {275.50}	7.61	7.88
		6	PANGO TO JORGING ROAD PKG-1 (NHIDCL) (N24002224)	1-2024	7/2027 (N.A.) {7/2027}	898.19 (N.A.) {898.19}	16.01	4.25
		7	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (Mar-2024) {12/2024}	180.57 (244.10) {180.57}	160.46	96.62
		8	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (Jun-2025) {12/2025}	1,718.59 (1,718.59) {1,718.59}	742.36	73.84
		9	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (May-2023) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		10	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (Apr-2025) {4/2025}	301.06 (N.A.) {301.06}	205.71	100
		11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	398.18	95.84
		12	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	194.62	44.56
		13	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (Aug-2024) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		14	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (Feb-2024) {7/2025}	184.88 (N.A.) {184.88}	99.32	97.42
ASSAM	CIVIL AVIATION	15	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (Sep-2025) {9/2025}	1,142.00 (N.A.) {2,333.00}	1,948.45	89.66
	COAL	16	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290)	7-2022	11/2030 (N.A.) {11/2030}	159.77 (N.A.) {159.77}	81.45	0
		17	TIRAP OCP (CIL) (N06000291)	11-2022	11/2027 (N.A.) {11/2027}	289.46 (N.A.) {289.46}	105.59	0
	HEALTH AND FAMILY WELFARE	18	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (Apr-2023) {6/2025}	875.00 (873.92) {860.00}	796.74	99.62

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	19	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	97.22	92
		20	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	255.51	55
		21	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	208.56	46.3
		22	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	99.52	27.3
		23	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (Jun-2025) {12/2025}	543.91 (726.93) {726.93}	491.56	93.98
		24	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	16,357.82	74.92
		25	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	9,579.31	85.1
		26	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (May-2026) {5/2026}	412.00 (595.20) {595.20}	396.15	83.4
		27	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (Sep-2026) {9/2026}	277.00 (N.A.) {277.00}	181.63	67.67

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		28	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (Jul-2025) {10/2025}	860.00 (N.A.) {860.00}	535.46	97.5
		29	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (Jun-2025) {12/2025}	430.76 (N.A.) {430.76}	320.71	83.94
		30	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	101.15	34.6
		31	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (Jul-2027) {7/2027}	156.36 (156.36) {156.36}	44.33	35.4
		32	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (Jul-2027) {7/2027}	384.04 (N.A.) {384.04}	97.54	44
	RAILWAYS	33	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2026 (N.A.) {3/2027}	4,059.65 (N.A.) {4,962.40}	3,668.09	92.31
	ROAD TRANSPORT AND HIGHWAYS	34	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.78	100
		35	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG- 7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	159.30	82.9
		36	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (1,019.17) {925.47}	192.50	30.65

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		37	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,464.49	62.82
		38	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (May-2025) {12/2025}	261.13 (N.A.) {261.13}	70.08	57.5
		39	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (Apr-2025) {12/2025}	217.50 (N.A.) {217.50}	89.21	68.03
		40	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (Jun-2025) {8/2025}	216.49 (241.52) {216.49}	114.38	87.02
		41	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	217.31	97.76
		42	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {7/2025}	437.39 (N.A.) {437.39}	586.89	97.43
		43	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	517.62	78.19
		44	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH- 52 (NHIDCL) (N24000431)	1-1991	6/2019 (Jun-2019) {7/2025}	520.01 (N.A.) {520.01}	306.13	98.42
		45	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (Jul-2021) {12/2025}	289.99 (N.A.) {289.99}	233.23	88.03

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		46	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {7/2025}	294.17 (N.A.) {294.17}	396.49	98.4
		47	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {7/2025}	252.00 (N.A.) {330.30}	242.97	95.42
		48	SILCHAR- CHURAI BARI PKG-5 (NHIDCL) (N24002243)	2-2024	10/2027 (N.A.) {10/2027}	1,258.13 (N.A.) {1,258.13}	0.00	0
		49	BILASIPURA- GUWAHATI ROAD PKG-1 (NHIDCL) (N24002225)	2-2024	8/2027 (N.A.) {8/2027}	1,081.15 (N.A.) {1,081.15}	33.93	2.76
		50	SILCHAR-JIRIBAM PKG-1 (NHIDCL) (N24002226)	1-2024	1/2028 (N.A.) {1/2028}	957.95 (N.A.) {957.95}	0.00	21.98
		51	BILASIPURA- GUWAHATI ROAD PKG-2 (NHIDCL) (N24002229)	11-2023	6/2027 (N.A.) {6/2027}	1,338.61 (N.A.) {1,338.61}	0.50	0
		52	BADARPUR ? CHURAI BARI PKG-6 (NHIDCL) (N24002230)	3-2024	3/2027 (N.A.) {3/2027}	870.00 (N.A.) {870.00}	0.00	5.86
		53	KARIMGANI - SUTARKANDI SECTION ON SILCHAR-CHURAI BARI PKG-7 (NHIDCL) (N24002231)	2-2024	2/2027 (N.A.) {2/2027}	791.79 (N.A.) {791.79}	0.00	1.02
		54	CONSTRUCTION OF 4 LANE GAURIPUR BYPASS ON NH-17 IN THE STATE OF ASSAM (MoRTH) (N24002237)	3-2024	10/2026 (N.A.) {10/2026}	421.15 (N.A.) {421.15}	0.00	0

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		55	CONSTRUCTION OF 2 LANE BARPETA BYPASS FROM KM 77+900(BARADI) TO KM 86+150(DEURIKUCHI) (LENGTH=8.25K (MoRTH) (N24002238)	3-2023	8/2026 (N.A.) {8/2026}	173.65 (N.A.) {173.65}	0.00	0
		56	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	551.88	47.5
		57	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	308.11	29.01
		58	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	425.17	27.99
		59	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	242.92	75.51
		60	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	134.02	18.15
		61	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.87	100
		62	SILCHAR VAIRENGTE SAIRANG ROAD PKG- 1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	539.19	40.36
		63	SILCHAR VAIRENGTE SAIRANG ROAD PKG- 2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	989.94	64.56

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		64	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	297.70	54.97
		65	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	407.11	68.95
		66	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	290.90	43.16
		67	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	213.67	50.88
		68	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	344.27	67.85
		69	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {5/2025}	625.64 (N.A.) {625.64}	556.44	100
		70	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {7/2025}	204.10 (N.A.) {204.10}	143.66	96.8
		71	FOUR LANING OF SRIRAMPUR-DHUBRI PKG- 2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {6/2025}	909.02 (N.A.) {909.02}	532.44	100
		72	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (Sep-2024) {6/2024}	175.00 (N.A.) {175.00}	209.02	100

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		73	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	683.00	78.92
		74	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {5/2025}	457.72 (N.A.) {457.72}	366.34	100
		75	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	110.76	35.77
		76	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {11/2025}	458.59 (N.A.) {458.59}	205.87	66.12
		77	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {3/2026}	535.03 (N.A.) {535.03}	102.23	34.54
		78	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	409.15	68.26
		79	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	417.17	68.6
		80	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	467.83	65.56

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MANIPUR		81	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	323.24	98.48
		82	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	303.89	99.06
	CIVIL AVIATION	83	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (Dec-2025) {12/2025}	499.00 (N.A.) {499.00}	154.47	40.82
	RAILWAYS	84	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	12/2026 (Mar-2028) {3/2028}	14,322.79 (12,274.06) {22,234.60}	15,485.02	69.2
	ROAD TRANSPORT AND HIGHWAYS	85	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (Aug-2025) {8/2025}	315.56 (N.A.) {315.56}	137.81	88.74
		86	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (Jan-2026) {3/2026}	410.68 (N.A.) {410.68}	152.34	70.11
		87	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (Sep-2025) {12/2025}	504.76 (N.A.) {504.76}	190.26	78.25
		88	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (Feb-2025) {3/2025}	152.11 (N.A.) {152.11}	73.48	100
		89	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (Oct-2024) {2/2025}	467.41 (N.A.) {467.41}	264.83	100

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		90	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (Mar-2025) {7/2025}	310.76 (N.A.) {310.76}	129.15	96.77
		91	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (Jul-2025) {12/2025}	579.63 (N.A.) {579.63}	180.72	72.5
		92	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (Jan-2025) {1/2026}	477.86 (N.A.) {477.86}	246.09	84.87
		93	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (Nov-2024) {12/2025}	311.18 (N.A.) {311.18}	190.96	83.78
		94	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (Mar-2026) {3/2026}	578.98 (N.A.) {578.98}	153.92	71.25
		95	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (Dec-2025) {3/2026}	760.16 (N.A.) {760.16}	157.48	62.92
		96	CHOITHAR TO MARREM KHULLEN SECTION IMPHAL- UKHRUL - JESSAMI PKG-5 (NHIDCL) (N24002242)	3-2023	3/2027 (N.A.) {3/2027}	564.05 (N.A.) {564.05}	0.00	0
		97	IMPHAL-KOHIMA ROAD PKG-5A (NHIDCL) (N24002232)	9-2020	8/2026 (N.A.) {8/2026}	228.97 (N.A.) {228.97}	0.00	10.13
		98	JESSAMI TO LAYNEN BRIDGE UKHRUL - JESSAMI PKG-7 (NHIDCL) (N24002227)	3-2023	6/2026 (N.A.) {6/2026}	164.89 (N.A.) {164.89}	3.83	9.78

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		99	MARREM KHULLEN TO JESSAMI SECTION IMPHAL- UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	17.79	15
		100	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	13.14	18.04
		101	IMPHAL - KHONGSANG - JIRIBAM PKG-2 (NHIDCL) (N24002244)	3-2021	3/2026 (N.A.) {3/2026}	195.14 (N.A.) {195.14}	4.42	11.53
		102	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (Jun-2025) {9/2025}	292.24 (N.A.) {292.24}	130.66	90.69
		103	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (Jun-2025) {10/2025}	365.53 (N.A.) {365.53}	156.31	77.69
		104	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (Jun-2025) {12/2025}	379.39 (N.A.) {379.39}	218.03	70.94
		105	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (Mar-2025) {12/2025}	226.32 (N.A.) {226.32}	105.78	74.48
		106	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (Jan-2025) {9/2025}	188.36 (N.A.) {188.36}	126.71	99.02
		107	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (Sep-2024) {11/2025}	234.08 (N.A.) {234.08}	139.45	92.82

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		108	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (May-2025) {10/2025}	211.70 (N.A.) {211.70}	83.79	71.06
		109	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (Mar-2025) {10/2025}	467.00 (N.A.) {467.00}	193.81	79.81
		110	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (Jan-2025) {1/2025}	185.80 (N.A.) {185.80}	117.78	100
		111	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (Jan-2025) {12/2025}	483.87 (N.A.) {483.87}	278.89	92.94
		112	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (Feb-2025) {3/2025}	198.77 (N.A.) {198.77}	127.86	100
		113	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (Mar-2025) {12/2025}	673.27 (N.A.) {673.27}	382.37	80.28
MEGHALAYA	DEPARTMENT OF HIGHER EDUCATION	114	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (Jul-2025) {7/2025}	484.32 (429.70) {494.52}	270.55	84
	ROAD TRANSPORT AND HIGHWAYS	115	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	214.34	30.3
		116	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	107.86	24

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		117	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM ((NHIDCL) (N24001313)	11-2020	12/2023 (Oct-2025) {10/2025}	351.12 (N.A.) {351.12}	299.22	63
		118	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	434.50	32
		119	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (Jun-2025) {6/2025}	553.51 (610.09) {553.51}	438.16	88.07
		120	DAINADUBI-DARUGIRI PKG-1B (NHIDCL) (N24002233)	3-2023	3/2027 (N.A.) {3/2027}	705.83 (N.A.) {705.83}	0.32	2.13
		121	IMPROVEMENT AND WIDENING TWO LANNIG WITH PAVED SHOULDER OF NATIONAL HIGHWAY 127B FROM KM 31.500 (GOE (MoRTH) (N24002239)	12-2023	5/2027 (N.A.) {5/2027}	504.00 (N.A.) {504.00}	0.00	0
		122	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	222.26	30
		123	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	293.36	25.52
		124	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	297.91	25.27

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		125	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (May-2026) {5/2026}	359.86 (N.A.) {359.86}	233.26	60.81
		126	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (N.A.) {7/2025}	302.88 (N.A.) {302.88}	228.68	96
		127	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11-2021	6/2024 (Dec-2024) {5/2025}	283.50 (N.A.) {283.50}	257.26	100
MIZORAM	RAILWAYS	128	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2025 (N.A.) {6/2025}	6,527.45 (5,021.45) {8,071.30}	8,066.76	97
	ROAD TRANSPORT AND HIGHWAYS	129	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWL RANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {12/2025}	523.78 (N.A.) {523.78}	379.40	95.31
		130	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	279.44	75.4
		131	ZORINPUI- HMAWNGBU-LONGMASU (NH-502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	33.77	3
		132	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (N.A.) {4/2025}	519.09 (N.A.) {785.65}	670.91	97.51
		133	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (N.A.) {5/2024}	640.07 (N.A.) {1,286.35}	1,195.84	98.9

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		134	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (N.A.) {4/2025}	473.18 (N.A.) {688.25}	541.04	95
		135	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (N.A.) {4/2025}	537.82 (N.A.) {789.05}	779.37	99.88
		136	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (N.A.) {5/2025}	518.53 (N.A.) {906.76}	849.68	97.9
		137	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (N.A.) {5/2025}	404.29 (N.A.) {750.32}	666.58	100
		138	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (N.A.) {5/2025}	428.11 (N.A.) {746.39}	613.69	99.82
		139	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (N.A.) {6/2024}	206.88 (N.A.) {219.33}	265.38	100
		140	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (N.A.) {10/2024}	292.24 (N.A.) {331.17}	294.78	94.4
		141	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (Apr-2024) {4/2024}	233.25 (N.A.) {233.25}	172.09	100

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
NAGALAND		142	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (N.A.) {3/2026}	698.44 (N.A.) {698.45}	502.24	63.7
		143	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (N.A.) {3/2026}	740.58 (N.A.) {740.58}	373.89	61
	PETROLEUM	144	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	6.62	19
	RAILWAYS	145	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2026 (N.A.) {12/2029}	6,663.20 (6,663.20) {6,663.20}	4,942.71	74
	ROAD TRANSPORT AND HIGHWAYS	146	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7-2021	3/2023 (Sep-2025) {9/2025}	258.52 (N.A.) {258.52}	89.46	81.4
		147	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	119.20	65.06
		148	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (Nov-2025) {11/2025}	330.80 (N.A.) {330.80}	171.89	92.44
		149	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (Nov-2026) {11/2026}	232.29 (350.88) {232.29}	79.69	17.31
		150	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (Sep-2024) {6/2026}	277.44 (N.A.) {277.44}	169.46	67.91

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		151	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)]	8-2020	10/2022 (Jun-2025) {12/2025}	159.85 (342.29) {159.85}	108.15	33.55
		152	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)]	8-2020	4/2022 (Apr-2023) {8/2025}	202.36 (N.A.) {202.36}	75.39	32.67
		153	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)]	3-2016	8/2022 (Sep-2025) {9/2025}	429.52 (794.74) {794.74}	321.40	92.46
		154	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)]	2-2017	9/2020 (Feb-2023) {4/2025}	387.00 (688.12) {688.12}	392.01	100
		155	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)]	3-2018	11/2022 (Aug-2024) {4/2025}	500.09 (698.81) {698.81}	393.53	100
		156	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)]	3-2018	12/2021 (Aug-2022) {8/2025}	215.79 (N.A.) {215.79}	132.93	80.38
		157	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)]	3-2018	9/2018 (Jun-2023) {9/2025}	323.98 (N.A.) {323.98}	119.94	60.11
		158	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)]	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	100.51	58.57

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		159	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	50.60	28.05
		160	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	168.20	66.03
		161	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (Sep-2025) {9/2025}	192.93 (N.A.) {192.93}	112.09	93.38
		162	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {12/2025}	177.77 (199.02) {199.02}	46.94	63.33
		163	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	65.19	73.34
		164	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (Jun-2026) {6/2026}	252.19 (N.A.) {252.19}	14.33	20.27
		165	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3-2021	7/2024 (Dec-2025) {12/2025}	297.24 (N.A.) {297.24}	150.10	80.31
		166	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (Mar-2025) {3/2025}	226.44 (N.A.) {226.44}	140.24	100

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
SIKKIM	<u>CIVIL AVIATION</u>	167	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	29.68	12.5
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	168	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim University) (N44000002)	8-2020	1/2025 (N.A.) {1/2025}	314.06 (N.A.) {303.55}	157.24	80
	<u>POWER</u>	169	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	4,424.21	68.17
		170	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,524.17	89.45
	<u>RAILWAYS</u>	171	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	5/2015 (Dec-2027) {12/2027}	7,876.92 (11,963.43) {11,963.43}	8,743.57	79.5
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	172	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (Mar-2026) {3/2026}	385.15 (N.A.) {385.15}	175.16	83.3
		173	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (May-2022) {12/2023}	375.80 (N.A.) {375.80}	288.56	96.55
		174	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {10/2025}	402.94 (N.A.) {402.94}	247.12	76.54
		175	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (Nov-2024) {10/2025}	295.97 (N.A.) {295.97}	249.97	95.71

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		176	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {10/2025}	311.00 (N.A.) {273.78}	257.86	95.12
		177	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (Aug-2024) {10/2025}	345.38 (395.59) {395.59}	362.61	89.81
		178	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (Dec-2025) {12/2025}	410.60 (379.30) {379.30}	238.13	74.82
		179	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (Oct-2024) {3/2026}	230.45 (244.91) {244.91}	206.95	82.8
		180	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (Jul-2025) {3/2026}	493.42 (478.79) {478.79}	308.18	59.49
		181	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (Jun-2025) {12/2026}	816.79 (786.60) {786.60}	332.24	45.9
		182	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (Oct-2023) {12/2025}	292.80 (N.A.) {292.80}	202.92	61.41
		183	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (Oct-2023) {12/2025}	183.31 (439.56) {439.56}	355.31	51.85

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		184	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (Aug-2024) {12/2025}	262.84 (414.20) {414.20}	221.86	49.2
TRIPURA	PETROLEUM	185	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (Sep-2025) {9/2025}	656.00 (N.A.) {656.00}	427.77	83.17
	ROAD TRANSPORT AND HIGHWAYS	186	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (N.A.) {12/2025}	354.79 (N.A.) {354.79}	34.08	0
		187	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (Feb-2024) {12/2024}	277.50 (302.02) {302.02}	262.91	99.94
		188	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {4/2025}	201.99 (N.A.) {287.47}	148.22	100
		189	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (Oct-2023) {11/2024}	159.13 (171.50) {171.50}	84.33	100
		190	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (May-2025) {5/2025}	456.88 (N.A.) {456.88}	122.67	50.18
		191	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {12/2025}	195.95 (N.A.) {195.95}	46.46	45.42
		192	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	81.54	24.56

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		193	KHOWAI ?TELIAMURA-AMARPUR-HARINA-SABROOM SECTION PKG-4 (NHIDCL) (N24002228)	1-2024	12/2026 (N.A.) {12/2026}	726.90 (N.A.) {726.90}	7.36	3.85
		194	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	26.34	8.82
		195	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGTH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	9.54	16.61
		196	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	52.82	34.61
		197	KHOWAI ?TELIAMURA-AMARPUR-HARINA-SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	95.71	32.85
		198	KHOWAI ?TELIAMURA-AMARPUR-HARINA-SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	3.81	3.05
			Total			204,650.98 (49,956.05) {250,765.20}	1,47,918.48	

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ANDAMAN AND NICOBAR ISLANDS	CIVIL AVIATION	1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR (AAI) (N04000073)	10-2013	9/2018 (Jun-2023) {6/2023}	417.23 (707.73) {707.73}	698.80	100.00
	RAILWAYS	2	LUDHIANA KILA RAIPUR (19 KMS) WITH FREIGHT LINE AT GILL STATION ON LDH-JHL SECTION (NR) (N22000584)	3-2019	3/2025 (Aug-2025) {3/2026}	235.72 (N.A.) {235.72}	59.78	55.00
	ROAD TRANSPORT AND HIGHWAYS	3	MAJOR BRIDGE OVER MIDDLE STRAIT CREEK (NHIDCL) (N24002207)	12-2024	2/2026 (N.A.) {2/2026}	371.80 (207.99) {207.99}	0.00	5.23
		4	PACKAGE-3A (NHIDCL) (N24002208)	2-2018	9/2025 (Mar-2024) {9/2025}	207.54 (154.01) {154.01}	16.21	39.27
		5	PACKAGE-3B (NHIDCL) (N24002209)	2-2018	11/2025 (N.A.) {11/2025}	183.47 (N.A.) {183.47}	18.36	34.01
		6	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N (NHIDCL) (N24000745)	3-2017	12/2019 (Mar-2023) {6/2025}	409.85 (N.A.) {409.85}	214.23	95.23
		7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O (NHIDCL) (N24000749)	3-2018	9/2020 (Nov-2022) {7/2025}	234.27 (N.A.) {234.27}	126.50	83.00
		8	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 (MoRTH) (N24000820)	11-2017	11/2019 (N.A.) {11/2019}	237.80 (N.A.) {238.00}	222.13	98.23

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		9	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000821)	11-2017	11/2019 (N.A.) {11/2019}	257.34 (N.A.) {238.00}	214.90	100.00
ANDHRA PRADESH	CIVIL AVIATION	10	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT (AAI) (N04000091)	4-2020	3/2023 (Aug-2025) {8/2025}	611.80 (N.A.) {611.80}	449.66	75.25
		11	RAJAHMUNDY AIRPORT: CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUD (AAI) (N04000103)	12-2022	8/2025 (N.A.) {8/2025}	347.15 (347.15) {347.15}	76.86	46.00
		12	KADAPPA AIRPORT- CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUDING MA (AAI) (N04000106)	3-2023	1/2026 (Mar-2026) {3/2026}	265.91 (265.91) {265.91}	39.54	29.00
	DEPARTMENT OF HIGHER EDUCATION	13	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE (CPWD EDUCATION) (N42000005)	2-2019	6/2020 (N.A.) {6/2020}	655.34 (N.A.) {655.34}	366.21	95.00
		14	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT (CPWD EDUCATION) (N42000007)	9-2019	9/2022 (N.A.) {6/2024}	588.72 (656.39) {656.39}	630.55	100.00
	PETROLEUM	15	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT (ONGC) (N16000247)	3-2016	6/2020 (Mar-2025) {6/2025}	34,012.00 (N.A.) {34,012.00}	33,167.16	96.40
		16	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY (HPCL) (N16000432)	9-2021	6/2024 (Mar-2026) {3/2026}	160.00 (220.00) {220.00}	75.86	59.40

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		17	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS (IOCL) (N16000485)	3-2022	3/2030 (N.A.) {3/2030}	1,420.00 (N.A.) {1,420.00}	153.86	6.20
		18	MULTI-PRODUCT PIPELINE FROM KRISHNAPATNAM COASTAL INSTALLATION TO THE PROPOSED INSTALLATION AT HYDER (BPCL) (N16000499)	9-2019	3/2025 (N.A.) {10/2025}	1,932.00 (N.A.) {1,932.00}	1,498.21	94.30
		19	HP TRIJET UNIT IN VR (HPCL) (N16000535)	7-2024	7/2027 (N.A.) {7/2027}	193.00 (N.A.) {193.00}	0.43	23.00
		20	CONSTRUCTION OF AVIATION FUEL FARM FACILITIES AT BHOGAPURAM AIRPORT (HPCL) (N16000538)	8-2024	3/2026 (N.A.) {3/2026}	240.00 (N.A.) {240.00}	22.34	42.80
		21	VISAKHA RAIPUR PIPELINE PROJECT (HPCL) (N16000539)	9-2024	9/2027 (N.A.) {9/2027}	2,212.00 (N.A.) {2,212.00}	8.32	6.03
		22	TRANSMISSION SCHEME FOR SOLAR ENERGY ZONE IN ANANTHPURAM (2500MW) AND KURNOOL (1000MW) (PGCIL) (N18000380)	9-2023	3/2025 (N.A.) {9/2025}	1,249.00 (N.A.) {1,249.00}	761.69	67.50
	POWER	23	AUGMENTATION OF 1500MVA 3RD 765/400KV TRANSFORMATION CAPACITY AT KURNOOL NEW SUBSTATION (PGCIL) (N18000395)	5-2023	9/2025 (N.A.) {9/2025}	164.00 (N.A.) {164.00}	60.00	33.00
		24	TRANSMISSION SYSTEM FOR INTEGRATION OF KURNOOL-IV REZ PHASE-I (FOR 4.5 GW) (PGCIL) (N18000413)	3-2025	3/2027 (N.A.) {3/2027}	5,000.00 (N.A.) {5,000.00}	20.00	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		25	TRANSMISSION SYSTEM STRENGTHENING AT KURNOOL- III PS FOR INTEGRATION OF ADDITIONAL RE GENERATION PRO (PGCIL) (N18000416)	3-2025	3/2027 (N.A.) {3/2027}	2,886.00 (N.A.) {2,886.00}	20.20	-
	RAILWAYS	26	KOTLPALLI-NARASAPUR (NL) (SCR) (SCR) (220100265)	12-2001	3/2028 (N.A.) {3/2027}	2,500.98 (N.A.) {2,500.98}	1,141.44	18.00
		27	NADIKUDE-SRI KALAHASTI (SCR) (N22000286)	4-2011	5/2027 (N.A.) {5/2027}	2,312.00 (N.A.) {3,122.35}	1,977.09	-
		28	GUNTUR-GUNTAKAL (SCR) (N22000368)	4-2016	12/2025 (N.A.) {12/2025}	3,733.37 (N.A.) {3,887.48}	3,606.85	-
		29	VIJAYAWADA-GUDUR (RVNL) (N22000369)	4-2015	11/2024 (N.A.) {12/2024}	6,654.00 (N.A.) {6,238.67}	5,883.89	-
		30	KOTTAVALSA - KORAPUT DOUBLING (ECOR) (N22000377)	4-2015	3/2022 (N.A.) {3/2022}	2,499.71 (N.A.) {2,499.71}	1,965.11	70.00
		31	PENUKONDA-DHARMAVARAM, EXCL. DHARMAVARAM (41.5 KM) (SWR) (N22000555)	4-2019	3/2026 (N.A.) {12/2025}	294.67 (307.66) {307.66}	213.03	60.00
		32	MALUGUR-PALASAMUDRAM (17.98 KM) (PB#29/NR/2022-23) (SWR) (N22000556)	9-2022	12/2025 (N.A.) {12/2026}	323.14 (342.41) {342.41}	46.89	12.00
		33	DOUBLING BETWEEN GOOTY- PENDAKALLU (29.225) (SCR) (N22000585)	3-2023	3/2027 (N.A.) {3/2027}	351.83 (N.A.) {351.83}	0.00	-
		34	VIJAYAWADA KAZIPET BYEPASS LINE (SCR) (N22000586)	4-2016	12/2025 (N.A.) {12/2025}	647.37 (N.A.) {226.72}	261.07	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	35	RENIGUNTA WADI GOOTY - BYPASS (SCR) (N22000587)	4-2016	12/2025 (N.A.) {12/2025}	302.00 (N.A.) {302.00}	226.67	50.00
		36	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI (NHAI) (N24001476)	9-2021	9/2022 (Sep-2024) {7/2025}	517.05 (N.A.) {655.06}	543.03	94.50
		37	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP (NHAI) (N24001477)	9-2021	9/2022 (Sep-2024) {6/2025}	622.00 (N.A.) {817.91}	541.73	75.96
		38	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16 (NHAI) (N24001817)	2-2019	3/2023 (Oct-2024) {10/2024}	757.45 (N.A.) {757.45}	711.37	99.61
		39	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) (NHAI) (N24001818)	2-2021	1/2025 (N.A.) {1/2025}	818.73 (N.A.) {1,105.00}	564.03	25.32
		40	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) (NHAI) (N24001819)	3-2021	1/2025 (N.A.) {1/2025}	1,102.63 (N.A.) {1,303.00}	1,171.71	97.26
		41	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) (NHAI) (N24001820)	2-2021	12/2024 (N.A.) {12/2024}	1,484.83 (N.A.) {1,768.00}	1,544.65	93.29
		42	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP (NHAI) (N24001821)	11-2020	10/2024 (N.A.) {10/2024}	1,137.74 (N.A.) {1,289.00}	1,256.44	97.43

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		43	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE (NHAI) (N24001822)	12-2020	10/2024 (N.A.) {10/2024}	1,075.27 (N.A.) {1,307.00}	1,132.36	85.89
		44	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A (NHAI) (N24001823)	1-2022	1/2025 (Jan-2023) {1/2025}	1,852.12 (N.A.) {1,787.00}	777.18	93.00
		45	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP (NHAI) (N24001824)	3-2020	1/2024 (Dec-2024) {12/2024}	1,863.09 (N.A.) {2,238.00}	1,227.61	98.76
		46	6L KANTAKAPALLE ? SABBAVARAM SECTION OF NH-130CD ROAD FROM KM 445.100 TO KM 464.662 (PKG-4) (NHAI) (N24001836)	2-2021	10/2024 (N.A.) {3/2026}	824.29 (N.A.) {924.00}	521.51	76.13
		47	6L JAKKUVA ? KORLAM SECTION OF NH-130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) (NHAI) (N24001837)	2-2021	3/2024 (Jul-2024) {12/2025}	663.60 (N.A.) {768.00}	464.74	98.84
		48	6L ALURU - JAKKUVA SECTION OF NH- 130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) (NHAI) (N24001838)	2-2021	3/2024 (N.A.) {12/2025}	922.50 (N.A.) {1,128.68}	534.51	84.38
		49	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA (NHAI) (N24001841)	12-2022	9/2025 (N.A.) {2/2026}	912.94 (N.A.) {912.94}	238.84	59.65
		50	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 (NHAI) (N24001842)	12-2022	11/2025 (N.A.) {11/2025}	750.81 (N.A.) {750.81}	145.15	50.78

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		51	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH (NHAI) (N24001843)	12-2022	11/2025 (N.A.) {11/2025}	992.89 (N.A.) {992.89}	197.36	47.00
		52	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. (NHAI) (N24001844)	12-2022	10/2025 (N.A.) {10/2025}	1,058.90 (N.A.) {1,058.90}	251.41	47.64
		53	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 (NHAI) (N24001845)	2-2023	10/2025 (N.A.) {10/2025}	1,253.24 (N.A.) {1,253.24}	197.29	23.20
		54	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. (NHAI) (N24001846)	2-2023	10/2025 (N.A.) {10/2025}	1,200.42 (N.A.) {1,200.42}	98.82	8.90
		55	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA (NHAI) (N24001847)	1-2023	11/2025 (N.A.) {11/2025}	956.14 (N.A.) {956.14}	215.17	43.11
		56	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTLA 196.000 KM. PACK (NHAI) (N24001848)	2-2023	10/2025 (N.A.) {10/2025}	909.02 (N.A.) {909.02}	161.56	23.44
		57	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 (NHAI) (N24001849)	5-2022	7/2025 (N.A.) {9/2025}	1,063.72 (N.A.) {1,063.72}	467.94	82.10
		58	CONSTRUCTION OF 4-LANE HIGHWAY FROM SAMARLAKOTA TO ACHAMPETA JUNCTION (FROM KM. 0.000 TO KM. 12.250 (NHAI) (N24001856)	5-2023	8/2025 (N.A.) {8/2025}	648.75 (N.A.) {648.75}	253.96	64.67

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		59	2L+PS FROM KM. 0+000 TO KM. 32+000 (MUDIGUBBA TO PUTTAPARTHI) OF NH- 342 (MoRTH) (N24001932)	3-2022	9/2024 (N.A.) {6/2025}	401.72 (N.A.) {401.72}	190.74	80.00
		60	NH440 RAYACHOTY TO VEMPALLI 2LPS (MoRTH) (N24001934)	12-2021	5/2024 (N.A.) {7/2025}	439.82 (N.A.) {439.82}	174.96	-
		61	4 LANE WITH PAVED SHOULDER FROM KM 0.000 TO KM 51.119 OF TADIPATRI TO MUDDANUR OF NH67 (MoRTH) (N24001935)	3-2022	8/2025 (N.A.) {8/2025}	724.17 (N.A.) {724.17}	464.48	-
		62	NH165 FROM KM 0.000 TO KM 64.020 PAMARRU TO AKIVEEDU SECTION TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001939)	3-2020	9/2023 (N.A.) {12/2026}	529.24 (N.A.) {529.24}	353.88	62.70
		63	2LPS FROM KM36.400 TO KM. 107.224 OF NH167BG FROM DUTTALUR TO KAVALI SECTION (MoRTH) (N24001942)	3-2021	7/2024 (N.A.) {6/2026}	423.67 (N.A.) {423.67}	222.39	83.59
		64	NH167AD FROM MACHERLA TO DACHEPALLI FROM KM.0.000 TO 43.659 TO 2LPS (MoRTH) (N24001951)	1-2022	1/2025 (N.A.) {1/2025}	403.22 (N.A.) {403.22}	296.69	98.82
		65	NH 167 B KADAPA NELLORE BORDER TO CSPURAM I.E. FROM KM 58.635 TO KM 99.409 (MoRTH) (N24001952)	3-2022	8/2025 (N.A.) {8/2025}	285.50 (N.A.) {285.50}	204.29	95.00
		66	NH-30-BHADRACHALAM TO KONTA SECTION 2LPS (MoRTH) (N24001953)	12-2021	9/2024 (N.A.) {9/2025}	388.71 (N.A.) {388.71}	242.09	89.60

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		67	WIDENING TO 2LPS OF RAMPACHODAVARAM - KOYYURU SECTION OF NH516E FROM KM.43.700 TO KM 113.820 (MoRTH) (N24001954)	3-2022	1/2025 (N.A.) {1/2025}	568.12 (N.A.) {568.12}	350.64	91.05
		68	GUDIWADA TOWN 2 LANE ROB AND ROAD IMPROVEMENT OF NH165 IN REPLACEMENT OF LC NO 3ESPL3 AT KM 231.700 (MoRTH) (N24001955)	3-2022	5/2025 (N.A.) {5/2025}	317.22 (N.A.) {317.22}	190.90	80.00
		69	2LPS FROM GONDIGUDA TO ARAKU BHALLAGUDA KM 27.480 TO KM 51.772 SECTION OF NH 516E (MoRTH) (N24001956)	8-2020	9/2023 (N.A.) {12/2024}	296.66 (N.A.) {296.66}	246.11	87.49
		70	2LPS OF KOYYURU TO CHAPRATHIPALEM SECTION OF NH 516E (MoRTH) (N24001957)	8-2020	7/2024 (N.A.) {7/2024}	349.29 (N.A.) {349.29}	216.90	-
		71	2LPS OF CHAPRATHIPALEM TO LAMBASINGI SECTION OF NH 516E (MoRTH) (N24001958)	8-2020	10/2024 (N.A.) {6/2025}	311.22 (N.A.) {311.22}	151.24	72.00
		72	4 LANE FROM KM 56.400 TO KM 120.300 FROM B.KOTHAPALLI JUNCTION TO GORANTLA OF NH 716G (MoRTH) (N24001959)	3-2022	9/2025 (N.A.) {9/2025}	839.98 (N.A.) {839.98}	418.51	-
		73	4L GREENFIELD ROAD CONNECTING NORTH AND SOUTH INDUSTRIAL CLUSTER OF KHANDALERU CREEK NEAR KRISHNAPAT (NHAI) (N24001979)	8-2022	9/2025 (N.A.) {9/2025}	609.43 (N.A.) {609.43}	25.24	56.70
		74	4 LANING OF NH 544D FROM EXISTING KM 346.300 OF NH 44 (DESIGN CHAINAGE KM 0.000) TO KM 39.380 (DESIG (NHAI) (N24001980)	10-2022	7/2025 (N.A.) {7/2025}	907.76 (N.A.) {907.76}	388.70	84.29

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		75	CONSTRUCTION OF SIX LANING OF NAIDUPETA JUNCTION - TURPUKANUPUR SECTION FROM KM.57+046 TO KM.91+927 (NHAI) (N24001981)	7-2022	10/2025 (N.A.) {10/2025}	1,398.84 (N.A.) {1,398.84}	58.68	19.10
		76	4L PS FROM KURNOOL (EXISTING KM. 5.400 OF NH-40/DESIGN KM.0.000) TO MANDLEM (EXISTING KM.38.000/DESI (NHAI) (N24001982)	3-2023	10/2025 (N.A.) {10/2025}	827.39 (N.A.) {827.39}	333.88	99.65
		77	4 LANING FROM EXISTING KM 39.380 (DESIGN CH. 37.000) TO KM 74.450 (DESIGN CH. 69.000) OF MUCHUKOTA ? (NHAI) (N24001983)	10-2022	8/2025 (N.A.) {8/2025}	972.63 (N.A.) {1,055.23}	310.77	54.96
		78	4L PS FROM MANDLEM (EXISTING KM. 38.000/DESIGN KM.30.600) TO ATMAKUR (EXISTING KM.73.000/DESIGN KM 6 (NHAI) (N24001984)	3-2023	10/2025 (N.A.) {10/2025}	887.28 (N.A.) {887.28}	297.95	89.20
		79	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-II) FROM KM.96.000 TO KM 127.000 (BAIREDDYPALLE TO BANGAR (NHAI) (N24001985)	3-2021	6/2025 (N.A.) {6/2025}	1,942.94 (2,171.00) {2,171.00}	1,736.95	64.50
		80	4L OF PILERU TO KALUR SECTION FROM KM 55.900 TO KM 92.800 AND KM 94.500 TO KM 95.717 (NHAI) (N24001986)	10-2023	4/2025 (N.A.) {4/2025}	1,047.32 (N.A.) {1,047.32}	301.20	93.00
		81	CONSTRUCTION OF 1 NOS ROB, 2 NOS VUPS, SERVICE ROADS, PROVISION OF LIGHTING AND CONSTRUCTION OF OTHE (NHAI) (N24001987)	6-2023	12/2024 (N.A.) {12/2024}	152.05 (N.A.) {152.05}	139.12	76.83
		82	6L OF CHITTOOR TO THATCHUR FROM KUMARAJAPET TO VEERA KAVERI RAJA PURAM FROM KM 43.800 TO KM 61.380 O (NHAI) (N24001988)	2-2021	10/2025 (N.A.) {10/2025}	591.99 (703.00) {703.00}	506.67	70.95

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		83	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED HIGHWAY FROM CHILLAKURU CROSS ROAD TO TURPUKANUPUR KM 0+000 (NHAI) (N24002033)	7-2022	12/2025 (N.A.) {12/2025}	909.47 (N.A.) {909.47}	97.03	32.30
		84	COMPLETION OF BALANCE WORKS PENDING IN BIT AND PIECES (INCOMPLETE STRETCH AT 7 LOCATIONS) AND LISTED (NHAI) (N24002103)	9-2022	1/2025 (N.A.) {6/2025}	166.52 (N.A.) {166.52}	60.34	98.00
		85	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NARAYANMPET (CH. 203+500) TO CHANDRASEKHARPURAM (CH. 22 (NHAI) (N24002122)	2-2024	2/2026 (N.A.) {2/2026}	813.66 (N.A.) {813.66}	91.93	24.20
		86	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM CHANDRASEKHARAPURAM (CH. 228+000) TO POLAVARAM (CH. 260 (NHAI) (N24002123)	2-2024	2/2026 (N.A.) {2/2026}	1,292.65 (N.A.) {1,292.65}	135.27	18.96
		87	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM POLAVARAM (CH. 260+000) TO MARRIPUDI (CH. 285+500) OF [(NHAI) (N24002124)	2-2024	2/2026 (N.A.) {2/2026}	747.29 (N.A.) {747.29}	142.65	32.02
		88	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MARRIPUDI (CH. 285+500) TO SOMAVARAPPADU (CH. 314+600) (NHAI) (N24002125)	2-2024	2/2026 (N.A.) {2/2026}	976.40 (N.A.) {976.40}	229.68	43.60
		89	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM SOMAVARAPPADU (CH.314.600) TO MUPPAVARAM (CH.343+240) O (NHAI) (N24002126)	2-2024	2/2026 (N.A.) {2/2026}	1,103.89 (N.A.) {1,103.89}	133.89	15.98
		90	4-LANE WITH PAVED SHOULDERS FROM KM 32/0 TO KM 79/650 (DESIGN CHAINAGE KM 32+000 TO KM 78+760) PUTTA (MoRTH) (N24002139)	3-2023	12/2025 (N.A.) {11/2025}	1,318.57 (N.A.) {1,318.57}	424.42	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		91	SOMAYAJULAPALLI ? DHONE SECTION OF NH ? 340B FROM KM.0/0 TO 56/200 [DESIGN CH. KM 0/00 TO KM 53/33] (MoRTH) (N24002140)	4-2023	12/2025 (N.A.) {12/2025}	629.73 (N.A.) {629.73}	369.43	-
		92	2-LANE WITH PAVED SHOULDER CONFIGURATION OF LAMBASINGI TO PADERU SECTION (KM 205+000 TO KM 253+974) (MoRTH) (N24002142)	8-2023	11/2025 (N.A.) {11/2025}	361.24 (N.A.) {361.24}	63.54	-
		93	BYPASS ROAD TO ADONI TOWN CONNECTING NH-167 (HAGARI - JADCHARLA ROAD) FROM KM.62/700 TO 71/400 IN KU (MoRTH) (N24002143)	8-2023	2/2026 (N.A.) {2/2026}	361.24 (N.A.) {361.24}	109.65	56.00
		94	VODAREVU-CHILAKALURIPET SECTION (DESIGN CHAINAGE 0+00 TO 47+000) OF NH-167A (PACKAGE-I) (MoRTH) (N24002144)	8-2023	2/2026 (N.A.) {2/2026}	1,064.24 (N.A.) {1,064.24}	584.25	-
		95	TADIPATRI BYPASS (KM 0+000 TO KM 6+285) OF 4-LANE ON NH-67 IN ANANTAPURAMU (MoRTH) (N24002145)	11-2023	3/2026 (N.A.) {3/2026}	159.66 (N.A.) {159.66}	60.51	63.50
		96	KURNOOL/KADAPA BORDER- JAMMALAMADUGU SECTION OF NH- 167K I.E. DESIGN CH. KM 248+010 TO KM 269+900 (MoRTH) (N24002146)	11-2023	11/2025 (N.A.) {11/2025}	292.63 (N.A.) {292.63}	81.57	-
		97	DORNALA TO KUNTA JUNCTION FROM DESIGN CHAINAGE KM 244+000 TO 267+990 SECTION OF NH-765 (PACKAGE-2) (MoRTH) (N24002147)	12-2022	1/2024 (N.A.) {3/2026}	244.83 (N.A.) {244.83}	111.65	-
		98	PADERU BYPASS (KM 0+000 TO KM 13+000) OF 2- LANE WITH PAVED SHOULDER ON NH-516E (MoRTH) (N24002148)	3-2023	3/2024 (N.A.) {2/2026}	244.43 (N.A.) {244.43}	23.40	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		99	DAVUALAPALLY TO MALLAPALEM SECTION (DESIGN CH. KM 133+922 TO KM 154+216 (EXISTING CH. KM 133+922 TO (MoRTH) (N24002149)	1-2024	2/2024 (N.A.) {2/2026}	393.61 (N.A.) {393.61}	135.13	-
		100	DEVELOPMENT OF SIX LANE ACCESS CONTROLLED GREEN FIELD HIGHWAY FROM KAVULAKUNTALA (KM.196+000) TO NARA (NHAI) (N24002215)	2-2023	2/2027 (N.A.) {2/2027}	1,092.18 (N.A.) {1,092.18}	0.14	-
		101	ACCESS CONTROLLED HIGHWAY OF 4 LANE WITH PAVED SHOULDERS FROM TN/AP BORDER (DESIGN CHAINAGE KM 61+51 (NHAI) (N24002217)	12-2024	12/2026 (N.A.) {12/2026}	1,346.82 (N.A.) {1,346.82}	37.35	8.20
		102	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 (NHAI) (N24000811)	3-2018	12/2020 (Dec-2022) {12/2024}	314.43 (N.A.) {348.72}	85.61	71.49
		103	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 (MoRTH) (N24000931)	11-2016	5/2017 (N.A.) {11/2024}	290.15 (N.A.) {236.16}	205.03	90.00
		104	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG (MoRTH) (N24000937)	3-2018	8/2018 (N.A.) {11/2024}	289.67 (290.00) {285.29}	256.60	98.50
		105	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH- 214(NH216)(KAKINAD (MoRTH) (N24000964)	8-2016	1/2017 (N.A.) {5/2025}	350.61 (N.A.) {411.18}	390.28	98.20
		106	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 (MoRTH) (N24000969)	1-2017	9/2017 (N.A.) {6/2025}	263.45 (N.A.) {263.45}	265.51	85.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		107	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) (NHAI) (N24001301)	11-2019	1/2024 (N.A.) {7/2024}	1,601.10 (N.A.) {1,601.10}	1,445.67	92.34
		108	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU- GONDIGUDA SECT (MoRTH) (N24001386)	8-2020	3/2021 (N.A.) {6/2025}	222.61 (N.A.) {222.61}	183.91	95.00
	<u>WATER RESOURCES</u>	109	POLAVARAM IRRIGATION PROJECT (PPA) (N30000002)	2-2009	3/2020 (Mar-2027) {12/2027}	10,151.04 (N.A.) {55,548.87}	23,775.68	76.00
<u>ARUNACHAL PRADESH</u>	<u>CIVIL AVIATION</u>	110	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (Jul-2025) {7/2025}	645.63 (732.00) {732.00}	694.26	99.89
	<u>POWER</u>	111	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	24,484.77	96.60
		112	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	3,380.24	15.81
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	113	HUNLI TO HAYULIANG PKG-1 (NHIDCL) (N24002222)	2-2024	2/2028 (N.A.) {2/2028}	1,262.43 (N.A.) {1,262.43}	12.12	2.76
		114	HUNLI TO ITHUN BRIDGE SECTION (NHIDCL) (N24002223)	2-2024	1/2027 (N.A.) {1/2027}	275.50 (N.A.) {275.50}	7.61	7.88
		115	PANGO TO JORGING ROAD PKG-1 (NHIDCL) (N24002224)	1-2024	7/2027 (N.A.) {7/2027}	898.19 (N.A.) {898.19}	16.01	4.25

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		116	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (Mar-2024) {12/2024}	180.57 (244.10) {180.57}	160.46	96.62
		117	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (Jun-2025) {12/2025}	1,718.59 (1,718.59) {1,718.59}	742.36	73.84
		118	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (May-2023) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59
		119	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (Apr-2025) {4/2025}	301.06 (N.A.) {301.06}	205.71	100.00
		120	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	398.18	95.84
		121	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	194.62	44.56
		122	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (Aug-2024) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		123	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (Feb-2024) {7/2025}	184.88 (N.A.) {184.88}	99.32	97.42

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ASSAM	CIVIL AVIATION	124	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (Sep-2025) {9/2025}	1,142.00 (N.A.) {2,333.00}	1,948.45	89.66
	COAL	125	TIKAK EXTENSION OCP - 0.2 MTY (CIL) (N06000290)	7-2022	11/2030 (N.A.) {11/2030}	159.77 (N.A.) {159.77}	81.45	-
		126	TIRAP OCP (CIL) (N06000291)	11-2022	11/2027 (N.A.) {11/2027}	289.46 (N.A.) {289.46}	105.59	-
	HEALTH AND FAMILY WELFARE	127	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (Apr-2023) {6/2025}	875.00 (873.92) {860.00}	796.74	99.62
	PETROLEUM	128	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (Jun-2025) {12/2025}	543.91 (726.93) {726.93}	491.56	93.98
		129	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	16,357.82	74.92
		130	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	9,579.31	85.10
		131	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (May-2026) {5/2026}	412.00 (595.20) {595.20}	396.15	83.40
		132	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (Sep-2026) {9/2026}	277.00 (N.A.) {277.00}	181.63	67.67

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		133	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (Jul-2025) {10/2025}	860.00 (N.A.) {860.00}	535.46	97.50
		134	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (Jun-2025) {12/2025}	430.76 (N.A.) {430.76}	320.71	83.94
		135	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	101.15	34.60
		136	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (Jul-2027) {7/2027}	156.36 (156.36) {156.36}	44.33	35.40
		137	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (Jul-2027) {7/2027}	384.04 (N.A.) {384.04}	97.54	44.00
		138	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	97.22	92.00
		139	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	255.51	55.00
		140	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	208.56	46.30
		141	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	99.52	27.30

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>RAILWAYS</u>	142	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2026 (N.A.) {3/2027}	4,059.65 (N.A.) {4,962.40}	3,668.09	92.31
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	143	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	344.27	67.85
		144	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {5/2025}	625.64 (N.A.) {625.64}	556.44	100.00
		145	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {7/2025}	204.10 (N.A.) {204.10}	143.66	96.80
		146	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {6/2025}	909.02 (N.A.) {909.02}	532.44	100.00
		147	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (Sep-2024) {6/2024}	175.00 (N.A.) {175.00}	209.02	100.00
		148	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	683.00	78.92
		149	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {5/2025}	457.72 (N.A.) {457.72}	366.34	100.00
		150	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	110.76	35.77

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		151	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {11/2025}	458.59 (N.A.) {458.59}	205.87	66.12
		152	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {3/2026}	535.03 (N.A.) {535.03}	102.23	34.54
		153	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	409.15	68.26
		154	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	417.17	68.60
		155	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	467.83	65.56
		156	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	323.24	98.48
		157	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	303.89	99.06
		158	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	551.88	47.50

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		159	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	308.11	29.01
		160	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	425.17	27.99
		161	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	242.92	75.51
		162	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	134.02	18.15
		163	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.87	100.00
		164	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	539.19	40.36
		165	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	989.94	64.56
		166	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	297.70	54.97
		167	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	407.11	68.95

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		168	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	290.90	43.16
		169	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	213.67	50.88
		170	BILASIPURA- GUWAHATI ROAD PKG-1 (NHIDCL) (N24002225)	2-2024	8/2027 (N.A.) {8/2027}	1,081.15 (N.A.) {1,081.15}	33.93	2.76
		171	SILCHAR-JIRIBAM PKG-1 (NHIDCL) (N24002226)	1-2024	1/2028 (N.A.) {1/2028}	957.95 (N.A.) {957.95}	0.00	21.98
		172	BILASIPURA- GUWAHATI ROAD PKG-2 (NHIDCL) (N24002229)	11-2023	6/2027 (N.A.) {6/2027}	1,338.61 (N.A.) {1,338.61}	0.50	-
		173	BADARPUR ? CHURAIBARI PKG-6 (NHIDCL) (N24002230)	3-2024	3/2027 (N.A.) {3/2027}	870.00 (N.A.) {870.00}	0.00	5.86
		174	KARIMGANI - SUTARKANDI SECTION ON SILCHAR-CHURAIBARI PKG-7 (NHIDCL) (N24002231)	2-2024	2/2027 (N.A.) {2/2027}	791.79 (N.A.) {791.79}	0.00	1.02
		175	CONSTRUCTION OF 4 LANE GAURIPUR BYPASS ON NH-17 IN THE STATE OF ASSAM (MoRTH) (N24002237)	3-2024	10/2026 (N.A.) {10/2026}	421.15 (N.A.) {421.15}	0.00	-
		176	CONSTRUCTION OF 2 LANE BARPETA BYPASS FROM KM 77+900(BARADI) TO KM 86+150(DEURIKUCHI) (LENGTH=8.25K (MoRTH) (N24002238)	3-2023	8/2026 (N.A.) {8/2026}	173.65 (N.A.) {173.65}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		177	SILCHAR- CHURAIBARI PKG-5 (NHIDCL) (N24002243)	2-2024	10/2027 (N.A.) {10/2027}	1,258.13 (N.A.) {1,258.13}	0.00	-
		178	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {7/2025}	437.39 (N.A.) {437.39}	586.89	97.43
		179	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	517.62	78.19
		180	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1-1991	6/2019 (Jun-2019) {7/2025}	520.01 (N.A.) {520.01}	306.13	98.42
		181	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (Jul-2021) {12/2025}	289.99 (N.A.) {289.99}	233.23	88.03
		182	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {7/2025}	294.17 (N.A.) {294.17}	396.49	98.40
		183	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {7/2025}	252.00 (N.A.) {330.30}	242.97	95.42
		184	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	217.31	97.76

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		185	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (Jun-2025) {8/2025}	216.49 (241.52) {216.49}	114.38	87.02
		186	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,464.49	62.82
		187	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (May-2025) {12/2025}	261.13 (N.A.) {261.13}	70.08	57.50
		188	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (Apr-2025) {12/2025}	217.50 (N.A.) {217.50}	89.21	68.03
		189	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.78	100.00
		190	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	159.30	82.90
		191	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (1,019.17) {925.47}	192.50	30.65
BIHAR	CIVIL AVIATION	192	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II (AAI) (N04000082)	5-2018	10/2022 (Nov-2025) {11/2025}	1,216.90 (N.A.) {1,216.90}	1,029.05	93.14
		193	DARBHANGA:DEVELOPMENT OF NEW CIVIL ENCLAVE AT DARBHANGA, BIHAR. SH- CONSTRUCTION OF NEW TERMINAL BUI (AAI) (N04000112)	7-2024	7/2026 (N.A.) {7/2026}	911.66 (N.A.) {911.66}	113.58	20.75

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	194	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA (CPWD EDUCATION) (N28000100)	2-2016	6/2017 (N.A.) {1/2024}	496.18 (496.00) {460.00}	390.15	100.00
		195	PERMANENT CAMPUS FOR IIM BODH GAYA (CPWD EDUCATION) (N42000009)	9-2018	9/2020 (N.A.) {3/2025}	375.00 (N.A.) {375.00}	342.18	100.00
	<u>PETROLEUM</u>	196	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA (IOCL) (N16000386)	1-2020	4/2023 (Aug-2026) {8/2026}	14,810.00 (18,113.00) {18,113.00}	11,055.42	89.00
		197	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA (IOCL) (N16000423)	6-2019	12/2029 (Mar-2030) {3/2030}	163.00 (N.A.) {163.00}	96.08	40.10
		198	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI (IOCL) (N16000453)	1-2022	4/2025 (N.A.) {5/2026}	389.00 (N.A.) {389.00}	38.25	35.40
		199	CITY GAS DISTRIBUTION PROJECTS AT GOPALGANJ SIWAN WEST CHAMPARAN EAST CHAMPARAN AND DEORIA DISTRICTS (BPCL) (N16000523)	12-2022	6/2030 (N.A.) {6/2030}	3,919.00 (N.A.) {3,919.00}	382.99	13.60
		200	CITY GAS DISTRIBUTION PROJECTS AT DARBHANGA, MADHUBANI, SUPAUL, SITAMARHI AND SHEOHAR DISTRICTS (BPCL) (N16000524)	12-2022	3/2030 (N.A.) {3/2030}	3,638.00 (N.A.) {3,638.00}	390.34	20.80
	<u>POWER</u>	201	BARH STPP(3X660MW) NTPC (NTPC) (180100242)	2-2005	10/2011 (Jul-2023) {3/2025}	8,692.97 (21,312.11) {21,312.11}	22,561.37	95.00
		202	BUXAR THERMAL POWER PLANT (1320 MW) (SJVN) (N18000194)	3-2019	1/2024 (N.A.) {10/2025}	10,439.09 (N.A.) {14,390.09}	11,845.16	91.56

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		203	EASTERN REGION EXPANSION SCHEME: 43 [ERES: 43] (PGCIL) (N18000421)	5-2025	5/2026 (N.A.) {5/2026}	343.00 (N.A.) {343.00}	0.00	-
		204	EASTERN REGION EXPANSION SCHEME: 44 [ERES: 44] (PGCIL) (N18000422)	5-2025	5/2026 (N.A.) {5/2026}	409.00 (N.A.) {409.00}	0.00	-
	RAILWAYS	205	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) (ECR) (220100257)	4-1997	12/2024 (N.A.) {3/2027}	614.45 (614.45) {614.45}	483.57	52.00
		206	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR (ECR) (220100303)	4-2003	12/2014 (N.A.) {12/2026}	2,066.78 (2,087.36) {2,087.36}	2,454.59	73.00
		207	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR (NFR) (N22000087)	9-2006	12/2024 (N.A.) {6/2025}	2,650.00 (2,132.03) {4,351.54}	4,074.75	92.00
		208	SAKRI-HASANPUR ROAD (NL) (ECR) (N22000171)	4-1999	(N.A.) {3/2027}	325.00 (735.20) {735.20}	604.94	78.00
		209	ARARIA-SUPAUL (NL) (ECR) (N22000177)	4-2008	3/2024 (N.A.) {5/2025}	1,605.17 (1,605.17) {1,605.17}	1,749.92	65.00
		210	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA- BARDIBAS(NEPAL) GC (ECR) (N22000181)	4-2009	3/2022 (N.A.) {3/2026}	819.00 (548.00) {783.83}	566.62	75.00
		211	SAMASTIPUR-DARBANGHA (ECR) (N22000329)	5-2015	3/2025 (N.A.) {10/2025}	519.33 (519.33) {519.33}	651.94	80.00
		212	KIUL - GAYA DOUBLING PROJECT (ECR) (N22000349)	12-2015	9/2024 (N.A.) {2/2025}	2,462.11 (1,200.20) {1,771.07}	1,896.91	99.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		213	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE (ECR) (N22000350)	12-2015	12/2024 (N.A.) {12/2025}	2,373.64 (1,491.47) {1,600.00}	1,776.70	77.00
		214	SAGALI VALMIKINAGAR DOUBLING 109.7 KM (ECR) (N22000472)	4-2016	12/2024 (N.A.) {6/2025}	1,215.54 (1,215.54) {1,215.54}	1,595.74	91.00
		215	MUZAFFARPUR SAGALI DOUBLING 100.60 KM (ECR) (N22000473)	4-2016	6/2024 (N.A.) {5/2025}	1,586.22 (1,185.73) {1,300.00}	1,487.54	96.00
		216	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN- BIHARSHARIF, (ECR) (N22000476)	4-1991	3/2023 (N.A.) {5/2025}	1,473.30 (803.09) {2,722.16}	2,794.05	90.00
		217	BARAUNI- BACHWARA 3RD AND 4TH LINE (ECR) (N22000524)	7-2022	7/2027 (N.A.) {12/2025}	486.00 (N.A.) {486.00}	135.31	33.00
		218	JHAJHA - BATIA (UMBRELLA WORK PB#23/2018-19/NR) (ECR) (N22000526)	2-2019	6/2028 (N.A.) {12/2026}	496.47 (N.A.) {496.47}	22.55	-
		219	SONENAGAR BYE PASS LINE FROM CHIRALAPOTHU TO BAGHA BISHUNPUR (ECR) (N22000528)	10-2022	10/2027 (N.A.) {12/2026}	234.00 (223.69) {223.69}	22.57	-
		220	KATIHAR-KUMEDPUR AND KATIHAR- MUKURIA (64.5 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NFR) (N22000570)	8-2022	8/2027 (N.A.) {8/2026}	745.00 (N.A.) {1,500.00}	356.14	35.00
		221	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH-119D (PKG-III) (NHAI) (N24001697)	2-2023	2/2025 (N.A.) {12/2025}	1,358.00 (N.A.) {1,358.00}	228.72	22.00
	ROAD TRANSPORT AND HIGHWAYS							

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		222	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH (NHAI) (N24001698)	8-2022	8/2024 (Dec-2025) {12/2025}	1,198.02 (N.A.) {1,198.02}	43.77	-
		223	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT- GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH-3 (NHAI) (N24001699)	3-2022	12/2024 (Dec-2025) {12/2025}	312.58 (N.A.) {312.58}	205.99	85.88
		224	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO (NHAI) (N24001700)	12-2021	3/2024 (Dec-2024) {12/2024}	552.55 (553.00) {553.00}	378.25	86.60
		225	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU (NHAI) (N24001701)	4-2022	4/2024 (Sep-2025) {9/2025}	1,769.50 (N.A.) {1,769.50}	69.23	-
		226	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT-GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH: (NHAI) (N24001702)	12-2021	9/2024 (N.A.) {6/2025}	184.90 (185.00) {185.00}	166.56	99.78
		227	6 L OF AURANGABAD TO BIHAR- JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N (NHAI) (N24001703)	2-2022	5/2025 (N.A.) {5/2025}	786.81 (787.00) {787.00}	0.00	8.30
		228	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI (NHAI) (N24001704)	3-2021	3/2024 (Sep-2025) {9/2025}	1,020.84 (N.A.) {1,020.84}	163.19	-
		229	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C (NHAI) (N24001705)	3-2022	3/2024 (Dec-2025) {12/2025}	1,485.66 (N.A.) {1,485.66}	35.16	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		230	BAKHTIYARPUR RAJAULI PKG-II FROM KM 54.405 TO KM 101.630 NH20 (NHAI) (N24001709)	9-2020	4/2023 (Dec-2024) {12/2024}	897.45 (N.A.) {1,090.00}	1,037.63	97.85
		231	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO (NHAI) (N24001712)	8-2020	7/2023 (May-2025) {5/2025}	690.00 (N.A.) {690.00}	770.73	98.90
		232	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI?MOTIHARI- RAXAUL SECTION OF NH-28A FRO (NHAI) (N24001715)	12-2018	10/2020 (N.A.) {1/2024}	333.60 (466.59) {461.41}	460.38	100.00
		233	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH 122B FROM KM 29.730 TO KM 72.348 IN STATE OF BIH (MoRTH) (N24001870)	2-2022	11/2024 (N.A.) {11/2025}	624.43 (N.A.) {624.43}	292.16	88.00
		234	WIDENING AND STRENGTHENING FROM KM 70.15 TO KM 121.025 OF NH-80 (MoRTH) (N24001875)	3-2021	1/2025 (N.A.) {7/2025}	477.54 (N.A.) {477.54}	360.27	94.50
		235	WIDENING and STRENGTHENING FROM KM132.895 TO KM 190.15 NH-80 (MoRTH) (N24001876)	3-2021	3/2024 (N.A.) {9/2025}	566.15 (N.A.) {566.15}	258.29	58.60
		236	CONSTRUCTION OF NEW 4-LANE BRIDGE (PARALLEL TO EXISTING VIKRAMASHILA SETU)FROM KM 8+920 TO KM 13+375 (MoRTH) (N24001877)	7-2020	5/2027 (N.A.) {5/2027}	1,110.23 (N.A.) {1,110.23}	478.96	42.90
		237	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH-319A FROM KM 0 TO KM 45 IN STATE OF BIHAR UNDER (MoRTH) (N24001878)	2-2022	12/2024 (N.A.) {7/2025}	427.29 (N.A.) {427.29}	210.22	80.00
		238	CONSTRUCTION OF PROPOSED 4_LANE REVELGUNJ BYPASS NH-19 IN THE STATE OF BIHAR ON EPC MODE CONNECTING (MoRTH) (N24001879)	3-2022	7/2025 (N.A.) {10/2025}	295.24 (N.A.) {295.24}	93.14	63.05

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		239	CONSTRUCTION OF 6- LANE BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD (NH- (NHAI) (N24002062)	3-2023	9/2027 (N.A.) {9/2028}	3,012.27 (N.A.) {3,012.27}	303.67	10.83
		240	BALANCE WORK - WB-10 (GANDAK BRIDGE) KM 402.00 TO KM 440.00 (DEVANPUR - KOTWA) (NHAI) (N24002063)	12-2021	1/2024 (N.A.) {3/2026}	210.05 (N.A.) {210.05}	104.35	69.00
		241	PERMANENT RECTIFICATION OF 3 NOS. OF BLACK SPOTS IN PROJECT HIGHWAY NH-27 OF U.P BORDER - DEWAPUR - (NHAI) (N24002064)	12-2022	12/2025 (N.A.) {12/2025}	381.80 (N.A.) {381.80}	119.56	52.00
		242	4L GREENFIELD ALIGNMENT OF AMAS TO SHIVRAMPUR FROM 0.000 KM. TO 55.002 KM. OF NH 119 D (PKG-I) (NHAI) (N24002065)	2-2022	3/2025 (N.A.) {3/2025}	1,390.92 (N.A.) {1,390.92}	17.54	22.56
		243	4L GREENFIELD ALIGNMENT OF SHIVRAMPUR TO RAMNAGAR FROM KM. 55.002 TO KM. 109.300 OF NH 119 D (PKG-I) (NHAI) (N24002066)	2-2022	7/2025 (N.A.) {7/2025}	1,494.31 (N.A.) {1,494.31}	38.28	4.59
		244	IMPROVEMENT OF 2 LANE WITH PAVED SHOULDER OF STRETCH FROM BIKRAMGANJ DAWATH MELAYABAGH NAWANAGR -DUM (MoRTH) (N24002133)	3-2021	3/2025 (N.A.) {8/2025}	178.63 (N.A.) {178.63}	124.52	96.00
		245	CONSTRUCTION OF 4 LANE ROB AND ITS APPROACHES AT THE LEVEL OF CROSSING (L C NO. 29-B) OF KM 29 (EKAN (MoRTH) (N24002193)	3-2023	7/2026 (N.A.) {7/2026}	201.08 (N.A.) {201.08}	25.42	28.00
		246	CONSTRUCTION OF 6-LANE ELEVATED / EXTRA DOSE CABLE BRIDGE ON RIVER GANGA PARALLEL TO AND WESTERN SID (MoRTH) (N24002194)	1-2024	11/2027 (N.A.) {11/2027}	3,064.45 (N.A.) {3,064.45}	142.38	5.19

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		247	ESTIMATE FOR IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM RAMNAGAR TO ROSEDA FROM (KM 3.500 TO 4 (MoRTH) (N24002195)	1-2022	4/2026 (N.A.) {4/2026}	495.16 (N.A.) {495.16}	134.57	11.50
		248	CONSTRUCTION OF BHABHUA BYPASS FROM CH. 10+800 (DESIGN CH. 10+800) TO CH. 19+860 (DESIGN CH. 18+150) (MoRTH) (N24002196)	2-2022	3/2026 (N.A.) {7/2026}	179.86 (N.A.) {179.86}	26.15	-
		249	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM JUNCTION OF NH-22 NEAR HAJIPUR TO JUNCTION OF NH-12 (MoRTH) (N24002197)	2-2024	2/2026 (N.A.) {2/2026}	226.15 (N.A.) {226.15}	14.44	20.00
		250	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF BH/WBBORDER-AMDABAD-MANIHARI SECTION FROM DESIGN KM (MoRTH) (N24002198)	1-2022	3/2026 (N.A.) {3/2026}	353.27 (N.A.) {353.27}	29.82	2.50
		251	PERMANENT RECTIFICATION OF 4 NOS. OF BLACKSPOTS ON NH 27 OF KOTWA MEHSI MUZAFFARPUR SECTION FROM (NHAI) (N24002220)	12-2022	11/2026 (N.A.) {11/2026}	410.75 (N.A.) {410.75}	50.64	26.20
		252	4L OF GREENFIELD ALIGNMENT FROM KM. 47.000 TO KM. 89.210 OF BALBHADARPUR TO BELA NAWDA SECTION OF NH (NHAI) (N24002221)	2-2022	3/2026 (N.A.) {3/2026}	2,185.75 (N.A.) {2,185.75}	595.71	12.84
		253	PATNA-MUZZAFFARPUR (NHAI) (N24000165)	8-2010	2/2013 (N.A.) {6/2025}	671.30 (N.A.) {671.30}	1,830.13	98.87
		254	4-LANNING OF CHAPRA-HAJIPUR (NHAI) (N24000187)	1-2011	7/2013 (Jan-2026) {1/2026}	575.00 (N.A.) {575.00}	573.48	89.81

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		255	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR (MoRTH) (N24000382)	1-2014	10/2019 (Aug-2025) {8/2025}	675.00 (N.A.) {780.77}	764.76	97.50
		256	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 (NHAI) (N24000480)	12-2015	4/2019 (Mar-2025) {11/2025}	1,041.10 (567.00) {639.58}	553.73	97.68
		257	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 (NHAI) (N24000507)	12-2015	12/2019 (N.A.) {8/2025}	1,167.45 (N.A.) {1,182.94}	775.79	99.43
		258	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 (MoRTH) (N24000531)	2-2016	11/2018 (N.A.) {8/2025}	319.68 (N.A.) {503.28}	453.00	98.80
		259	CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-I-KM 40.00 TO KM 65.400 AND K (MoRTH) (N24000576)	2-2016	5/2016 (N.A.) {8/2025}	178.85 (N.A.) {278.54}	232.61	98.35
		260	PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-III-KM 156.5 (MoRTH) (N24000578)	2-2016	5/2016 (N.A.) {8/2025}	553.30 (N.A.) {706.39}	712.38	98.00
		261	FOUR LANING OF GAYA-HISUA- RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR (MoRTH) (N24000579)	1-2014	10/2016 (N.A.) {8/2025}	1,408.85 (N.A.) {2,138.16}	1,739.19	97.00
		262	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN (NHAI) (N24000665)	3-2017	3/2020 (Dec-2025) {12/2025}	672.89 (893.92) {893.92}	714.74	86.71

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		263	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 (NHAI) (N24000696)	8-2017	2/2022 (Oct-2024) {8/2025}	950.64 (1,161.00) {1,168.33}	1,156.29	99.56
		264	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 (NHAI) (N24000714)	12-2017	10/2024 (Dec-2026) {12/2026}	2,598.00 (N.A.) {1,978.01}	1,427.02	77.90
		265	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I (NHAI) (N24000723)	1-2018	12/2021 (Aug-2025) {12/2025}	573.70 (644.50) {726.99}	509.99	82.51
		266	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER (NHAI) (N24000813)	3-2018	11/2021 (Dec-2024) {8/2025}	496.20 (470.18) {470.18}	399.41	98.50
		267	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND (MoRTH) (N24000943)	9-2018	6/2024 (N.A.) {5/2026}	1,478.40 (N.A.) {1,478.40}	972.42	75.15
		268	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 (MoRTH) (N24001201)	2-2019	9/2024 (N.A.) {9/2026}	2,926.42 (N.A.) {2,926.42}	1,354.63	59.29
		269	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT (NHAI) (N24001303)	10-2013	12/2020 (Dec-2024) {12/2024}	649.90 (N.A.) {750.00}	711.53	98.30
		270	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE (NHAI) (N24001304)	10-2013	11/2020 (Dec-2024) {12/2024}	446.97 (598.48) {740.50}	638.80	96.30

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		271	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA (NHAI) (N24001305)	10-2013	11/2020 (Dec-2024) {12/2024}	464.09 (605.53) {765.12}	698.25	97.30
		272	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N (NHAI) (N24001371)	10-2019	8/2023 (Apr-2026) {4/2026}	1,101.99 (N.A.) {1,101.99}	890.20	78.48
	<u>URBAN DEVELOPMENT</u>	273	PATNA METRO RAIL CORPORATION LIMITED (PATNA METRO RAI) (N28000148)	2-2019	6/2024 (N.A.) {6/2024}	13,365.77 (N.A.) {13,925.50}	3,318.85	45.31
	<u>WATER RESOURCES</u>	274	SEWER NETWORK SPS AND STP BEGUSARAI (BUIDCO) (N30000026)	3-2018	7/2021 (Dec-2019) {4/2025}	230.06 (N.A.) {230.06}	261.47	97.00
		275	I AND D AND STP WORKS FOR BHAGALPUR (BUIDCO) (N30000027)	10-2017	9/2020 (Nov-2020) {9/2025}	254.13 (413.29) {413.29}	126.67	90.00
		276	SEWER NETWORKS SPS AND STP HAJIPUR (BUIDCO) (N30000035)	3-2018	8/2021 (Mar-2018) {9/2025}	305.19 (N.A.) {305.19}	346.46	95.00
		277	SEWER NETWORKS, SPS AND STP, MUNGER (BUIDCO) (N30000036)	3-2018	10/2021 (Mar-2018) {6/2024}	294.02 (350.79) {522.85}	428.70	100.00
		278	SAIDPUR SEWER NETWORK PATNA (BUIDCO) (N30000039)	4-2015	1/2021 (N.A.) {6/2022}	268.63 (N.A.) {493.85}	491.13	100.00
		279	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK (BUIDCO) (N30000044)	3-2017	5/2021 (Mar-2017) {2/2023}	277.42 (253.98) {277.42}	355.31	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
CHHATTISGARH	COAL	280	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA (BUIDCO) (N30000050)	8-2017	6/2022 (N.A.) {12/2025}	578.89 (453.83) {578.89}	165.88	53.00
		281	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA (BUIDCO) (N30000051)	8-2017	6/2022 (N.A.) {12/2025}	824.00 (734.09) {824.00}	385.33	55.00
		282	GEVRA EXPANSION OCP (SECL) (35-70) MTY (SECL) (060100093)	6-2010	3/2023 (Mar-2026) {3/2026}	11,816.40 (N.A.) {11,816.40}	6,617.04	77.20
		283	PELMA OCP(15.00MTY) (SECL) (N06000045)	10-2022	3/2023 (N.A.) {3/2033}	1,624.59 (N.A.) {1,725.04}	15.53	17.00
		284	CHHAL OC SEAM -III (6.00 MTY) (SECL) (N06000104)	12-2013	3/2022 (Jun-2025) {6/2025}	610.63 (N.A.) {610.63}	576.48	85.00
		285	AMERA OC RCE (SECL) (N06000123)	2-2015	3/2018 (Mar-2026) {3/2026}	335.97 (N.A.) {335.97}	87.47	42.00
		286	AMGAON OPENCASST PROJECT RCE (SECL) (N06000135)	7-2015	3/2020 (Mar-2026) {3/2026}	316.10 (N.A.) {316.10}	188.33	71.00
		287	MAHAMAYA OPENCASST PROJECT (SECL) (N06000164)	5-2018	3/2026 (N.A.) {3/2026}	410.26 (N.A.) {410.26}	180.94	38.00
		288	JHIRIA WEST OPENCASST PROJECT (SECL) (N06000166)	1-2024	3/2029 (N.A.) {3/2029}	366.94 (N.A.) {366.94}	33.67	41.00
		289	BAROUD OC EXPANSION (3-10 MTY) (SECL) (N06000197)	8-2020	3/2029 (N.A.) {3/2029}	2,309.80 (N.A.) {2,309.80}	916.35	47.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		290	JAMPALI OCP RCE (SECL) (N06000198)	5-2020	3/2024 (Mar-2025) {6/2025}	278.64 (N.A.) {278.64}	210.90	82.00
		291	PORDA CHINTAPANI OCP (10 MTY) (SECL) (N06000199)	12-2020	3/2029 (N.A.) {3/2029}	2,310.12 (N.A.) {2,310.12}	83.30	10.00
		292	DIPKA OC EXPANSION 40 MTY (SECL) (N06000200)	12-2020	3/2029 (N.A.) {3/2029}	5,241.40 (N.A.) {5,241.40}	2,821.87	37.30
		293	JAGANNATHPUR OC RCE (3.0 MTY) (SECL) (N06000232)	7-2016	3/2020 (Mar-2026) {3/2026}	459.49 (N.A.) {459.49}	264.00	92.00
		294	KATKONA RO UG PROJECT (1.74 MTY) (SECL) (N06000274)	1-2023	3/2029 (N.A.) {3/2029}	329.22 (N.A.) {329.22}	60.38	2.00
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	295	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. (CPWD EDUCATION) (N28000141)	3-2020	7/2022 (Feb-2024) {3/2024}	808.62 (879.22) {808.62}	640.70	100.00
	<u>POWER</u>	296	WESTERN REGION EXPANSION SCHEME XXV (PGCIL) (N18000350)	2-2023	11/2023 (N.A.) {8/2025}	385.84 (N.A.) {385.84}	370.41	95.00
		297	LARA SUPER THERMAL POWER PROJECT, STAGE-II (2X800 MW) (NTPC) (N18000381)	8-2023	6/2028 (N.A.) {6/2028}	15,530.00 (N.A.) {15,530.00}	2,124.99	6.50
	<u>RAILWAYS</u>	298	KIRANDUL - JAGDALPUR DOUBLING (ECOR) (N22000318)	12-2012	3/2020 (N.A.) {3/2024}	1,588.70 (N.A.) {1,553.11}	1,534.73	94.90
		299	JHARSUGUDA-BILASPUR 4TH LINE (SECR) (N22000484)	4-2015	10/2024 (Dec-2023) {12/2025}	2,140.34 (2,135.34) {2,135.34}	2,306.80	88.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		300	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I (IRCON) (N22000489)	4-2013	9/2018 (N.A.) {3/2026}	3,055.00 (N.A.) {3,438.39}	3,117.24	93.00
		301	Gauge conversion of Raipur(Kendri)- Dhamtari and Abhanpur-Rajim branch (67.20 km) (SECR) (N22000572)	7-2011	10/2024 (N.A.) {6/2025}	1,171.30 (N.A.) {1,171.30}	617.69	82.00
		302	NIPANIA-BHATAPRA (14.4 KM) 4TH LINE (PB#72/NR/2022-23) (SECR) (N22000573)	9-2022	12/2026 (N.A.) {12/2026}	170.49 (N.A.) {170.49}	0.13	2.00
		303	4TH LINE - BHATAPARA-HATHBAND (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000574)	12-2022	12/2026 (N.A.) {12/2026}	177.03 (N.A.) {177.03}	14.52	2.00
		304	4TH LINE - BHILAI-BHILAI NAGAR (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000575)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {177.34}	1.72	2.00
		305	4TH LINE - DADHAPARA-BELHA (9.2 KM) (PB#72/NR/2022-23) (SECR) (N22000576)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {169.06}	17.96	30.00
		306	4TH LINE - RAJNANDGAON- DONGARHGARH (31.2 KM) (PB#72/NR/2022-23) (SECR) (N22000577)	9-2022	9/2026 (N.A.) {9/2026}	328.34 (N.A.) {328.34}	38.80	20.00
		307	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (N22000579)	9-2022	9/2026 (N.A.) {9/2026}	167.64 (N.A.) {167.64}	0.00	-
		308	DOUBLING OF BORIDAND - AMBIKAPUR (SURAJPUR) (SECR) (N22000580)	6-2022	6/2030 (N.A.) {3/2027}	1,376.20 (1,242.94) {1,242.94}	217.79	12.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		309	DALLIRAJHARA - ROWGHAT (95 KM) {PART OF DALLIRAJHARA-JAGDALPUR (235 KM)} (RVNL) (N22000602)	3-2008	6/2025 (N.A.) {6/2025}	1,627.56 (N.A.) {1,627.56}	1,349.09	-
		310	CHIRIMIRI-NAGPUR HALT (SECR) (N22000616)	10-2018	6/2030 (N.A.) {6/2030}	241.00 (N.A.) {241.00}	0.00	-
	ROAD TRANSPORT AND HIGHWAYS	311	DEVELOPMENT OF SIX LANE SARGI- BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA (NHAI) (N24001588)	12-2021	1/2025 (N.A.) {12/2025}	1,470.73 (N.A.) {1,470.73}	700.39	83.00
		312	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA (NHAI) (N24001593)	11-2021	9/2024 (N.A.) {4/2026}	1,368.19 (N.A.) {1,368.19}	928.78	96.50
		313	4 LANE OF BILASPUR TO URGAL PROJECT (KM 0.00 TO KM 70.2) OF NH- 130A (NHAI) (N24001611)	4-2020	3/2024 (N.A.) {12/2025}	1,855.59 (2,523.86) {2,523.86}	730.18	94.27
		314	UP GRADATION OF NH 930 SHERPAR TO KOHKA FROM KM 67.880 TO KM 114.860 TO TWO LANE WITH PAVED SHOULDER (MoRTH) (N24001917)	3-2020	5/2024 (N.A.) {6/2025}	278.97 (N.A.) {278.97}	206.61	87.00
		315	UP GRADATION OF NH 130C ABHANPUR TO PAUND FROM NK KM 0.000 TO KM. 40.380 TO TWO LANE WITH PAVED SHOU (MoRTH) (N24001919)	12-2020	9/2023 (Feb-2025) {6/2025}	193.16 (N.A.) {193.16}	103.83	81.00
		316	UPGRADATION OF NH 130A MUNGELI TO PONDY FROM NH KM. 51.600 TO KM. 77.870 KM. 80.970 TO 96.970 TO 2 (MoRTH) (N24001920)	3-2021	9/2024 (N.A.) {5/2025}	218.57 (N.A.) {218.57}	136.26	89.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		317	DEVELOPMENT OF SIX LANE BASANWAHI-MARANGPURI OF NH 130 CD FROM KM.99+500 TO 124+661 UNDER RAIPUR VIS (NHAI) (N24002017)	3-2022	10/2025 (N.A.) {9/2026}	1,307.16 (N.A.) {1,307.16}	252.68	36.23
		318	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 1 SECTION OF NH 53 FROM CH 0.000 TO CH 44.50 (NHAI) (N24002045)	6-2022	7/2025 (N.A.) {7/2025}	1,828.00 (N.A.) {1,828.00}	575.00	47.51
		319	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 2 SECTION OF NH 53 FROM CH 44+500 TO CH.92+230 I (NHAI) (N24002046)	6-2022	5/2025 (N.A.) {5/2025}	1,958.94 (1,959.00) {1,958.94}	725.20	40.88
		320	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 (MoRTH) (N24001217)	1-2016	8/2016 (N.A.) {6/2025}	497.14 (572.66) {572.66}	385.27	60.00
		321	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION (MoRTH) (N24001221)	1-2016	10/2016 (N.A.) {3/2025}	624.98 (N.A.) {731.50}	620.67	100.00
		322	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI (MoRTH) (N24001222)	3-2016	7/2016 (N.A.) {12/2025}	452.94 (N.A.) {435.61}	322.59	70.00
		323	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. (MoRTH) (N24001227)	3-2018	1/2019 (N.A.) {5/2025}	349.03 (N.A.) {349.03}	316.52	98.00
		324	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH- 130A (MoRTH) (N24001228)	11-2017	5/2019 (N.A.) {5/2025}	188.80 (N.A.) {188.80}	136.81	97.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>STEEL</u>	325	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 (NMDC) (N12000124)	11-2015	6/2023 (Jul-2024) {12/2025}	2,907.00 (5,427.06) {5,427.06}	2,955.56	80.70
		326	SCREENING PLANT-III AT KIRANDUL (NMDC) (N12000127)	3-2021	8/2024 (N.A.) {1/2026}	2,092.97 (2,718.84) {2,718.84}	1,503.52	71.31
		327	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (NMDC) (N12000130)	7-2021	11/2024 (N.A.) {12/2025}	282.44 (349.75) {349.75}	238.99	81.86
		328	REPLACEMENT OF CONVERTER VESSELS, TRUNNION RINGS, SUPPORT SYSTEM AND INSTALLATION OF SECONDARY EMISS (SAIL) (N12000131)	10-2023	6/2026 (N.A.) {6/2026}	471.83 (N.A.) {471.83}	109.38	31.06
		329	REBUILDING OF COKE OVEN BATTERY NO.7 AND 8 OF BHILAI STEEL PLANT (SAIL) (N12000134)	11-2023	10/2025 (N.A.) {10/2025}	884.10 (N.A.) {884.10}	411.94	72.24
		330	REPLACEMENT OF HOT LEVELLER-1 OF PLATE MILL AT BHILAI STEEL PLANT (SAIL) (N12000137)	7-2024	7/2026 (N.A.) {7/2026}	198.62 (N.A.) {198.62}	0.00	6.76
	<u>URBAN DEVELOPMENT</u>	331	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V- 68 TYPE-VI-5 SHOPS COMMUNI (CPWD) (N28000149)	5-2019	9/2020 (Oct-2024) {10/2024}	299.97 (299.97) {299.97}	272.05	93.00
	<u>CIVIL AVIATION</u>	332	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR (AAI) (N04000076)	11-2016	4/2020 (Apr-2024) {4/2024}	303.80 (374.98) {351.21}	344.93	100.00
DELHI								

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DPIIT</u>	333	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE (IICC FOR DPIIT) (N40000002)	11-2017	12/2019 (N.A.) {4/2024}	4,773.00 (N.A.) {5,401.00}	4,969.89	100.00
	<u>FINANCE</u>	334	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA (NPCC) (N07000001)	7-2018	4/2022 (N.A.) {4/2022}	228.50 (N.A.) {220.27}	176.28	85.00
	<u>HOME AFFAIRS</u>	335	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI (CPWD FOR MHA) (N28000071)	10-2013	10/2019 (N.A.) {9/2024}	1,219.21 (2,091.53) {2,091.53}	1,947.12	100.00
		336	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI (CPWD FOR MHA) (N45000002)	6-2019	7/2022 (N.A.) {9/2025}	277.35 (N.A.) {277.35}	111.00	66.00
	<u>RAILWAYS</u>	337	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE (NR) (N22000281)	4-2012	3/2023 (N.A.) {12/2027}	586.36 (N.A.) {699.00}	178.54	45.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	338	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR (NHAI) (N24001771)	6-2020	12/2024 (N.A.) {12/2024}	1,479.22 (N.A.) {1,479.22}	1,491.26	99.00
		339	6L ACCESS CONTROLLED HIGHWAY FROM DND MAHARANI BAGH JN. WITH JAITPUR PUSHTA ROAD OF NH 148NA FROM (NHAI) (N24001773)	5-2020	7/2024 (N.A.) {9/2025}	1,467.44 (N.A.) {1,942.89}	1,214.36	91.58
		340	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-)0.70 (NHAI) (N24001777)	7-2020	10/2023 (N.A.) {6/2025}	2,171.80 (N.A.) {2,171.80}	958.13	99.99

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		341	DWARKA EXPRESSWAY FROM KM - 0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) (NHAI) (N24001779)	3-2018	9/2022 (N.A.) {9/2025}	2,507.00 (N.A.) {3,030.73}	1,155.70	95.05
		342	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21- DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O (NHAI) (N24001781)	1-2018	10/2021 (N.A.) {8/2025}	2,067.67 (N.A.) {2,160.00}	1,496.49	99.40
		343	DEVELOPMENT OF 6L UER II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM (NHAI) (N24001825)	7-2020	10/2023 (N.A.) {8/2025}	1,894.96 (N.A.) {1,894.96}	741.88	98.25
	TELECOMMUNI CATIONS	344	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT (CPWD FOR TELECO) (N28000115)	10-2014	3/2018 (N.A.) {10/2025}	248.20 (N.A.) {248.20}	236.97	98.00
	URBAN DEVELOPMENT	345	DELHI MRTS PHASE-III (DMRC) (N28000056)	9-2011	3/2016 (Aug-2021) {8/2021}	38,585.00 (43,095.35) {40,180.91}	40,685.45	100.00
		346	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR (NBCC) (N28000105)	7-2016	(N.A.) {}	2,694.00 (N.A.) {2,694.00}	2,247.61	98.00
		347	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I (CPWD) (N28000128)	10-2016	7/2021 (N.A.) {6/2024}	1,180.00 (N.A.) {1,100.80}	36.69	2.00
		348	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I (CPWD) (N28000129)	10-2016	3/2022 (N.A.) {6/2024}	1,128.00 (N.A.) {1,128.00}	740.35	68.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		349	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS (DMRC) (N28000135)	7-2019	3/2025 (N.A.) {3/2026}	24,948.65 (N.A.) {24,948.65}	16,369.75	67.19
		350	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI (CPWD) (N28000153)	1-2022	11/2024 (Aug-2025) {8/2025}	646.52 (N.A.) {646.52}	506.00	94.00
		351	REDEVELOPMENT OF GPRA AT NETAJI NAGAR NEW DELHI PACKAGE 2 (NBCC) (N28000156)	10-2016	3/2024 (Aug-2025) {3/2025}	1,536.72 (N.A.) {1,536.72}	507.85	91.50
	<u>WATER RESOURCES</u>	352	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD ? 10MG/L (DJB) (N30000014)	3-2017	12/2022 (N.A.) {3/2025}	665.78 (N.A.) {665.78}	782.51	100.00
<u>GOA</u>	<u>CIVIL AVIATION</u>	353	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. (AAI) (N04000095)	11-2017	9/2021 (Aug-2025) {8/2025}	255.69 (255.69) {255.69}	125.92	86.75
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	354	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. (CPWD EDUCATION) (N42000002)	5-2019	8/2021 (N.A.) {12/2024}	303.90 (N.A.) {390.40}	360.00	99.30
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	355	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM. 508.000 TO KM. 513.150 INCLUDING APPROACHES ON N (MoRTH) (N24002181)	4-2023	4/2026 (N.A.) {4/2026}	641.46 (N.A.) {641.46}	0.00	-
<u>GUJARAT</u>	<u>CIVIL AVIATION</u>	356	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT (AAI) (N04000088)	1-2018	8/2022 (Dec-2024) {12/2024}	1,405.00 (N.A.) {1,405.00}	1,304.63	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		357	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. (AAI) (N04000093)	8-2018	2/2021 (Mar-2025) {3/2025}	353.25 (N.A.) {353.25}	348.78	100.00
		358	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1. (AAI) (N04000099)	6-2022	12/2025 (N.A.) {12/2025}	1,305.00 (1,143.95) {1,143.95}	648.65	61.00
	COAL	359	50 MW WIND POWER PROJECT PART OF 150 MW SECI HYBRID (NLC) (N06000292)	7-2022	6/2025 (Jan-2026) {1/2026}	383.84 (N.A.) {383.84}	303.50	41.00
	PETROLEUM	360	REDEVELOPMENT OF SANTHAL FIELD (ONGC) (N16000279)	2-2017	3/2026 (N.A.) {3/2026}	1,162.56 (N.A.) {1,162.56}	1,156.90	94.10
		361	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY (IOCL) (N16000382)	11-2019	5/2023 (Mar-2024) {7/2025}	5,251.00 (5,894.00) {5,894.00}	4,689.83	99.70
		362	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY (IOCL) (N16000409)	9-2020	8/2024 (Dec-2025) {12/2025}	18,936.00 (N.A.) {18,936.00}	11,161.74	82.50
		363	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM (IOCL) (N16000411)	10-2020	8/2023 (Jun-2025) {6/2025}	1,614.00 (N.A.) {1,614.00}	1,139.60	100.00
		364	REDEVELOPMENT OF LINCH FIELD (ONGC) (N16000428)	4-2021	3/2025 (N.A.) {7/2025}	631.03 (860.04) {860.04}	435.64	76.60
		365	REDEVELOPMENT OF SOBHASAN COMPLEX (ONGC) (N16000431)	8-2021	2/2026 (N.A.) {2/2026}	885.63 (1,286.67) {1,286.67}	584.23	71.40

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		366	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD (ONGC) (N16000444)	1-2022	11/2024 (N.A.) {11/2025}	621.40 (N.A.) {621.40}	137.69	21.40
		367	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT (IOCL) (N16000454)	1-2022	9/2024 (N.A.) {5/2026}	328.00 (N.A.) {328.00}	101.12	51.30
		368	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT (ONGC) (N16000477)	5-2022	2/2025 (N.A.) {9/2025}	249.43 (N.A.) {249.43}	209.42	93.70
		369	KALOL REDEVELOPMENT PROJECT (ONGC) (N16000481)	8-2022	3/2027 (N.A.) {3/2027}	1,487.41 (N.A.) {1,487.41}	952.00	60.00
		370	OLD PIPE LINE REPLACEMENT (OPRP) GROUP-A (ONGC) (N16000483)	7-2021	7/2025 (N.A.) {7/2025}	173.03 (N.A.) {169.84}	143.32	86.50
		371	REVAMPING OF SV STATIONS, GAS TERMINAL AND KRIBHCO TERMINAL (ONGC) (N16000514)	11-2022	8/2026 (N.A.) {8/2026}	837.34 (N.A.) {837.34}	187.10	46.70
	POWER	372	GUJARAT 200 MW (GUVNL TENDER) (NTPC) (N18000295)	1-2021	7/2022 (Mar-2026) {3/2026}	842.27 (1,049.61) {1,049.61}	779.79	66.00
		373	Bagodara Solar Power Project (SJVN) (N18000297)	5-2021	10/2022 (N.A.) {12/2025}	339.35 (N.A.) {339.35}	317.59	51.86
		374	DAYAPAR WIND ENERGY PROJECT 150MW (NTPC) (N18000319)	11-2021	5/2023 (Aug-2025) {8/2025}	937.80 (N.A.) {937.80}	803.82	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		375	DAYAPAR WIND ENERGY PROJECT 200MW (NTPC) (N18000345)	7-2022	3/2025 (Jan-2026) {1/2026}	1,316.02 (N.A.) {1,316.02}	324.36	28.00
		376	KHAVDA 1255MW SOLAR PROJECT (KHAVDA SOLAR PARK) (NTPC) (N18000346)	9-2022	9/2024 (Feb-2026) {2/2026}	7,179.54 (7,235.79) {7,235.79}	5,220.20	89.00
		377	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) (NTPC) (N18000349)	11-2022	3/2024 (Mar-2026) {3/2026}	1,442.60 (N.A.) {1,442.60}	793.56	2.51
		378	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK (PGCIL) (N18000357)	3-2023	12/2024 (N.A.) {7/2025}	922.30 (N.A.) {922.30}	830.14	90.50
		379	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT (PGCIL) (N18000358)	3-2023	3/2025 (N.A.) {7/2025}	815.12 (N.A.) {815.12}	758.09	100.00
		380	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK (PGCIL) (N18000359)	3-2023	12/2024 (N.A.) {8/2025}	966.79 (N.A.) {966.79}	870.10	93.60
		381	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000360)	3-2023	3/2025 (N.A.) {9/2025}	1,167.55 (N.A.) {1,167.55}	957.39	90.00
		382	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000361)	3-2023	3/2025 (N.A.) {9/2025}	2,820.99 (N.A.) {2,820.99}	2,418.00	82.60
		383	KHAVDA 1200MW (4X300MW) IN KHAVDA RE PARK (NTPC) (N18000365)	6-2023	12/2024 (Jan-2026) {1/2026}	6,283.81 (N.A.) {6,283.81}	1,828.84	42.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		384	DAYAPAR WIND- III (HYBRID TRANCHE-V) (NTPC) (N18000366)	5-2023	1/2025 (Mar-2026) {3/2026}	1,095.01 (N.A.) {1,095.01}	382.54	18.00
		385	TS FOR EVACUATION OF POWER FROM POTENTIAL RE ZONE IN KHAVDA AREA OF GUJARAT UNDER PH-IV PART E3 (PGCIL) (N18000383)	7-2023	7/2025 (N.A.) {9/2025}	334.00 (N.A.) {334.00}	63.46	21.00
		386	TS FOR EVACUATION OF ADDITIONAL 7GW RE POWER FROM KHAVDA RE PARK UNDER PHASE-III PART B [VATAMAN TRA (PGCIL) (N18000384)	12-2023	12/2025 (N.A.) {6/2026}	3,752.00 (N.A.) {3,752.00}	1,463.23	20.00
		387	TS FOR EVACUATION OF POWER FROM 7GW REZ IN KHAVDA AREA UNDER PHASE-IV PART E2 (PGCIL) (N18000390)	5-2024	5/2026 (N.A.) {2/2026}	679.00 (N.A.) {679.00}	67.90	16.80
		388	AUGMENTATION OF TRANSFORMATION CAPACITY AT JAM KHAMBHALIYA PS [GIS] [SPV NAME POWERGRID JAM KHAMBHAL (PGCIL) (N18000398)	10-2024	7/2026 (N.A.) {7/2026}	329.00 (N.A.) {329.00}	9.87	1.00
		389	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000400)	10-2024	10/2026 (N.A.) {10/2026}	4,766.00 (N.A.) {4,766.00}	333.62	5.10
		390	PROVISION OF DYNAMIC REACTIVE COMPENSATION AT KHAVDA POOLING STATION 1 [KPS1] AND KHAVDA POOLING STA (PGCIL) (N18000402)	11-2024	11/2026 (N.A.) {11/2026}	501.00 (N.A.) {501.00}	5.01	1.00
		391	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000405)	11-2024	5/2029 (N.A.) {5/2029}	24,819.00 (N.A.) {24,819.00}	1,240.30	1.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		392	600 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000406)	4-2022	3/2026 (Mar-2023) {11/2026}	4,100.45 (N.A.) {4,100.45}	11.05	5.00
		393	AUGMENTATION OF TRANSFORMATION CAPACITY AT KPS2 AND KPS2 (PGCIL) (N18000411)	3-2025	3/2027 (N.A.) {3/2027}	466.00 (N.A.) {466.00}	6.52	-
		394	AUGMENTATION OF BANASKANTHA (RAGHANESDA) PS (GIS) (PGCIL) (N18000412)	3-2025	3/2027 (N.A.) {3/2027}	172.00 (N.A.) {172.00}	1.72	-
	RAILWAYS	395	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) (WR) (N22000142)	4-2011	3/2021 (Oct-2026) {10/2026}	844.10 (844.10) {844.10}	605.51	41.00
		396	ANAND GODHRA DOUBLING PROJECT 79 KMS (WR) (N22000504)	4-2017	12/2024 (Jun-2025) {6/2025}	692.26 (692.26) {692.26}	688.88	100.00
		397	4TH LINE BETWEEN BAREJADI NANDEJ (GERATPUR)- SANAND (38.20 KM) (AHMEDABAD BYPASS). (WR) (N22000532)	2-2023	3/2027 (Mar-2027) {3/2027}	961.67 (961.67) {961.67}	103.15	16.00
		398	QUADRUPLING BETWEEN GANDHIDHAM - ADIPUR WITH Y CONNECTION AT ADIPUR FOR PROVIDING DIRECT ENTRY TOWAR (WR) (N22000533)	2-2023	12/2025 (Dec-2025) {12/2025}	152.44 (152.44) {152.44}	19.54	63.00
		399	RAJKOT-KANALUS (111.20 KM) (WR) (N22000535)	10-2021	10/2026 (Jun-2026) {6/2026}	1,080.58 (1,080.58) {1,080.58}	315.70	72.00
		400	HIMMATNAGAR-KHEDBRAHMA (54.83 KM) (WR) (N22000537)	6-2022	8/2025 (Jul-2025) {7/2025}	354.99 (482.42) {482.42}	322.59	96.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		401	PETLAD-BHADLAN (22.5 KM) (WR) (N22000538)	5-2022	5/2030 (Dec-2025) {12/2025}	202.50 (307.12) {307.12}	81.76	8.00
		402	NADIAD-PETLAD (37.26 KM) (WR) (N22000539)	5-2022	6/2030 (N.A.) {12/2025}	335.34 (461.91) {461.91}	74.35	7.00
		403	SAMLAYA-TIMBA ROAD (53.53 KM) (WR) (N22000540)	2-2023	3/2030 (Jul-2026) {7/2026}	670.00 (670.17) {670.17}	101.79	12.00
		404	SAMNI-JAMBUSAR (24.08 KM) (WR) (N22000541)	5-2022	3/2030 (Dec-2025) {12/2025}	216.72 (349.93) {349.93}	86.46	25.00
		405	VIJAPUR-AMBLIYASAN (41.53 KM) (WR) (N22000547)	5-2022	8/2025 (Oct-2025) {10/2025}	309.81 (415.38) {415.38}	263.13	85.00
		406	ADRAJ MOTI-VIAJAPUR (39.75 KM) (WR) (N22000548)	5-2022	8/2025 (Sep-2025) {9/2025}	296.54 (N.A.) {296.54}	178.95	80.00
		407	NEW BG LINE BETWEEN NALIYA-JAKHAU PORT (WR) (N22000550)	2-2023	1/2028 (Dec-2026) {12/2026}	410.46 (410.46) {410.46}	5.89	2.00
		408	NEW BG LINE INTERSECTION (5 NOS) BETWEEN GERATPUR-SANAND AND BOTAD-AHMEDABAD (16.51 KM) (PB29/NR/20) (WR) (N22000551)	10-2022	10/2027 (Oct-2027) {10/2027}	437.21 (N.A.) {437.21}	43.26	9.00
		409	TARANGA HILL ABU ROAD VIA AMBAJI NEW LINE (NWR) (N22000592)	7-2022	7/2030 (N.A.) {12/2026}	2,798.16 (N.A.) {2,798.16}	1,103.16	12.50
		410	JUNAGARH -VISAVADAR (42.28) KM (RVNL) (N22000600)	6-2022	9/2028 (N.A.) {12/2026}	493.00 (N.A.) {492.83}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		411	MODASA- SHAMLAJI NEW LINE (MM OF AHMEDABAD-HIMMATNAGAR- UDAIPUR (299.2 KM)) (WR) (N22000622)	9-2012	3/2027 (Mar-2026) {3/2026}	261.68 (261.68) {261.68}	202.70	58.00
	ROAD TRANSPORT AND HIGHWAYS	412	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT (MoRTH) (N24001427)	6-2020	4/2023 (Sep-2024) {9/2024}	166.21 (N.A.) {166.21}	97.12	93.00
		413	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 (NHAI) (N24001443)	5-2020	3/2024 (Jul-2025) {7/2025}	690.30 (929.95) {929.95}	841.74	94.22
		414	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION (NHAI) (N24001444)	5-2020	1/2024 (Jul-2025) {7/2025}	882.00 (1,229.37) {1,229.37}	1,042.67	91.54
		415	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB (NHAI) (N24001445)	5-2020	7/2023 (Jun-2025) {6/2025}	691.52 (903.85) {903.85}	893.47	99.45
		416	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG (NHAI) (N24001446)	5-2020	12/2023 (Jun-2025) {6/2025}	894.00 (1,261.58) {1,261.58}	1,166.51	97.28
		417	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 (NHAI) (N24001515)	9-2020	2/2024 (N.A.) {3/2026}	1,542.02 (N.A.) {1,542.02}	989.98	68.50
		418	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 (NHAI) (N24001516)	9-2020	2/2024 (Aug-2025) {8/2025}	1,185.69 (N.A.) {1,185.69}	980.41	93.52

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		419	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 (NHAI) (N24001518)	11-2019	9/2023 (N.A.) {8/2025}	1,669.56 (N.A.) {1,669.56}	1,094.58	98.12
		420	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 (NHAI) (N24001519)	9-2020	11/2023 (N.A.) {7/2025}	1,198.55 (N.A.) {1,198.55}	911.23	95.78
		421	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 (NHAI) (N24001520)	11-2019	5/2024 (N.A.) {8/2025}	1,604.06 (N.A.) {1,604.06}	1,245.52	95.73
		422	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT (NHAI) (N24001785)	3-2022	6/2025 (N.A.) {6/2025}	1,373.06 (1,085.00) {1,373.06}	662.04	90.67
		423	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU (NHAI) (N24001786)	3-2021	3/2024 (N.A.) {3/2026}	1,259.00 (2,652.24) {1,910.00}	278.29	34.08
		424	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA (NHAI) (N24001789)	7-2020	8/2023 (N.A.) {7/2025}	1,710.30 (2,665.08) {1,927.00}	908.08	90.56
		425	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH-754K (AJ- RGBS-PACKAGE-3) (NHAI) (N24001790)	2-2020	8/2023 (Dec-2024) {12/2024}	752.30 (N.A.) {766.20}	452.13	98.14
		426	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II) (NHAI) (N24001792)	3-2021	9/2022 (N.A.) {1/2025}	536.03 (N.A.) {536.03}	480.77	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		427	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) (NHAI) (N24001793)	3-2021	9/2022 (N.A.) {5/2025}	485.75 (N.A.) {485.75}	393.88	99.57
		428	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH-754K (AJ-RGBS-PACKAGE-4) (NHAI) (N24001794)	2-2020	3/2023 (Dec-2024) {12/2024}	778.15 (N.A.) {785.67}	547.22	99.70
		429	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE (NHAI) (N24001827)	3-2022	3/2023 (N.A.) {4/2025}	162.73 (N.A.) {162.73}	131.79	100.00
		430	UPGRADATION AND STRENGTHENING TO 2 LANE PS FROM KM 95/500 TO KM 129/775 OF NH 168 G IDAR BHILODA SA (MoRTH) (N24002014)	9-2022	12/2023 (Dec-2025) {12/2025}	237.28 (N.A.) {237.28}	0.34	-
		431	UPGRADATION TO 4L PS DIVIDED CARRIAGEWAY FROM PATAN (NEAR RAJPUR) TO GOJARIYA FROM KM 52.000 TO KM 1 (NHAI) (N24002034)	12-2021	3/2025 (N.A.) {3/2025}	1,181.34 (1,181.00) {1,181.34}	555.81	79.50
		432	WIDENING TO 6L OF EXISTING 4L JETPUR - GONDAL - RAJKOT SECTION FROM KM. 117.600 TO KM. 185.00 ON NH- (NHAI) (N24002035)	9-2023	9/2025 (N.A.) {9/2025}	2,070.44 (N.A.) {2,070.44}	545.53	37.86
		433	UPGRADATION OF DHORAJI JAMKANDORNA KALAVAD SECTION OF NH 927D FROM DESIGN CHAINAGE KM 00 TO KM 58.11 (MoRTH) (N24002117)	10-2022	2/2024 (Feb-2026) {2/2026}	246.60 (291.00) {291.00}	27.57	15.00
		434	UPGRADATION TO TWO LANE WITH PAVED SHULDER CONFIGURATION FROM KM 00 TO 47 OF NH 351 MAHUVA TO BADHA (MoRTH) (N24002118)	12-2022	2/2024 (Aug-2025) {8/2025}	173.06 (N.A.) {219.00}	0.15	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		435	WORK OF DEVELOPMENT AND CONSTRUCTION OF ELEVATED CORRIDOR FROM KM 38/660 TO KM 42/690 (ISCON JUNCTION (MoRTH) (N24002182)	3-2023	3/2026 (N.A.) {3/2026}	530.20 (N.A.) {530.20}	0.00	-
		436	WIDENING 2 LANE TO 4-LANE FROM KM 92/320 TO KM 115/320 (VAV CHOKDI- SATLASANA TO TO VRUNDAVAN CHOKDI, (MoRTH) (N24002183)	3-2022	3/2026 (N.A.) {3/2026}	151.13 (N.A.) {171.00}	0.00	-
		437	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST (NHAI) (N24000569)	5-2016	9/2019 (May-2024) {6/2025}	723.64 (N.A.) {723.64}	562.31	97.00
		438	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 (NHAI) (N24000592)	7-2016	7/2020 (N.A.) {5/2025}	829.97 (N.A.) {829.97}	486.93	96.98
		439	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. (NHAI) (N24000649)	1-2017	12/2020 (Oct-2025) {10/2025}	1,251.11 (1,527.75) {1,527.75}	685.73	91.08
		440	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR (NHAI) (N24000834)	3-2018	10/2021 (May-2025) {7/2025}	1,161.39 (1,738.03) {1,404.00}	684.22	83.00
		441	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA (MoRTH) (N24000925)	10-2018	11/2020 (Sep-2024) {9/2024}	400.76 (394.44) {394.44}	287.04	87.00
	URBAN DEVELOPMENT	442	AHMEDABAD METRO RAIL PROJECT PHASE 1 (AMR) (N28000122)	11-2014	12/2018 (N.A.) {8/2025}	10,773.00 (N.A.) {12,924.55}	12,486.28	99.90

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		443	AHMEDABAD METRO RAIL PROJECT PHASE II (AMR) (N28000137)	3-2019	3/2024 (N.A.) {12/2025}	5,384.17 (N.A.) {5,384.17}	4,135.88	87.68
		444	SURAT METRO RAIL PROJECT (AMR) (N28000138)	3-2019	3/2024 (N.A.) {6/2026}	12,020.32 (N.A.) {12,020.32}	7,043.17	67.49
HARYANA	HEALTH AND FAMILY WELFARE	445	ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT MANETHI, HARYANA. (HITES) (N21000032)	3-2019	3/2023 (Mar-2026) {3/2026}	1,294.34 (1,294.34) {1,294.34}	307.21	26.14
	HOME AFFAIRS	446	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" (CPWD FOR MHA) (N28000147)	1-2020	10/2023 (Mar-2025) {8/2025}	166.98 (170.23) {170.23}	150.98	97.50
	PETROLEUM	447	R and D CAMPUS II AT FARIDABAD (IOCL) (N16000375)	6-2019	12/2022 (Jul-2025) {3/2026}	2,281.94 (3,219.94) {3,219.94}	1,744.23	63.10
		448	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA (IOCL) (N16000412)	2-2021	9/2024 (Dec-2025) {12/2025}	34,627.00 (38,231.00) {38,231.00}	21,454.90	87.60
		449	POLY BUTADIENE RUBBER PLANT AT PANIPAT (IOCL) (N16000458)	3-2022	3/2025 (Jun-2026) {6/2026}	1,459.00 (2,948.62) {2,948.62}	930.86	68.30
	POWER	450	IMPLEMENTATION OF LILO OF BOTH CIRCUITS OF 400KV VIDHYACHAL PS TO SASAN D/C LINE AT HINDALCO SWITCHY (PGCIL) (N18000420)	2-2025	12/2026 (N.A.) {12/2026}	370.00 (N.A.) {370.00}	0.00	-
	RAILWAYS	451	DOUBLING BETWEEN BHIWANI-DOBH BAHALI (NWR) (N22000604)	2-2023	2/2028 (Mar-2026) {3/2026}	471.06 (N.A.) {471.06}	121.18	55.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		452	DOUBLING BETWEEN REWARI- KATHUWAS (27.73 KM) (NWR) (N22000606)	2-2023	6/2027 (May-2026) {5/2026}	352.41 (N.A.) {352.41}	179.38	53.00
	ROAD TRANSPORT AND HIGHWAYS	453	4-LANING OF GOHANA-SONIPAT (PKG- 2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 (NHAI) (N24001535)	7-2020	7/2022 (May-2024) {8/2025}	899.00 (1,882.46) {1,882.46}	1,123.98	97.86
		454	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F (NHAI) (N24001633)	12-2020	12/2023 (Mar-2024) {7/2025}	1,430.88 (1,813.91) {1,813.91}	1,190.27	99.90
		455	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO (NHAI) (N24001634)	1-2021	12/2023 (Mar-2024) {7/2025}	1,306.95 (1,564.14) {1,564.14}	949.76	99.97
		456	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O (NHAI) (N24001635)	3-2022	2/2025 (N.A.) {2/2025}	1,269.50 (N.A.) {1,269.50}	176.00	53.00
		457	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K (NHAI) (N24001673)	3-2020	3/2023 (Nov-2024) {7/2025}	510.97 (N.A.) {510.97}	529.00	97.30
		458	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH- 352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU (NHAI) (N24001774)	12-2020	11/2023 (N.A.) {6/2024}	1,524.03 (N.A.) {1,524.03}	1,105.10	67.61
		459	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH-11 AS A FEEDER ROUTE IN THE STATE (NHAI) (N24001775)	2-2020	1/2023 (Dec-2024) {12/2024}	808.31 (N.A.) {958.00}	930.44	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		460	UPGRADATION OF EXISTING 4 LANE ISMAILABAD-AMBALA SECTION (KM. 0+000 TO KM 42+500) (PART OF AMBALA-KO (NHAI) (N24002037)	1-2023	12/2025 (N.A.) {3/2026}	609.32 (609.00) {609.00}	204.06	52.50
		461	CONSTRUCTION OF 6-LANE GREENFIELD KARNAL RING ROAD STARTING FROM NH-44 NEAR VILLAGE SHAMGARH (DESIGN (NHAI) (N24002038)	11-2022	8/2025 (N.A.) {8/2025}	1,691.45 (1,998.00) {1,998.00}	649.71	58.76
		462	CONSTRUCTION OF 6-LANE GREENFIELD AMBALA RING ROAD STARTING FROM JUNCTION WITH SHAMLI-AMBALA SECTION (NHAI) (N24002039)	2-2023	10/2025 (N.A.) {10/2025}	1,088.64 (1,178.00) {1,178.00}	425.85	53.55
		463	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM RANIPUR BARS (SAHARANPUR DISTRICT) TO ADHOYA (NHAI) (N24002040)	4-2022	5/2025 (N.A.) {5/2028}	1,554.21 (N.A.) {1,554.21}	522.92	54.00
		464	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM ADHOYA MUSALMANA (AMBALA DISTRICT) TO SADOPUR (NHAI) (N24002041)	4-2022	5/2025 (N.A.) {5/2025}	1,491.71 (N.A.) {1,491.71}	706.26	49.70
		465	CONSTRUCTION OF 4-LANING OF BHIWANI HANSI ROAD SECTION OF NH 148B (DESIGN LENGTH 42.934 KM) UNDER BH (NHAI) (N24002042)	11-2022	12/2025 (N.A.) {12/2025}	1,322.13 (N.A.) {1,322.13}	393.46	93.01
		466	CONSTRUCTION OF 4-LANE GREENFIELD JALBEHRA - SHAHBAD SECTION OF NH ? 152G FROM KM 0+000 TO KM 22+850 (NHAI) (N24002043)	3-2022	6/2025 (N.A.) {10/2025}	927.22 (1,173.66) {1,173.66}	504.21	83.50
		467	4L AMBALA - KALAAMB FROM KM. - 0.800 TO KM. 33.015 OF OLD NH-72 (NHAI) (N24002044)	6-2023	6/2025 (N.A.) {6/2025}	629.16 (N.A.) {629.16}	154.00	98.90

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		468	CONSTRUCTION OF GREENFIELD CONNECTIVITY TO JEWAR INTERNATIONAL AIRPORT FROM DND FARIDABAD BALLABHGAR (NHAI) (N24002048)	7-2022	6/2025 (N.A.) {3/2026}	2,414.67 (2,898.00) {2,898.00}	1,232.13	49.10
HIMACHAL PRADESH	DEPARTMENT OF HIGHER EDUCATION	469	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR (CPWD EDUCATION) (N42000008)	9-2018	6/2022 (Dec-2024) {8/2025}	392.51 (N.A.) {446.43}	316.16	91.50
		470	CONSTRUCTION OF PERMANENT CAMPUSES OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND DHARAMSHAL (CPWD) (N42000011)	3-2021	11/2024 (Jul-2025) {7/2025}	512.37 (300.45) {300.45}	169.63	74.00
	POWER	471	LUHRI HYDROELECTRIC PROJECT (STAGE1) (SJVN) (N18000279)	11-2020	1/2026 (N.A.) {12/2028}	1,810.56 (N.A.) {3,584.53}	1,732.67	51.32
		472	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) (SJVN) (N18000291)	10-2020	11/2025 (N.A.) {3/2027}	687.97 (N.A.) {1,511.87}	891.77	67.61
		473	SUNNI DAM HYDRO ELECTRIC PROJECT (SJVN) (N18000344)	1-2023	4/2028 (N.A.) {12/2028}	2,614.51 (N.A.) {4,540.71}	948.35	29.41
	RAILWAYS	474	BHANUPALI-BILASPUR BERI NL (RVNL) (N22000273)	4-2008	12/2026 (N.A.) {3/2025}	13,370.29 (N.A.) {6,753.42}	5,369.57	-
	ROAD TRANSPORT AND HIGHWAYS	475	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K (MoRTH) (N24001422)	2-2021	9/2021 (N.A.) {7/2024}	345.89 (N.A.) {345.89}	178.19	95.08

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		476	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR-KARNOHAL SECTION (KM 141.000 TO K (MoRTH) (N24001447)	8-2020	12/2024 (N.A.) {12/2024}	371.93 (N.A.) {371.93}	154.04	81.00
		477	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF KALWAHAN-MANDI SECTION (KM 208.950 TO KM 2 (MoRTH) (N24001470)	8-2020	4/2025 (N.A.) {4/2025}	314.32 (N.A.) {314.32}	49.26	51.00
		478	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF (NHAI) (N24001808)	3-2021	12/2024 (Dec-2024) {12/2024}	1,322.95 (1,442.47) {1,442.47}	888.73	96.61
		479	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU (NHAI) (N24001809)	5-2022	3/2024 (Dec-2024) {12/2024}	469.95 (N.A.) {280.00}	302.91	98.57
		480	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP (NHAI) (N24001810)	2-2022	6/2024 (N.A.) {6/2024}	190.60 (N.A.) {163.00}	103.48	100.00
		481	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH-20 (NEW NH-154) (PACKAGE-IB) (NHAI) (N24001811)	4-2021	6/2024 (N.A.) {5/2025}	583.93 (770.00) {770.00}	173.60	100.00
		482	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) (NHAI) (N24001812)	3-2021	5/2024 (N.A.) {12/2025}	1,002.11 (1,361.79) {1,361.76}	190.30	46.68
		483	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A (NHAI) (N24001813)	7-2021	9/2024 (N.A.) {9/2024}	1,692.05 (N.A.) {1,692.05}	942.14	21.60

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		484	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS-5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001915)	3-2021	6/2026 (N.A.) {6/2026}	230.54 (N.A.) {230.54}	20.16	28.00
		485	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS 5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001916)	3-2021	5/2026 (N.A.) {5/2026}	314.67 (N.A.) {314.67}	76.05	47.00
		486	PKG NAME: 4L OF KATHLIGHAT TO SHAKRAL VILLAGE FROM KM 128.835 TO KM 146.300 OF NH- 5 (SHIMLA BYPASS (NHAI) (N24002049)	3-2022	4/2026 (N.A.) {4/2026}	1,703.48 (2,278.00) {2,278.00}	651.98	14.50
		487	REHABILITATION AND UPGRADATION TO 4L CONFIGURATION and STRENGTHENING OF SIHUNI TO RAJOL FROM KM 51.0 (NHAI) (N24002050)	2-2022	9/2025 (N.A.) {9/2025}	696.65 (698.46) {698.46}	391.62	67.73
		488	CONSTRUCTION OF NEW 2 LANE WITH PAVED SHOULDER OF HAMIRPUR BYPASS (PACKAGE IVA) OF NH-88 (NEW NH-103 (NHAI) (N24002051)	7-2022	10/2025 (N.A.) {10/2025}	739.39 (N.A.) {739.39}	347.45	81.53
		489	REHABILITATION AND UP-GRADATION OF EXISTING ROAD TO 2L PS FROM END OF HAMIRPUR BYPASS (NEAR CHILBAHA (NHAI) (N24002052)	2-2022	4/2025 (N.A.) {4/2025}	1,146.19 (N.A.) {1,146.19}	940.81	71.23
		490	REHABILITATION AND UP-GRADATION TO 4L CONFIGURATION AND STRENGTHENING OF THANPURI TO PAROR SECTION F (NHAI) (N24002192)	6-2022	12/2025 (N.A.) {12/2025}	815.69 (815.69) {815.69}	400.63	33.56
		491	FOUR LANNING OF NERCHOWK- PANDOH BYPASS SECTION OF NH- 21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH (NHAI) (N24000613)	9-2016	7/2020 (N.A.) {3/2025}	1,273.71 (N.A.) {1,478.61}	1,450.53	97.43

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		492	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M (NHAI) (N24000852)	3-2018	5/2021 (Dec-2024) {12/2024}	478.74 (N.A.) {1,514.46}	1,349.59	83.00
		493	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA (MoRTH) (N24001381)	8-2020	4/2021 (N.A.) {4/2021}	272.98 (N.A.) {272.98}	140.69	100.00
		494	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. (MoRTH) (N24001382)	8-2020	3/2021 (N.A.) {7/2024}	242.80 (N.A.) {242.80}	100.95	94.76
		495	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 (MoRTH) (N24001383)	8-2020	4/2021 (N.A.) {4/2021}	349.20 (N.A.) {349.20}	239.34	100.00
JAMMU AND KASHMIR	CIVIL AVIATION	496	JAMMU - CONSTRUCTION OF NEW CIVIL ENCLAVE (AAI) (N04000107)	7-2022	6/2026 (N.A.) {6/2026}	861.37 (N.A.) {861.37}	154.30	30.25
	DEPARTMENT OF HIGHER EDUCATION	497	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) (CPWD EDUCATION) (N28000130)	3-2019	7/2022 (Jan-2025) {1/2025}	424.93 (N.A.) {500.91}	448.15	96.00
		498	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) (CPWD EDUCATION) (N28000131)	1-2018	4/2023 (Apr-2025) {4/2025}	676.00 (1,144.68) {1,144.68}	54.75	100.00
	HEALTH AND FAMILY WELFARE	499	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR (CPWD FOR HEALTH) (N28000150)	3-2019	9/2025 (N.A.) {11/2025}	1,828.00 (N.A.) {1,577.00}	1,302.38	64.50

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		500	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR (CPWD FOR HEALTH) (N21000029)	3-2019	9/2023 (May-2025) {5/2025}	1,404.00 (1,642.00) {1,642.00}	1,461.68	100.00
	<u>PETROLEUM</u>	501	SETTING UP A COMMON USER PETROLEUM TERMINAL AT JAMMU FOR RE-SITEMENT OF EXISTING DEPOTS OF PSU OMCS (BPCL) (N16000500)	4-2021	3/2025 (N.A.) {3/2025}	676.89 (N.A.) {676.89}	503.55	76.00
		502	CGD PROJECT AT JAMMU DISTRICTS (IOCL) (N16000527)	3-2022	3/2032 (Sep-2034) {9/2034}	538.00 (N.A.) {538.00}	4.09	0.60
	<u>POWER</u>	503	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) (CVPPPL) (N18000172)	10-2014	4/2020 (Jul-2025) {12/2026}	8,112.12 (N.A.) {12,727.76}	6,692.58	70.00
		504	KIRU HYDRO ELECTRIC PROJECT (CVPPPL) (N18000278)	3-2019	8/2024 (N.A.) {12/2026}	4,287.59 (N.A.) {5,409.00}	2,713.25	63.87
		505	RATLE HE PROJECT (NHPC) (N18000324)	2-2021	2/2026 (N.A.) {8/2028}	5,281.94 (N.A.) {5,281.94}	1,011.56	23.57
		506	KWAR HE PROJECT (CVPPPL) (N18000363)	5-2022	11/2026 (N.A.) {3/2028}	4,526.12 (N.A.) {4,526.12}	1,159.97	22.15
		507	TRANSMISSION SCHEME FOR EVACUATION OF POWER FROM RATLE HEP (850 MW) AND KIRU (624 MW): PART B (PGCIL) (N18000417)	3-2025	3/2027 (N.A.) {3/2027}	219.00 (N.A.) {219.00}	0.00	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	508	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA (NHAI) (N24001472)	9-2021	12/2023 (Jun-2024) {6/2024}	811.19 (N.A.) {811.19}	848.72	99.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		509	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY (NHAI) (N24001511)	3-2021	2/2024 (Oct-2025) {10/2025}	2,919.96 (N.A.) {2,919.96}	2,334.99	70.00
		510	FOUR LANING OF JAMMU-AKHNOOR PKG-1 (NHIDCL) (N24001543)	7-2022	1/2025 (N.A.) {10/2025}	245.34 (N.A.) {245.34}	57.20	40.95
		511	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH-4 (NHAI) (N24001550)	9-2021	9/2024 (Dec-2025) {12/2025}	1,821.72 (1,917.32) {1,917.32}	1,005.37	83.71
		512	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT- GURDASPUR ROAD (NH-5 (NHAI) (N24001551)	10-2021	9/2024 (Dec-2025) {12/2025}	3,044.02 (3,044.02) {3,044.02}	1,589.44	70.21
		513	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B (NHAI) (N24001552)	10-2021	9/2024 (Feb-2026) {2/2026}	2,714.95 (2,714.95) {2,714.95}	1,663.19	85.78
		514	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH- (NHAI) (N24001619)	8-2022	6/2024 (Jun-2025) {6/2025}	200.05 (200.05) {208.92}	153.30	63.20
		515	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SLIP ZONES AT KM.130.550 TO KM.130.750; KM. (NHAI) (N24001620)	9-2021	10/2023 (Dec-2025) {12/2025}	442.14 (N.A.) {442.14}	352.62	19.88
		516	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL. (NHAI) (N24001621)	7-2021	8/2024 (Jul-2025) {7/2025}	614.48 (N.A.) {614.48}	187.59	7.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		517	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX (NHAI) (N24001622)	7-2021	6/2024 (Jul-2025) {7/2025}	1,401.87 (N.A.) {1,401.87}	751.11	-
		518	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM. 187.00 TO KM. 189.350 (NHAI) (N24001623)	1-2020	1/2024 (Feb-2025) {2/2025}	336.01 (N.A.) {336.01}	223.02	34.00
		519	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI (NHAI) (N24001624)	7-2019	10/2020 (Apr-2023) {9/2024}	157.05 (N.A.) {157.05}	139.54	100.00
		520	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K (NHAI) (N24001627)	7-2021	2/2025 (May-2026) {5/2026}	1,912.17 (N.A.) {1,912.17}	148.88	-
		521	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B (NHIDCL) (N24001833)	7-2022	3/2025 (N.A.) {8/2025}	198.28 (N.A.) {198.28}	85.49	71.09
		522	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 102 TO KM 13 (BRO) (N24001897)	3-2021	7/2024 (Mar-2025) {3/2024}	642.24 (N.A.) {642.24}	345.14	95.00
		523	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 30.000 TO K (BRO) (N24001898)	7-2020	11/2024 (N.A.) {11/2024}	272.49 (N.A.) {272.49}	133.66	87.24
		524	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 134.95 TO KM (BRO) (N24001899)	2-2021	7/2024 (N.A.) {3/2025}	395.25 (N.A.) {395.25}	140.42	64.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		525	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 49.150 TO KM (BRO) (N24001900)	3-2020	8/2024 (N.A.) {3/2025}	796.97 (N.A.) {796.97}	323.85	79.00
		526	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 64.535 TO K (BRO) (N24001901)	3-2020	9/2023 (N.A.) {3/2025}	152.93 (N.A.) {152.93}	90.30	78.27
		527	CONSTRUCTION OF TWIN TUBE TUNNELS ON JAMMU KASHMIR RING ROAD (NH-244A) BETWEEN DESIGN CH. 50+600 TO (NHAI) (N24001926)	3-2023	6/2025 (N.A.) {3/2026}	939.86 (N.A.) {939.86}	475.07	69.93
		528	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER FROM (DESIGN CH. 14+200 TO 24+400), (DESIGN CH. 35+300 TO (BRO) (N24001998)	6-2022	8/2025 (N.A.) {8/2025}	832.46 (N.A.) {823.46}	227.50	46.00
		529	2L NH-1 FROM KM 8.660 TO KM 33.775 (SUMBAL TO WAYUL) TO 4L DUAL CARRIAGEWAY NH STANDARD AS PART OF S (NHAI) (N24002059)	9-2022	6/2026 (Jun-2026) {12/2026}	1,183.60 (N.A.) {1,183.60}	197.13	16.63
		530	DELHI AMRITSAR KATRA EXPRESSWAY (PHASE-II PKG XVIII) DEVELOPMENT AND UPGRADATION OF FOUR LANE ACCESS (NHAI) (N24002060)	3-2023	11/2025 (N.A.) {3/2026}	1,107.00 (N.A.) {975.38}	338.91	38.81
		531	4/6L ACCESS CONTROL EXPRESSWAY FROM DESIGN CHAINAGE KM 515.000 TO 528.300 (KUNJWANI TO SIDHRA SECTIO (NHAI) (N24002061)	8-2022	6/2025 (N.A.) {2/2026}	2,474.47 (N.A.) {2,894.74}	923.64	40.17

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		532	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM 162.800 TO KM (BRO) (N24002119)	10-2022	1/2026 (N.A.) {1/2026}	562.45 (N.A.) {562.45}	99.06	25.00
		533	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER (PATTAN BYPASS) GREENFIELD BYPASS FROM EXISTING CH. KM 24 (BRO) (N24002179)	3-2023	7/2026 (N.A.) {7/2026}	980.21 (N.A.) {980.21}	300.02	8.00
		534	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 166.100 TO KM (BRO) (N24002180)	9-2021	7/2026 (N.A.) {7/2026}	734.64 (N.A.) {734.64}	19.60	8.00
		535	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDERS (BARAMULLA BYPASS) GREENFIELD BYPASS FROM EXISTING CH. K (BRO) (N24002185)	3-2023	9/2026 (N.A.) {9/2026}	992.43 (N.A.) {992.43}	338.33	-
		536	WIDENING AND STRENGTHENING OF RAFIABAD-KUPWARA-CHOWKIBAL- TANGDHAR-CHAMKOT (NH-701) ROAD FROM DESIGN (BRO) (N24002210)	3-2024	5/2027 (N.A.) {5/2027}	1,404.94 (N.A.) {1,404.94}	0.00	-
		537	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A (NHAI) (N24000488)	12-2015	12/2018 (Nov-2024) {11/2024}	2,136.97 (2,644.00) {2,644.00}	2,386.51	99.50
		538	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE (NHAI) (N24000717)	12-2017	7/2021 (Jul-2025) {7/2025}	1,471.75 (1,471.75) {1,903.98}	1,731.65	98.94
		539	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU- AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA (NHIDCL) (N24000868)	3-2018	7/2021 (Aug-2023) {10/2025}	253.44 (N.A.) {253.44}	191.14	83.23

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		540	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D (NHIDCL) (N24001256)	8-2020	9/2026 (N.A.) {9/2026}	6,808.69 (N.A.) {6,808.69}	3,013.84	49.92
		541	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL (NHIDCL) (N24001264)	7-2020	4/2022 (Oct-2024) {10/2026}	228.39 (N.A.) {228.39}	69.32	88.09
		542	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K (NHIDCL) (N24001266)	7-2020	4/2022 (Nov-2023) {8/2025}	210.79 (N.A.) {210.79}	72.72	93.63
		543	KHELLANI-KHANABAL PKG-1 (NHIDCL) (N24001323)	3-2021	9/2022 (Oct-2024) {11/2024}	486.45 (N.A.) {486.45}	126.73	96.84
		544	KHELLANI-KHANABAL PKG-3 (NHIDCL) (N24001341)	3-2021	12/2022 (Oct-2024) {5/2025}	398.51 (N.A.) {398.51}	80.64	98.36
		545	KHELLANI-KHANABAL PKG-2 (NHIDCL) (N24001394)	7-2021	2/2023 (Jun-2025) {6/2026}	512.43 (N.A.) {512.43}	71.65	51.75
		546	KHELLANI-KHANABAL PKG-4 (NHIDCL) (N24001395)	7-2021	8/2023 (Dec-2025) {6/2026}	859.67 (N.A.) {859.67}	196.00	44.02
		547	KHELLANI-KHANABAL PKG-5 (NHIDCL) (N24001396)	7-2021	2/2023 (Mar-2025) {8/2025}	497.09 (N.A.) {497.09}	178.73	90.01
		548	GOHA-KHELLANI PKG-3 (NHIDCL) (N24001397)	2-2021	3/2023 (Feb-2025) {3/2025}	431.28 (433.08) {431.28}	372.31	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
JHARKHAND	COAL	549	RAJRAPPA RCE OCP (3.0 MTY) (CCL) (N06000087)	12-2009	3/2016 (N.A.) {3/2027}	510.85 (N.A.) {510.85}	488.57	75.00
		550	MURAI DIH UG TURN-KEY PROJECT (BCCL) (N06000096)	2-2011	4/2014 (N.A.) {12/2026}	339.88 (N.A.) {339.88}	190.48	70.00
		551	MOONIDIH XV SEAM UG (BCCL) (N06000098)	8-2011	3/2019 (N.A.) {5/2026}	1,230.27 (N.A.) {1,230.27}	620.97	81.00
		552	CHITRA EAST (RCE) OCP (ECL) (N06000169)	8-2018	3/2026 (Mar-2026) {3/2026}	513.98 (N.A.) {513.98}	228.35	51.00
		553	TETARIAKHAR EXPANSION OCP (CCL) (N06000186)	11-2019	3/2023 (N.A.) {3/2027}	243.52 (N.A.) {243.52}	44.64	26.00
		554	PACHWARA SOUTH COAL BLOCK (NLC) (N06000193)	7-2013	9/2028 (N.A.) {9/2028}	2,242.92 (2,242.90) {2,242.90}	1,151.23	54.00
		555	PATHERDIH 2.5 NLW COAL WASHERY (BCCL) (N06000194)	10-2015	4/2018 (N.A.) {3/2026}	334.27 (N.A.) {334.27}	135.86	47.00
		556	REVISED PROJECT REPORT MAGADH EXPANSION OCP (CCL) (N06000216)	8-2020	3/2028 (N.A.) {3/2028}	7,254.37 (N.A.) {7,254.37}	1,527.57	38.00
		557	EXPANSION PROJECT AMRAPALI OCP (CCL) (N06000217)	8-2020	3/2028 (N.A.) {3/2028}	5,136.15 (N.A.) {5,136.15}	1,092.17	43.00
		558	UCE OF EPR OF NORTH URIMARI OCP (CCL) (N06000218)	7-2021	3/2029 (N.A.) {3/2029}	778.80 (N.A.) {778.80}	694.11	75.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		559	KOTRE BASANTPUR PACHMO OCP (CCL) (N06000237)	8-2020	3/2032 (N.A.) {3/2032}	625.40 (625.40) {625.40}	441.24	41.00
		560	CHANDRAGUPT OCP (CCL) (N06000238)	8-2020	3/2032 (N.A.) {3/2032}	973.50 (N.A.) {973.50}	440.56	12.40
		561	SIRKA OCP (CCL) (N06000239)	5-2020	3/2028 (N.A.) {3/2028}	222.82 (N.A.) {222.82}	139.31	51.00
		562	JHARKHAND LAIYO OCP (CCL) (N06000240)	8-2020	3/2031 (N.A.) {3/2031}	764.57 (N.A.) {764.57}	145.80	28.00
		563	EPR TAPIN SOUTH OCP (CCL) (N06000241)	11-2020	3/2028 (N.A.) {3/2028}	230.41 (N.A.) {230.41}	21.12	18.30
		564	EPR PUNDI OCP (CCL) (N06000242)	11-2020	3/2027 (N.A.) {3/2027}	713.35 (N.A.) {713.35}	236.57	21.00
		565	EPR ROHINI KARKATA OCP (CCL) (N06000243)	1-2021	3/2028 (N.A.) {3/2028}	1,020.42 (N.A.) {1,020.42}	83.44	18.00
		566	EXPANSION OF KONAR OCP (CCL) (N06000245)	1-2022	3/2032 (N.A.) {3/2032}	799.34 (N.A.) {799.34}	416.73	32.00
		567	EXPANSION OF KARO OCP (CCL) (N06000246)	1-2022	3/2029 (N.A.) {3/2029}	908.47 (N.A.) {908.47}	217.68	21.00
		568	EXPANSION OF ASHOK OCP (CCL) (N06000247)	5-2021	3/2028 (N.A.) {3/2028}	2,898.28 (N.A.) {2,898.28}	176.50	20.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		569	AMALGAMATED NTST KUJAMA OCP 8.5 MTY (BCCL) (N06000273)	1-2023	3/2030 (N.A.) {3/2030}	4,011.85 (N.A.) {4,011.85}	398.49	25.10
		570	HURA C OC (ECL) (N06000275)	8-2022	3/2029 (N.A.) {3/2029}	859.41 (N.A.) {859.41}	448.72	62.00
		571	CHUPERBHITA- SIMLONG OCP (ECL) (N06000280)	12-2023	3/2037 (Mar-2037) {3/2037}	979.08 (N.A.) {979.08}	0.00	0.01
		572	BLOCK-E OCP (15 MTY) (BCCL) (N06000287)	3-2024	3/2029 (N.A.) {3/2029}	5,850.83 (N.A.) {5,850.83}	5.96	2.00
		573	JARANGDIH OCP (CCL) (N06000295)	2-2020	3/2029 (N.A.) {3/2029}	414.37 (N.A.) {414.37}	85.60	-
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	574	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD (CPWD EDUCATION) (N28000067)	9-2012	3/2016 (N.A.) {3/2016}	171.86 (N.A.) {171.86}	174.48	99.00
	<u>PETROLEUM</u>	575	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) (ONGC) (N16000445)	11-2019	1/2024 (Mar-2025) {6/2025}	431.00 (N.A.) {431.00}	204.31	58.00
		576	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI (IOCL) (N16000480)	3-2023	2/2026 (N.A.) {2/2026}	202.07 (N.A.) {202.07}	52.94	42.95
		577	CGD PROJECT IN BIHAR JHARKHAND (HPCL) (N16000497)	6-2022	6/2030 (N.A.) {6/2030}	1,377.00 (N.A.) {1,377.00}	282.88	24.15
	<u>POWER</u>	578	NORTH KARANPURA STPP (3X660 MW) (NTPC) (N18000177)	2-2014	6/2019 (Oct-2022) {3/2025}	16,242.90 (N.A.) {16,242.90}	17,323.08	98.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		579	PATRATU STPP-I (3X800MW) (NTPC) (N18000275)	11-2017	3/2023 (N.A.) {3/2026}	17,112.00 (N.A.) {17,112.00}	17,219.35	81.00
		580	BADAM COAL MINING PROJECT (NTPC) (N18000367)	2-2019	10/2024 (Apr-2027) {4/2027}	501.79 (784.39) {501.79}	368.94	59.79
		581	KERANDARI COAL MINING PROJECT (NTPC) (N18000370)	9-2015	11/2019 (Mar-2025) {3/2025}	1,553.00 (2,896.64) {2,896.64}	2,095.17	64.00
	RAILWAYS	582	KODERMA-TILAIYA (NL), ECR (ECR) (220100305)	4-2002	3/2023 (N.A.) {12/2025}	1,625.87 (1,625.87) {1,700.00}	2,039.52	80.00
		583	BONDAMUNDA RANCHI DOUBLING (SER) (N22000396)	3-2016	6/2024 (N.A.) {6/2026}	3,029.04 (3,029.04) {3,029.04}	2,436.91	84.50
		584	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) (SER) (N22000508)	4-2018	6/2026 (N.A.) {6/2026}	501.52 (N.A.) {472.50}	275.97	4.00
		585	DOUBLING OF PRADHANKHUNTA JN - PATHERDIH BAZAR-BHOJUDIH (ECR) (N22000529)	11-2022	11/2027 (N.A.) {3/2026}	202.00 (349.22) {349.22}	76.94	2.00
		586	KHARAGPUR-ADITYAPUR - 3RD LINE (132 KM) (RVNL) (N22000595)	12-2015	3/2025 (N.A.) {3/2025}	3,249.98 (N.A.) {3,270.07}	2,899.45	-
		587	3RD LINE BETWEEN DHANBAD SONNAGAR (RVNL) (N22000599)	11-2016	3/2026 (N.A.) {3/2026}	8,975.00 (N.A.) {7,906.38}	4,705.38	-
		588	GARHWA ROAD - RAIL OVER RAIL (ECR) (N22000610)	3-2017	6/2024 (N.A.) {2/2026}	262.71 (N.A.) {262.71}	227.86	70.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	589	GOMOH - FLYOVER FOR DOWN TRAINS (ECR) (N22000611)	1-2018	3/2023 (N.A.) {3/2026}	686.03 (N.A.) {487.73}	419.46	45.00
		590	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 (NHAI) (N24001589)	9-2020	3/2024 (Dec-2024) {4/2025}	755.26 (N.A.) {1,039.00}	635.78	88.10
		591	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH-75 [REHLA / GARHWA BYPASS] (NHAI) (N24001590)	9-2020	10/2023 (Dec-2024) {1/2025}	748.99 (N.A.) {903.00}	831.75	100.00
		592	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM (NHAI) (N24001594)	2-2022	1/2025 (Mar-2025) {3/2025}	534.73 (N.A.) {534.73}	282.33	99.57
		593	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH (NHAI) (N24001595)	8-2020	3/2024 (Sep-2025) {9/2025}	1,034.00 (1,879.55) {1,879.55}	41.50	97.30
		594	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF (NHAI) (N24001596)	11-2021	7/2023 (Jun-2025) {12/2025}	1,302.72 (1,504.80) {1,504.80}	957.00	75.74
		595	FOUR LANING WITH PAVED SHOULDER OF SECTION FROM KM 53.600 (GOLA ON NH-320) TO KM 81.446 (ORMANJHI ON (NHAI) (N24001854)	6-2023	6/2025 (N.A.) {6/2025}	1,214.93 (1,324.95) {1,462.00}	808.69	75.50
		596	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM 0.00 TO 44.00 (KURU-GHAGHRA SECTION) OF NH- 143A INCLU (MoRTH) (N24001922)	2-2020	8/2023 (N.A.) {12/2024}	153.01 (N.A.) {153.01}	83.63	96.23

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		597	WIDENING AND STRENGTHENING OF EXISTING PAVEEMNT TO TWO LANE WITH PAVED SHOULDERS FROM KM 116.00 TO K (MoRTH) (N24001923)	1-2022	7/2024 (N.A.) {12/2024}	315.21 (N.A.) {315.21}	117.26	80.00
		598	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDER/TWO LANE+ PAVED SHOULDER WITH SERVICE ROA (MoRTH) (N24001924)	3-2022	8/2025 (N.A.) {8/2025}	514.22 (N.A.) {514.22}	15.19	6.10
		599	WIDENING AND STRENGTHENING/RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDER/ TWO LANE WITH PAVED SHOUL (MoRTH) (N24001925)	3-2022	8/2025 (N.A.) {8/2025}	423.18 (N.A.) {423.18}	0.11	-
		600	FOUR LANING OF KHAJURI TO WYNDHAMGANJ FROM KM 219.600 TO KM 260.483 ON NH-75 PKG SEC-V ON HAM (NHAI) (N24002053)	4-2022	9/2025 (N.A.) {9/2025}	1,232.00 (1,343.00) {1,400.00}	606.60	81.76
		601	FOUR LANING OF BHOGU TO SANKHA FROM KM 147.450 TO KM 196.870 ON NH-75 PKG SEC-III (NHAI) (N24002054)	10-2022	11/2025 (N.A.) {11/2025}	1,390.77 (1,391.00) {1,600.00}	319.69	75.01
		602	FOUR LANING OF BASUKINATH-DEOGHAR SECTION OF NH-114A FROM KM 85.081 TO KM 130.240 UNDER NHDP PHASE-I (NHAI) (N24002055)	3-2023	12/2025 (N.A.) {12/2025}	1,444.94 (N.A.) {1,444.94}	0.00	-
		603	BHARATMALA PARIYOJANA OF BOKARO JAINA MORE - GOLA SECTION OF NH-320 FROM KM. 21.110 TO KM. 53.600 IN (NHAI) (N24002056)	6-2020	6/2025 (N.A.) {6/2025}	964.64 (N.A.) {964.64}	458.58	61.20
		604	FOUR LANING OF MEHGAMA HANSDIHA SECTION OF NH-33 FROM EXISTING KM 41.900 TO 93.000 IN THE STATE OF J (NHAI) (N24002057)	12-2022	5/2025 (N.A.) {5/2025}	1,443.77 (N.A.) {1,443.77}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		605	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION (NHAI) (N24000726)	1-2018	11/2021 (May-2026) {5/2026}	1,155.16 (N.A.) {950.49}	657.82	73.00
		606	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I (MoRTH) (N24001216)	12-2016	9/2021 (N.A.) {12/2024}	196.00 (N.A.) {196.00}	164.21	90.10
	STEEL	607	NEW SINTER PLANT AT BOKARO STEEL PLANT (SAIL) (N12000095)	3-2015	10/2017 (Nov-2026) {11/2026}	1,034.01 (1,752.30) {1,752.30}	882.41	51.75
		608	REVAMPING OF OLD SUB SYSTEM OF BLAST FURNACE 3 AT BOKARO STEEL PLANT (SAIL) (N12000129)	9-2023	7/2025 (Nov-2025) {11/2025}	513.82 (N.A.) {513.82}	195.71	67.00
		609	REBUILDING OF COKE OVEN BATTERY NO.6 OF BOKARO STEEL PLANT (SAIL) (N12000133)	11-2023	11/2026 (N.A.) {11/2026}	627.31 (N.A.) {627.31}	84.56	35.00
		610	REPLACEMENT OF REMAINING 04 NOS. OF BATTERY CYCLONES WITH 04 NOS. OF ESPS IN SINTER PLANT-1 AT BSL (SAIL) (N12000135)	3-2024	6/2026 (N.A.) {6/2026}	260.37 (N.A.) {260.37}	44.22	18.00
		611	REPLACEMENT OF EXISTING GRINDERS IN CRM-I & II AT BOKARO STEEL PLANT (SAIL) (N12000142)	1-2025	1/2027 (N.A.) {1/2027}	211.94 (N.A.) {211.94}	0.00	-
		612	SECONDARY EMISSION CONTROL IN CONVERTERS OF SMS-II AT BOKARO STEEL PLANT (SAIL) (N12000143)	1-2025	10/2026 (N.A.) {10/2026}	207.13 (N.A.) {207.13}	0.00	5.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
KARNATAKA	CIVIL AVIATION	613	BELAGAVI AIRPORT- EXPANSION OF TERMINAL BUILDING AND ASSOCIATED WORKS (AAI) (N04000105)	6-2023	2/2026 (N.A.) {2/2026}	322.45 (N.A.) {322.45}	104.38	43.00
		614	HUBBALI AIRPORT - CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS (AAI) (N04000108)	6-2023	2/2026 (N.A.) {2/2026}	320.47 (N.A.) {320.47}	53.87	32.50
		615	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) (CPWD EDUCATION) (N42000006)	7-2019	3/2022 (N.A.) {11/2025}	851.00 (851.00) {930.36}	918.06	-
		616	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL (CPWD) (N42000010)	8-2021	2/2024 (Nov-2024) {11/2024}	316.25 (N.A.) {316.25}	281.32	91.00
	PETROLEUM	617	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE (HPCL) (N16000369)	12-2018	12/2022 (Aug-2025) {8/2025}	854.00 (854.00) {854.00}	717.44	99.70
		618	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE (IOCL) (N16000437)	1-2022	7/2025 (Dec-2025) {12/2025}	463.00 (500.62) {500.62}	244.46	71.10
		619	POWER SYSTEM UPGRADATION PROJECT (MANGALORE REFIN) (N16000509)	10-2023	2/2026 (N.A.) {2/2026}	385.00 (N.A.) {385.00}	129.72	59.70
		620	DEMO PLANT FOR PRODUCTION OF BIO-ATF (MANGALORE REFIN) (N16000536)	3-2024	3/2027 (N.A.) {3/2027}	364.00 (N.A.) {364.00}	22.78	10.10

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	621	TS FOR INTRGRATION OF RE ZONE (PHASE II) IN KOPPAL II (PHASE A and B) AND GADAG II (PHASE A) IN KARN (PGCIL) (N18000385)	12-2023	12/2025 (N.A.) {12/2025}	2,889.00 (N.A.) {2,889.00}	1,011.29	36.70
		622	TS FOR SOLAR ENERGY ZONE IN BIDAR (2500MW), KARNATAKA [BIDAR TRANSMISSION LTD] (PGCIL) (N18000388)	2-2024	2/2026 (N.A.) {2/2026}	2,148.00 (N.A.) {2,148.00}	923.47	52.20
		623	SYSTEM STRENGTHENING AT KOPPAL- II AND GADAG-II FOR INTEGRATION OF RE GENERATION PROJECTS (PGCIL) (N18000409)	1-2025	1/2027 (N.A.) {1/2027}	1,354.00 (N.A.) {1,354.00}	16.25	-
		624	AUGMENTATION OF TRANSFORMATION CAPACITY AT BIDAR PS (PGCIL) (N18000410)	2-2025	2/2027 (N.A.) {2/2027}	288.00 (N.A.) {288.00}	4.03	-
		625	TRANSMISSION SCHEME FOR INTEGRATION OF DAVANAGERE / CHITRADURGA AND BELLARY REZ IN KARNATAKA (PGCIL) (N18000419)	3-2025	3/2027 (N.A.) {3/2027}	3,453.00 (N.A.) {3,453.00}	20.70	-
	RAILWAYS	626	TUMKUR-CHITRADURGA-DAVENGERE NL (SWR) (N22000256)	4-2011	3/2019 (N.A.) {12/2027}	1,876.00 (N.A.) {1,801.01}	503.99	12.00
		627	BAGALKOT-KUDACHI NL (SWR) (N22000258)	4-2010	3/2027 (N.A.) {12/2028}	1,378.00 (1,378.00) {1,378.00}	646.95	34.00
		628	HOSPET-HUBLI-LONDA- VASCODAGAMA DL (RVNL) (N22000297)	4-2010	3/2027 (N.A.) {12/2026}	5,060.36 (N.A.) {3,692.60}	3,505.49	-
		629	GADAG-WADI NL (SWR) (N22000299)	4-2013	3/2027 (N.A.) {3/2028}	2,841.84 (N.A.) {2,841.84}	1,352.94	29.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		630	MARIKUPPAM - KUPPAM (SWR) (N22000308)	4-2012	3/2016 (N.A.) {12/2027}	279.54 (296.72) {296.72}	121.12	14.00
		631	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) (SWR) (N22000486)	3-1996	6/2025 (N.A.) {3/2026}	825.31 (825.31) {825.31}	692.24	83.00
		632	BAIYYAPPANAHALLI-HOSUR (48 KM) (NCRTC) (N22000542)	4-2019	3/2026 (N.A.) {3/2026}	375.67 (N.A.) {375.67}	0.00	-
		633	YESHVANTHPUR-CHANNASANDRA (21.7 KM) (NCRTC) (N22000543)	4-2019	3/2026 (N.A.) {3/2026}	169.65 (N.A.) {169.65}	71.75	-
		634	BELGAUM-DHARWAD VIA KITTUR (73.10 KM) (UMBRELLA WORK PB#22/2019-20/NR) (SWR) (N22000557)	9-2020	12/2027 (N.A.) {3/2029}	1,590.80 (927.42) {927.42}	0.75	-
		635	HASSAN (ALUR) - BELUR (32 KM) (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000558)	6-2019	4/2028 (N.A.) {3/2028}	748.86 (748.85) {748.85}	0.88	1.00
		636	SHIMOGA-SHIKARIPURA-RANEENNUR (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000559)	9-2019	12/2027 (N.A.) {12/2028}	1,453.73 (994.47) {994.47}	87.33	7.00
		637	BANGALORE-WHITEFIELD-BANGALORE CITY-KRISHNARAJAPURAM QUADRUPLING (SWR) (N22000621)	3-2018	6/2025 (N.A.) {2/2026}	492.87 (492.87) {492.87}	254.35	75.00
	ROAD TRANSPORT AND HIGHWAYS	638	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN (NHAI) (N24001425)	3-2021	11/2021 (Nov-2025) {11/2025}	1,100.88 (1,687.31) {1,687.31}	1,156.26	80.30

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		639	4L OF ADDAHOLE TO BANTWAL CROSS SECTION (NHAI) (N24001426)	3-2021	10/2021 (Jul-2025) {7/2025}	317.90 (572.01) {572.01}	370.84	98.00
		640	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) (NHAI) (N24001598)	1-2022	4/2025 (May-2026) {5/2026}	1,388.70 (1,388.70) {1,388.70}	509.84	71.60
		641	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. (NHAI) (N24001599)	3-2018	12/2022 (Dec-2022) {12/2025}	440.16 (N.A.) {440.16}	355.97	75.27
		642	BANGALORE/TN BORDER TO HOSKOTE (NHAI) (N24001674)	2-2023	2/2025 (Sep-2025) {9/2025}	1,240.60 (1,181.68) {1,181.68}	952.87	83.25
		643	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 (NHAI) (N24001676)	12-2022	6/2025 (Mar-2026) {6/2025}	2,718.46 (N.A.) {2,718.46}	438.90	54.52
		644	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12 (NHAI) (N24001677)	11-2022	5/2024 (Apr-2025) {4/2025}	226.76 (226.76) {226.76}	86.76	71.95
		645	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 (NHAI) (N24001679)	10-2022	4/2025 (Dec-2025) {12/2025}	1,479.30 (1,479.30) {1,479.30}	676.61	83.98
		646	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE (NHAI) (N24001680)	3-2021	10/2024 (Jun-2026) {6/2026}	1,409.68 (1,808.12) {1,808.12}	1,039.17	59.00
		647	TUMKUR - NELAMANGALA(6L) (NHAI) (N24001681)	8-2022	8/2025 (Mar-2026) {3/2026}	2,032.15 (2,032.15) {2,032.15}	185.64	52.88

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		648	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA (NHAI) (N24001682)	11-2021	3/2024 (Mar-2024) {12/2026}	294.62 (309.90) {309.90}	57.86	15.14
		649	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION (NHAI) (N24001684)	9-2020	1/2023 (Sep-2020) {5/2025}	688.00 (602.09) {688.00}	514.23	80.07
		650	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 (NHAI) (N24001687)	10-2021	10/2023 (Dec-2025) {12/2025}	1,331.77 (2,082.98) {2,082.98}	483.94	77.06
		651	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM. 54.370 TO KM. 101.400 (BI (MoRTH) (N24001936)	3-2021	3/2023 (Jul-2024) {7/2024}	344.79 (N.A.) {344.79}	10.00	90.00
		652	BALANCE WORK OF REHABILITATION AND UPGRADING TO 2LANE/2LANE WITH PAVED SHOULDER CONFIGURATION AND ST (MoRTH) (N24001937)	2-2023	2/2024 (Feb-2025) {2/2025}	398.48 (N.A.) {398.48}	5.00	50.00
		653	CONSTRUCTION OF ELEVATED CORRIDOR FROM KM. 135.650 TO 136.300 ON 63, FROM KM. 249 TO KM. 250.050 ON (MoRTH) (N24001938)	6-2021	6/2024 (Jun-2025) {6/2025}	298.00 (N.A.) {298.00}	10.70	52.00
		654	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24001940)	1-2023	1/2026 (Sep-2025) {9/2025}	166.58 (N.A.) {166.58}	3.54	-
		655	WIDENING TO 4 LANE FROM KM. 133.00 TO 158.04 (DESIGN CHAINAGE KM. 130.88 TO 155.145) (SHIRUR CROSS T (MoRTH) (N24001941)	1-2023	1/2025 (Jan-2025) {1/2025}	350.69 (N.A.) {350.69}	10.00	56.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		656	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM. 33.13 TO KM. 40.23 AND KM. 52.00 TO KM. 71.00 (EX (MoRTH) (N24001943)	9-2022	3/2024 (Jan-2025) {1/2025}	172.98 (N.A.) {172.98}	6.48	65.00
		657	WIDENING TO INTERMEDIATE/TWO LANE TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHANAGES KM 112.750 TO (MoRTH) (N24001944)	1-2023	6/2024 (Jul-2024) {7/2024}	255.88 (N.A.) {255.88}	60.99	78.24
		658	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 116.800 TO 149.070(DESIGN CHANGES) ON HOSADURGA HOL (MoRTH) (N24001945)	8-2022	2/2024 (Dec-2024) {12/2024}	170.34 (N.A.) {170.34}	4.25	72.00
		659	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM 24.400 TO 27.270, 40.500 TO 41.900, 84.300 TO 88.20 (MoRTH) (N24001946)	11-2022	11/2024 (Nov-2024) {11/2024}	218.93 (N.A.) {218.93}	10.00	95.25
		660	WIDENING TO EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FROM DESIGN KM 153.00 (MoRTH) (N24001947)	2-2023	2/2025 (Feb-2025) {2/2025}	177.94 (N.A.) {177.94}	6.66	47.00
		661	WIDENING TO 4 LANE FROM KM 51.60 TO 76.20 (HEBRI TO PARKALA) AND FROM KM 85.20 TO 88.90 (KARAVALI JU (MoRTH) (N24001948)	10-2022	10/2024 (Dec-2024) {12/2024}	355.72 (N.A.) {355.72}	11.32	60.00
		662	FOUR LANING OF LEFT OVER WORKS OF HOSPET BELLARY KARNATAKA/ AP BORDER FROM KM.280.080 TO KM. 375.450 (NHAI) (N24001989)	3-2023	5/2025 (N.A.) {5/2025}	830.28 (N.A.) {830.28}	692.62	77.10
		663	DEVELOPMENT OF 6 LANE ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KM. 97.000 TO KM. 162.500 MARADGI S (NHAI) (N24001993)	12-2022	10/2025 (N.A.) {10/2025}	1,589.00 (N.A.) {1,589.00}	732.47	63.15

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		664	4/6L OF BANGALORE - PUNE SECTION OF BYPASS CONNECTING DHARWAD - HUBLI FROM KM. 403.80 TO KM. 433.20 (NHAI) (N24001994)	5-2022	3/2023 (Sep-2025) {9/2025}	1,135.39 (N.A.) {1,135.39}	396.27	70.68
		665	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM 422.000 TO 523.600 (CHITR (MoRTH) (N24002011)	12-2021	6/2024 (Dec-2024) {12/2024}	516.96 (N.A.) {516.96}	19.93	75.00
		666	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 40.00 TO KM 75.00 (EXISTING CHAINAGES) OF MANGALOR (MoRTH) (N24002012)	3-2023	3/2025 (Mar-2025) {3/2025}	718.52 (N.A.) {718.52}	24.81	23.00
		667	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM KM.0 TO KM. 80 ON NH 548B (VIJAYAPURA- SANKESWAR SE (MoRTH) (N24002013)	3-2021	2/2022 (Oct-2024) {10/2024}	766.64 (N.A.) {766.64}	13.55	75.00
		668	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24002186)	3-2024	9/2025 (N.A.) {9/2025}	166.58 (N.A.) {166.58}	3.62	-
		669	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM 55.6 TO KM 90.7 (EXISTING CHAINAGES) OF NH- 766C ((MoRTH) (N24002187)	2-2024	2/2026 (N.A.) {2/2026}	313.56 (N.A.) {313.56}	53.65	-
		670	WIDENING TO 2L+PS FROM KM 71.00 TO 104.00 (EXISTING CHAINAGES) (SARJAPUR TO PATTADKALLU) ON BHANAPUR (MoRTH) (N24002188)	3-2024	3/2026 (N.A.) {3/2026}	445.62 (N.A.) {445.62}	33.24	-
		671	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 (DESIGN CHAINAGE 0.00) TO KM 23.338 (DESIGN C (MoRTH) (N24002189)	9-2024	3/2026 (N.A.) {3/2026}	196.05 (N.A.) {196.05}	2.34	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		672	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP (MoRTH) (N24000334)	3-2015	11/2015 (Aug-2024) {8/2024}	165.67 (N.A.) {165.67}	126.47	98.99
		673	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION (NHAI) (N24000462)	7-2012	8/2016 (Jan-2020) {12/2025}	1,655.01 (1,990.99) {1,990.99}	1,824.10	97.80
		674	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS ? PA (MoRTH) (N24001156)	1-2017	9/2017 (May-2023) {5/2023}	166.67 (N.A.) {264.34}	192.08	100.00
		675	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH (MoRTH) (N24001157)	8-2016	2/2017 (Jul-2024) {7/2024}	175.50 (N.A.) {241.60}	178.73	90.01
		676	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 (MoRTH) (N24001158)	3-2018	6/2019 (Dec-2023) {12/2023}	159.97 (N.A.) {242.61}	113.15	100.00
		677	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHA SECTION (MoRTH) (N24001159)	1-2018	7/2018 (N.A.) {3/2022}	159.70 (N.A.) {159.70}	142.88	100.00
		678	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR (MoRTH) (N24001160)	9-2017	10/2018 (Apr-2022) {4/2022}	191.60 (N.A.) {191.60}	112.01	100.00
		679	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- (MoRTH) (N24001161)	12-2017	1/2019 (Apr-2022) {4/2022}	297.30 (N.A.) {318.28}	277.27	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		680	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN (MoRTH) (N24001162)	3-2018	10/2018 (Nov-2022) {11/2022}	325.86 (N.A.) {386.41}	356.76	100.00
		681	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH- 50 UNDER EPC MODE IN THE STATE OF KARN (MoRTH) (N24001164)	10-2016	3/2017 (Jul-2022) {7/2022}	396.96 (N.A.) {396.96}	329.58	100.00
		682	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT (MoRTH) (N24001165)	11-2016	3/2017 (Oct-2021) {10/2021}	314.90 (N.A.) {314.90}	233.95	100.00
		683	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15- 775) (MoRTH) (N24001166)	3-2015	1/2016 (N.A.) {7/2024}	159.12 (N.A.) {159.12}	127.72	98.00
		684	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT (MoRTH) (N24001168)	5-2018	5/2018 (Dec-2023) {12/2023}	171.60 (N.A.) {171.60}	129.72	100.00
		685	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U (MoRTH) (N24001172)	1-2017	8/2017 (N.A.) {6/2022}	291.49 (N.A.) {291.49}	238.77	100.00
		686	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI ? JADERCELA SECTION (MoRTH) (N24001173)	2-2017	5/2019 (N.A.) {10/2025}	157.32 (188.00) {187.61}	43.16	60.00
		687	WIDENING TO 2-LANE WIH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT (MoRTH) (N24001387)	1-2017	9/2017 (May-2023) {5/2023}	264.34 (N.A.) {264.34}	201.07	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		688	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA (MoRTH) (N24001388)	3-2019	12/2019 (Nov-2024) {11/2024}	423.15 (N.A.) {423.15}	268.97	82.00
	<u>STEEL</u>	689	SCREENING PLANT-II, DONIMALAI (NMDC) (N12000136)	9-2023	8/2026 (N.A.) {8/2026}	1,043.63 (N.A.) {1,043.63}	201.25	21.50
	<u>URBAN DEVELOPMENT</u>	690	BANGALORE METRO RAIL PROJECT PHASE-2 (BMRCL) (N28000058)	2-2014	2/2021 (N.A.) {3/2025}	26,405.14 (N.A.) {26,405.14}	20,936.29	-
		691	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B (BMRCL) (N28000151)	6-2021	6/2026 (N.A.) {6/2026}	14,788.10 (N.A.) {14,788.10}	2,424.04	-
<u>KERALA</u>	<u>CIVIL AVIATION</u>	692	CALICUT AIRPORT - DEVELOPMENT OF ADDITIONAL RESA ON EITHER END ON RUNWAY 10-28 AT CALICUT AIRPORT (AAI) (N04000111)	6-2023	9/2025 (N.A.) {9/2025}	484.57 (323.98) {323.98}	74.67	18.30
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	693	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA (CPWD EDUCATION) (N28000140)	7-2019	3/2021 (N.A.) {11/2025}	753.63 (N.A.) {753.63}	411.86	67.00
	<u>PETROLEUM</u>	694	REPLACEMENT AND EXTENSION OF JETTY PIPELINES AT KOCHI REFINERY (BPCL) (N16000508)	3-2023	3/2026 (N.A.) {3/2026}	621.87 (N.A.) {621.87}	180.09	82.50
		695	SETTING UP POLYPROPYLENE UNIT AT KOCHI REFINERY (BPCL) (N16000530)	12-2023	10/2027 (N.A.) {10/2027}	4,460.00 (N.A.) {4,460.00}	240.70	11.10

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>RAILWAYS</u>	696	TRIVANDRUM-KANYAKUMARI DOUBLING (SR) (N22000399)	2-2015	3/2024 (N.A.) {12/2027}	1,431.90 (N.A.) {3,785.45}	3,184.42	42.10
		697	ERNAKULAM-KUMBALAM - PATCH DOUBLING (7.71 KM) (SR) (N22000619)	12-2010	3/2028 (N.A.) {12/2026}	600.82 (N.A.) {595.39}	282.77	8.00
		698	KUMBALAM-THURAVUR - PATCH DOUBLING (15.59 KM) (SR) (N22000620)	12-2011	3/2027 (N.A.) {12/2026}	812.85 (N.A.) {802.80}	287.48	7.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	699	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE (NHAI) (N24001648)	8-2022	1/2026 (N.A.) {1/2026}	2,429.52 (N.A.) {2,429.52}	1,185.00	62.02
		700	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 (NHAI) (N24001649)	12-2021	2/2025 (Feb-2025) {1/2026}	3,273.61 (N.A.) {3,273.61}	789.16	61.81
		701	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTAM SECTION OF NH- 66(OLD NH-47) FROM KM. 517+250 TO KM.54 (NHAI) (N24001650)	12-2021	1/2025 (Apr-2026) {4/2026}	3,635.64 (N.A.) {3,635.64}	324.02	39.20
		702	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O (NHAI) (N24001651)	9-2021	9/2024 (Mar-2026) {9/2024}	2,878.97 (N.A.) {2,878.97}	570.80	44.65
		703	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR (NHAI) (N24001652)	3-2020	6/2022 (Feb-2024) {6/2024}	210.37 (216.94) {216.94}	198.10	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		704	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH ?66 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 ((NHAI) (N24001653)	11-2021	4/2025 (N.A.) {4/2025}	3,565.82 (N.A.) {3,064.11}	2,082.00	62.43
		705	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 (NHAI) (N24001654)	6-2021	3/2025 (Feb-2026) {2/2026}	2,641.37 (N.A.) {2,641.37}	607.07	76.90
		706	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX (NHAI) (N24001655)	6-2021	2/2025 (N.A.) {11/2025}	3,606.00 (3,946.56) {3,946.56}	3,120.31	73.35
		707	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. (NHAI) (N24001656)	6-2021	3/2025 (N.A.) {12/2025}	2,595.00 (N.A.) {4,009.57}	3,071.01	66.73
		708	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC (NHAI) (N24001657)	6-2021	10/2024 (Dec-2025) {12/2025}	2,842.14 (N.A.) {2,842.14}	477.69	71.30
		709	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM (NHAI) (N24001658)	1-2021	7/2024 (Mar-2025) {3/2025}	4,265.42 (N.A.) {4,728.40}	3,474.31	99.10
		710	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH (NHAI) (N24001659)	2-2021	7/2024 (Mar-2025) {3/2025}	3,375.31 (3,824.07) {3,824.07}	2,351.62	98.40

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		711	SIX LANING OF THALIPARAMBHA-MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH (NHAI) (N24001660)	8-2020	2/2024 (Aug-2025) {3/2026}	2,714.60 (3,557.65) {2,714.60}	1,904.06	72.77
		712	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 (NHAI) (N24001661)	10-2020	4/2024 (May-2025) {3/2026}	3,219.47 (3,898.46) {3,896.46}	2,295.34	58.14
		713	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH (NHAI) (N24001662)	5-2020	5/2024 (Nov-2021) {7/2025}	1,981.07 (2,651.79) {1,981.07}	1,543.14	97.38
		714	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ (NHAI) (N24001663)	6-2020	4/2024 (Oct-2021) {3/2026}	3,041.65 (3,867.66) {3,041.65}	2,406.52	82.75
		715	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ (NHAI) (N24001664)	6-2020	4/2024 (Oct-2021) {3/2026}	1,746.45 (2,538.06) {1,746.45}	1,262.19	79.25
		716	WIDENING/DEVELOPMENT OF EXISTING NH-85 FROM KM 0.000 TO KM 124.636 SECTION TO 2L/@L+PS SECTION IN TH (NHAI) (N24002074)	8-2022	6/2025 (N.A.) {6/2025}	1,231.74 (N.A.) {1,231.74}	486.00	49.70
		717	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH (NHAI) (N24000784)	2-2018	2/2023 (Dec-2024) {7/2025}	1,424.77 (2,065.95) {2,065.95}	902.09	95.50
		718	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK (MoRTH) (N24001369)	2-2017	8/2017 (Mar-2022) {8/2024}	294.28 (296.53) {296.53}	286.80	98.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		719	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) (MoRTH) (N24001370)	2-2017	9/2017 (Jan-2023) {8/2024}	380.76 (372.87) {372.87}	347.04	100.00
	<u>URBAN DEVELOPMENT</u>	720	KOCHI METRO RAIL PROJECT PHASE II FROM JLN STADIUM TO INFOPARK VIA KAKKANAD (KMRCL) (N28000158)	7-2018	11/2026 (N.A.) {11/2026}	1,957.05 (N.A.) {1,957.05}	250.63	7.40
<u>LADAKH</u>	<u>CIVIL AVIATION</u>	721	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT (AAI) (N04000078)	7-2018	9/2021 (Oct-2025) {10/2025}	480.33 (640.00) {640.00}	416.49	65.92
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	722	CONSTRUCTION OF REALIGNMENT BETWEEN PANDRASS- PASHKYUN (TOTAL LENGTH 27.10 KM) ON ROAD ZOZILA-KARGIL (BRO) (N24001999)	11-2021	6/2025 (N.A.) {6/2025}	426.14 (N.A.) {426.14}	16.27	37.00
		723	KARGIL-ZANSKR PACKAGE-1 (NHIDCL) (N24001343)	3-2021	1/2023 (Dec-2024) {11/2025}	384.23 (N.A.) {384.23}	162.54	60.40
		724	KARGIL-ZANSKR PACKAGE-2 (NHIDCL) (N24001344)	3-2021	1/2023 (Feb-2025) {11/2025}	404.89 (N.A.) {404.89}	244.21	67.27
		725	KARGIL-ZANSKR PACKAGE-3 (NHIDCL) (N24001345)	8-2020	1/2023 (Aug-2025) {8/2025}	381.01 (N.A.) {381.01}	230.28	76.11
		726	KARGIL-ZANSKR PACKAGE-8 (NHIDCL) (N24001348)	3-2021	1/2023 (Aug-2025) {8/2025}	398.37 (N.A.) {398.37}	279.84	84.05
<u>MADHYA PRADESH</u>	<u>CIVIL AVIATION</u>	727	UPGRADATION OF JABALPUR AIRPORT (AAI) (N04000087)	6-2016	6/2021 (Jul-2024) {7/2024}	412.24 (N.A.) {412.24}	403.17	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		728	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 (AAI) (N04000098)	10-2021	8/2023 (Aug-2024) {8/2024}	446.12 (455.00) {455.00}	451.55	100.00
	COAL	729	KANCHAN OC EXPANSION (SECL) (N06000125)	12-2014	3/2021 (Mar-2026) {3/2026}	371.04 (N.A.) {371.04}	137.63	47.00
		730	AMADAND OPENCAST EXPANSION PROJECT (SECL) (N06000148)	3-2016	3/2021 (Mar-2027) {3/2027}	869.44 (N.A.) {869.44}	272.09	75.00
		731	GANDHIGRAM UG MINE (WCL) (N06000183)	8-2019	3/2026 (N.A.) {3/2026}	414.16 (N.A.) {414.16}	11.75	28.00
		732	BLOCK-B EXPANSION OPENCAST PROJECT (NCL) (N06000184)	7-2019	3/2023 (N.A.) {3/2027}	998.71 (N.A.) {998.71}	453.75	46.24
		733	NIGAH EXPANSION OCP (15 TO 25 MTPA) (NCL) (N06000196)	11-2020	3/2025 (N.A.) {3/2028}	1,729.68 (N.A.) {1,729.68}	772.95	44.93
		734	RAMPUR BATURA OC (4.0 MTY) (SECL) (N06000233)	7-2019	3/2026 (N.A.) {3/2026}	1,248.93 (N.A.) {1,248.93}	490.58	44.00
		735	TAWA III UG MINE (WCL) (N06000250)	12-2021	3/2027 (N.A.) {3/2027}	314.09 (N.A.) {324.25}	0.56	9.00
		736	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY) (WCL) (N06000257)	9-2022	3/2027 (N.A.) {3/2027}	399.20 (N.A.) {497.01}	64.13	42.00
		737	VISHNUPURI UG TO OC (WCL) (N06000260)	11-2022	3/2029 (N.A.) {3/2029}	220.62 (N.A.) {227.65}	0.00	7.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		738	URDHAN OC (WCL) (N06000265)	1-2023	3/2031 (N.A.) {3/2031}	206.88 (N.A.) {228.42}	22.12	9.00
		739	SHARDA UG (WCL) (N06000266)	9-2023	3/2028 (N.A.) {3/2028}	166.25 (N.A.) {200.16}	1.69	11.00
	<u>PETROLEUM</u>	740	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF (BPCL) (N16000518)	5-2023	5/2028 (N.A.) {5/2028}	43,367.00 (N.A.) {43,367.00}	1,687.00	13.00
	<u>POWER</u>	741	SHAJAPUR 325MW SOLAR PV PROJECT (NTPC) (N18000348)	6-2022	3/2024 (Jun-2025) {6/2025}	1,530.49 (N.A.) {1,578.34}	1,219.41	100.00
		742	TS FOR EVACUATION POWER RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX): PART- C (PGCIL) (N18000392)	8-2024	8/2026 (N.A.) {8/2026}	2,708.00 (N.A.) {2,708.00}	622.84	25.70
		743	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-2 5.5GW] [JAISALMER/BARME (PGCIL) (N18000399)	10-2024	10/2026 (N.A.) {10/2026}	3,674.00 (N.A.) {3,674.00}	345.36	12.70
	<u>RAILWAYS</u>	744	RAMGANJMUNDI-BHOPAL (NL),WCR (WCR) (220100314)	4-2001	12/2025 (Dec-2025) {6/2026}	3,032.00 (3,032.46) {5,125.16}	3,513.09	69.00
		745	RATLAM-MHOW-KHANDWA-AKOLA (GC) (WR) (N22000120)	4-2008	2/2027 (Feb-2027) {2/2027}	5,677.88 (5,677.80) {6,203.51}	4,314.25	80.00
		746	KATNI - SINGRAULI DOUBLING PROJECT (WCR) (N22000351)	12-2015	12/2026 (Dec-2027) {12/2027}	2,445.29 (2,445.30) {4,353.50}	3,122.03	92.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		747	KATNI GRADE SEPARATOR/BYE PASS (WCR) (N22000416)	8-2016	9/2024 (Jun-2025) {9/2024}	1,247.64 (1,247.64) {2,300.00}	1,453.81	89.00
		748	ANUPPUR-KATNI (SECR) (N22000485)	4-2015	12/2021 (Dec-2023) {3/2025}	1,860.94 (1,680.00) {2,311.02}	1,955.51	100.00
		749	NIMACH BADI SADRI NEW LINE PROJECT (WR) (N22000503)	4-2017	3/2022 (Dec-2026) {12/2026}	495.18 (N.A.) {495.18}	306.32	46.00
		750	NIMACH-RATLAM (133 KM) (WR) (N22000536)	10-2021	10/2027 (Dec-2025) {12/2025}	1,095.88 (1,095.88) {1,095.88}	1,197.14	72.00
		751	SATNA - REWA (50 KM) (WCR) (N22000554)	11-2015	3/2026 (N.A.) {3/2026}	500.00 (40.00) {500.00}	1.41	80.00
		752	INDORE BUDNI (INDORE JABALPUR) (RVNL) (N22000601)	9-2018	9/2030 (N.A.) {9/2030}	7,474.01 (N.A.) {7,393.75}	1,004.86	-
	ROAD TRANSPORT AND HIGHWAYS	753	4LBERKHEDI TO GODPEHRA NH-44 (NHAI) (N24001614)	2-2022	11/2024 (N.A.) {12/2025}	524.84 (N.A.) {524.84}	2,455.45	60.00
		754	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I) (NHAI) (N24001615)	3-2021	4/2024 (Jun-2025) {6/2025}	790.78 (N.A.) {790.78}	2,141.21	77.02
		755	KATNI BYPASS FROM KM. 359.50 TO KM. 378.50 (NHAI) (N24001618)	9-2019	9/2022 (N.A.) {2/2025}	194.40 (235.00) {235.00}	208.32	98.84
		756	4L OF CHANDESARA TO KHEDAKHAJURIYA FROM KM. 0.000 TO (-) 750 AND KM 0.000 TO KM 41.400 OF NH-752D (NHAI) (N24001759)	1-2020	6/2024 (Dec-2025) {12/2025}	909.84 (N.A.) {909.84}	503.76	99.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		757	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] (NHAI) (N24001762)	10-2021	1/2024 (Dec-2025) {12/2025}	1,146.22 (N.A.) {1,146.22}	663.10	91.40
		758	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] (NHAI) (N24001766)	1-2022	10/2024 (N.A.) {12/2025}	1,011.29 (N.A.) {1,011.29}	318.76	70.68
		759	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND (NHAI) (N24001767)	1-2021	4/2024 (N.A.) {12/2025}	1,001.69 (N.A.) {1,001.69}	520.29	83.00
		760	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69 (NHAI) (N24001770)	2-2022	3/2024 (Mar-2025) {7/2025}	417.51 (N.A.) {417.51}	312.94	100.00
		761	2- LANE WITH PAVED SHOULDERS OF HINOTIYA TO MEHULWA FROM DESIGN KM 27+000 9OF EXISTING SH-19 KM 26+5 (NHAI) (N24001921)	8-2021	9/2025 (N.A.) {9/2025}	581.65 (592.03) {581.65}	135.75	45.78
		762	CONSTRUCTION OF MIHONA BYPASS, LAHAR BYPASS, DABOH BYPASS and BHANDER BYPASS (TOTAL LENGTH 20.60 KM) (MoRTH) (N24001962)	3-2022	12/2024 (N.A.) {3/2025}	179.19 (N.A.) {179.19}	47.91	96.00
		763	UPGRADATION OF NASRULLAGANI-REHTI-BUDHNI SCCTION TO 2-LANE WITH PAVED SHOULDER FROM KM 0+150 TO KM (MoRTH) (N24001963)	12-2021	10/2024 (N.A.) {9/2025}	305.12 (N.A.) {305.12}	71.47	34.46
		764	UPGRADATION and WIDENING OF JHARKHEDA- BERASIA - DHOLKHEDI FROM DESIGN KM 0+000 TO KM 87+900 (DESIGN (MoRTH) (N24001964)	3-2022	5/2025 (N.A.) {5/2025}	365.21 (N.A.) {365.21}	112.27	64.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		765	REHABILITATION AND UPGRADATION OF KURWAI?MUNGAOLI?CHANDERI ROAD SECTION OF NH-346, FROM DESIGN CHAIN (MoRTH) (N24001965)	3-2022	2/2025 (N.A.) {12/2025}	386.49 (N.A.) {386.49}	77.42	48.77
		766	4L GREENFIELD RUDHI TO DESHGAON (PKG V OF BETUL- KHANDWA/DESHGAON) - N/04015/06003/MP (NHAI) (N24001967)	11-2018	10/2025 (N.A.) {10/2025}	521.21 (N.A.) {521.21}	110.63	49.57
		767	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF JIRAPUR- SUSNER-MP-RJ B (MoRTH) (N24002018)	1-2022	3/2025 (N.A.) {3/2025}	239.72 (232.22) {232.22}	73.40	100.00
		768	UPGRADATION OF DINDORI- SAGARTOLA-KABICHABUTRA (MP-CG BORDER) SECTION OF NH -45 FROM KM 0+00(DESIGN) (MoRTH) (N24002019)	1-2022	9/2025 (N.A.) {9/2025}	329.14 (319.09) {319.09}	52.70	50.12
		769	CONSTRUCTION OF KAITHI-PADARIA KALA BYPASS, PATNA-TAMOLI BYPASS, JASO BYPASS , NAGOD BYPASS (TOTAL L (MoRTH) (N24002020)	3-2022	10/2025 (N.A.) {10/2025}	158.36 (158.00) {158.36}	22.68	30.00
		770	BALANCE WORK OF 4L OF NAURADEHI SANCTUARY DE-SCOPED STRETCH OF HIRAN RIVER TO SINDOOR RIVER FROM KM. (NHAI) (N24002067)	1-2021	7/2023 (N.A.) {4/2025}	178.18 (N.A.) {178.18}	161.64	94.65
		771	CONSTRUCTION OF 4-LANE FROM BARELA TO MANEGAON SECTION OF NH-30 FROM DESIGN CH. 2.900 TO DESIGN CH. (NHAI) (N24002068)	12-2022	3/2025 (N.A.) {12/2025}	652.33 (N.A.) {652.33}	334.34	73.16
		772	CONSTRUCTION OF ADDITIONAL 3 LANE WITH PAVED SHOULDER (DESIGN LENGTH 8.87 KM) AS REALIGNMENT OF BAKA (NHAI) (N24002069)	7-2022	12/2024 (N.A.) {12/2024}	209.29 (N.A.) {209.29}	140.22	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		773	INDORE - EDLABAD (PKG-II) [TEJAJINAGAR TO BALWARA] (NHAI) (N24002070)	1-2022	1/2025 (N.A.) {1/2026}	1,162.80 (N.A.) {1,162.80}	537.71	80.50
		774	CONSTRUCTION OF (I) 4-LANE HIGHWAY FROM VIDISHA TO HINOTIYA FROM KM. 0.000 TO KM. 27.000 (LENGTH=27 (NHAI) (N24002077)	9-2022	12/2025 (N.A.) {12/2025}	1,000.63 (N.A.) {1,000.63}	210.15	53.86
		775	FOUR LANING OF RAGHOGARH (DESIGN CH.29.300/EXISTING CH. 29.555) TO NANASA (DESIGN CH.92.971/EXISTING (NHAI) (N24002166)	3-2024	3/2026 (Mar-2026) {3/2026}	799.20 (N.A.) {799.20}	306.28	35.10
		776	BALANCE WORKS OF 4 LANE DIVIDED CARRIAGEWAY OF MISSING LINK SECTION OF NH-39 (REWA BYPASS) FROM JUNC (NHAI) (N24002200)	4-2024	4/2026 (N.A.) {4/2026}	355.36 (N.A.) {355.36}	66.14	34.40
		777	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 (MoRTH) (N24000513)	3-2015	8/2017 (Dec-2023) {6/2025}	511.83 (N.A.) {511.83}	478.84	93.06
	URBAN DEVELOPMENT	778	BHOPAL METRO RAIL (MPMRCL) (N28000124)	11-2018	2/2023 (Jun-2028) {6/2028}	6,941.40 (N.A.) {6,941.40}	3,043.74	42.16
		779	INDORE METRO RAIL (MPMRCL) (N28000125)	11-2018	2/2023 (Dec-2028) {12/2028}	7,500.80 (N.A.) {7,500.80}	3,798.28	53.54
MAHARASHTRA	CIVIL AVIATION	780	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT (AAI) (N04000079)	3-2017	4/2021 (Dec-2023) {12/2023}	475.39 (N.A.) {533.56}	533.14	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		781	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM (AAI) (N04000096)	6-2017	12/2020 (Apr-2024) {4/2024}	255.68 (270.00) {270.00}	267.86	100.00
	<u>COAL</u>	782	AMALGAMATED YEKONA-I YEKONA-II (WCL) (N06000132)	8-2015	3/2025 (N.A.) {3/2025}	727.28 (N.A.) {727.28}	530.02	86.00
		783	UKNI DEEP OC (WCL) (N06000179)	1-2019	3/2021 (Mar-2025) {3/2025}	237.06 (N.A.) {318.14}	163.86	91.00
		784	GHONSA EXPANSION DEEP OC (WCL) (N06000205)	3-2021	3/2028 (N.A.) {3/2029}	184.71 (N.A.) {241.72}	9.25	6.00
		785	SASTI EXPANSION OC (WCL) (N06000206)	8-2020	3/2026 (N.A.) {3/2026}	319.04 (N.A.) {371.59}	68.64	24.00
		786	DHUPTALA OC(SASTI UG TO OC) (WCL) (N06000209)	10-2021	3/2028 (N.A.) {3/2028}	711.00 (N.A.) {720.87}	159.15	33.00
		787	ADASA UG TO OC (1.50 MTY) (WCL) (N06000219)	11-2018	3/2024 (Mar-2025) {3/2025}	316.00 (N.A.) {333.43}	208.20	78.00
		788	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) (WCL) (N06000222)	2-2020	3/2027 (N.A.) {3/2027}	822.88 (N.A.) {1,184.33}	578.89	48.00
		789	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) (WCL) (N06000226)	9-2018	3/2024 (Mar-2025) {3/2025}	235.90 (N.A.) {313.34}	116.46	87.00
		790	SAONER UG MINE I EXPANSION (WCL) (N06000251)	1-2022	3/2028 (N.A.) {3/2028}	228.64 (N.A.) {253.51}	118.34	27.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		791	SINGHORI DEEP OC (WCL) (N06000252)	5-2022	3/2029 (N.A.) {3/2029}	335.75 (N.A.) {421.84}	22.01	16.00
		792	MAKARDHOKDA I EXPANSION OC (WCL) (N06000253)	6-2022	3/2026 (N.A.) {3/2026}	361.87 (N.A.) {497.06}	33.90	12.00
		793	BHATADI EXPANSION OC (WCL) (N06000254)	5-2022	3/2028 (N.A.) {3/2028}	580.60 (N.A.) {729.86}	61.33	17.00
		794	NEW MAJARI UG TO OC (3.0 MTY) (WCL) (N06000255)	9-2022	3/2027 (N.A.) {3/2027}	402.27 (N.A.) {496.38}	47.99	27.00
		795	BHANEKAON OC (1.15MTY) (WCL) (N06000256)	9-2022	3/2028 (N.A.) {3/2028}	405.20 (N.A.) {494.60}	10.21	7.00
		796	GOKUL EXPANSION OC (WCL) (N06000264)	4-2021	3/2026 (N.A.) {3/2026}	309.58 (N.A.) {456.95}	3.65	7.00
		797	KOLGAON EXPANSION (DEEP) OC (WCL) (N06000267)	9-2023	3/2027 (N.A.) {3/2027}	198.71 (N.A.) {206.19}	0.55	5.00
		798	AMALGAMATED GAURI PAUNI EXPANSION OC (WCL) (N06000271)	3-2024	3/2030 (N.A.) {3/2030}	1,225.21 (N.A.) {1,428.25}	52.83	17.00
		799	GAURI CENTRAL OCM (WCL) (N06000278)	6-2024	3/2030 (N.A.) {3/2030}	973.07 (N.A.) {1,015.07}	0.00	-
		800	BALLARPUR NORTHWEST OC MINE (WCL) (N06000282)	12-2022	3/2029 (N.A.) {3/2029}	360.18 (N.A.) {360.18}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		801	NORTHERN EXTENSION OF MUNGOLI NIRGUDA DEEP OC (WCL) (N06000283)	6-2024	3/2029 (N.A.) {3/2029}	1,024.91 (N.A.) {1,184.44}	0.00	-
		802	AMALGAMATED GONDEGAON - GHATROHAN EXPANSION OCM (WCL) (N06000284)	9-2024	3/2029 (N.A.) {3/2029}	668.54 (N.A.) {871.59}	0.00	-
		803	WAGHODA UG (WCL) (N06000293)	1-2025	3/2030 (N.A.) {3/2030}	379.30 (N.A.) {379.30}	0.00	-
		804	KOLARPIMPRI EXPANSION OCM (2.50 MTY) (WCL) (N06000294)	2-2025	3/2030 (N.A.) {3/2030}	630.37 (N.A.) {630.37}	0.00	-
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	805	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI (CPWD EDUCATION) (N28000117)	1-2018	7/2020 (Nov-2023) {2/2024}	223.37 (275.00) {230.00}	141.16	100.00
	<u>HEALTH AND FAMILY WELFARE</u>	806	500 BEDDED HOSPITAL INCLUDING 50 SUPERSPECIALITY BEDS FOR ESIC AT PUNE (CPWD) (N21000033)	7-2022	9/2025 (N.A.) {9/2025}	429.25 (N.A.) {429.25}	99.08	-
	<u>PETROLEUM</u>	807	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS (ONGC) (N16000213)	12-2015	4/2018 (Dec-2023) {6/2025}	3,190.69 (3,375.90) {3,375.90}	3,051.26	89.50
		808	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND (GAIL) (N16000430)	5-2019	4/2025 (Oct-2025) {10/2025}	8,797.00 (11,256.00) {11,256.00}	6,694.98	84.50
		809	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL (BPCL) (N16000442)	4-2021	6/2024 (N.A.) {4/2025}	1,164.69 (N.A.) {1,164.69}	893.78	84.10

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		810	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY (IOCL) (N16000446)	9-2021	10/2023 (Jun-2025) {6/2025}	378.00 (N.A.) {378.00}	142.31	90.60
		811	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI (BPCL) (N16000452)	5-2022	3/2024 (N.A.) {9/2024}	423.39 (N.A.) {423.39}	268.34	76.00
		812	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA) (IOCL) (N16000456)	9-2022	8/2025 (N.A.) {3/2026}	165.00 (N.A.) {165.00}	79.17	69.80
		813	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK (ONGC) (N16000470)	6-2022	10/2025 (N.A.) {2/2026}	4,144.41 (6,406.90) {6,406.90}	3,203.26	80.50
		814	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS (IOCL) (N16000487)	3-2022	3/2030 (N.A.) {9/2031}	865.00 (N.A.) {865.00}	66.06	2.80
		815	ANDHERI RESIDENTIAL TOWERS MUMBAI (IOCL) (N16000503)	6-2017	5/2025 (Jun-2026) {6/2026}	281.35 (389.67) {389.67}	218.84	50.80
		816	CONSTRUCTION OF ADDITIONAL TANKAGES AND ALLIED FACILITIES AT JNPT TERMINAL (IOCL) (N16000504)	4-2022	10/2024 (Aug-2026) {8/2026}	341.43 (436.14) {436.14}	244.76	49.50
		817	INSTALLATION OF INDEPENDENT DE- AROMATIZED SOLVENTS PRODUCTION FACILITIES AT MUMBAI REFINERY (BPCL) (N16000507)	3-2023	7/2025 (N.A.) {7/2025}	405.00 (N.A.) {405.00}	189.80	81.50

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		818	PART REPLACEMENT PIPELINE PROJECT (PRPP) (ONGC) (N16000515)	11-2022	5/2024 (Dec-2024) {11/2025}	1,219.48 (N.A.) {1,145.10}	1,145.10	87.00
		819	POL AND LOBS INSTALLATIONS WITH RECEIPT PIPELINES AT RASAYANI (BPCL) (N16000519)	5-2023	5/2026 (N.A.) {5/2026}	2,585.00 (N.A.) {2,585.00}	525.74	56.50
		820	MHN TCPP PGC BGC PROJECT (MTPBP) (ONGC) (N16000526)	2-2024	5/2026 (N.A.) {5/2026}	2,329.45 (N.A.) {2,354.23}	672.00	45.90
		821	PRP-VIII GROUP B (NH AND BS ASSET) (ONGC) (N16000533)	6-2024	5/2026 (N.A.) {2/2026}	2,379.84 (N.A.) {2,379.84}	1,646.11	57.80
		822	HP TDAE UNIT IN MUMBAI REFINERY (HPCL) (N16000534)	6-2024	4/2026 (N.A.) {4/2026}	240.00 (N.A.) {240.00}	27.90	33.60
		823	INTEGRATED DEVELOPMENT OF 4 CONTRACT AREAS UNDER DSF2 (ONGC) (N16000537)	5-2023	4/2027 (N.A.) {4/2027}	6,183.79 (N.A.) {6,183.79}	0.00	12.60
		824	LUBE MODERNIZATION AND BOTTOM UPGRADATION PROJECT (HPCL) (N16000540)	12-2024	3/2028 (N.A.) {3/2028}	4,679.00 (N.A.) {4,679.00}	177.41	4.20
		825	BIKANER SOLAR POWER PROJECT (SJVN) (N18000335)	4-2022	5/2024 (N.A.) {9/2025}	5,491.89 (532.00) {5,491.89}	4,374.00	80.35
	POWER	826	TS FOR EVACUATION OF 7GW RE INJECTION AT KHAVDA PS UNDER PHASE-IV PART E4 (PGCIL) (N18000377)	11-2023	7/2025 (N.A.) {11/2025}	224.00 (N.A.) {224.00}	15.68	7.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	827	AHMEDNAGAR-PARLI VAIJNATH(NL) CR (CR) (N20100181)	2-1997	3/2026 (N.A.) {1/2026}	2,539.00 (N.A.) {4,957.27}	4,909.30	97.00
		828	MUMBAI URBAN TRANSPORT PROJECT PHASE-II (MRTP) (N22000092)	4-2008	3/2014 (N.A.) {3/2014}	8,087.11 (N.A.) {918.53}	7,349.29	-
		829	WARDHA-NANDED MAHARASHTRA (CR) (N22000231)	4-2008	3/2027 (N.A.) {1/2026}	3,445.48 (N.A.) {3,445.34}	3,156.47	47.00
		830	KALYAN-KASARA 3RD LINE (CR) (N22000233)	4-2011	12/2025 (N.A.) {12/2026}	792.89 (N.A.) {1,395.79}	882.04	50.00
		831	WARDHA-SEWAGRAM NGP 3RD LINE (CR) (N22000250)	4-2012	12/2025 (N.A.) {2/2026}	540.02 (N.A.) {540.02}	737.54	80.00
		832	WARDHA-BALHARSHAH - 3RD LINE (132 KM) (CR) (N22000356)	2-2015	12/2025 (N.A.) {3/2026}	1,384.72 (N.A.) {1,384.72}	1,590.45	67.00
		833	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) (CR) (N22000358)	2-2015	3/2027 (N.A.) {3/2027}	2,449.91 (N.A.) {2,449.91}	1,761.99	50.00
		834	PUNE-MIRAJ-LONDA (467 KM) (CR) (N22000359)	2-2015	2/2025 (N.A.) {5/2025}	3,627.47 (3,627.00) {7,037.24}	4,742.07	84.00
		835	DAUND - MANMAD (236 KM) (CR) (N22000360)	2-2016	12/2025 (N.A.) {1/2026}	2,081.27 (N.A.) {2,081.27}	2,768.50	88.00
		836	MANMAD - JALGAON - 3RD LINE (160 KM) (CR) (N22000361)	2-2016	12/2024 (N.A.) {3/2026}	1,035.16 (N.A.) {1,558.75}	1,692.15	97.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		837	WARDHA - NAGPUR - 4TH LINE (76 KM) (CR) (N22000362)	2-2016	12/2025 (N.A.) {2/2026}	638.00 (N.A.) {637.95}	968.65	80.00
		838	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) (SECR) (N22000420)	9-2016	12/2024 (N.A.) {12/2026}	3,544.92 (N.A.) {3,544.25}	3,081.12	95.00
		839	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (WR) (N22000434)	3-2010	10/2024 (N.A.) {3/2024}	311.00 (N.A.) {311.36}	0.00	-
		840	WADSA-GADHCHIROLI NEW LINE (52.36 KM) (SECR) (N22000480)	6-2018	3/2027 (N.A.) {12/2026}	1,886.05 (N.A.) {1,880.61}	807.87	25.00
		841	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (N22000511)	8-2022	8/2027 (N.A.) {3/2029}	955.00 (N.A.) {2,089.25}	117.54	-
		842	SOLAPUR-TULJAPUR-OSMANABAD (UMBRELLA WORK) (CR) (N22000513)	1-2019	3/2028 (N.A.) {12/2027}	904.92 (N.A.) {2,933.01}	1,150.11	10.00
		843	DHULE (BORVIHIR)-NARDANA (UMBRELLA WORK) (CR) (N22000514)	1-2019	12/2026 (N.A.) {3/2028}	492.76 (N.A.) {1,158.99}	234.48	5.00
		844	KALYAN-MURBAD VIA ULHASNAGAR (UMBRELLA WORK) (CR) (N22000515)	2-2023	3/2027 (N.A.) {3/2027}	836.12 (N.A.) {836.12}	9.29	-
		845	BARAMATI - LONAND (CR) (N22000615)	2-1999	3/2027 (N.A.) {3/2027}	736.44 (N.A.) {1,843.90}	712.06	50.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		846	MUMBAI URBAN TRANSPORT PROJECT IIIA (MRVC) (N22000627)	4-2019	12/2027 (N.A.) {12/2027}	33,690.00 (N.A.) {33,690.00}	2,156.62	-
		847	NAGPUR- NAGBHIR RAILWAY LINE GAUGE CONVERSION PROJECT (MRIDC) (N22000629)	10-2019	6/2024 (N.A.) {10/2025}	1,400.00 (N.A.) {2,383.00}	1,791.72	87.00
	ROAD TRANSPORT AND HIGHWAYS	848	UPGRADATION OF ADHALGAON- JAMKHED SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH (MoRTH) (N24001448)	11-2021	2/2022 (N.A.) {2/2022}	223.35 (N.A.) {223.35}	209.36	87.88
		849	REPANPALLI TO SIRONCHA (MoRTH) (N24001468)	3-2022	6/2022 (N.A.) {6/2024}	282.07 (N.A.) {282.07}	34.65	-
		850	TUNNEL AT KHAMBATAKI GHAT SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0 (NHAI) (N24001486)	2-2019	2/2022 (Dec-2024) {8/2025}	493.00 (N.A.) {493.00}	409.36	77.64
		851	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL- ALANDI SECTION (NHAI) (N24001488)	9-2021	9/2023 (Dec-2024) {8/2025}	618.45 (N.A.) {618.45}	672.67	96.90
		852	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) (NHAI) (N24001493)	12-2022	12/2024 (N.A.) {11/2025}	1,749.86 (N.A.) {1,749.86}	1,858.98	69.14
		853	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 ((NHAI) (N24001495)	11-2022	11/2024 (N.A.) {9/2025}	930.00 (N.A.) {930.00}	675.62	77.15
		854	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH- 965G (SAINT TUKARAM MARG) (NHAI) (N24001502)	9-2021	9/2023 (Jul-2025) {8/2025}	624.45 (580.15) {580.15}	420.42	0.50

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		855	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH- 965G (SAINT TUKARAM MARG) (NHAI) (N24001503)	9-2021	9/2023 (Jan-2025) {3/2025}	667.66 (666.21) {666.21}	610.63	3.00
		856	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) (NHAI) (N24001504)	5-2022	5/2024 (Jun-2025) {6/2025}	1,260.00 (N.A.) {1,260.00}	665.73	99.00
		857	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) (NHAI) (N24001505)	3-2022	3/2024 (Jun-2025) {6/2025}	1,549.02 (N.A.) {1,549.02}	699.00	87.24
		858	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) (NHAI) (N24001506)	2-2022	2/2024 (Jun-2025) {6/2025}	2,747.00 (N.A.) {2,747.00}	1,130.30	84.22
		859	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) (NHAI) (N24001507)	11-2022	5/2024 (Jun-2025) {6/2025}	1,124.00 (N.A.) {1,124.00}	483.84	75.15
		860	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) (NHAI) (N24001508)	11-2022	10/2024 (Jun-2025) {6/2025}	1,450.00 (N.A.) {1,450.00}	718.65	86.02
		861	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XV) [KM. 20.200 TO KM. 43.000 OF SPUR] (AKLOLI - AMNE) (NHAI) (N24001521)	11-2022	10/2024 (Jul-2025) {7/2025}	990.00 (N.A.) {990.00}	406.91	77.38
		862	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) (NHAI) (N24001546)	1-2023	1/2025 (N.A.) {1/2025}	1,025.20 (N.A.) {1,025.20}	457.33	44.61

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		863	BALANCE WORKS OF 4L PANVEL- INDAPUR SECTION OF NH-66 (OLD NH- 17) FROM KM 42.300 (KASU) TO KM 84.600 ((NHAI) (N24001607)	10-2022	5/2024 (Dec-2025) {12/2025}	332.00 (N.A.) {332.00}	283.14	74.75
		864	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) (NHAI) (N24001608)	9-2021	7/2025 (N.A.) {7/2025}	2,208.68 (N.A.) {2,208.68}	565.20	76.26
		865	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH- 66(OLD NH- 17) FROM KM 0.000 (PANVEL) TO (NHAI) (N24001609)	1-2023	12/2023 (Jun-2025) {9/2025}	151.26 (N.A.) {151.26}	153.77	89.80
		866	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL ? ALANDI S (NHAI) (N24001610)	1-2022	5/2024 (Mar-2025) {8/2025}	1,833.73 (N.A.) {1,833.73}	554.81	96.94
		867	FOUR LANING OF AURANGABAD- PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA . (NHAI) (N24001795)	10-2022	7/2024 (Jun-2025) {12/2024}	490.40 (N.A.) {289.00}	275.78	96.00
		868	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B (NHAI) (N24001796)	3-2022	10/2024 (Apr-2025) {4/2025}	1,013.33 (1,013.33) {1,111.33}	355.07	62.01
		869	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800 (NHAI) (N24001797)	10-2021	1/2024 (N.A.) {5/2025}	815.77 (N.A.) {815.77}	732.70	100.00
		870	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH- 53 (NHAI) (N24001798)	2-2021	11/2023 (N.A.) {5/2025}	540.21 (N.A.) {540.21}	457.12	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		871	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J (NHAI) (N24001799)	2-2021	10/2023 (N.A.) {12/2025}	1,166.96 (N.A.) {1,251.00}	1,098.21	81.17
		872	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794) (NHAI) (N24001804)	12-2019	9/2022 (Jun-2024) {12/2025}	1,654.07 (N.A.) {980.00}	887.38	97.66
		873	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH-166 (PKG ? II) (NHAI) (N24001834)	5-2023	5/2025 (N.A.) {5/2025}	839.00 (N.A.) {839.00}	478.38	58.80
		874	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH-166 (PKG?III) (NHAI) (N24001835)	5-2023	5/2025 (N.A.) {5/2025}	986.00 (N.A.) {986.00}	580.10	56.40
		875	REHABILITATION AND UP-GRADATION TO 4 LANE ROAD WITH PAVED SHOULDER CONFIGURATION OF SECTION FROM UND (MoRTH) (N24001880)	3-2022	7/2025 (N.A.) {7/2025}	778.18 (N.A.) {778.18}	135.78	-
		876	CONSTRUCTION OF NEW FOUR LANE BYPASS TO PARBHANI CITY (PARWA TO ASOLA) KM 463/265 TO KM 481/180 (DES (MoRTH) (N24001882)	3-2022	10/2024 (N.A.) {10/2024}	496.64 (N.A.) {496.64}	0.00	8.00
		877	CONSTRUCTION OF 4 LANE FLYOVER AT NAGPUR RTO CHOWK TO NAGPUR UNIVERSITY CAMPUS FROM CH 2/250 TO 5/10 (MoRTH) (N24001883)	3-2021	3/2024 (N.A.) {4/2024}	478.83 (N.A.) {478.83}	233.48	65.00
		878	REHABILITATION AND UPGRADATION OF SATANA TO MANGRUL (CHANDWAD) SECTION OF NH752 G DESIGN CH: KM 64.0 (MoRTH) (N24001884)	3-2023	5/2025 (N.A.) {5/2025}	428.80 (N.A.) {428.80}	54.11	30.69

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		879	REHABILITATION AND UP-GRADATION OF JINTUR- SHIRAD SHAHAPUR SECTION KM 258.300 TO KM 306.300 [DESIGN (MoRTH) (N24001885)	2-2023	12/2024 (N.A.) {12/2024}	414.81 (N.A.) {414.81}	0.00	-
		880	DEVELOPMENT/WIDENING OF TALEGAON ? CHAKAN ? SHIKRAPUR ? NHAVARA SECTION OF NH 548DG (NHAVARA TO CHOU (MoRTH) (N24001886)	10-2022	8/2024 (N.A.) {8/2024}	304.68 (N.A.) {304.68}	97.09	59.00
		881	REHABILITATION AND UPGRADATION OF PARLI TO SIRSALA SECTION OF NH- 361F (KM 136+700 TO 115+000) (LENGT (MoRTH) (N24001890)	2-2023	12/2024 (N.A.) {12/2024}	261.82 (N.A.) {261.82}	70.59	46.00
		882	BALANCE WORK OF REHABILITATION AND UP-GRADATION TO NH-166F FROM MAHAD JUNCTION (AT KM 123/400 ON NH- (MoRTH) (N24001891)	7-2021	11/2023 (N.A.) {3/2024}	256.54 (N.A.) {256.54}	80.10	60.00
		883	REHABILITATION AND UPGRADATION OF SHIRAPUR JUNCTION TO SHIVAJI CHOWK (DESIGN CHAINAGE KM. 130+00 TO (MoRTH) (N24001892)	2-2023	12/2024 (N.A.) {12/2024}	245.61 (N.A.) {245.61}	43.39	33.00
		884	UPGRADATION AND REHABILITATION OF SECTION OF NH 361 F FROM PARLI (00/000) TO GANGAKHED (30/400) TO (MoRTH) (N24001896)	11-2021	9/2023 (N.A.) {4/2024}	224.44 (N.A.) {224.44}	75.34	45.63
		885	REHABILITATION AND UP-GRADATION OF SABALKHED TO ASHTI SECTION FROM KM 37+900 TO KM 55+100 AND CHINCH (MoRTH) (N24001902)	12-2022	9/2024 (N.A.) {9/2024}	213.32 (N.A.) {213.32}	20.00	34.00
		886	REHABILITATION AND UP-GRADATION OF MUDKHED TO NANDED SECTION FROM KM. 372+000 TO KM 388+400 OF NH 16 (MoRTH) (N24001903)	8-2022	4/2025 (N.A.) {4/2025}	206.54 (N.A.) {206.54}	21.36	10.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		887	KOPARGAON TO SAVALI VIHIR SECTION (MoRTH) (N24001904)	9-2022	7/2024 (N.A.) {7/2024}	195.38 (N.A.) {195.38}	29.59	19.76
		888	UP-GRADATION TO 4 LANING OF DAULTABAD T-POINT TO MALIWADA [FROM DESIGN KM.0.000 TO KM 4.000] AND UPG (MoRTH) (N24001906)	8-2022	3/2024 (N.A.) {3/2024}	185.59 (N.A.) {185.59}	63.56	48.00
		889	CONSTRUCTION OF SIX LANE FLYOVER AT KATRAJ JUNCTION AT KM, 3/880 OF NH 548-DD (VADGAON - KATRAJ - KO (MoRTH) (N24001907)	6-2021	2/2024 (N.A.) {3/2024}	169.15 (N.A.) {169.15}	36.94	35.96
		890	UPGRADATION OF EXHISTING 2 LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDERS RIGID PAVEMENT FROM DESI (MoRTH) (N24001908)	12-2021	5/2024 (N.A.) {5/2024}	167.97 (N.A.) {167.97}	35.28	36.76
		891	REHABILITATION AND UPGRADATION OF JAMKHEDE TO SAUTADA SECTION OF NH548 D (FROM KM 195.375 TO KM 208.7 (MoRTH) (N24001910)	9-2022	7/2024 (N.A.) {7/2024}	157.62 (N.A.) {157.62}	13.86	17.03
		892	PANGAON TO DHARMAPURI AND PARALI TO INJEGAON 2L+PS (MoRTH) (N24001911)	3-2018	7/2024 (N.A.) {12/2023}	152.03 (N.A.) {152.03}	81.35	97.57
		893	4L OF INDORA CHOWK TO PACHPAOLI AND AGRASEN CHOWK - ASHOKA CHOWK (NHAI) (N24002071)	3-2023	6/2026 (N.A.) {6/2026}	998.27 (N.A.) {998.27}	348.48	48.34
		894	IMPROVEMENT OF EXISTING ALIGNMENT OF PANDHARPUR TOWN PART BYPASSED SECTION FROM WAKHARI TO LORD VITT (NHAI) (N24002072)	7-2022	10/2025 (N.A.) {10/2025}	150.21 (150.21) {150.21}	33.70	6.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		895	REHABILITATION/UPGRADATION OF EXISTING HIGHWAY TO 2L+PS/4 LANE OF DHAWALI TO RAJOLI FROM DESIGN KM.1 (MoRTH) (N24002169)	3-2022	9/2025 (N.A.) {9/2025}	316.44 (N.A.) {316.44}	0.00	-
		896	REHABILITATION/ UPGRADATION OF EXISTING HIGHWAY TO FOUR LANE STANDARDS IN KURKHEDA TOWN FROM (KM.413 (MoRTH) (N24002170)	3-2022	5/2025 (N.A.) {5/2025}	163.86 (N.A.) {163.86}	0.00	-
		897	REHABILITATION AND UP-GRADATION FOR TALERE A?? GAGANBAWDAA?? KOLHAPUR ROAD (NH-166G) STRETCHES START (MoRTH) (N24002171)	2-2023	4/2025 (N.A.) {4/2025}	249.13 (N.A.) {249.13}	0.00	-
		898	UP-GRADATION TO 4 LANE CONFIGURATION FOR THE WORK OF PETH NAKA TO SANGLI ROAD, NH- 166H, FROM KM 0+00 (MoRTH) (N24002172)	2-2023	12/2025 (N.A.) {12/2025}	856.82 (N.A.) {856.82}	0.00	-
		899	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF MAHUD SANGOLA ROAD NH (MoRTH) (N24002173)	2-2023	4/2025 (N.A.) {4/2025}	253.78 (N.A.) {253.78}	0.00	-
		900	UP-GRADATION TO FOUR LANE/ TWO LANE WITH PAVED SHOULDERS CONFIGURATION OF KALYAN - MURBAD - MALSHEJ (MoRTH) (N24002174)	2-2023	8/2026 (N.A.) {8/2026}	984.07 (N.A.) {984.07}	0.00	-
		901	CONSTRUCTION OF FOUR-LANE CONCRETE ROAD FROM POLICE HEADQUARTER GONDIA CITY TO RAWANWADI VILLAGE (BI (MoRTH) (N24002175)	2-2023	8/2025 (N.A.) {8/2025}	328.11 (N.A.) {328.11}	0.00	-
		902	REHABILITATION/UP GRADATION OF KARANJA ? KHERDA - MURTIZAPUR SECTION TO 4LANE+PAVED SHOULDER STAND A (MoRTH) (N24002176)	3-2023	2/2026 (N.A.) {2/2026}	594.44 (N.A.) {594.44}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		903	REHABILITATION / UPGRADATION TO 4 LANE WITH PAVED SHOULDER OF EXISTING SECTION IN SILLOD TOWN WITH D (MoRTH) (N24002177)	3-2023	7/2025 (N.A.) {7/2025}	153.79 (N.A.) {153.79}	0.00	-
		904	REHABILITATION, UPGRADATION AND WIDENING OF EXISTING HIGHWAY TO RIGID PAVEMENT 2 LANE WITH PAVED SHO (MoRTH) (N24002178)	2-2023	7/2026 (N.A.) {7/2026}	723.13 (N.A.) {723.13}	0.00	-
		905	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN (NHAI) (N24000442)	12-2015	3/2019 (Nov-2023) {7/2025}	649.50 (N.A.) {649.50}	623.82	94.10
		906	NAGPUR RING ROAD PACKAGE-2 (NHAI) (N24000560)	3-2016	7/2019 (Mar-2024) {6/2025}	591.66 (N.A.) {591.66}	632.92	100.00
		907	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000584)	3-2016	(N.A.) {12/2023}	1,142.62 (1,907.03) {1,142.62}	1,056.08	95.17
		908	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000585)	3-2016	(N.A.) {}	1,101.58 (N.A.) {1,101.58}	608.53	-
		909	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) (NHAI) (N24000656)	3-2017	3/2020 (Jul-2022) {12/2025}	744.64 (N.A.) {1,007.00}	467.65	97.69
		910	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF (NHAI) (N24000851)	3-2018	7/2021 (N.A.) {12/2025}	1,162.92 (1,182.87) {1,182.87}	412.38	64.00
		911	SARSAM TO KOTHARI (MoRTH) (N24001002)	2-2016	7/2019 (N.A.) {12/2023}	545.64 (N.A.) {545.64}	232.64	93.68

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		912	DIGRAS DARWAH KARANJA (MoRTH) (N24001013)	1-2017	6/2019 (N.A.) {12/2023}	391.06 (391.00) {391.06}	287.60	92.76
		913	DAHEGAON TO KUHI (MoRTH) (N24001017)	1-2017	6/2019 (N.A.) {12/2023}	228.89 (229.00) {228.89}	154.82	99.00
		914	WADI TO ASOLA (MoRTH) (N24001022)	1-2017	9/2019 (N.A.) {12/2023}	363.82 (364.00) {363.82}	154.65	93.15
		915	VITA TO NAGAJ (MoRTH) (N24001050)	3-2018	12/2019 (N.A.) {12/2023}	304.58 (305.00) {304.58}	154.68	68.39
		916	KARAD PATAN CHIPLUN GUHAGAR (MoRTH) (N24001057)	2-2017	6/2019 (N.A.) {6/2019}	407.19 (407.00) {407.19}	323.02	-
		917	KARWANDI TO RAJURI (MoRTH) (N24001058)	3-2018	12/2019 (N.A.) {3/2024}	276.95 (277.00) {276.95}	160.94	92.06
		918	PALPHATA TO PHULAMBARI (MoRTH) (N24001060)	3-2018	12/2019 (N.A.) {12/2023}	227.19 (227.00) {227.19}	141.92	95.00
		919	NANDED TO JALKOT (MoRTH) (N24001069)	12-2017	9/2019 (N.A.) {9/2019}	456.93 (457.00) {456.93}	278.22	95.00
		920	PUNE RAIGARH DISTRICT BORDER TO MANGAON (MoRTH) (N24001082)	3-2018	12/2019 (N.A.) {12/2023}	223.46 (N.A.) {223.46}	123.46	100.00
		921	SATARA TO MHASWAD (MoRTH) (N24001092)	1-2017	7/2019 (N.A.) {12/2023}	653.46 (N.A.) {653.46}	369.62	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		922	MHASWAD TO TEMBHURNI (MoRTH) (N24001099)	1-2017	7/2019 (N.A.) {12/2023}	488.60 (N.A.) {488.60}	279.42	76.50
		923	PEN TO KHOPOLI (MoRTH) (N24001106)	3-2018	3/2018 (N.A.) {1/2024}	301.39 (302.00) {301.39}	170.12	82.07
		924	PANCHARAL TO MANDANGHAR (MoRTH) (N24001107)	7-2018	5/2020 (N.A.) {5/2020}	381.08 (302.00) {381.08}	45.66	-
		925	NASRATPUR TO BARASGAON (MoRTH) (N24001112)	7-2016	9/2019 (N.A.) {9/2019}	406.54 (407.00) {406.54}	274.30	-
		926	INDAPUR TO VADPALE (MoRTH) (N24001114)	1-2017	12/2019 (N.A.) {3/2024}	1,202.52 (1,656.94) {1,202.52}	1,450.82	61.42
		927	PAITHAN TO SHIRUR (MoRTH) (N24001122)	3-2017	6/2019 (N.A.) {3/2024}	341.80 (N.A.) {341.80}	226.19	79.00
		928	SHIRUR TO KHARDA (MoRTH) (N24001123)	2-2017	6/2019 (N.A.) {12/2023}	381.77 (N.A.) {381.77}	199.48	83.93
		929	AURANGABAD TO SILLOD (MoRTH) (N24001124)	2-2017	6/2019 (N.A.) {12/2023}	456.32 (541.93) {456.32}	355.54	94.07
		930	SILLOD TO FARDAPUR (MoRTH) (N24001125)	2-2017	6/2019 (N.A.) {12/2023}	337.46 (432.98) {337.46}	335.30	91.56
		931	BHOGAN KHURD TO KASHEDI (MoRTH) (N24001132)	9-2017	6/2021 (N.A.) {12/2023}	743.21 (743.00) {743.21}	911.64	88.69

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		932	KANTE TO WAKED (MoRTH) (N24001134)	3-2016	11/2019 (N.A.) {12/2024}	1,230.02 (1,230.00) {1,230.02}	791.80	-
	URBAN DEVELOPMENT	933	MUMBAI METRO LINE 3 (COLABA- BANDRA-SEEPZ) (MMRCL) (N28000086)	7-2013	3/2020 (Jul-2025) {7/2025}	23,136.00 (N.A.) {37,276.00}	28,615.78	94.77
		934	NAGPUR METRO RAIL PROJECT PHASE II (NMRCL) (N28000155)	12-2022	12/2027 (N.A.) {12/2027}	6,708.00 (N.A.) {6,708.00}	895.38	23.82
		935	PCMC NIGDI PROJECT EXTENSION OF CORRIDOR 1 OF PUNE METRO PHASE 1 (MMRC) (N28000157)	10-2023	1/2027 (N.A.) {1/2027}	910.18 (N.A.) {910.18}	103.13	19.08
		936	PUNE METRO PHASE-1 EXTENSION FROM SWARGATE TO KATRAJ (MMRC) (N28000160)	9-2024	3/2029 (N.A.) {3/2029}	2,954.53 (N.A.) {2,954.53}	17.35	2.91
MANIPUR	CIVIL AVIATION	937	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (Dec-2025) {12/2025}	499.00 (N.A.) {499.00}	154.47	40.82
	RAILWAYS	938	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	12/2026 (Mar-2028) {3/2028}	14,322.79 (12,274.06) {22,234.60}	15,485.02	69.20
	ROAD TRANSPORT AND HIGHWAYS	939	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (Jan-2025) {1/2026}	477.86 (N.A.) {477.86}	246.09	84.87
		940	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (Nov-2024) {12/2025}	311.18 (N.A.) {311.18}	190.96	83.78

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		941	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (Oct-2024) {2/2025}	467.41 (N.A.) {467.41}	264.83	100.00
		942	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (Jul-2025) {12/2025}	579.63 (N.A.) {579.63}	180.72	72.50
		943	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (Mar-2025) {7/2025}	310.76 (N.A.) {310.76}	129.15	96.77
		944	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (Jan-2026) {3/2026}	410.68 (N.A.) {410.68}	152.34	70.11
		945	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (Sep-2025) {12/2025}	504.76 (N.A.) {504.76}	190.26	78.25
		946	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (Feb-2025) {3/2025}	152.11 (N.A.) {152.11}	73.48	100.00
		947	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (Aug-2025) {8/2025}	315.56 (N.A.) {315.56}	137.81	88.74
		948	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (Dec-2025) {3/2026}	760.16 (N.A.) {760.16}	157.48	62.92
		949	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (Mar-2026) {3/2026}	578.98 (N.A.) {578.98}	153.92	71.25

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		950	MARREM KHULLEN TO JESSAMI SECTION IMPHAL- UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	17.79	15.00
		951	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	13.14	18.04
		952	JESSAMI TO LAYNEN BRIDGE UKHRUL - JESSAMI PKG-7 (NHIDCL) (N24002227)	3-2023	6/2026 (N.A.) {6/2026}	164.89 (N.A.) {164.89}	3.83	9.78
		953	IMPHAL-KOHIMA ROAD PKG-5A (NHIDCL) (N24002232)	9-2020	8/2026 (N.A.) {8/2026}	228.97 (N.A.) {228.97}	0.00	10.13
		954	CHOITHAR TO MARREM KHULLEN SECTION IMPHAL- UKHRUL - JESSAMI PKG-5 (NHIDCL) (N24002242)	3-2023	3/2027 (N.A.) {3/2027}	564.05 (N.A.) {564.05}	0.00	-
		955	IMPHAL - KHONGSANG - JIRIBAM PKG- 2 (NHIDCL) (N24002244)	3-2021	3/2026 (N.A.) {3/2026}	195.14 (N.A.) {195.14}	4.42	11.53
		956	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (Jun-2025) {9/2025}	292.24 (N.A.) {292.24}	130.66	90.69
		957	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (Jun-2025) {10/2025}	365.53 (N.A.) {365.53}	156.31	77.69
		958	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (Jun-2025) {12/2025}	379.39 (N.A.) {379.39}	218.03	70.94

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		959	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (Mar-2025) {12/2025}	226.32 (N.A.) {226.32}	105.78	74.48
		960	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (Jan-2025) {9/2025}	188.36 (N.A.) {188.36}	126.71	99.02
		961	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (Sep-2024) {11/2025}	234.08 (N.A.) {234.08}	139.45	92.82
		962	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (May-2025) {10/2025}	211.70 (N.A.) {211.70}	83.79	71.06
		963	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (Mar-2025) {10/2025}	467.00 (N.A.) {467.00}	193.81	79.81
		964	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (Jan-2025) {1/2025}	185.80 (N.A.) {185.80}	117.78	100.00
		965	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (Jan-2025) {12/2025}	483.87 (N.A.) {483.87}	278.89	92.94
		966	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (Feb-2025) {3/2025}	198.77 (N.A.) {198.77}	127.86	100.00
		967	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (Mar-2025) {12/2025}	673.27 (N.A.) {673.27}	382.37	80.28

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MEGHALAYA	<u>DEPARTMENT OF HIGHER EDUCATION</u>	968	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (<i>RITES OF HIGHER</i>) (<i>N42000001</i>)	9-2013	9/2014 (Jul-2025) {7/2025}	484.32 (429.70) {494.52}	270.55	84.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	969	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (<i>MoRTH</i>) (<i>N24001441</i>)	8-2020	2/2022 (N.A.) {7/2025}	302.88 (N.A.) {302.88}	228.68	96.00
		970	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (<i>NHIDCL</i>) (<i>N24001474</i>)	9-2021	5/2024 (May-2026) {5/2026}	359.86 (N.A.) {359.86}	233.26	60.81
		971	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 (<i>NHIDCL</i>) (<i>N24001541</i>)	11-2021	6/2024 (Dec-2024) {5/2025}	283.50 (N.A.) {283.50}	257.26	100.00
		972	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (<i>NHIDCL</i>) (<i>N24002156</i>)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	222.26	30.00
		973	SHILLONG WESTERN BYPASS PACKAGE-2 (<i>NHIDCL</i>) (<i>N24002157</i>)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	293.36	25.52
		974	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (<i>NHIDCL</i>) (<i>N24002158</i>)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	297.91	25.27
		975	DAINADUBI-DARUGIRI PKG-1B (<i>NHIDCL</i>) (<i>N24002233</i>)	3-2023	3/2027 (N.A.) {3/2027}	705.83 (N.A.) {705.83}	0.32	2.13

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		976	IMPROVEMENT AND WIDENING TWO LANNIG WITH PAVED SHOULDER OF NATIONAL HIGHWAY 127B FROM KM 31.500 (GOE (MoRTH) (N24002239)	12-2023	5/2027 (N.A.) {5/2027}	504.00 (N.A.) {504.00}	0.00	-
		977	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (Jun-2025) {6/2025}	553.51 (610.09) {553.51}	438.16	88.07
		978	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM ((NHIDCL) (N24001313)	11-2020	12/2023 (Oct-2025) {10/2025}	351.12 (N.A.) {351.12}	299.22	63.00
		979	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	434.50	32.00
		980	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	214.34	30.30
		981	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	107.86	24.00
<u>MIZORAM</u>	<u>RAILWAYS</u>	982	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2025 (N.A.) {6/2025}	6,527.45 (5,021.45) {8,071.30}	8,066.76	97.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	983	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWLIRANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {12/2025}	523.78 (N.A.) {523.78}	379.40	95.31

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		984	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	279.44	75.40
		985	ZORINPUI- HMAWNGBU-LONGMASU (NH-502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	33.77	3.00
		986	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (N.A.) {4/2025}	519.09 (N.A.) {785.65}	670.91	97.51
		987	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (N.A.) {5/2024}	640.07 (N.A.) {1,286.35}	1,195.84	98.90
		988	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (N.A.) {4/2025}	473.18 (N.A.) {688.25}	541.04	95.00
		989	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (N.A.) {4/2025}	537.82 (N.A.) {789.05}	779.37	99.88
		990	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (N.A.) {5/2025}	518.53 (N.A.) {906.76}	849.68	97.90

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		991	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (N.A.) {5/2025}	404.29 (N.A.) {750.32}	666.58	100.00
		992	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (N.A.) {5/2025}	428.11 (N.A.) {746.39}	613.69	99.82
		993	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (N.A.) {6/2024}	206.88 (N.A.) {219.33}	265.38	100.00
		994	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (N.A.) {10/2024}	292.24 (N.A.) {331.17}	294.78	94.40
		995	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (Apr-2024) {4/2024}	233.25 (N.A.) {233.25}	172.09	100.00
		996	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (N.A.) {3/2026}	698.44 (N.A.) {698.45}	502.24	63.70
		997	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (N.A.) {3/2026}	740.58 (N.A.) {740.58}	373.89	61.00
MULTI STATE	COAL	998	NILJAI EXPANSION (DEEP) OC (3.5 MTY) (WCL) (N06000154)	8-2016	3/2022 (Mar-2025) {3/2025}	319.76 (319.76) {319.76}	183.67	98.00
		999	BINA KAKRI AMALGAMATION OCP 14 MTPA (NCL) (N06000192)	8-2020	3/2024 (N.A.) {3/2027}	836.42 (N.A.) {836.42}	778.71	89.08

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DPIIT</u>	1000	NATIONAL INDUSTRIAL CORRIDOR PROJECT (DMIC FOR DPIIT) (N40000001)	9-2011	3/2027 (Mar-2032) {3/2032}	20,084.00 (26,684.00) {26,684.00}	11,262.06	50.99
	<u>PETROLEUM</u>	1001	KOCHI-KOOTTANAD-BANGALORE- MANGALORE PIPELINE PHASE-II (GAIL) (N16000285)	6-2009	12/2012 (Dec-2025) {12/2025}	2,915.00 (5,909.00) {5,909.00}	4,381.20	94.20
		1002	SRIKAKULAM ANGUL PIPELINE PROJECT (GAIL) (N16000388)	9-2019	7/2022 (Dec-2025) {12/2025}	2,658.34 (N.A.) {2,658.34}	2,179.10	94.60
		1003	DHAMRA HALDIA PIPELINE PROJECT (GAIL) (N16000391)	3-2020	11/2022 (Dec-2025) {12/2025}	1,030.65 (N.A.) {1,030.65}	841.90	86.80
		1004	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT (GAIL) (N16000398)	6-2020	5/2023 (Sep-2025) {9/2025}	7,844.25 (N.A.) {7,844.25}	6,412.20	95.10
		1005	NORTH EAST GAS GRID (IGGL) (N16000439)	11-2020	3/2024 (Jul-2025) {3/2027}	9,265.00 (9,265.00) {9,265.00}	6,270.19	84.51
		1006	GURDASPUR JAMMU PIPELINE (GAIL) (N16000531)	7-2023	7/2026 (Jul-2026) {7/2026}	521.92 (521.92) {521.92}	153.20	35.50
	<u>POWER</u>	1007	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P (PGCIL) (N18000249)	12-2014	12/2018 (Mar-2025) {3/2027}	4,754.42 (9,129.32) {9,129.32}	7,602.44	81.70
		1008	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES (PGCIL) (N18000250)	12-2014	12/2018 (Mar-2025) {9/2025}	5,111.33 (6,700.00) {6,700.00}	5,230.02	96.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1009	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM (PGCIL) (N18000328)	2-2022	4/2025 (N.A.) {8/2025}	318.12 (N.A.) {318.12}	254.50	98.00
		1010	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM (PGCIL) (N18000330)	3-2022	12/2024 (N.A.) {9/2025}	288.71 (N.A.) {288.71}	199.53	48.00
		1011	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000331)	2-2022	9/2023 (N.A.) {8/2025}	359.47 (N.A.) {359.47}	327.28	90.00
		1012	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000332)	5-2022	11/2023 (N.A.) {9/2025}	1,666.00 (2,218.00) {2,218.00}	2,029.28	94.10
		1013	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B (PGCIL) (N18000337)	7-2022	6/2023 (N.A.) {9/2025}	4,546.26 (N.A.) {4,546.26}	4,091.67	93.00
		1014	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION (PGCIL) (N18000343)	10-2022	10/2025 (N.A.) {6/2025}	307.87 (N.A.) {307.87}	298.87	100.00
		1015	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B (PGCIL) (N18000352)	3-2023	11/2024 (N.A.) {9/2025}	3,546.94 (N.A.) {3,546.94}	2,837.55	94.00
		1016	ER WR TRANSMISSION LIMITED (PGCIL) (N18000353)	3-2023	3/2025 (N.A.) {6/2025}	281.16 (N.A.) {281.16}	281.15	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	1017	NANGALDAM-TALWARA(NL),NR (NR) (220100188)	3-1981	12/2025 (Jan-2027) {6/2027}	2,018.00 (603.00) {2,017.96}	1,629.74	75.00
		1018	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) (WCR) (220100232)	9-1998	3/2027 (N.A.) {3/2025}	8,913.94 (63.57) {8,248.50}	2,500.34	43.00
		1019	CHHAPRA-BALLIA UP (NER) (N22000134)	3-2013	2/2025 (N.A.) {12/2025}	941.05 (954.00) {1,045.82}	1,004.59	95.50
		1020	CHOTTAUDEPUR-DHAR(NL) (WR) (N22000138)	4-2007	12/2026 (Dec-2027) {12/2027}	1,793.65 (1,793.63) {1,793.63}	1,641.84	59.00
		1021	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) (WR) (N22000139)	4-2007	2/2027 (Feb-2027) {2/2027}	1,942.00 (1,873.10) {2,873.11}	3,119.79	59.00
		1022	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) (NCR) (N22000148)	4-2011	3/2025 (N.A.) {12/2024}	2,912.96 (N.A.) {3,845.60}	1,024.32	-
		1023	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR AND TANPUR- BANSI PAHARPUR (NCR) (N22000158)	4-2010	2/2019 (N.A.) {12/2026}	746.83 (N.A.) {746.83}	391.89	39.00
		1024	NEW BG LINE FROM BALURGHAT TO HILLY NFR (NFR) (N22000206)	4-2010	3/2027 (N.A.) {3/2027}	1,208.67 (N.A.) {1,181.57}	425.12	8.00
		1025	NEW BG LINE FROM JAGBANI TO BIRATNAGAR (NFR) (N22000207)	4-2010	3/2022 (Dec-2026) {12/2026}	401.65 (485.96) {485.96}	361.33	86.00
		1026	MURKONGSELEK-PASIGHAT NL (NFR) (N22000208)	4-2011	3/2025 (N.A.) {11/2025}	435.06 (N.A.) {1,249.35}	803.88	54.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1027	PIRPAINTI-JASIDIH (ER) (N22000219)	4-2013	3/2028 (Mar-2028) {3/2028}	2,555.03 (N.A.) {2,610.84}	1,140.05	45.00
		1028	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION (SCR) (N22000261)	4-2012	2/2025 (N.A.) {3/2025}	1,953.00 (N.A.) {1,952.68}	1,936.28	-
		1029	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL (NR) (N22000274)	4-2007	3/2024 (N.A.) {3/2025}	1,053.23 (N.A.) {1,053.00}	592.53	99.00
		1030	RAYADURGA-TUMKUR NL (SWR) (N22000279)	4-2007	9/2015 (N.A.) {2/2028}	2,495.59 (2,495.86) {2,495.86}	1,675.34	65.00
		1031	HOTGI-KUDGI-GADAG (SWR) (N22000333)	3-2015	12/2024 (N.A.) {2/2026}	1,877.81 (1,877.81) {2,458.87}	2,574.88	89.00
		1032	KAZIPET-BALHRSHA (SCR) (N22000367)	4-2015	1/2025 (N.A.) {1/2025}	2,594.59 (N.A.) {2,909.00}	2,862.60	-
		1033	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT (NHSRCL) (N22000463)	12-2015	8/2027 (N.A.) {8/2027}	108,000.00 (N.A.) {108,000.00}	78,839.00	52.89
		1034	WESTERN DEDICATED FREIGHT CORRIDOR (DFCC) (N22000464)	11-2007	3/2022 (N.A.) {3/2020}	51,101.00 (N.A.) {51,101.00}	47,476.00	83.00
		1035	CHANDIGARH-BADDI (NR) (N22000467)	4-2007	6/2025 (Dec-2026) {12/2026}	1,540.13 (1,540.14) {1,540.14}	956.13	30.00
		1036	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) (SER) (N22000506)	3-2019	12/2024 (N.A.) {6/2026}	2,400.00 (N.A.) {1,866.31}	2,112.20	61.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1037	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 (NHAI) (N24001628)	11-2021	2/2025 (Aug-2025) {8/2025}	2,155.95 (N.A.) {2,155.95}	1,360.04	71.01
		1038	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O (NHAI) (N24001629)	4-2022	11/2024 (Jul-2025) {7/2025}	796.65 (N.A.) {796.65}	452.41	91.71
		1039	VARANASI-AURANGABAD KM.786 TO KM.978.40 (NHAI) (N24000182)	9-2011	3/2014 (N.A.) {6/2025}	2,848.00 (N.A.) {3,241.56}	3,901.66	90.42
	<u>SHIPPING AND PORTS</u>	1040	JAL MARG VIKAS PROJECT (IWAI) (N25000072)	1-2018	3/2023 (Dec-2025) {12/2025}	5,369.18 (5,061.15) {5,061.15}	3,472.54	69.48
	<u>TELECOMMUNI CATIONS</u>	1041	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (N26000114)	3-2020	6/2021 (Nov-2021) {12/2025}	461.42 (461.42) {461.42}	166.02	81.00
		1042	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LABEL SWITCHING (IPMPLS) NETWORK and (BSNL) (N26000115)	3-2023	3/2024 (Jul-2024) {3/2025}	239.60 (N.A.) {239.60}	179.63	100.00
		1043	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (N26000116)	5-2023	8/2024 (Nov-2024) {6/2025}	645.13 (N.A.) {645.13}	348.03	89.15
		1044	PLANNIN ENGINEERING SUPPLY INSTALLATION TESTING COMMISSIONING INTEGARTION and ANNUAL MAINTENANCE OF (BSNL) (N26000117)	6-2023	6/2025 (N.A.) {6/2025}	24,556.35 (24,544.55) {24,544.55}	8,211.15	95.54

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1045	OPTICAL TRANSPORT NETWORK (OTN) PH-4 IN BSNL (BSNL) (N26000118)	2-2024	8/2025 (N.A.) {8/2025}	810.99 (N.A.) {810.99}	635.37	100.00
	URBAN DEVELOPMENT	1046	DELHI GHAZIABAD MEERUT RRTS CORRIDOR (NCRTC) (N28000134)	3-2019	6/2025 (N.A.) {6/2025}	30,274.00 (N.A.) {30,274.00}	25,812.28	86.80
NAGALAND	PETROLEUM	1047	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	6.62	19.00
	RAILWAYS	1048	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2026 (N.A.) {12/2029}	6,663.20 (6,663.20) {6,663.20}	4,942.71	74.00
	ROAD TRANSPORT AND HIGHWAYS	1049	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	65.19	73.34
		1050	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (Jun-2026) {6/2026}	252.19 (N.A.) {252.19}	14.33	20.27
		1051	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH- 61 (N (MoRTH) (N24001466)	3-2021	7/2024 (Dec-2025) {12/2025}	297.24 (N.A.) {297.24}	150.10	80.31
		1052	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (Mar-2025) {3/2025}	226.44 (N.A.) {226.44}	140.24	100.00
		1053	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (Sep-2025) {9/2025}	192.93 (N.A.) {192.93}	112.09	93.38

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1054	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {12/2025}	177.77 (199.02) {199.02}	46.94	63.33
		1055	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	100.51	58.57
		1056	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	50.60	28.05
		1057	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	168.20	66.03
		1058	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (Sep-2025) {9/2025}	429.52 (794.74) {794.74}	321.40	92.46
		1059	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (Feb-2023) {4/2025}	387.00 (688.12) {688.12}	392.01	100.00
		1060	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (Aug-2024) {4/2025}	500.09 (698.81) {698.81}	393.53	100.00
		1061	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG- TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (Aug-2022) {8/2025}	215.79 (N.A.) {215.79}	132.93	80.38

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1062	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG- TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (Jun-2023) {9/2025}	323.98 (N.A.) {323.98}	119.94	60.11
		1063	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (Sep-2024) {6/2026}	277.44 (N.A.) {277.44}	169.46	67.91
		1064	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (Jun-2025) {12/2025}	159.85 (342.29) {159.85}	108.15	33.55
		1065	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (Apr-2023) {8/2025}	202.36 (N.A.) {202.36}	75.39	32.67
		1066	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	119.20	65.06
		1067	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (Nov-2025) {11/2025}	330.80 (N.A.) {330.80}	171.89	92.44
		1068	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (Nov-2026) {11/2026}	232.29 (350.88) {232.29}	79.69	17.31
		1069	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7-2021	3/2023 (Sep-2025) {9/2025}	258.52 (N.A.) {258.52}	89.46	81.40
ODISHA	COAL	1070	BASUNDHARA (WEST) OC EXTN(7.00 MTY) (MCL) (N06000112)	5-2014	3/2019 (N.A.) {3/2028}	479.15 (N.A.) {479.15}	271.99	63.04

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1071	SIARMAL OCP (40.00MTY) (MCL) (N06000113)	2-2021	3/2029 (N.A.) {3/2029}	5,194.96 (N.A.) {5,194.96}	3,454.71	53.63
		1072	INTEGRATED LAKHANPUR-BELPAHAR- LILARI OCP (MCL) (N06000167)	5-2018	3/2027 (N.A.) {3/2027}	2,434.75 (N.A.) {2,434.75}	1,765.96	61.49
		1073	REORGANISATION OF BHARATPUR OCP EXPANSION (MCL) (N06000171)	11-2018	3/2029 (N.A.) {3/2029}	2,838.87 (N.A.) {2,838.87}	1,837.17	47.35
		1074	NAINI COAL MINE (SCCL) (N06000203)	3-2020	3/2024 (N.A.) {3/2027}	494.30 (N.A.) {494.30}	491.33	80.00
		1075	GOPALJI-KANIHA OCP (MCL) (N06000229)	4-2022	3/2028 (N.A.) {3/2028}	6,107.87 (N.A.) {6,107.87}	1,703.67	17.73
		1076	BALARAM EXPANSION OCP (MCL) (N06000230)	8-2020	3/2029 (N.A.) {3/2029}	3,504.21 (N.A.) {3,504.21}	1,026.96	52.44
		1077	SUBHADRA OCP (MCL) (N06000249)	5-2021	3/2029 (Mar-2029) {3/2029}	1,693.81 (N.A.) {1,693.81}	1,277.82	40.05
		1078	NLC TALABIRA THERMAL POWER PROJECT (PHASE-1: 3 X 800 MW) (NLC) (N06000270)	1-2024	5/2029 (Mar-2030) {3/2030}	27,213.00 (N.A.) {27,213.00}	1,928.60	1.55
		1079	RPR OF HINGULA EXPANSION OCP (MCL) (N06000285)	11-2022	3/2029 (N.A.) {3/2029}	1,561.85 (N.A.) {1,561.85}	49.85	23.57
		1080	BHUBANESWARI EXPANSION OCP (MCL) (N06000286)	3-2024	3/2031 (N.A.) {3/2031}	5,366.28 (N.A.) {5,366.28}	9.08	9.59

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1081	BALABHADRA OCP (MCL) (N06000288)	4-2023	3/2030 (N.A.) {3/2030}	978.44 (N.A.) {978.44}	209.50	7.68
		1082	INTEGRATED KULDA GARJANBAHAL OCP (MCL) (N06000289)	4-2023	3/2030 (N.A.) {3/2030}	3,563.50 (N.A.) {3,563.50}	505.09	4.00
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1083	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR (CPWD EDUCATION) (N28000126)	1-2019	3/2022 (N.A.) {10/2025}	790.79 (N.A.) {790.79}	708.50	97.00
	<u>MINES</u>	1084	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT (NALCO) (N10000010)	12-2014	4/2021 (Jun-2026) {6/2026}	4,103.00 (5,677.40) {5,677.40}	3,831.39	74.52
		1085	UTKAL D AND E COAL BLOCK (NALCO) (N10000011)	5-2016	1/2020 (Nov-2023) {3/2024}	534.00 (N.A.) {1,021.97}	829.39	88.50
		1086	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (NALCO) (N10000012)	12-2015	11/2020 (Sep-2025) {8/2027}	355.00 (581.00) {581.00}	163.55	12.60
		1087	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN (NALCO) (N10000013)	11-2017	4/2021 (May-2026) {5/2026}	483.00 (483.00) {495.00}	387.75	89.43
		1088	POTTANGI BAUXITE MINES (NALCO) (N10000016)	5-2018	12/2024 (N.A.) {5/2025}	1,437.00 (N.A.) {1,381.00}	650.05	51.10
		1089	CONSTRUCTION OF RED MUD POND - II AT NALCO DAMANJODI ODISHA (NALCO) (N10000017)	9-2019	3/2023 (May-2024) {5/2024}	225.79 (N.A.) {270.66}	5.00	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	1090	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY (IOCL) (N16000396)	7-2020	1/2024 (Apr-2025) {4/2026}	13,805.00 (N.A.) {13,805.00}	7,704.73	90.00
	POWER	1091	EASTERN REGION EXPANSION SCHEME XXIX (PGCIL) (N18000351)	3-2023	11/2025 (N.A.) {7/2025}	524.04 (N.A.) {524.04}	482.12	99.80
		1092	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) (NTPC) (N18000364)	8-2022	5/2027 (N.A.) {12/2027}	11,844.00 (N.A.) {12,539.00}	3,703.12	21.40
	RAILWAYS	1093	KHURDA ROAD-BOLANGIR(NL)ECOR (ECOR) (220100284)	4-1994	12/2026 (Dec-2026) {12/2026}	3,550.00 (3,791.66) {5,089.37}	4,910.22	86.00
		1094	TALCHER-BIMALAGARH(NL)(ECOR) (ECOR) (220100328)	4-2005	3/2025 (N.A.) {3/2026}	1,928.10 (N.A.) {1,928.07}	1,757.75	40.00
		1095	BHADRAK - NERGUNDI 3RD LINE (ECOR) (N22000316)	3-2013	11/2024 (Jan-2026) {6/2026}	1,284.39 (1,284.39) {1,284.39}	1,297.80	80.00
		1096	JAGADALPUR-KORAPUT DOUBLING (ECOR) (N22000376)	4-2015	3/2024 (N.A.) {3/2022}	1,547.38 (N.A.) {1,547.38}	1,304.60	93.70
		1097	KORAPUT - SINGAPUR ROAD DOUBLING (ECOR) (N22000379)	4-2015	12/2027 (Mar-2026) {3/2026}	2,362.00 (2,361.74) {2,361.74}	1,816.25	80.00
		1098	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE (ECOR) (N22000380)	4-2015	3/2027 (N.A.) {8/2026}	820.61 (N.A.) {810.02}	580.59	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1099	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. (ECOR) (N22000381)	4-2015	3/2026 (Nov-2025) {11/2025}	1,172.92 (N.A.) {2,022.75}	1,971.33	80.00
		1100	VIZIANAGARAM -SAMABALPUR 3RD LINE (RVNL) (N22000409)	1-1991	12/2026 (N.A.) {12/2026}	4,803.16 (N.A.) {4,803.16}	4,691.52	-
		1101	JEYPORE MALKANGIRI NEW LINE (ECOR) (N22000516)	2-2018	7/2033 (N.A.) {7/2033}	2,344.00 (N.A.) {642.69}	220.78	90.10
		1102	JEYPORE NABARANGPUR NEWLINE (ECOR) (N22000517)	7-2017	7/2028 (Dec-2029) {12/2029}	748.00 (N.A.) {747.91}	0.00	-
		1103	TALCHER - ANGUL NEW LINE WITH Y CONNECTION AT TALCHER (ECOR) (N22000518)	7-2018	12/2026 (N.A.) {12/2026}	278.96 (495.00) {494.62}	29.50	-
		1104	KODINGAMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (ECOR) (N22000519)	8-2022	8/2027 (N.A.) {8/2027}	190.90 (N.A.) {190.90}	10.00	-
		1105	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION (ECOR) (N22000520)	9-2022	9/2027 (N.A.) {3/2028}	189.93 (N.A.) {189.93}	14.04	-
		1106	BRUNDAMAL-JHARSUGUDA- FLYOVER CONNECTION FOR JOINING DN LINE (ECOR) (N22000521)	12-2009	12/2026 (N.A.) {12/2026}	296.51 (N.A.) {297.00}	162.44	10.00
		1107	BAGHUAPAL FLY OVER (20 KM) (ECOR) (N22000522)	8-2019	8/2027 (Aug-2027) {8/2027}	183.00 (257.97) {257.97}	0.83	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1108	ROURKELA-BONDAMUNDA A-CABIN 5TH LINE (10 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SER) (N22000571)	9-2022	9/2026 (N.A.) {2/2026}	209.75 (N.A.) {244.99}	82.27	30.00
	ROAD TRANSPORT AND HIGHWAYS	1109	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 (NHAI) (N24001647)	8-2020	3/2022 (N.A.) {7/2025}	200.00 (154.73) {154.73}	150.38	100.00
		1110	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE- OD-8 (NHAI) (N24001665)	12-2021	10/2024 (N.A.) {12/2025}	1,592.00 (1,592.00) {1,592.00}	1,127.76	78.13
		1111	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130-CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE- OD (NHAI) (N24001666)	12-2021	9/2024 (N.A.) {8/2025}	714.00 (714.00) {714.00}	589.97	95.45
		1112	6L GREENFIELD KALIAGURA ? BAUNSAGUAR SECTION OF NH-130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG (NHAI) (N24001667)	9-2021	5/2024 (N.A.) {12/2025}	1,734.00 (1,734.00) {1,734.00}	1,238.62	86.47
		1113	6L OF BADAKUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH-130-CD (PACKAGE ? OD-3) (NHAI) (N24001668)	3-2021	4/2024 (N.A.) {11/2025}	1,249.00 (N.A.) {1,249.00}	522.17	87.16
		1114	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH- 130-CD (PACKAGE ? OD-1) (NHAI) (N24001669)	2-2021	3/2024 (N.A.) {7/2025}	586.00 (N.A.) {586.00}	241.77	92.98
		1115	6L OF KARKI ? KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH-130-CD (PACKAGE ? OD-4) (NHAI) (N24001670)	2-2021	3/2024 (N.A.) {7/2025}	593.00 (N.A.) {593.00}	282.15	94.55

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1116	6L OF HATIBENA - BADAUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130-CD (PACKAGE ? OD- 2) (NHAI) (N24001671)	2-2021	3/2024 (N.A.) {7/2025}	925.00 (N.A.) {925.00}	460.47	97.00
		1117	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE ? (NHAI) (N24001678)	8-2021	6/2024 (N.A.) {12/2025}	1,460.00 (1,460.00) {1,460.00}	986.76	91.52
		1118	CONSTRUCTION OF ROAD FROM KM 0/0 TO 72/0 OF NH-26 SUCH AS 4 LANE FROM KM 0/0 TO 21/0 (BARGARH TO BAR (MoRTH) (N24001857)	6-2020	12/2023 (Aug-2025) {8/2025}	414.24 (N.A.) {414.24}	307.52	98.00
		1119	WIDENING AND STRENGTHENING TO 2L+PS INCLUDING LA OF KANDARPUR- BALIKUDA FROM KM 277/500 TO 318/970 OF (MoRTH) (N24001858)	3-2022	6/2025 (N.A.) {12/2025}	499.79 (N.A.) {499.79}	285.58	48.20
		1120	CONSTRUCTION OF BYPASS ON NH-59 FROM KM 336/350 TO 349/910 (13.56 KM) NEAR BERHAMPUR TOWN INCLUDING (MoRTH) (N24001859)	3-2021	3/2024 (N.A.) {8/2025}	196.94 (N.A.) {196.94}	71.55	93.00
		1121	CONSTRUCTION OF BYPASS TO NAYAGARH TOWN FROM KM 235.469 TO 252.482 OF NH-57 INCLUDING LAND ACQUISITI (MoRTH) (N24001860)	1-2022	4/2025 (N.A.) {8/2025}	300.33 (N.A.) {300.33}	203.81	70.00
		1122	CONSTRUCTION OF BYPASS TO KHORDHA TOWN FROM KM 294/000 TO 300/300 ON NH-57 INCLUDING LA IN THE STATE (MoRTH) (N24001861)	2-2022	11/2024 (Aug-2025) {8/2025}	157.49 (N.A.) {157.49}	72.57	54.00
		1123	CONSTRUCTION OF BYPASS ROAD TO BALANGIR TOWN FROM KM 72/400 (DESING KM 0/0) TO KM 79/800 (DESIGN KM (MoRTH) (N24001862)	2-2022	10/2025 (Nov-2025) {11/2025}	238.78 (N.A.) {238.78}	50.64	40.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1124	CONSTRUCTION OF 5 HL BRIDGES AT KM 379/000 (PANGAM), KM 439/400 (POTTERU), KM 444/237 (KONGURUKONDA) (MoRTH) (N24001863)	3-2021	6/2024 (Oct-2025) {5/2025}	154.05 (N.A.) {154.05}	47.47	30.00
		1125	CONSTRUCTION OF FOUR LANE ROB AND ITS APPROACHES IN LIEU OF EXISTING LEVEL CROSSING NO. RV-71 AT KM (MoRTH) (N24001864)	11-2021	6/2025 (N.A.) {10/2025}	154.49 (N.A.) {154.49}	60.48	45.00
		1126	CONSTRUCTION OF 4 LANE ROB WITH APPROACHES IN LIEU OF LC NO. RV- 172 AT KM 176.00 OF NH-201 (PRESENT (MoRTH) (N24001865)	12-2021	5/2025 (Oct-2025) {10/2025}	324.09 (N.A.) {324.09}	111.45	35.00
		1127	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM. (NHAI) (N24002078)	12-2023	12/2025 (N.A.) {3/2026}	711.00 (N.A.) {711.00}	217.96	60.80
		1128	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002079)	12-2023	12/2025 (N.A.) {3/2026}	742.25 (N.A.) {742.25}	223.47	55.10
		1129	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002080)	12-2023	12/2025 (N.A.) {3/2026}	762.75 (N.A.) {762.75}	266.33	60.70
		1130	3L MAJOR BRIDGE OVER RIVER BRAHMANI AT KM. 401.250 (DUBURI CHANDIKHOLE SECTION) OF NH 200 (NEW NH 5 (NHAI) (N24002081)	8-2022	1/2025 (N.A.) {12/2026}	153.61 (N.A.) {153.61}	22.77	34.49

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1131	WIDENING AND STRENGTHENING TO 2L+PS FROM KM 0.000 TO 40.000 (DHAUGAON- PODAMARI SECTION) OF NH 326 I (MoRTH) (N24002135)	3-2022	2/2026 (N.A.) {2/2026}	186.52 (N.A.) {186.52}	48.30	35.00
		1132	WIDENING AND STRENGTHENING TO 4L+PS/2L+PS FROM KM 0.000 TO 35.800 (KUAKHIA - MANGALPUR SECTION) OF NH 326 I (MoRTH) (N24002136)	3-2022	2/2026 (N.A.) {2/2026}	636.10 (N.A.) {636.10}	264.98	36.53
		1133	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANE OF CHANDIKHOLE ? PARADIP SECTION OF NH-53 (OLD NH 53) (NHAI) (N24002219)	3-2024	10/2026 (N.A.) {10/2026}	882.45 (N.A.) {882.45}	82.62	14.10
		1134	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S (NHAI) (N24000619)	9-2016	8/2019 (N.A.) {7/2025}	2,510.04 (N.A.) {2,510.04}	1,181.34	99.98
		1135	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO 0+400) (NHAI) (N24000715)	12-2017	7/2020 (N.A.) {7/2025}	686.65 (565.00) {686.65}	574.26	98.00
		1136	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (CHANDIKHOLE) (NHAI) (N24000733)	1-2018	8/2022 (N.A.) {12/2025}	633.68 (492.83) {633.68}	560.38	86.00
		1137	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG (NHAI) (N24000734)	1-2018	8/2021 (N.A.) {7/2025}	614.48 (503.30) {757.12}	664.48	99.00
		1138	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON NH-42 (NHAI) (N24000736)	1-2018	9/2020 (N.A.) {7/2025}	686.65 (504.09) {1,015.16}	488.98	98.35

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1139	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141) (NHAI) (N24000738)	1-2018	9/2021 (N.A.) {12/2025}	999.00 (1,152.70) {1,152.70}	540.10	82.01
		1140	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) () (NHAI) (N24000739)	1-2018	6/2021 (Jul-2025) {7/2025}	503.88 (609.03) {609.03}	536.89	98.50
		1141	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. (MoRTH) (N24000912)	8-2016	2/2017 (N.A.) {12/2025}	287.70 (N.A.) {293.66}	275.42	98.66
		1142	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA (MoRTH) (N24000914)	12-2016	8/2018 (N.A.) {9/2025}	223.50 (N.A.) {223.50}	220.50	100.00
		1143	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA (MoRTH) (N24000917)	3-2018	8/2018 (N.A.) {4/2025}	199.16 (N.A.) {199.16}	158.73	100.00
	STEEL	1144	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY (SAIL) (N12000122)	11-2020	5/2023 (Mar-2025) {3/2025}	377.18 (N.A.) {377.18}	434.90	
		1145	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP (SAIL) (N12000125)	1-2022	5/2025 (Aug-2025) {8/2025}	970.18 (N.A.) {970.18}	720.07	94.31
PUNJAB	DEPARTMENT OF HIGHER EDUCATION	1146	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. (CPWD EDUCATION) (N28000142)	10-2019	5/2022 (N.A.) {8/2025}	348.24 (N.A.) {348.24}	245.37	91.20

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	1147	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB (HPCL) (N16000402)	5-2020	2/2023 (Sep-2024) {3/2026}	1,421.46 (N.A.) {1,421.46}	1,163.10	95.63
		1148	BHATINDA SANGRUR PIPELINE (HPCL) (N16000440)	11-2021	5/2024 (Feb-2025) {8/2025}	367.00 (397.00) {397.00}	334.26	91.90
		1149	CGD PROJECT AT PATHANKOT DISTRICT (IOCL) (N16000488)	3-2022	3/2030 (Sep-2033) {9/2033}	151.00 (N.A.) {151.00}	8.73	2.00
	RAILWAYS	1150	LUDHIANA MULLANPUR DOUBLING (NR) (N22000589)	9-2020	3/2025 (N.A.) {7/2025}	235.00 (N.A.) {235.00}	7.99	98.00
		1151	FEROZPUR - PATTI (25.72 KM) (NR) (N22000614)	4-2017	3/2027 (N.A.) {3/2027}	299.74 (N.A.) {781.00}	0.00	-
	ROAD TRANSPORT AND HIGHWAYS	1152	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO (NHAI) (N24001415)	12-2020	4/2024 (Jul-2024) {7/2024}	881.00 (N.A.) {881.00}	960.36	92.34
		1153	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI (NHAI) (N24001416)	12-2020	1/2024 (Mar-2025) {3/2025}	989.66 (N.A.) {989.66}	338.21	31.08
		1154	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO (NHAI) (N24001417)	12-2020	4/2024 (Sep-2025) {9/2025}	1,234.40 (N.A.) {1,234.40}	853.68	61.88
		1155	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO (NHAI) (N24001418)	12-2020	4/2024 (Sep-2025) {9/2025}	1,094.46 (N.A.) {1,094.46}	802.93	62.99

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1156	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- (NHAI) (N24001419)	2-2021	4/2024 (Nov-2024) {11/2024}	1,269.96 (N.A.) {1,269.96}	585.86	43.45
		1157	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA- SRIHARGOBINDPUR- (NHAI) (N24001420)	2-2021	4/2024 (Dec-2025) {12/2025}	853.66 (N.A.) {853.66}	177.27	20.65
		1158	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA (NHAI) (N24001630)	7-2021	2/2025 (N.A.) {2/2025}	1,501.02 (N.A.) {1,501.02}	282.00	75.00
		1159	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD (NHAI) (N24001631)	3-2021	10/2024 (N.A.) {10/2024}	1,525.31 (N.A.) {1,525.31}	290.00	95.00
		1160	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM (NHAI) (N24001632)	1-2021	5/2024 (Jun-2025) {8/2025}	1,741.86 (2,281.02) {2,281.02}	1,294.40	96.50
		1161	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA ? RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR (NHAI) (N24001636)	5-2021	12/2024 (Oct-2026) {10/2026}	1,368.91 (1,368.91) {1,368.91}	163.58	15.31
		1162	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K (NHAI) (N24001637)	3-2021	1/2025 (N.A.) {1/2025}	1,754.84 (N.A.) {1,754.84}	1,145.02	40.01
		1163	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6 (NHAI) (N24001638)	11-2021	7/2024 (Aug-2025) {8/2025}	646.42 (646.42) {646.42}	481.67	96.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1164	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE (NHAI) (N24001639)	5-2020	12/2024 (Aug-2025) {8/2025}	864.23 (864.23) {864.23}	434.88	65.00
		1165	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N (NHAI) (N24001640)	3-2021	11/2024 (N.A.) {11/2024}	1,229.38 (N.A.) {1,229.38}	762.83	48.58
		1166	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR (NHAI) (N24001641)	3-2021	10/2024 (Dec-2025) {12/2025}	1,641.75 (N.A.) {1,641.75}	188.55	26.01
		1167	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI (NHAI) (N24001642)	2-2021	8/2024 (Dec-2025) {12/2025}	1,474.77 (N.A.) {1,474.77}	475.88	75.25
		1168	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I (NHAI) (N24001643)	12-2020	6/2024 (Jun-2025) {6/2025}	857.91 (N.A.) {857.91}	164.88	41.02
		1169	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV (NHAI) (N24001644)	12-2020	9/2023 (Sep-2025) {9/2025}	524.88 (416.58) {416.58}	157.14	73.00
		1170	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION OF NH-354 SECTION ARIFKES- FEROZEPUR-MUKTS (MoRTH) (N24001960)	3-2021	10/2023 (N.A.) {10/2025}	263.19 (N.A.) {220.00}	119.50	61.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1171	WORK OF WIDENING/UPGRADATION OF 2-LANE WITH PAVED SHOULDER OF SRI MUKTSAR SAHIB TO MALOUT ROAD FROM (MoRTH) (N24001961)	3-2022	10/2023 (N.A.) {7/2025}	152.58 (N.A.) {152.58}	97.00	85.00
		1172	6L OF JODHPUR ROMANA (BATHINDA) - MANDI DABWALI (PUNJAB HARYANA BORDER) SECTION OF NH-54 FROM KM. 0. (NHAI) (N24002075)	12-2020	8/2025 (Aug-2025) {8/2025}	757.13 (757.00) {757.00}	246.51	98.75
		1173	6L AMRITSAR-BATHINDA GREENFIELD SECTION FROM JN. WITH BHAGTA BHAI KA-BHADOUR ROAD NEAR DYALPURA BHAI (NHAI) (N24002076)	3-2021	10/2025 (Jun-2026) {6/2026}	2,029.17 (2,029.00) {2,029.00}	84.23	47.00
		1174	6L ACCESS CONTROLLED LUDHIANA- BATHINDA GREENFIELD HIGHWAY FROM JN. WITH AMRITSAR-BATHINDA GREENFIELD (NHAI) (N24002091)	6-2021	9/2025 (Mar-2026) {3/2026}	906.51 (906.51) {906.51}	170.39	54.00
		1175	6-LANE AMRITSAR-BATHINDA GREENFIELD SECTION OF NH-754A FROM JUNCTION WITH MOGA JALANDHAR ROAD (NH-70 (NHAI) (N24002092)	3-2021	10/2025 (N.A.) {10/2025}	1,801.37 (N.A.) {1,801.37}	1,075.64	51.20
		1176	6L OF AMBALA-CHANDIGARH GREENFIELD SECTION FROM KM. 0.000 TO KM. 25.000 WITH 4L SPUR TO LALRU FROM K (NHAI) (N24002098)	3-2022	10/2025 (N.A.) {10/2025}	1,641.66 (N.A.) {1,641.66}	100.00	55.00
		1177	4L OF EXISTING BEAS ? BABA BAKALA - DERA BABA NANAK SECTION FROM START OF BATALA BYPASS TILL INTERSE (NHAI) (N24002100)	10-2021	6/2025 (N.A.) {12/2025}	1,003.38 (N.A.) {1,003.38}	281.62	72.58
		1178	4L OF BEAS-MEHTA-BATALA-DERA BABA NANAK FROM INTERSECTION WITH JALANDHAR-AMRITSAR HIGHWAY (NH-3) NEA (NHAI) (N24002101)	8-2021	6/2025 (Dec-2025) {12/2025}	809.51 (N.A.) {809.51}	220.73	53.54

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1179	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I SPUR-I) FROM JN. WITH KAPURTHALA - SULTANPUR LODHI ROAD (NH (NHAI) (N24002102)	1-2020	4/2026 (N.A.) {4/2027}	2,165.23 (N.A.) {2,165.23}	180.85	20.50
		1180	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA (MoRTH) (N24000907)	3-2018	8/2020 (N.A.) {6/2025}	293.10 (N.A.) {315.00}	318.24	100.00
		1181	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 (MoRTH) (N24000909)	10-2017	10/2019 (N.A.) {12/2025}	1,069.59 (N.A.) {1,069.59}	739.08	44.00
		1182	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 (MoRTH) (N24000910)	3-2018	11/2020 (N.A.) {6/2026}	170.57 (N.A.) {150.00}	135.00	79.00
RAJASTHAN	CIVIL AVIATION	1183	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT (AAI) (N04000101)	5-2022	11/2024 (Oct-2025) {10/2025}	480.00 (N.A.) {480.00}	254.71	77.75
		1184	UDAIPUR AIRPORT- CONSTRUCTION OF NEW INTEGRATED PASSENGER TERMINAL BUILDING (AAI) (N04000104)	6-2023	3/2026 (N.A.) {3/2026}	887.00 (N.A.) {887.00}	312.40	44.61
	COAL	1185	NLCIL 300 MW SOLAR POWER PROJECT (PART OF 510 MW CPSU SCHEME) (NLC) (N06000269)	3-2023	9/2024 (N.A.) {11/2025}	1,813.00 (N.A.) {1,813.00}	746.26	66.00
	PETROLEUM	1186	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE (IOCL) (N16000435)	12-2021	10/2024 (Dec-2025) {12/2025}	9,028.00 (N.A.) {9,028.00}	6,734.76	82.30

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1187	SETTING UP OF PETROCHEMICAL EVACUATION MARKETING TERMINAL (PEMT) AT BARMER (HPCL) (N16000512)	12-2023	12/2026 (N.A.) {12/2026}	461.05 (N.A.) {461.05}	98.70	47.50
		1188	RAJASTHAN REFINERY PROJECT (HPCLRRL(JV)) (N16000513)	10-2017	10/2022 (Mar-2025) {12/2025}	43,129.00 (72,937.00) {72,937.00}	58,305.57	87.40
		1189	CGD PROJECTS AT FAZILKA (EXCEPT AREA ALREADY AUTHORIZED) GANGANAGAR AND HANUMANGARH DISTRICTS (BPCL) (N16000520)	12-2022	6/2030 (N.A.) {6/2030}	3,207.00 (N.A.) {3,207.00}	324.65	21.90
	POWER	1190	BHADLA-II 500MW SOLAR PV PROJECT (NTPC) (N18000347)	6-2022	3/2024 (Sep-2025) {9/2025}	2,598.92 (N.A.) {2,598.92}	1,815.27	60.00
		1191	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART (PGCIL) (N18000356)	3-2023	9/2024 (N.A.) {9/2025}	1,433.28 (N.A.) {1,433.28}	1,290.22	91.90
		1192	300 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000368)	5-2022	11/2023 (N.A.) {9/2025}	1,677.12 (N.A.) {1,677.12}	1,295.80	92.00
		1193	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III, PART E1 (PGCIL) (N18000373)	8-2023	2/2025 (N.A.) {9/2025}	688.74 (N.A.) {688.74}	564.77	93.00
		1194	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART H (PGCIL) (N18000374)	10-2023	4/2025 (N.A.) {8/2025}	2,211.00 (N.A.) {2,211.00}	1,702.27	69.40
		1195	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART C1 (PGCIL) (N18000375)	10-2023	4/2025 (Oct-2025) {10/2025}	1,796.00 (N.A.) {1,796.00}	1,149.44	77.30

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1196	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART B1 (PGCIL) (N18000376)	9-2023	4/2025 (N.A.) {9/2025}	2,191.00 (N.A.) {2,191.00}	1,511.45	75.70
		1197	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART J (PGCIL) (N18000378)	12-2022	3/2025 (Apr-2026) {4/2026}	331.00 (N.A.) {331.00}	18.23	27.00
		1198	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART E2 (PGCIL) (N18000379)	11-2023	6/2025 (N.A.) {9/2025}	428.00 (N.A.) {428.00}	85.60	45.00
		1199	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART A [BIKANER III N (PGCIL) (N18000386)	12-2023	12/2025 (N.A.) {12/2025}	2,998.00 (N.A.) {2,998.00}	1,439.18	47.10
		1200	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART D [NEEMRANA II B (PGCIL) (N18000387)	12-2023	12/2025 (N.A.) {12/2025}	2,056.00 (N.A.) {2,056.00}	1,318.23	53.30
		1201	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PH-III PART D [SIKAR KHETRI TRANSMISSI (PGCIL) (N18000389)	2-2024	8/2025 (N.A.) {9/2025}	2,000.00 (N.A.) {2,000.00}	1,200.00	58.00
		1202	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) PART-B (JAISALMER/BARMER COMPLEX) (PGCIL) (N18000391)	8-2024	8/2026 (N.A.) {8/2026}	3,279.00 (N.A.) {3,279.00}	491.85	18.60
		1203	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART- C (PGCIL) (N18000393)	8-2024	8/2026 (N.A.) {8/2026}	2,227.00 (N.A.) {2,227.00}	489.94	18.60

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1204	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART- E (PGCIL) (N18000394)	8-2024	8/2026 (N.A.) {8/2026}	3,251.00 (N.A.) {3,251.00}	650.20	16.20
		1205	ADDITIONAL TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM BHADLA-III PS AS PART OF RAJASTHAN REZ P (PGCIL) (N18000396)	8-2024	2/2026 (N.A.) {2/2026}	369.00 (N.A.) {369.00}	10.30	3.80
		1206	TRANSMISSION SYSTEM STRENGTHENING FOR INTERCONNECTIONS OF BHADLA-III AND BIKANER III COMPLEX [SPV NA (PGCIL) (N18000397)	8-2024	8/2026 (N.A.) {8/2026}	1,382.00 (N.A.) {1,382.00}	27.60	1.00
		1207	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BAR (PGCIL) (N18000401)	11-2024	11/2026 (N.A.) {11/2026}	2,735.00 (N.A.) {2,735.00}	27.35	3.80
		1208	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6GW)] [BIKANER COMPLEX (PGCIL) (N18000403)	11-2024	11/2026 (N.A.) {11/2026}	5,969.00 (N.A.) {5,969.00}	101.47	-
		1209	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6 GW)] [BIKANER COMPLE (PGCIL) (N18000404)	11-2024	11/2026 (N.A.) {11/2026}	5,357.00 (N.A.) {5,357.00}	107.14	3.80
		1210	RAJASTHAN REZ PH-V (PART-1: 4 GW) [SIROHI/NAGAUR] COMPLEX (PGCIL) (N18000414)	3-2025	3/2027 (N.A.) {3/2027}	5,028.00 (N.A.) {5,028.00}	20.12	-
		1211	AUGMENTATION AT FATEHGARH-II PS, FATEHGARH-IV PS (SECTION-II) AND BARMER-I (PGCIL) (N18000415)	3-2025	12/2026 (N.A.) {12/2026}	404.00 (N.A.) {428.00}	4.04	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1212	NOKH SOLAR PV PROJECT 735 MW (NTPC) (N18000418)	3-2022	4/2024 (Jul-2025) {7/2025}	4,189.17 (4,378.17) {4,378.17}	213.45	97.00
	RAILWAYS	1213	AGRA FORT-BANDIKUI (NCR) (N22000553)	6-2022	6/2027 (May-2026) {5/2026}	1,389.81 (N.A.) {987.83}	42.46	12.00
		1214	GUDHA THATHANA MITHRI TEST TRACK FOR RDSO (NWR) (N22000593)	4-2019	3/2025 (Jun-2025) {6/2025}	528.48 (N.A.) {500.85}	357.48	98.00
		1215	DEDICATED TEST TRACK FOR RDSO (PHASE II) (NWR) (N22000594)	11-2021	11/2026 (N.A.) {12/2025}	466.42 (N.A.) {466.22}	743.91	83.00
		1216	DOUBLING BETWEEN CHURU- RATANGARH (42.81 KM) (NWR) (N22000605)	2-2023	2/2028 (N.A.) {6/2025}	422.60 (N.A.) {422.60}	216.78	95.00
		1217	SAWAIMADHOPUR - BYPASS LINE (6.98 KM) (UMBRELLA WORK PB#57/2019- 20/NR) (NWR) (N22000607)	12-2022	6/2026 (May-2027) {5/2027}	304.00 (239.54) {239.54}	133.73	35.00
		1218	GC OF NATHDWARA - DEVGARH MADARIYA (82.5KM) (NWR) (N22000608)	1-2023	6/2028 (Dec-2026) {12/2026}	968.92 (N.A.) {968.92}	410.60	42.00
	ROAD TRANSPORT AND HIGHWAYS	1219	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR (MoRTH) (N24001527)	12-2021	5/2024 (Dec-2025) {12/2025}	411.40 (N.A.) {411.40}	219.61	72.00
		1220	WIDENING OF PACHPADRA-BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH-25 ON EPC MODE IN THE (MoRTH) (N24001528)	1-2022	12/2024 (Aug-2025) {8/2025}	194.88 (N.A.) {194.88}	105.69	83.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1221	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH- 68) IN THE STATE OF RAJASTHAN ON EPC M (MoRTH) (N24001529)	12-2021	8/2024 (May-2025) {5/2025}	451.66 (N.A.) {451.66}	401.78	99.00
		1222	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN-LALSOT- KAROLI-DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH (MoRTH) (N24001530)	12-2021	9/2024 (N.A.) {8/2025}	150.11 (N.A.) {150.11}	82.83	88.00
		1223	4L GREENFIELD SPUR FROM DELHI- VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR (NHAI) (N24001557)	3-2022	11/2024 (Aug-2025) {8/2025}	1,636.15 (N.A.) {1,636.15}	553.96	99.80
		1224	4L OF KARWAR (KM. 281.980 OF NH-62 NAGPUR ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II) (NHAI) (N24001558)	11-2021	8/2024 (Jul-2025) {7/2025}	736.75 (N.A.) {736.75}	260.95	97.80
		1225	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE - 0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK (NHAI) (N24001559)	9-2021	6/2024 (Apr-2025) {4/2025}	672.35 (N.A.) {672.35}	328.24	99.50
		1226	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6) (NHAI) (N24001563)	10-2019	8/2023 (Jul-2025) {7/2025}	846.59 (N.A.) {846.59}	167.92	99.25
		1227	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-7) (NHAI) (N24001564)	10-2019	7/2023 (Jul-2025) {7/2025}	662.08 (N.A.) {662.08}	128.28	96.50
		1228	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA (NHAI) (N24001567)	11-2019	10/2022 (Aug-2025) {8/2025}	1,272.97 (N.A.) {1,272.97}	527.31	89.63

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1229	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N (NHAI) (N24001568)	11-2019	5/2023 (Jul-2025) {7/2025}	1,119.35 (N.A.) {1,119.35}	1,447.44	99.80
		1230	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M (NHAI) (N24001573)	11-2019	12/2022 (Jul-2025) {7/2025}	1,658.06 (N.A.) {1,658.06}	157.42	99.90
		1231	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH (NHAI) (N24001612)	7-2020	1/2024 (Dec-2025) {12/2025}	1,788.69 (N.A.) {1,788.69}	965.50	78.50
		1232	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FOR FATEHPUR BYPASS, MANDAWA BYPASS AND JHUNJHUNU BYPAS (MoRTH) (N24001866)	3-2022	8/2024 (N.A.) {6/2025}	186.29 (N.A.) {186.29}	142.69	90.00
		1233	UPGRADATION OF TWO LANE PAVED SHOULDER FROM SHAHPURA TO THANAGAZI OF NH-248A ON EPC MODE IN THE STAT (MoRTH) (N24001867)	3-2022	7/2024 (N.A.) {8/2025}	174.34 (N.A.) {174.34}	118.08	90.00
		1234	Sagwara Bypass and Garhi- Partapur Bypass of NH-927A in the State of Rajasthan. (MoRTH) (N24001868)	3-2022	8/2025 (N.A.) {8/2025}	187.65 (N.A.) {187.65}	117.57	90.00
		1235	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FROM CHARBHUJA AT DESIGN KM 0.00 (EXISTING KM 150.00) TO (MoRTH) (N24001927)	2-2022	9/2025 (N.A.) {9/2025}	838.43 (N.A.) {838.43}	455.87	99.00
		1236	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER NORTHERN BYPASS PHASE-II OF KOTA CITY FROM DESIGN CHAINAG (MoRTH) (N24001928)	3-2022	4/2025 (N.A.) {12/2025}	317.74 (N.A.) {317.74}	136.23	13.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1237	ADDITIONAL STRUCTURES ON 6LGURGAON-JAIPUR SECTION OF NH- 48 BETWEEN KM 42.700 TO KM 273.00 (NHAI) (N24002058)	8-2022	6/2024 (Jul-2025) {7/2025}	409.64 (N.A.) {409.64}	240.90	81.65
		1238	UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF HANUMANGARH TO KENCHIYAN OF NH 54 ON EPC MODE IN THE ST (MoRTH) (N24002167)	3-2024	10/2026 (N.A.) {10/2026}	334.64 (N.A.) {334.64}	128.00	50.00
		1239	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM NEECHLI ODEN (NATHDWARA) AT DESIGN KM 88.800 TO BHATE (MoRTH) (N24002168)	3-2023	10/2026 (N.A.) {10/2026}	606.61 (N.A.) {606.61}	118.00	20.00
		1240	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT- RAMGARH BHADASAR-JA (NHAI) (N24000795)	2-2018	4/2021 (Jun-2025) {6/2025}	741.86 (649.00) {649.00}	663.37	99.99
		1241	4L+PS OF NH -58 FROM BEAWAR- GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. (MoRTH) (N24001411)	12-2020	10/2023 (N.A.) {12/2025}	379.23 (N.A.) {379.23}	268.62	96.10
SIKKIM	CIVIL AVIATION	1242	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	29.68	12.50
	DEPARTMENT OF HIGHER EDUCATION	1243	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8-2020	1/2025 (N.A.) {1/2025}	314.06 (N.A.) {303.55}	157.24	80.00
	POWER	1244	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	4,424.21	68.17

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1245	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,524.17	89.45
	<u>RAILWAYS</u>	1246	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	5/2015 (Dec-2027) {12/2027}	7,876.92 (11,963.43) {11,963.43}	8,743.57	79.50
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1247	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (Mar-2026) {3/2026}	385.15 (N.A.) {385.15}	175.16	83.30
		1248	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (May-2022) {12/2023}	375.80 (N.A.) {375.80}	288.56	96.55
		1249	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {10/2025}	402.94 (N.A.) {402.94}	247.12	76.54
		1250	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (Nov-2024) {10/2025}	295.97 (N.A.) {295.97}	249.97	95.71
		1251	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {10/2025}	311.00 (N.A.) {273.78}	257.86	95.12
		1252	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (Aug-2024) {10/2025}	345.38 (395.59) {395.59}	362.61	89.81

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1253	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (Oct-2023) {12/2025}	183.31 (439.56) {439.56}	355.31	51.85
		1254	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (Aug-2024) {12/2025}	262.84 (414.20) {414.20}	221.86	49.20
		1255	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (Oct-2023) {12/2025}	292.80 (N.A.) {292.80}	202.92	61.41
		1256	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO) (NHIDCL) (N24001336)	8-2020	4/2023 (Oct-2024) {3/2026}	230.45 (244.91) {244.91}	206.95	82.80
		1257	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (Jul-2025) {3/2026}	493.42 (478.79) {478.79}	308.18	59.49
		1258	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (Jun-2025) {12/2026}	816.79 (786.60) {786.60}	332.24	45.90
		1259	RISHI BORDER- ROLEP- MENLA PKG-3B (NHIDCL) (N24001362)	12-2020	2/2024 (Dec-2025) {12/2025}	410.60 (379.30) {379.30}	238.13	74.82
TAMIL NADU	CIVIL AVIATION	1260	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI (AAI) (N04000074)	6-2018	2/2022 (Jun-2026) {6/2026}	2,467.00 (N.A.) {2,467.00}	1,620.03	71.65

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1261	DEVELOPMENT OF TUTICORIN AIRPORT (AAI) (N04000090)	6-2019	3/2022 (Apr-2025) {4/2025}	380.87 (451.74) {451.74}	362.06	100.00
	COAL	1262	JAWAHAR KHANI OPENCAST (JK OC) MINE (SCCL) (N06000259)	12-2021	3/2025 (N.A.) {3/2026}	297.88 (N.A.) {297.88}	46.37	20.00
		1263	50 MW SOLAR POWER PROJECT - NEYVELI MINED OUT AREA (NLC) (N06000279)	5-2023	6/2025 (Nov-2025) {11/2025}	218.03 (N.A.) {218.03}	148.89	40.00
	FINANCE	1264	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI (CPWD FOR FINANC) (N28000109)	11-2017	11/2021 (N.A.) {11/2022}	348.77 (N.A.) {348.77}	223.39	100.00
	MINES	1265	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (NALCO) (N10000014)	9-2017	6/2019 (Dec-2025) {12/2025}	166.62 (163.17) {163.17}	135.63	65.00
	PETROLEUM	1266	IRUGUR-DEVANGONTHI POL PIPELINE (BPCL) (N16000234)	11-2012	2/2017 (Oct-2025) {10/2025}	678.00 (1,732.00) {1,732.00}	642.76	64.10
		1267	CBR 9 MMTPA PROJECT (CPCL) (N16000434)	1-2021	6/2025 (N.A.) {6/2025}	31,580.00 (31,580.00) {36,354.00}	1,326.17	10.20
		1268	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI (IOCL) (N16000438)	1-2022	7/2024 (Jun-2025) {12/2025}	827.00 (887.71) {887.71}	580.94	85.90
		1269	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI) (IOCL) (N16000455)	1-2022	7/2024 (May-2026) {5/2026}	829.00 (N.A.) {829.00}	259.48	60.16

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1270	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS (IOCL) (N16000486)	3-2022	3/2030 (N.A.) {12/2030}	501.00 (N.A.) {501.00}	112.66	5.30
		1271	CGD PROJECTS AT THE NILGIRIS AND ERODE DISTRICTS (BPCL) (N16000521)	12-2022	3/2030 (N.A.) {3/2030}	3,685.00 (N.A.) {3,685.00}	213.89	11.20
	<u>POWER</u>	1272	TRANSMISSION SYSTEM UNDER ISTS FOR EVACUATION OF POWER FROM KUDANKULAM UNIT - 3 AND 4 (2X1000 MW) (PGCIL) (N18000408)	1-2025	7/2028 (N.A.) {7/2028}	548.00 (N.A.) {548.00}	9.32	2.50
	<u>RAILWAYS</u>	1273	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP (MRTP) (N22000028)	4-2006	7/2024 (Aug-2025) {8/2025}	734.01 (981.83) {981.83}	640.43	98.00
		1274	TIDIVANAM-NAGARI (NL) (SR) (N22000085)	9-2006	9/2016 (Mar-2028) {3/2028}	3,631.34 (3,631.34) {3,631.34}	873.31	15.00
		1275	CHENNAI BEACH-CHENNAI EGMORE (4.3 KM) (UMBRELLA WORK PB#57/2019- 20/NR) (SR) (N22000568)	3-2022	3/2026 (Feb-2025) {3/2025}	359.60 (274.20) {310.00}	305.93	95.00
		1276	MORAPPUR-DHARMAPURI (SR) (N22000618)	2-2019	3/2028 (Mar-2028) {3/2028}	358.95 (N.A.) {358.95}	40.09	-
		1277	NAGAPATTINAM THIRUTURAI PUNDI (38KM)- NEW LINE PROJECT (SR) (N22000626)	7-2008	3/2026 (Mar-2027) {3/2027}	677.12 (N.A.) {668.44}	146.95	20.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1278	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER (NHAI) (N24001429)	3-2018	11/2021 (Jul-2025) {7/2025}	1,294.47 (1,588.40) {1,588.40}	867.34	98.72

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1279	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN (NHAI) (N24001431)	3-2018	10/2020 (Jan-2026) {1/2026}	1,872.68 (2,899.77) {2,899.77}	1,341.26	65.00
		1280	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 (MoRTH) (N24001455)	2-2022	8/2022 (N.A.) {3/2025}	191.33 (207.97) {207.97}	100.42	100.00
		1281	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 (NHAI) (N24001601)	1-2019	1/2023 (Nov-2025) {11/2025}	1,051.69 (N.A.) {1,051.69}	589.46	81.87
		1282	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001602)	1-2019	12/2022 (Nov-2025) {11/2025}	1,409.38 (N.A.) {1,409.38}	660.29	91.20
		1283	4-LANING OF MELUR - PILLAYARPATTI - KARAIKUDI SECTION OF NH-338, NH- 36, NH-383 (NHAI) (N24001605)	6-2018	3/2022 (N.A.) {8/2025}	1,103.86 (N.A.) {1,103.86}	568.15	87.00
		1284	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH-744A (MADURAI RING ROAD) (NHAI) (N24001606)	12-2018	3/2022 (Sep-2025) {9/2025}	854.94 (N.A.) {854.94}	400.13	80.30
		1285	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS (NHAI) (N24001692)	1-2022	9/2024 (Feb-2025) {8/2025}	467.99 (N.A.) {468.00}	113.05	84.34
		1286	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 (NHAI) (N24001693)	9-2021	10/2024 (N.A.) {10/2024}	1,751.18 (N.A.) {1,757.27}	49.69	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1287	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM (NHAI) (N24001694)	2-2019	12/2023 (Dec-2024) {12/2024}	1,243.57 (N.A.) {1,243.57}	171.63	-
		1288	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG-III) FROM KM.60+100 TO KM.94+460 (NHAI) (N24001696)	2-2019	8/2023 (Dec-2024) {12/2024}	1,291.37 (N.A.) {1,291.37}	215.02	-
		1289	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM (NHAI) (N24001716)	7-2022	8/2023 (Dec-2024) {12/2024}	186.50 (242.40) {242.40}	34.33	100.00
		1290	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K (NHAI) (N24001717)	11-2020	8/2024 (N.A.) {3/2026}	1,155.49 (1,525.10) {1,525.10}	489.94	53.56
		1291	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2 (NHAI) (N24001718)	12-2020	7/2024 (N.A.) {10/2025}	843.48 (1,077.40) {1,068.60}	434.49	91.26
		1292	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT (NHAI) (N24001719)	2-2021	7/2024 (N.A.) {12/2025}	2,948.31 (3,605.73) {3,605.73}	820.23	78.11
		1293	BANGALORE CHENNAI EXPRESSWAY PHASE-III ? PACKAGE I (GUDIPALA TO WALAJHPET) FROM KM 156.000 TO KM 1 (NHAI) (N24001720)	10-2020	5/2024 (N.A.) {10/2025}	1,023.91 (1,438.62) {1,438.62}	635.04	86.22

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1294	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 (NHAI) (N24001721)	2-2019	5/2024 (Aug-2025) {3/2026}	1,008.99 (1,360.53) {1,360.53}	324.81	50.33
		1295	6L OF MADURAVOYAL TO SRIPERUMBUDUR SECTION FROM KM. 13.800 TO KM. 37.000 OF NH-4 THROUGH STATE HIGH (NHAI) (N24001722)	11-2021	2/2023 (N.A.) {12/2024}	463.44 (463.07) {463.44}	334.80	99.00
		1296	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091 (NHAI) (N24001723)	10-2018	2/2021 (N.A.) {8/2025}	707.90 (766.51) {766.51}	542.69	91.00
		1297	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48 (NHAI) (N24001725)	1-2019	5/2021 (N.A.) {1/2025}	819.89 (1,314.82) {922.85}	419.84	57.32
		1298	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 ? 29/250 INCLUDING LA AND SHIFTING OF NH-234 (MoRTH) (N24001828)	1-2022	11/2024 (N.A.) {5/2025}	221.03 (243.95) {243.95}	176.50	100.00
		1299	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH-83) INCLU (MoRTH) (N24001829)	10-2022	11/2024 (N.A.) {5/2025}	172.15 (N.A.) {172.15}	163.82	100.00
		1300	CONSTRUCTION OF STRR (WEST SIDE)-NH948A-BALAGONDAPALLI (TAMIL NADU) TO KARNATAKA/TAMIL NADU BORDER F (NHAI) (N24001968)	4-2022	5/2025 (N.A.) {5/2025}	1,260.74 (N.A.) {1,260.74}	487.46	44.95
		1301	4L OF THIRUMANGALAM TO VADUGAPATTI SECTION FROM KM 0.000 TO KM 36.000 OF NH-744 (NHAI) (N24002084)	3-2022	2/2025 (N.A.) {9/2025}	1,076.97 (N.A.) {1,076.97}	540.46	87.42

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1302	CONSTRUCTION OF NEW DOUBLE TIER 4 LANE ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI (NHAI) (N24002107)	3-2023	5/2026 (N.A.) {5/2026}	1,382.00 (N.A.) {1,382.00}	0.00	-
		1303	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002108)	3-2023	5/2026 (N.A.) {5/2026}	1,618.96 (N.A.) {1,618.96}	0.00	-
		1304	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002109)	3-2023	5/2026 (N.A.) {5/2026}	1,301.37 (N.A.) {1,301.37}	0.00	-
		1305	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002110)	3-2023	5/2026 (N.A.) {5/2026}	1,207.40 (N.A.) {1,207.40}	0.00	-
		1306	FOUR LANING OF MUGAIYUR TO MARAKKANAM SECTION OF NH-332A FROM KM 31.000 TO KM 62.000 (NHAI) (N24002111)	2-2019	12/2025 (May-2026) {5/2026}	825.94 (1,116.13) {1,116.13}	344.92	40.55
		1307	SIX LANING OF TUTICORIN PORT ROAD SECTION OF NH-7A (NEW NH- 138) FROM KM 0.000 TO KM 6.140 [EFFECTIVE (NHAI) (N24002112)	3-2023	7/2024 (N.A.) {7/2025}	200.30 (N.A.) {200.30}	113.71	93.11
		1308	4L OF LEFT-OVER WORKS INCLUDING ADDITIONAL STRUCTURES FROM KERALA/TAMIL NADU BORDER TO KANYAKUMARI S (NHAI) (N24002113)	3-2023	8/2025 (N.A.) {8/2025}	1,141.78 (N.A.) {1,141.78}	466.20	47.86

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1309	4L OF VADUGAPATTI TO THERKUVENGANALLUR (RAJAPALYAM) SECTION FROM KM 36.000 TO KM 71.600 OF NH744 UND (NHAI) (N24002114)	2-2022	4/2025 (N.A.) {10/2025}	1,097.59 (N.A.) {1,317.06}	705.17	97.80
		1310	WIDENING TO 4L/4L+PS AND STRENGTHENING IN SELECTED STRETCHES FROM KM 0/8 TO 50/570 OF NH 532 INCLUD (MoRTH) (N24002151)	3-2022	1/2024 (N.A.) {7/2025}	257.14 (294.70) {294.70}	277.57	90.00
		1311	WIDENING FROM 2L+PS TO 4L/4L+PS AND IMPROVEMENTS THE SELECTED STRETHCES FROM KM 26/5 - 81/2 INCLU (MoRTH) (N24002152)	3-2023	11/2023 (N.A.) {11/2025}	274.84 (N.A.) {274.84}	265.83	100.00
		1312	STRENGTHENING OF 2L+PS FROM KM 17/8 ? 18/2, CONSTRUCTION OF 2L+PS FROM KM 18/2 TO KM 20/0 AND CONSTR (MoRTH) (N24002153)	3-2023	2/2024 (N.A.) {8/2025}	169.68 (N.A.) {169.68}	145.29	100.00
		1313	CONSTRUCTION OF BYPASS TO MADURAI - ACHAMBATHU - VIRATIPATHU IN KM 6/850 - 10/382 OF NH 49 EXTN. (NE (MoRTH) (N24002165)	3-2022	8/2026 (N.A.) {8/2026}	238.97 (260.07) {260.07}	118.00	50.00
		1314	ACCESS CONTROLLED HIGHWAY OF 4 LANE WITH PAVED SHOULDERS FROM TIRUVALLUR (DESIGN CHAINAGE KM 17+56) (NHAI) (N24002216)	12-2024	12/2026 (N.A.) {12/2026}	1,376.10 (N.A.) {1,376.10}	39.00	8.74
		1315	FOUR LANNING OF CHOLOPURAM- THANJAVUR (NHAI) (N24000697)	8-2017	9/2020 (N.A.) {7/2025}	1,176.37 (N.A.) {1,176.37}	1,325.06	99.50
		1316	4-LANNING OF STHIYATHOPU- CHOLOPURAM (NHAI) (N24000708)	9-2017	8/2020 (Jul-2025) {7/2025}	1,227.87 (N.A.) {1,227.87}	1,436.16	99.50

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1317	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 (NHAI) (N24000826)	3-2018	10/2022 (Jul-2025) {7/2025}	505.35 (N.A.) {837.69}	376.61	99.75
TELANGANA	COAL	1318	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 (SCCL) (N06000161)	3-2017	3/2022 (N.A.) {3/2026}	413.84 (N.A.) {413.84}	397.54	85.00
		1319	GODAVARIKHANI COAL MINE (SCCL) (N06000202)	7-2019	3/2023 (N.A.) {3/2026}	438.98 (N.A.) {438.98}	178.21	70.00
		1320	VENKATESH KHANI COAL MINE (SCCL) (N06000204)	10-2020	3/2023 (N.A.) {3/2027}	484.51 (N.A.) {484.51}	318.12	55.00
		1321	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT (SCCL) (N06000210)	11-2015	3/2023 (N.A.) {3/2026}	489.62 (N.A.) {489.62}	405.54	70.00
		1322	RCE OF INDARAM OPENCAST PROJECT (SCCL) (N06000211)	8-2017	3/2021 (N.A.) {3/2025}	349.28 (N.A.) {424.81}	402.64	80.00
		1323	RCE OF KALYANIKHANI OPENCAST PROJECT (SCCL) (N06000213)	3-2016	3/2020 (N.A.) {3/2026}	384.32 (N.A.) {384.32}	265.53	75.00
		1324	RCE OF KAKATHIYAKHANI OC - 2 PROJECT (SCCL) (N06000214)	8-2017	3/2020 (N.A.) {3/2026}	442.42 (N.A.) {442.42}	203.14	63.00
		1325	GOLETI OPENCAST MINE (SCCL) (N06000258)	7-2021	3/2026 (N.A.) {3/2026}	345.60 (N.A.) {345.60}	72.09	20.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>HEALTH AND FAMILY WELFARE</u>	1326	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD (CPWD FOR HEALTH) (N28000098)	10-2016	3/2020 (Jan-2025) {1/2025}	209.84 (281.05) {281.05}	253.64	98.50
		1327	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR (HITES) (N21000031)	12-2018	7/2024 (N.A.) {12/2025}	1,110.55 (N.A.) {1,110.55}	753.76	83.07
	<u>RAILWAYS</u>	1328	MANOHARABAD-KOTHPALL NEW LINE(SCR) (SCR) (N22000032)	4-2006	3/2027 (N.A.) {3/2025}	1,160.00 (N.A.) {3,014.00}	1,568.57	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1329	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED (GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM (NHAI) (N24001482)	8-2022	10/2024 (Aug-2022) {12/2025}	772.11 (N.A.) {772.11}	558.24	80.51
		1330	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM VILLAGE TO CHINTAGUDEM V (NHAI) (N24001483)	2-2022	9/2024 (Feb-2022) {9/2025}	637.11 (N.A.) {637.11}	415.98	85.40
		1331	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUDEM VILLAGE TO RECHERLA (NHAI) (N24001484)	9-2022	2/2024 (Sep-2022) {9/2025}	804.69 (N.A.) {804.69}	514.29	91.20
		1332	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 (NHAI) (N24001522)	1-2021	1/2024 (Jan-2021) {7/2025}	1,307.95 (N.A.) {1,307.95}	727.42	99.98
		1333	6 LANING OF EXISTING 4-LANE STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000, (NHAI) (N24001555)	3-2022	1/2025 (N.A.) {1/2025}	955.49 (N.A.) {955.49}	233.46	35.96

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1334	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44 (NHAI) (N24001556)	12-2021	7/2024 (N.A.) {7/2024}	521.53 (N.A.) {521.53}	250.70	49.63
		1335	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 (NHAI) (N24001625)	1-2022	1/2025 (N.A.) {7/2025}	1,227.57 (N.A.) {1,227.57}	288.58	45.65
		1336	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM (NHAI) (N24001626)	2-2022	1/2025 (N.A.) {1/2025}	972.06 (N.A.) {972.06}	408.48	70.26
		1337	WIDENING AND STRENGTHENING OF EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FRO (MoRTH) (N24002000)	3-2021	7/2024 (N.A.) {7/2024}	317.19 (N.A.) {317.19}	178.64	72.00
		1338	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF MEDAK - SIDDIPET SECTION FROM KM 0/0 TO KM 69/978 OF NH- (MoRTH) (N24002001)	1-2022	1/2025 (N.A.) {1/2025}	882.18 (N.A.) {882.18}	376.66	73.14
		1339	WIDENING AND IMPROVEMENT OF EXISTING CARRIAGE WAY TO 2 LANE WITH PAVED SHOULDERS FROM KM. 86/160 TO (MoRTH) (N24002002)	1-2022	12/2024 (N.A.) {12/2024}	423.48 (N.A.) {423.48}	166.39	71.65
		1340	REHABILITATION AND UP-GRADATION OF VALIGONDA TO THORRUR SECTION TO TWO LANE WITH PAVED SHOULDERS FRO (MoRTH) (N24002003)	1-2022	12/2024 (N.A.) {12/2024}	549.28 (N.A.) {549.28}	257.89	74.75
		1341	REHABILITATION AND UPGRADATION OF LB-NAGAR TO MALKAPUR SECTION TO 6-LANE MAIN CARRIAGEWAY WITH SERVI (MoRTH) (N24002004)	3-2021	7/2024 (N.A.) {7/2024}	545.11 (N.A.) {545.11}	198.03	76.64

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1342	WIDENING TO TWO LANE WITH PAVED SHOULDERS OF 'BODHAN BASAR BHAINSA' SECTION FROM KM 38/900 TO 95/3 (MoRTH) (N24002005)	3-2022	3/2025 (N.A.) {3/2025}	644.45 (N.A.) {644.45}	221.65	93.60
		1343	ONSTRUCTION OF 4-LANE FLYOVER AT AMBERPET-X ROAD, HYDERABAD ON NH-202 IN THE STATE OF TELANGANA (MoRTH) (N24002006)	10-2017	6/2023 (N.A.) {6/2023}	186.71 (N.A.) {186.71}	149.64	92.10
		1344	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/000 TO KM 79/300 OF KALWAKURTHY - KOLLAPUR SECTI (MoRTH) (N24002007)	3-2022	7/2025 (N.A.) {7/2025}	886.69 (N.A.) {886.69}	252.22	67.94
		1345	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF SIDDIPET- ELKATHURTHY SECTION FROM KM 69/978 TO KM 133/6 (MoRTH) (N24002008)	1-2022	12/2024 (N.A.) {12/2024}	578.85 (N.A.) {578.85}	292.69	82.05
		1346	WIDENING AND STRENGTHENING TO 2/4 LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR ? CHINCHOLI SECTION FROM (MoRTH) (N24002009)	1-2022	1/2025 (N.A.) {7/2025}	703.68 (N.A.) {703.68}	210.72	76.45
		1347	WIDENING AND STRENGTHENING TO 4 LANE / 2-LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR- CHINCHOLI SECTION (MoRTH) (N24002010)	3-2022	3/2024 (N.A.) {10/2025}	631.49 (N.A.) {631.49}	75.33	28.98
		1348	IMPROVEMENT OF GEOMETRICS OF THONDUPALLY TO KOTHUR FROM KM 22.300 TO KM 34.14 OF NH-44-RCW (NHAI) (N24002082)	2-2022	9/2024 (N.A.) {1/2026}	541.58 (N.A.) {541.58}	34.98	-
		1349	FOUR LANING OF KARIMNAGAR- WARANGAL SECTION OF NH-563 FROM DESIGN CH.48.860 KM NEAR SH-1 CH.170.400 K (NHAI) (N24002083)	3-2022	7/2025 (N.A.) {7/2025}	2,146.86 (2,413.00) {2,414.46}	999.54	72.35

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1350	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM- VIJAYAWADA) (NHAI) (N24002190)	3-2023	8/2026 (N.A.) {8/2026}	983.00 (N.A.) {983.00}	0.00	8.50
		1351	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM - VIJAYAWADA (NHAI) (N24002236)	3-2023	3/2025 (N.A.) {3/2027}	832.62 (N.A.) {832.62}	0.00	-
		1352	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT (MoRTH) (N24000245)	1-2014	3/2016 (Sep-2019) {9/2019}	270.00 (N.A.) {270.00}	0.00	72.15
		1353	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR (MoRTH) (N24000247)	10-2014	2/2017 (N.A.) {2/2017}	295.47 (N.A.) {295.47}	224.42	82.76
		1354	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM (MoRTH) (N24000248)	3-2015	1/2017 (N.A.) {1/2017}	153.21 (N.A.) {153.21}	100.96	93.20
		1355	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON (MoRTH) (N24000980)	10-2016	2/2019 (N.A.) {2/2019}	298.32 (N.A.) {298.32}	178.47	-
		1356	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ (MoRTH) (N24000981)	10-2016	3/2019 (N.A.) {3/2019}	248.83 (N.A.) {248.83}	173.79	-
		1357	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE (MoRTH) (N24000982)	1-2017	5/2019 (N.A.) {5/2019}	244.54 (N.A.) {244.54}	174.35	99.96

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1358	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH (MoRTH) (N24000983)	1-2017	10/2019 (N.A.) {10/2019}	196.52 (N.A.) {196.52}	125.53	92.74
		1359	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI (MoRTH) (N24000984)	1-2017	12/2019 (N.A.) {12/2019}	283.00 (N.A.) {283.00}	259.15	99.32
		1360	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION (MoRTH) (N24000986)	1-2017	5/2019 (N.A.) {5/2019}	300.00 (N.A.) {300.00}	239.93	99.09
		1361	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH (MoRTH) (N24000987)	1-2018	5/2020 (N.A.) {5/2020}	283.15 (N.A.) {283.15}	270.01	92.62
		1362	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 (MoRTH) (N24000988)	1-2018	12/2019 (N.A.) {12/2019}	230.03 (N.A.) {230.03}	231.31	100.00
		1363	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 (MoRTH) (N24000989)	2-2018	6/2020 (N.A.) {6/2020}	206.13 (N.A.) {206.13}	190.94	98.56
		1364	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT (MoRTH) (N24000990)	2-2018	11/2019 (N.A.) {11/2019}	294.13 (N.A.) {294.13}	198.75	90.10
		1365	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC (MoRTH) (N24000993)	3-2018	9/2020 (N.A.) {9/2020}	322.81 (N.A.) {322.81}	315.23	98.14

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1366	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES (MoRTH) (N24000994)	3-2018	7/2020 (N.A.) {2/2026}	626.76 (N.A.) {626.76}	272.64	46.00
		1367	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR (MoRTH) (N24000996)	1-2017	10/2019 (N.A.) {10/2019}	605.08 (N.A.) {605.08}	413.37	99.90
		1368	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL ? MALLAMPALLY SECTION OF NH-365 (MoRTH) (N24000997)	3-2018	7/2019 (N.A.) {7/2019}	192.67 (N.A.) {192.67}	176.37	96.00
		1369	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR (MoRTH) (N24000998)	1-2019	(N.A.) {}	193.19 (N.A.) {249.72}	222.58	100.00
<u>TRIPURA</u>	<u>PETROLEUM</u>	1370	GRASS ROOT RAIL FED DEPOT AT SEKEREKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (Sep-2025) {9/2025}	656.00 (N.A.) {656.00}	427.77	83.17
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1371	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (May-2025) {5/2025}	456.88 (N.A.) {456.88}	122.67	50.18
		1372	IMPROVEMENT AND WIDENING TO 2- LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {12/2025}	195.95 (N.A.) {195.95}	46.46	45.42
		1373	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	26.34	8.82

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1374	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGTH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	9.54	16.61
		1375	IMPROVEMENT AND WIDENING TO 2- LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	52.82	34.61
		1376	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	95.71	32.85
		1377	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	3.81	3.05
		1378	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	81.54	24.56
		1379	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM SECTION PKG-4 (NHIDCL) (N24002228)	1-2024	12/2026 (N.A.) {12/2026}	726.90 (N.A.) {726.90}	7.36	3.85
		1380	REHABILITATION AND UPGADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (Feb-2024) {12/2024}	277.50 (302.02) {302.02}	262.91	99.94
		1381	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (Oct-2023) {11/2024}	159.13 (171.50) {171.50}	84.33	100.00
		1382	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {4/2025}	201.99 (N.A.) {287.47}	148.22	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1383	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (N.A.) {12/2025}	354.79 (N.A.) {354.79}	34.08	-
UTTAR PRADESH	CIVIL AVIATION	1384	CCS INTERNATIONAL AIRPORT , LUCKNOW (AAI) (N04000077)	6-2018	9/2021 (Oct-2026) {10/2026}	1,383.00 (1,938.00) {3,291.81}	2,652.63	80.58
		1385	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 (AAI) (N04000094)	3-2021	12/2022 (Jul-2025) {7/2025}	242.14 (328.00) {358.00}	344.58	99.90
		1386	PRAYAGRAJ AIRPORT - CONSTRUCTION OF NEW TERMINAL BUILDING, SECOND LINK TAXI TRACK, APRON EXPANSION, (AAI) (N04000102)	5-2023	11/2024 (Jul-2025) {7/2025}	185.75 (274.38) {274.38}	206.39	97.25
		1387	AGRA: DEVELOPMENT OF NEW CIVIL ENCLAVE AT AGRA AIRPORT. (AAI) (N04000113)	6-2024	7/2026 (N.A.) {7/2026}	579.00 (N.A.) {579.00}	72.23	13.00
		1388	VARANASI: DEVELOPMENT OF LAL BAHADUR SHASTRI INTERNATIONAL AIRPORT, VARANASI. (AAI) (N04000114)	7-2024	7/2027 (N.A.) {7/2027}	2,869.65 (N.A.) {2,869.65}	283.00	14.51
	COAL	1389	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW (NLC) (N06000152)	7-2016	11/2021 (Oct-2025) {10/2025}	17,237.00 (21,780.94) {21,780.94}	19,949.00	91.39
		1390	KHADIA EXPANSION OCP (NCL) (N06000208)	6-2021	3/2025 (N.A.) {3/2027}	491.67 (N.A.) {491.67}	202.24	40.86
	PETROLEUM	1391	60 KTA POLYPROPYLENE PROJECT (GAIL) (N16000429)	3-2019	4/2024 (Apr-2024) {7/2025}	910.56 (1,299.02) {1,299.02}	974.00	96.90

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1392	AUGMENTATION OF FACILITIES AT MATHURA BITUMEN PLANT (IOCL) (N16000505)	4-2022	4/2025 (Dec-2026) {12/2026}	260.12 (N.A.) {260.12}	1.07	25.00
		1393	GRASS-ROOT TERMINAL AT MIRZAPUR UTTAR PRADESH (IOCL) (N16000506)	9-2022	6/2026 (N.A.) {11/2026}	980.45 (N.A.) {980.45}	206.85	50.75
		1394	CITY GAS DISTRIBUTION PROJECTS AT LAKHIMPUR KHERI , SITAPUR, BAHRAICH, SHRAVASTI,BALRAMPUR, (BPCL) (N16000525)	12-2022	6/2030 (N.A.) {6/2030}	16,654.00 (N.A.) {16,654.00}	550.36	9.70
	POWER	1395	KHURJA SUPER THERMAL POWER PROJECT (THDCIL) (N18000272)	3-2019	9/2023 (N.A.) {8/2025}	11,089.42 (13,276.16) {13,276.16}	12,580.53	96.00
		1396	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III (2X800 MW) (NTPC) (N18000382)	3-2024	2/2030 (N.A.) {2/2030}	17,195.31 (N.A.) {17,195.31}	1,569.79	0.50
		1397	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-4: 3.5 GW): PART A (PGCIL) (N18000407)	12-2024	12/2026 (N.A.) {12/2026}	5,846.00 (N.A.) {5,846.00}	198.76	2.10
		1398	TRANSMISSION SYSTEM FOR STRENGTHENING TO FACILITATE EVACUATION OF POWER FROM BHADLA/BIKANER COMPLEX (PGCIL) (N18000423)	12-2024	6/2026 (N.A.) {6/2026}	213.00 (N.A.) {213.00}	0.00	-
	RAILWAYS	1399	BURHWAL - GONDA - 3RD RUNNING LINE. (NER) (N22000468)	4-2016	3/2025 (N.A.) {9/2025}	1,015.59 (N.A.) {1,450.00}	1,277.57	52.00
		1400	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. (NER) (N22000470)	4-2016	12/2024 (N.A.) {8/2025}	1,177.96 (N.A.) {2,145.00}	2,050.16	85.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1401	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING (NCR) (N22000495)	3-2018	3/2026 (N.A.) {3/2027}	4,329.53 (N.A.) {4,329.53}	2,125.66	50.00
		1402	JHANSI BINA DOUBLING (NCR) (N22000496)	9-2016	3/2022 (N.A.) {4/2026}	2,002.00 (N.A.) {2,001.00}	1,745.48	90.00
		1403	MATHURA-JHANSI-3RD LINE (273.80 KM) (RVNL) (N22000501)	6-2016	12/2024 (N.A.) {12/2024}	5,323.39 (N.A.) {5,190.26}	5,046.07	-
		1404	SURFACE TRIANGLE LINE BETWEEN BHADURA STATION AND NEW CROSSING STN KARMA DOUBLING (ECR) (N22000525)	10-2022	10/2027 (N.A.) {10/2027}	199.96 (N.A.) {199.96}	55.09	-
		1405	MUGHALSARAI - ALLAHABAD - 3RD LINE (NCR) (N22000544)	8-2019	12/2026 (N.A.) {12/2026}	2,649.44 (N.A.) {2,390.00}	83.10	55.00
		1406	ALIGARH-HARDUAGANJ FLYOVER (22 KM) (NCR) (N22000545)	4-2020	6/2026 (N.A.) {6/2026}	1,456.89 (1,244.13) {1,456.89}	10.14	8.20
		1407	LALITPUR - BIRARI WITH FLYOVER AT LALITPUR (NCR) (N22000546)	3-2017	12/2024 (N.A.) {11/2025}	356.09 (N.A.) {356.00}	213.97	65.00
		1408	ALIGARH-DAUD KHAN - 3RD LINE 6.9 KM AND CONSTRUCTION OF FLYOVER AT DAUD KHAN (NCR) (N22000562)	4-2019	12/2025 (N.A.) {12/2025}	451.99 (779.49) {779.49}	122.08	44.00
		1409	ALLAHABAD-BAMHRAULI - 4TH LINE (10 KM) WITH FLY-OVER AT SUBEDARGANJ (NCR) (N22000563)	4-2019	3/2026 (N.A.) {3/2026}	494.11 (N.A.) {494.11}	42.61	42.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1410	BHANDAI - FLYOVER FOR ETAWAH BOUND DOWN TRAINS (NCR) (N22000564)	4-2019	12/2025 (N.A.) {3/2026}	187.21 (N.A.) {250.17}	1.29	8.00
		1411	SAHJANWA - DOHRIGHAT (NER) (N22000565)	8-2019	3/2029 (N.A.) {12/2027}	371.77 (N.A.) {1,319.75}	577.85	5.00
		1412	BAHRAICH - NANPARA -NEPALGANJ (56.15 KM) (NER) (N22000566)	7-2020	12/2024 (N.A.) {8/2025}	950.00 (N.A.) {500.00}	424.74	25.00
		1413	BAHRAICH SRAVASTI BALRAMPUR (TULSIPUR) (NER) (N22000569)	10-2018	10/2030 (N.A.) {3/2028}	4,939.78 (N.A.) {4,939.78}	1,334.98	7.50
		1414	JANGHAI PRATAPGARH AMETHI DOUBLING (NR) (N22000583)	11-2017	3/2025 (N.A.) {12/2025}	721.72 (N.A.) {1,100.00}	58.98	70.00
		1415	BARABANKI MALHAUR 3RD AND 4TH LINE (32.84 KM) (NR) (N22000590)	1-2019	3/2025 (Jan-2026) {1/2026}	323.85 (N.A.) {407.00}	18.91	59.00
		1416	DOUBLING BETWEEN JAUNPUR JN- ZAFFARABAD (6.28 KM) (NR) (N22000591)	3-2023	12/2026 (N.A.) {12/2026}	177.33 (N.A.) {177.33}	0.89	10.00
		1417	JANGHAI-PHAPHAMAU - DOUBLING WITH ELECTRIFICATION (46.79 KM) (RVNL) (N22000596)	11-2018	3/2025 (N.A.) {3/2025}	357.48 (N.A.) {409.38}	362.09	-
		1418	BHATNI - AUNRIHAR WITH ELECTRIFICATION (125 KM) (EXCL INDARA - MAU (116.95 KM)) (RVNL) (N22000598)	5-2018	12/2024 (N.A.) {2/2025}	2,529.46 (N.A.) {2,529.46}	1,636.33	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1419	MATHURA - VRINDAVAN (11 KM) (NCR) (N22000612)	8-2022	6/2025 (N.A.) {6/2025}	402.88 (N.A.) {402.88}	0.00	-
		1420	DOMINGARH - GORAKHPUR - GORAKHPUR CANTT - KUSUMHI - 3RD RUNNING LINE (21.15 KM) (NER) (N22000613)	11-2016	2/2025 (N.A.) {7/2025}	351.03 (N.A.) {500.37}	494.01	86.50
	ROAD TRANSPORT AND HIGHWAYS	1421	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD (MoRTH) (N24001421)	7-2018	2/2024 (N.A.) {8/2025}	1,948.25 (N.A.) {1,948.25}	1,146.61	79.00
		1422	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W (MoRTH) (N24001424)	3-2021	9/2023 (N.A.) {1/2025}	185.09 (269.81) {269.81}	266.35	100.00
		1423	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM (MoRTH) (N24001456)	4-2020	2/2024 (N.A.) {1/2025}	199.39 (212.96) {199.39}	200.01	100.00
		1424	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH- 730C F (MoRTH) (N24001457)	4-2020	7/2024 (N.A.) {9/2025}	172.50 (169.56) {172.50}	106.06	76.00
		1425	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP (MoRTH) (N24001461)	4-2020	3/2024 (N.A.) {8/2025}	236.47 (N.A.) {236.47}	145.95	88.00
		1426	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH- 92 FROM KM.30.000 TO 57.346 UNDER GNHCP (MoRTH) (N24001462)	4-2020	7/2024 (N.A.) {8/2025}	211.09 (N.A.) {211.09}	147.58	96.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1427	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00 (MoRTH) (N24001464)	3-2021	8/2023 (N.A.) {8/2025}	264.86 (N.A.) {264.86}	129.12	84.00
		1428	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO (MoRTH) (N24001469)	11-2021	5/2024 (N.A.) {7/2025}	307.11 (N.A.) {307.11}	199.38	91.00
		1429	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH-730C FROM KM.0.00 TO 52.770 UNDER GNHCP (MoRTH) (N24001471)	4-2020	11/2024 (N.A.) {7/2025}	325.24 (340.16) {325.24}	284.35	98.00
		1430	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR) (MoRTH) (N24001479)	3-2021	5/2024 (N.A.) {8/2025}	395.62 (392.03) {395.62}	281.93	76.00
		1431	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH- 334A (PURKAJI-LAKSAR-HARIDWAR ROAD) TO TW (MoRTH) (N24001480)	10-2021	4/2024 (N.A.) {3/2025}	227.06 (N.A.) {227.06}	141.89	100.00
		1432	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO(NEAR MOHAND) OF GANESHPUR ? DEHRADUN SECTION FROM K (NHAI) (N24001523)	3-2021	10/2023 (Jul-2025) {7/2025}	836.24 (N.A.) {836.24}	792.55	98.85
		1433	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR ? DEHRADUN SECTION FROM (NHAI) (N24001524)	3-2021	10/2023 (Jul-2025) {7/2025}	990.28 (N.A.) {990.28}	997.62	98.89
		1434	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF (MoRTH) (N24001587)	3-2020	9/2024 (N.A.) {8/2025}	262.37 (343.77) {343.77}	278.92	85.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1435	4L SPUR OF SHAMLI-MUZZAFARNAGAR CONNECTING NH-709AD (PANIPAT- SHAMLI-MUZZAFARNAGAR) AND NH-58 (MEERUT (NHAI) (N24001726)	1-2023	8/2024 (N.A.) {8/2024}	391.26 (N.A.) {391.26}	14.12	80.30
		1436	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF KHUTAR B (NHAI) (N24001727)	3-2022	2/2025 (N.A.) {9/2025}	762.62 (N.A.) {838.68}	571.23	95.50
		1437	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT ? SHAMLI ? MUZZAFARNAGAR) AND NH- 709A (KARN (NHAI) (N24001729)	8-2022	4/2024 (N.A.) {7/2025}	326.79 (N.A.) {329.79}	113.42	98.50
		1438	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) (NHAI) (N24001730)	12-2021	1/2025 (N.A.) {3/2025}	1,384.79 (N.A.) {1,384.79}	657.94	97.98
		1439	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 (NHAI) (N24001731)	12-2021	5/2025 (May-2025) {9/2025}	2,470.64 (N.A.) {2,335.00}	691.28	94.68
		1440	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS (NHAI) (N24001732)	12-2021	10/2024 (N.A.) {9/2025}	540.97 (N.A.) {540.97}	314.76	94.76
		1441	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.-MAVIKALAN) TO VILL.- LOHADDA FROM K (NHAI) (N24001733)	3-2022	8/2024 (N.A.) {7/2025}	1,602.48 (N.A.) {1,602.48}	454.77	94.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1442	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-LOHADDA TO VILL- KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. (NHAI) (N24001734)	3-2022	8/2024 (N.A.) {7/2025}	1,335.45 (N.A.) {1,335.45}	480.89	85.02
		1443	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KHYAWARI TO VILL- LATIFPUR AT SAHARANPUR BYPASS FROM KM (NHAI) (N24001735)	3-2022	8/2024 (N.A.) {7/2025}	1,428.19 (N.A.) {1,428.19}	544.15	89.50
		1444	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KARAUNDA MAHAJAN TO VILL-KHYAWARI FROM KM. 56.500 TO K (NHAI) (N24001736)	1-2022	8/2024 (N.A.) {7/2025}	1,159.96 (N.A.) {1,159.96}	515.80	98.69
		1445	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG-III (NHAI) (N24001737)	11-2021	4/2024 (N.A.) {4/2024}	923.15 (N.A.) {923.15}	455.61	100.00
		1446	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV (NHAI) (N24001738)	9-2021	10/2023 (Dec-2024) {12/2024}	300.79 (N.A.) {300.79}	122.56	80.61
		1447	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U (NHAI) (N24001739)	10-2019	11/2023 (Dec-2024) {12/2024}	1,779.83 (N.A.) {2,200.00}	1,066.00	100.00
		1448	4L OF SHAMLI BYAPSS- SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II (NHAI) (N24001744)	5-2019	11/2022 (N.A.) {7/2025}	779.17 (N.A.) {779.17}	71.39	98.50
		1449	KANPUR LUCKNOW EXPRESSWAY PKG- 1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N (NHAI) (N24001745)	12-2021	7/2025 (Jul-2025) {7/2025}	1,972.10 (N.A.) {1,936.00}	504.87	67.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1450	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4-LANE ON EPC MODE IN THE STATE OF UTTAR (NHAI) (N24001746)	3-2021	4/2024 (Jul-2025) {7/2025}	364.47 (N.A.) {364.47}	209.19	92.98
		1451	4 LANING OF NAJIBABAD BYPASS OF NH-119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH-74 (NHAI) (N24001753)	2-2022	6/2024 (Jun-2025) {6/2025}	570.98 (570.98) {570.98}	424.98	97.49
		1452	SPUR OF MEERUT-GARH-MUKTESHWAR SECTION(NH-709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN (NHAI) (N24001754)	1-2022	10/2024 (N.A.) {10/2024}	953.79 (N.A.) {953.79}	384.66	71.02
		1453	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM. 39.250 AND KM 86.590 TO KM. 112.545.IN TH (NHAI) (N24001755)	10-2019	3/2023 (Dec-2024) {12/2024}	1,936.68 (N.A.) {2,458.03}	1,380.90	100.00
		1454	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR (NHAI) (N24001772)	8-2021	3/2024 (Dec-2024) {12/2024}	1,147.26 (N.A.) {1,147.26}	172.34	60.00
		1455	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 (NHAI) (N24001826)	2-2019	2/2022 (Jun-2025) {12/2025}	927.77 (N.A.) {1,603.00}	1,202.77	91.25
		1456	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 (NHAI) (N24001830)	6-2020	11/2023 (Dec-2024) {12/2024}	2,002.79 (N.A.) {2,002.79}	1,989.85	99.00
		1457	4L FROM MATHURA BYPASS (START) AT EXISTING KM. 154.20 OF NH-44 TO GAJU VILLAGE AT KM 32.982 OF NH-53 (NHAI) (N24001851)	1-2022	3/2025 (N.A.) {3/2025}	1,738.20 (N.A.) {1,738.20}	742.13	65.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1458	6L OF AGRA BYPASS (NORTHERN) CONNECTING KM. 174.500 OF NH-2 (NEW NH-19) TO KM. 141.000 OF YAMUNA EXP (NHAI) (N24001852)	10-2021	2/2025 (N.A.) {2/2025}	957.62 (N.A.) {957.62}	832.80	86.00
		1459	CONSTRUCTION OF LEFT OUT PORTION OF AGRA INNER RING ROAD CONNECTING VILLAGE DEORI TO NH- 44 VILLAGE B (NHAI) (N24001853)	10-2021	9/2024 (Mar-2025) {3/2025}	772.05 (N.A.) {772.05}	593.39	67.50
		1460	CONSTRUCTION OF 4-LANE GREEN FIELD HIGHWAY FROM KM. 35.000 TO KM. 49.155 OF NH-731A WITH PAVED SHOUL (MoRTH) (N24001929)	1-2022	10/2025 (N.A.) {10/2025}	697.66 (N.A.) {697.66}	318.82	98.00
		1461	BALANCE WORKS OF 4-LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 (NEW NH NO. 09) FROM KM. 0.000 (KM 1 (NHAI) (N24001992)	8-2022	2/2024 (Jul-2025) {7/2025}	199.31 (244.26) {244.26}	190.10	97.62
		1462	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER HIGHWAY FROM DESIGN CH.0.000 TO CH.49.200 OF NH- 731B ON (MoRTH) (N24001996)	3-2022	11/2025 (N.A.) {11/2025}	640.18 (602.76) {602.76}	487.39	81.00
		1463	CONSTRUCTION OF SHOHRATGARH BYPASS ON NH-730 UNDER EPC MODE IN THE STATE OF UTTAR PRADESH (MoRTH) (N24001997)	10-2022	5/2025 (N.A.) {2/2026}	189.31 (N.A.) {189.31}	59.91	22.00
		1464	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 90.00 TO (MoRTH) (N24002015)	11-2021	6/2025 (N.A.) {8/2025}	403.36 (328.49) {403.36}	150.57	73.00
		1465	CONSTRUCTION OF PRATAPGARH BYPASS (EXTENSION) CONNECTING NH-31 TO NH-330 (MoRTH) (N24002016)	10-2022	6/2025 (N.A.) {8/2025}	225.17 (N.A.) {225.17}	96.56	55.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1466	WIDENING TO FOUR LANE WITH PAVED SHOULDER FROM DESIGN KM.49.200 TO KM.89.285 OF NH-731B ON EPC MODE (MoRTH) (N24002029)	3-2022	1/2026 (N.A.) {1/2026}	917.91 (956.30) {917.91}	615.53	47.00
		1467	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM EXISTING KM.0.000 TO KM.55.610 (DESIGN KM. 0.000 T (MoRTH) (N24002031)	12-2021	2/2026 (N.A.) {2/2026}	840.93 (773.58) {840.93}	524.04	44.00
		1468	CONSTRUCTION OF 4-LANE HIGHWAY WITH PAVED SHOULDERS FROM KM 49.155 TO KM 74.700 OF NH-731A ON HYBRID (MoRTH) (N24002032)	1-2022	1/2026 (N.A.) {1/2026}	1,156.72 (N.A.) {1,156.72}	407.20	70.00
		1469	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM GOGWAN JALALPUR (SHAMLI DISTRICT) TO RANIPUR (NHAI) (N24002036)	4-2022	5/2025 (N.A.) {5/2025}	1,843.59 (N.A.) {1,843.59}	843.87	50.20
		1470	GARHMUKTESHWAR (KM. 83.200 OF NH-24) TO MEERUT (KM. 9.860 OF NH- 235) INCLUDING CONNECTOR TO NH- 119 (NHAI) (N24002073)	10-2019	10/2023 (N.A.) {6/2025}	2,068.99 (2,171.00) {2,171.00}	209.60	53.08
		1471	CONSTRUCTION OF FOUR LANE HIGHWAY FORM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002086)	10-2022	7/2025 (N.A.) {7/2025}	1,706.47 (N.A.) {1,706.47}	719.13	77.25
		1472	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002087)	10-2022	10/2025 (N.A.) {10/2025}	1,493.14 (N.A.) {1,493.14}	93.30	66.00
		1473	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002088)	10-2022	8/2025 (N.A.) {8/2025}	1,493.50 (N.A.) {1,493.50}	492.86	58.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1474	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER GREENFIELD SECTION OF N (NHAI) (N24002089)	10-2022	6/2025 (N.A.) {6/2025}	617.87 (N.A.) {617.88}	106.20	72.00
		1475	CONSTRUCTION OF FOUR-LANE ?WESTERN SIDE SPUR OF RAMPUR- RUDRAPUR SECTION CONNECTING NH-24 TO NH-87 BY (NHAI) (N24002090)	3-2021	11/2024 (Dec-2025) {12/2025}	646.27 (N.A.) {646.27}	110.65	52.09
		1476	IMPROVEMENT , UP-GRADATION OF NH-734 SECTION OF MORADABAD - THAKURDWARA - KASHIPUR: ?PACKAGE-I: MORA (NHAI) (N24002093)	10-2022	9/2025 (N.A.) {2/2026}	1,841.92 (N.A.) {1,841.92}	449.98	54.40
		1477	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 123.650 TO 175.080, FROM START OF SHA (NHAI) (N24002094)	9-2022	11/2025 (N.A.) {11/2025}	1,212.26 (N.A.) {1,212.26}	361.81	34.19
		1478	FOUR LANING OF SONAULI GORAKHPUR SECTION OF NH 29E (NEW NH 24) FROM DESIGN CH. 0.000 TO DESIGN CH. 7 (NHAI) (N24002095)	12-2021	3/2025 (N.A.) {3/2025}	2,555.50 (N.A.) {2,555.50}	966.89	63.57
		1479	CONSTRUCTION OF 4 LANE GREEN FIELD NORTHERN EAST SIDE GORAKHPUR BYPASS (26.616 KMS) STARTING FROM NH (NHAI) (N24002096)	2-2023	1/2026 (N.A.) {1/2026}	1,973.98 (N.A.) {1,973.98}	736.14	48.50
		1480	STRENGTHENING OF EXISTING 4L AYODHYA BYPASS SECTION FROM DESIGN KM.121.600 TO KM. 144.020 OF NH 28 ((NHAI) (N24002097)	2-2023	9/2025 (N.A.) {8/2025}	526.45 (N.A.) {526.45}	228.37	83.00
		1481	CONSTRUCTION OF RING ROAD AROUND KANPUR FROM KM.000 TO KM. 23.325 (CHACHENDI SACHENDI I TO MAHARAJPU (NHAI) (N24002104)	1-2023	6/2026 (N.A.) {6/2026}	1,754.00 (N.A.) {1,754.00}	350.78	35.20

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1482	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS (PHASE-I) FROM DESIGN KM 43+200 (AT MAHUWARI VI (NHAI) (N24002105)	8-2023	6/2026 (N.A.) {6/2026}	1,378.36 (N.A.) {739.00}	213.86	30.89
		1483	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS FROM DESIGN KM 50.860 (NABABA URF NIBI KALA UPA (NHAI) (N24002106)	8-2023	3/2025 (N.A.) {10/2025}	993.77 (N.A.) {349.48}	372.98	92.98
		1484	CONSTRUCTION OF MARIAHU BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION (KM.53.540 TO KM.59.200) (MoRTH) (N24002115)	3-2023	8/2025 (N.A.) {2/2026}	438.24 (362.39) {438.24}	211.72	39.00
		1485	REHABILITATION AND UPGRADATION FROM KM 51.600 TO KM 75.700 OF NH- 321G (NUHKHAS TO ETAH SECTION) TO T (MoRTH) (N24002116)	1-2022	8/2025 (N.A.) {8/2025}	343.54 (N.A.) {343.54}	75.96	42.00
		1486	CONSTRUCTION OF JASRA BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION FROM KM. 379.670 ON NH-76 ((MoRTH) (N24002120)	2-2023	9/2025 (N.A.) {9/2025}	274.06 (N.A.) {274.06}	135.53	88.00
		1487	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM. 420.00 (MoRTH) (N24002121)	1-2022	9/2025 (N.A.) {2/2026}	509.65 (N.A.) {509.65}	188.84	34.00
		1488	REHABILITATION AND UP-GRADATION FROM KM. 0.000 TO KM. 40.390 OF NH- 730S (MAHARAJGANJ ? NICHLOUL ? TH (MoRTH) (N24002134)	3-2023	12/2025 (N.A.) {12/2025}	809.25 (N.A.) {809.25}	279.77	35.00
		1489	CONSTRUCTION OF FOUR LANE HIGHWAY WITH PAVED SHOULDER FROM KM.74.700 TO KM.112.950 OF NH- 731A (I/C Y (MoRTH) (N24002138)	3-2022	6/2026 (N.A.) {6/2026}	1,141.67 (N.A.) {1,141.67}	423.37	50.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1490	CONSTRUCTION OF BALRAMPUR BYPASS WITH 2L FLEXIBLE PAVEMENT CONFIGURATION FROM KM.223.000 OF NH-330 T (MoRTH) (N24002150)	12-2022	2/2026 (N.A.) {2/2026}	515.69 (N.A.) {515.69}	187.80	37.00
		1491	WIDENING TO 4L RIGID PAVEMENT CONFIGURATION FROM KM 90.00 TO KM 100.800 OF NH-96 (KM 42.0 TO KM 53.3 (MoRTH) (N24002199)	12-2022	11/2026 (N.A.) {11/2026}	309.63 (N.A.) {309.63}	13.52	15.00
		1492	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER/FOUR LANE CONFIGURATION FROM EXISTING K (MoRTH) (N24002201)	1-2022	5/2027 (N.A.) {5/2027}	974.19 (N.A.) {974.19}	616.12	14.00
		1493	REHABILITATION AND UPGRADATION TO FOUR LANE ROAD FROM KM 70.500 TO KM 78.600 OF NH-92 UNDER EPC MODE (MoRTH) (N24002211)	1-2022	1/2027 (N.A.) {1/2027}	296.02 (N.A.) {296.02}	27.96	-
		1494	WIDENING AND STRENGTHENING FROM DESIGN KM. 67.280 TO KM. 88.622 OF NH-727A (SALEMPUR- MAIRWA ROAD) TO (MoRTH) (N24002212)	3-2023	7/2026 (N.A.) {7/2026}	371.89 (N.A.) {371.89}	151.99	45.00
		1495	REHABILITATION and UP-GRADATION TO 2L+PS FROM KM. 0.0 TO KM. 7.80 AND KM. 35.400 TO KM. 52.345 (DESI (MoRTH) (N24002213)	3-2023	7/2026 (N.A.) {7/2026}	701.02 (N.A.) {701.02}	270.54	22.00
		1496	CONSTRUCTION OF AMETHI BYPASS (PART-II) AT KM.30.050 OF NH-931 UNDER EPC MODE IN THE STATE OF UTTAR (MoRTH) (N24002214)	12-2022	2/2027 (N.A.) {2/2027}	283.86 (N.A.) {283.86}	58.92	7.00
		1497	WIDENING TO 4L FROM KM.108.50 TO 139.00 OF NH-135A PKG-II (JAUNPUR TO AKBARPUR SECTION) ON HAM IN TH (MoRTH) (N24002234)	3-2023	3/2027 (N.A.) {3/2027}	1,511.57 (N.A.) {1,511.57}	154.69	12.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1498	CONSTRUCTION OF RAEBARELI RING ROAD (PHASE-2) WITH FOUR LANE CONFIGURATION FOR RAEBARELI CITY IN THE (MoRTH) (N24002235)	3-2022	5/2027 (N.A.) {5/2027}	1,273.72 (N.A.) {1,273.72}	330.15	-
		1499	IMPROVEMENT AND UP-GRADATION OF NH-227B (84 KOSI PARIKRAMA MARG) PACKAGE ?I, FROM KM 228.920 (JAGARN (MoRTH) (N24002240)	3-2022	11/2026 (N.A.) {11/2026}	912.50 (N.A.) {912.50}	388.50	1.00
		1500	IMPROVEMENT AND UP-GRADATION OF NH-227B (84 KOSI PARIKRAMA MARG) PACKAGE ?III, FROM KM.47.800 (GOSAI (MoRTH) (N24002241)	3-2022	11/2026 (N.A.) {11/2026}	587.97 (N.A.) {587.97}	107.68	3.00
		1501	CONSTRUCTION OF BASTI RING ROAD (PHASE-I) WITH 4L CONFIGURATION FOR BASTI CITY IN THE STATE OF UTTAR (MoRTH) (N24002245)	12-2022	6/2027 (N.A.) {6/2027}	1,138.72 (N.A.) {1,138.72}	263.70	-
		1502	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B (MoRTH) (N24000331)	12-2019	4/2022 (N.A.) {7/2025}	282.41 (N.A.) {319.96}	276.35	88.00
		1503	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 (NHAI) (N24000564)	3-2016	7/2020 (Jul-2025) {7/2025}	1,408.00 (1,659.12) {1,659.12}	1,336.33	91.39
		1504	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA (NHAI) (N24000798)	3-2018	11/2021 (N.A.) {6/2025}	2,140.93 (N.A.) {2,140.93}	2,081.52	100.00
		1505	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN (NHAI) (N24001306)	10-2020	3/2023 (N.A.) {8/2025}	724.60 (N.A.) {724.60}	569.96	96.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>URBAN DEVELOPMENT</u>	1506	KANPUR METRO RAIL PROJECT (LMRCL) (N28000144)	5-2019	3/2024 (N.A.) {3/2027}	11,076.48 (N.A.) {11,076.48}	8,839.21	72.60
		1507	AGRA METRO RAIL PROJECT (LMRCL) (N28000145)	5-2019	3/2024 (N.A.) {6/2027}	8,379.62 (N.A.) {8,379.62}	5,116.00	54.70
	<u>WATER RESOURCES</u>	1508	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH (UPJalNigam) (N30000021)	1-2019	12/2021 (Jan-2020) {3/2025}	231.79 (234.03) {234.03}	141.79	100.00
		1509	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH (UPJalNigam) (N30000024)	2-2019	6/2022 (N.A.) {12/2025}	681.78 (N.A.) {690.71}	13.34	27.00
	<u>CIVIL AVIATION</u>	1510	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN (AAI) (N04000085)	7-2018	9/2020 (Sep-2024) {9/2024}	456.86 (500.00) {500.00}	483.96	100.00
UTTARAKHAND	<u>POWER</u>	1511	TEHRI PUMPED STORAGE PLANT(1000MW) (THDCIL) (N18000010)	7-2006	7/2010 (Jun-2022) {9/2025}	1,657.00 (4,825.60) {8,182.00}	8,046.19	98.30
		1512	TAPOVAN-VISHNUGAD HEP (4X130MW) (NTPC) (N18000014)	11-2006	3/2013 (Dec-2021) {4/2029}	2,978.48 (N.A.) {10,907.00}	7,007.93	72.40
		1513	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT (THDCIL) (N18000042)	8-2008	6/2013 (N.A.) {3/2027}	2,491.58 (3,860.35) {6,823.72}	4,918.46	71.00
		1514	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW (NTPC) (N18000142)	7-2012	8/2017 (N.A.) {8/2017}	1,527.00 (N.A.) {1,527.00}	149.93	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>RAILWAYS</u>	1515	RISHIKESH - KARNAPRAYAG NEW LINE (RVNL) (N22000406)	4-2011	12/2025 (N.A.) {3/2025}	38,953.15 (N.A.) {24,659.00}	18,820.04	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1516	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR ? DEHRADUN SECTION FROM KM. (NHAI) (N24001525)	3-2021	3/2024 (May-2025) {5/2025}	169.08 (N.A.) {169.08}	105.77	99.99
		1517	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF (NHAI) (N24001526)	8-2021	10/2024 (Aug-2025) {8/2025}	1,377.79 (1,384.11) {1,377.79}	684.93	58.41
		1518	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH- 07(PKG-2) (NHAI) (N24001553)	3-2022	2/2025 (Nov-2025) {11/2025}	1,092.90 (1,092.90) {1,092.90}	463.92	89.25
		1519	4L POANTA SAHEB?MEDNIPUR FROM KM. 435.65 TO KM. 458.65 OF NH- 07(PKG-1) (NHAI) (N24001990)	6-2022	5/2025 (Oct-2025) {10/2025}	524.54 (683.26) {683.26}	91.94	74.78
		1520	ACCESS ROAD/BRIDGE CONNECTIVITY FROM NH-09 AT KM.40 NEAR JAGBUDA BRIDGE (INDIA) TO BOUNDARY PILLAR (NHAI) (N24001991)	5-2022	9/2024 (Nov-2026) {11/2026}	314.31 (N.A.) {314.31}	178.52	71.79
		1521	CONSTRUCTION FOR MITIGATION MEASURES KM 368.00-UTTARAKHAND- TO KM 433.00 ON NH-07-PKG-1 (NHIDCL) (N24002163)	12-2023	12/2025 (N.A.) {12/2025}	216.88 (N.A.) {216.88}	82.19	75.80
		1522	CONSTRUCTION FOR MITIGATION MEASURES KM 450.00-UTTARAKHAND- TO KM 468.00 ON NH-07-PKG-3 (NHIDCL) (N24002164)	12-2023	12/2025 (N.A.) {12/2025}	250.33 (N.A.) {250.33}	46.63	48.50

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1523	CONSTRUCTION FOR MITIGATION MEASURES PKG-2 (NHIDCL) (N24002206)	12-2023	6/2026 (N.A.) {6/2026}	259.64 (N.A.) {259.64}	18.62	20.23
		1524	4-LANING OF KASHIPUR-SITARGANJ SECTION (AMR) (N24000465)	11-2012	8/2016 (N.A.) {8/2016}	605.84 (N.A.) {605.84}	0.00	-
		1525	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI (NHIDCL) (N24000742)	3-2018	11/2020 (N.A.) {3/2024}	403.36 (N.A.) {403.36}	340.32	100.00
		1526	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA (NHIDCL) (N24000743)	3-2018	11/2020 (N.A.) {3/2024}	417.24 (N.A.) {417.24}	344.20	100.00
		1527	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000772)	12-2017	12/2019 (N.A.) {12/2019}	257.34 (N.A.) {257.34}	232.69	100.00
		1528	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000773)	12-2017	12/2019 (N.A.) {12/2019}	200.34 (N.A.) {200.34}	227.98	100.00
		1529	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 (MoRTH) (N24000774)	12-2017	12/2019 (N.A.) {12/2019}	248.22 (N.A.) {248.22}	236.80	100.00
		1530	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000775)	6-2017	6/2019 (N.A.) {6/2019}	282.08 (N.A.) {282.08}	234.97	100.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1531	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG (MoRTH) (N24000776)	11-2017	11/2019 (N.A.) {11/2019}	232.81 (N.A.) {232.81}	201.58	100.00
		1532	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION (MoRTH) (N24000777)	11-2017	11/2019 (N.A.) {11/2019}	283.51 (N.A.) {283.51}	278.51	100.00
		1533	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000778)	11-2017	11/2019 (N.A.) {11/2019}	266.52 (N.A.) {266.52}	250.34	100.00
		1534	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR (MoRTH) (N24000779)	2-2018	2/2020 (N.A.) {2/2020}	418.88 (N.A.) {418.88}	339.71	94.00
		1535	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K (MoRTH) (N24000780)	2-2018	(N.A.) {}	293.68 (N.A.) {293.68}	244.25	100.00
		1536	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN (MoRTH) (N24000781)	5-2018	5/2020 (N.A.) {5/2020}	248.00 (N.A.) {248.00}	120.50	67.00
		1537	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 (MoRTH) (N24000782)	3-2018	(N.A.) {}	460.73 (N.A.) {461.00}	0.00	-
		1538	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) (NHIDCL) (N24000855)	3-2018	7/2022 (N.A.) {9/2026}	1,383.78 (N.A.) {1,383.78}	714.33	64.27

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1539	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER (MoRTH) (N24001130)	8-2016	12/2017 (N.A.) {12/2017}	234.88 (N.A.) {234.88}	237.19	100.00
WEST BENGAL	CIVIL AVIATION	1540	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA (AAI) (N04000080)	1-2016	3/2020 (Dec-2023) {12/2023}	458.00 (N.A.) {458.00}	251.64	100.00
		1541	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA (AAI) (N04000081)	1-2019	11/2021 (May-2023) {5/2023}	389.71 (397.00) {397.00}	396.61	100.00
		1542	NSCBI AIRPORT KOLKATA: RE- CONSTRUCTION OF RIGID POSITIONS OF SECONDARY RUNWAY, 'K' AND 'A' TAXIWAY (AAI) (N04000109)	4-2023	10/2025 (N.A.) {10/2025}	328.30 (N.A.) {328.30}	91.70	42.50
		1543	BAGDOGRA AIRPORT: DEVELOPMENT OF NEW CIVIL ENCLAVE AT BAGDOGRA AIRPORT. SUB-HEAD : CONSTRUCTION OF N (AAI) (N04000115)	8-2024	3/2027 (N.A.) {3/2027}	1,549.00 (N.A.) {1,549.00}	239.75	9.62
	COAL	1544	RANIGANJ MASTER PLAN (ECL) (N06000163)	8-2009	8/2019 (N.A.) {8/2019}	2,661.73 (N.A.) {5,146.48}	787.60	42.00
		1545	SIDULI MINE (OC AND UG) (ECL) (N06000165)	5-2018	3/2027 (N.A.) {3/2027}	535.18 (N.A.) {535.17}	5.00	14.00
		1546	NAKRAKONDA KUMARDIH B OCP (ECL) (N06000170)	8-2018	3/2029 (N.A.) {3/2029}	502.68 (N.A.) {502.67}	71.07	25.51

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1547	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT (ECL) (N06000191)	4-2020	3/2026 (Mar-2026) {3/2026}	483.65 (N.A.) {483.65}	55.53	12.09
		1548	2.0 MTPA BHOJUDIH NLW WASHERY (BCCL) (N06000195)	12-2015	9/2020 (N.A.) {7/2025}	384.57 (N.A.) {384.57}	351.16	97.00
		1549	SONEPUR BAZARI EXPANSION OC (ECL) (N06000220)	7-2021	3/2029 (N.A.) {3/2029}	5,365.88 (5,366.00) {5,365.88}	562.41	17.38
		1550	EXPANSION PR OF JHANJRA UG (5.00 MTY) (ECL) (N06000223)	4-2020	3/2029 (N.A.) {3/2029}	1,210.12 (N.A.) {1,210.12}	495.37	40.00
		1551	MOHANPUR EXPANSION OC PHASE II (ECL) (N06000236)	11-2020	3/2026 (N.A.) {3/2026}	888.99 (N.A.) {888.99}	89.54	30.25
		1552	BONJEMEHARI EXPANSION OCP (ECL) (N06000244)	8-2021	3/2026 (Mar-2026) {3/2026}	570.12 (N.A.) {570.11}	81.58	16.00
		1553	ITAPARA OC (ECL) (N06000272)	12-2023	3/2030 (N.A.) {3/2030}	929.10 (N.A.) {929.10}	65.03	6.80
		1554	UCE OF TILABONI UG (ECL) (N06000276)	1-2023	3/2029 (N.A.) {3/2029}	749.07 (N.A.) {749.07}	52.09	10.30
		1555	UCE OF PARASEA BELBAID REORGANISATION UG (ECL) (N06000277)	1-2023	3/2029 (Mar-2028) {3/2028}	389.10 (N.A.) {389.10}	131.42	16.41
		1556	PARASCOLE JAMBAD OCP (ECL) (N06000281)	11-2024	3/2037 (N.A.) {3/2037}	1,193.55 (N.A.) {1,193.55}	6.04	0.01

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1557	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED (CPWD EDUCATION) (N28000146)	3-2020	6/2020 (N.A.) {3/2024}	193.83 (N.A.) {193.83}	187.65	99.00
	<u>MINES</u>	1558	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA (CPWD) (N10000015)	4-2019	4/2022 (N.A.) {8/2026}	255.37 (N.A.) {255.37}	74.13	40.00
	<u>PETROLEUM</u>	1559	DURGAPUR-HALDIA PIPELINE PROJECT (GAIL) (N16000275)	3-2017	12/2020 (Dec-2025) {12/2025}	1,740.00 (2,433.15) {2,433.15}	2,193.80	90.00
		1560	HALDIA PANAGARH PIPELINE PROJECT (HPCL) (N16000478)	11-2022	11/2025 (N.A.) {11/2025}	1,010.00 (N.A.) {1,010.00}	573.18	80.09
		1561	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS (IOCL) (N16000491)	3-2022	3/2030 (N.A.) {6/2031}	609.00 (N.A.) {609.00}	56.00	2.10
		1562	CGD PROJECT IN WEST BENGAL 11TH ROUND (HPCL) (N16000498)	6-2022	6/2030 (N.A.) {6/2030}	2,628.00 (N.A.) {2,628.00}	320.83	24.10
		1563	CITY GAS DISTRIBUTION PROJECTS AT ALIPURDUAR AND COOCH BEHAR (BPCL) (N16000522)	12-2022	3/2030 (N.A.) {3/2030}	1,017.00 (N.A.) {1,017.00}	168.34	31.90
	<u>POWER</u>	1564	RAMMAM-III HEPP (3X40 MW) (NTPC) (N18000178)	9-2014	9/2019 (Dec-2024) {3/2029}	1,381.84 (N.A.) {1,803.00}	1,302.76	43.68
	<u>RAILWAYS</u>	1565	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER (ER) (220100272)	4-2000	3/2019 (Feb-2026) {2/2026}	1,188.91 (N.A.) {2,582.49}	1,283.98	75.00

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1566	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA- BARASAI VIA BIMANBANDER (MTP) (KOMRCL) (N22000108)	4-2010	8/2026 (N.A.) {3/2016}	4,829.60 (N.A.) {2,397.72}	197.20	17.00
		1567	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) (RVNL) (N22000109)	4-2010	12/2026 (N.A.) {12/2025}	2,298.42 (N.A.) {2,733.86}	392.98	-
		1568	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) (RVNL) (N22000110)	4-2010	12/2025 (N.A.) {3/2026}	8,964.35 (N.A.) {8,964.35}	7,387.40	-
		1569	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. (RVNL) (N22000111)	4-2010	12/2026 (N.A.) {12/2026}	4,834.54 (N.A.) {4,834.54}	3,918.86	-
		1570	PURULIA TO KOTSHILA DOUBLING (39.1 KM) (SER) (N22000510)	4-2018	12/2024 (N.A.) {3/2025}	393.83 (N.A.) {393.83}	319.21	100.00
		1571	NAHATI - RANAGHAT 3RD LINE (MM OF KALINARAYANPUR - KRISHNANAGAR) (ER) (N22000624)	7-2015	3/2025 (N.A.) {3/2026}	1,000.00 (N.A.) {283.54}	171.63	44.00
		1572	EAST WEST METRO CORRIDOR KOLKATA (KOMRCL) (N22000628)	2-2009	9/2016 (N.A.) {9/2016}	4,874.58 (8,575.00) {10,442.41}	0.00	-
		1573	KALIPAHARI - BAKHTARNAGAR 5TH LINE (17.61 KM) (ER) (N22000630)	4-2024	6/2027 (N.A.) {6/2027}	350.46 (N.A.) {350.46}	0.00	-

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1574	SITARAMPUR BYE - PASS LINE (6.59 KM) (ER) (N22000631)	2-2023	3/2027 (N.A.) {3/2027}	461.64 (N.A.) {461.64}	26.87	-
		1575	MURARAI - BARHARWA 3RD LINE (48.90 KM) (ER) (N22000632)	5-2025	5/2028 (N.A.) {5/2028}	935.19 (N.A.) {935.19}	0.00	-
	ROAD TRANSPORT AND HIGHWAYS	1576	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 (NHAI) (N24001747)	3-2020	9/2024 (N.A.) {9/2024}	2,193.23 (2,314.00) {2,314.00}	2,085.00	97.04
		1577	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA (NHAI) (N24001748)	3-2021	9/2024 (N.A.) {12/2025}	2,200.93 (N.A.) {2,622.05}	2,622.05	97.60
		1578	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE (NHAI) (N24001749)	8-2021	8/2023 (N.A.) {9/2025}	557.55 (N.A.) {567.31}	473.26	91.41
		1579	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA (NHAI) (N24001750)	8-2018	12/2021 (N.A.) {8/2025}	622.04 (N.A.) {622.04}	579.31	91.64
		1580	DEVELOPMENT TO 4/6-LANNING OF NH-31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 (MoRTH) (N24001850)	3-2022	9/2025 (Sep-2025) {9/2025}	995.04 (995.04) {995.04}	422.06	51.21
		1581	CONSTRUCTION OR 4 LANE RANIGANJ BYPASS OF LENGTH 5 261 KM ON NH 60 NEW NH 14 FROM KM 273 00 OF NH (MoRTH) (N24002184)	3-2023	3/2026 (Mar-2026) {3/2026}	410.83 (N.A.) {410.83}	164.34	37.50

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1582	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF LEVEL CROSSING NO 10 B T AT KM 307 050 OF NH 60 B (MoRTH) (N24002191)	3-2016	8/2025 (N.A.) {8/2025}	155.87 (N.A.) {155.87}	21.68	10.61
		1583	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) (NHAI) (N24000463)	12-2015	6/2018 (May-2024) {8/2023}	1,083.00 (1,414.01) {1,414.01}	1,080.05	100.00
		1584	SIX-LANING OF BARWA ADDA- PANAGARH (NHAI) (N24000515)	4-2014	9/2016 (N.A.) {5/2025}	1,665.00 (N.A.) {4,980.13}	4,980.13	100.00
		1585	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU (NHAI) (N24000788)	3-2018	9/2022 (Dec-2022) {12/2025}	841.57 (708.30) {708.30}	12,485.63	96.49
		1586	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H (MoRTH) (N24000874)	3-2016	11/2018 (Dec-2023) {9/2025}	271.17 (291.20) {291.20}	199.72	82.56
		1587	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. (MoRTH) (N24000880)	2-2018	9/2020 (Jan-2024) {2/2025}	426.18 (426.18) {426.18}	364.92	100.00
		1588	REBUILDING OF COKE OVEN BATTERY NO.4 OF DURGAPUR STEEL PLANT (SAIL) (N12000132)	11-2023	12/2026 (N.A.) {12/2026}	916.78 (N.A.) {916.78}	110.08	10.98
	STEEL	1589	INSTALLATION OF NEW BAR MILL AT DURGAPUR STEEL PLANT (SAIL) (N12000138)	9-2024	6/2027 (N.A.) {6/2027}	2,115.44 (N.A.) {2,115.44}	100.12	19.97

Table:-7. Project List: Ongoing Projects as of 30th June 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1590	UP-GRADATION OF BLAST FURNACE NO. 3 AT DURGAPUR STEEL PLANT (SAIL) (N12000139)	9-2024	6/2026 (N.A.) {6/2026}	758.09 (N.A.) {758.09}	35.34	2.50
		1591	REVAMPING OF AIR POLLUTION CONTROL SYSTEMS OF SP-1 AT DURGAPUR STEEL PLANT (SAIL) (N12000140)	11-2024	5/2026 (N.A.) {5/2026}	196.40 (N.A.) {196.40}	0.19	1.00
		1592	THIRD LADLE FURNACE IN SECONDARY REFINERY UNIT AT IISCO STEEL PLANT (SAIL) (N12000141)	11-2024	7/2026 (N.A.) {7/2026}	227.96 (N.A.) {227.96}	2.61	29.00
	<u>WATER RESOURCES</u>	1593	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA (KMDA) (N30000032)	5-2018	2/2022 (N.A.) {8/2025}	198.43 (224.69) {286.97}	77.79	98.00
		1594	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA (KMDA) (N30000034)	8-2017	9/2022 (Jan-2023) {12/2026}	307.12 (N.A.) {653.67}	0.00	-
		1595	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH (KMDA) (N30000042)	5-2018	2/2022 (Sep-2020) {3/2025}	160.00 (154.73) {154.73}	93.32	92.00
			Total			2,685,568.07 (797,659.49) {2,975,429.26}	16,30,750.12	

Abbreviations used in the Report

AGENCY_NAME	AGENCY_NAME_SHORT
AIRPORT AUTHORITY OF INDIA LIMITED	AAI
ARTIFICIAL LIMBS MANUFACTURING CORPM. OF INDIA	ALIMCO
BHARAT ALUMINUM CORPORATION	BALCO
BHABHA ATOMIC RESEARCH CENTRE	BARC
BHARAT COKING COAL LIMITED	BCCL
BRAHMAPUTRA CRECKER & POLYMER LTD.	BCPL
BHAVINI LIMITED	BHAVNI
BHARAT HEAVY ELECTRICALS LIMITED	BHEL
BANGALORE METRO RAIL CORPORATION LIMITED	BMRCL
BOKARO STEEL PLANT	BOKARO STEEL PL
BRAHMAPUTRA BOARD	BPB
BHARAT PETROLEUM CORPORATION LIMITED	BPCL
BORDER ROAD ORGANISATION	BRO
BONGAIGAON REFINERY PETROLEUM LIMITED	BRPL
BHARAT SANCHAR NIGAM LIMITED	BSNL
Bihar Urban Infrastructure Development Corporation Ltd	BUIDCO
BRAHMAPUTRA VALLY FERTILISER CORPORATION	BVFC
CENTRE FOR DEVELOPMENT OF TELEMATICS, TELECOM, TECHNOLOGY	C-DOT
CENTRAL COAL FIELDS LIMITED	CCL
CONTAINER CORPORATION OF INDIA	CCOI
CHENAB VALLEY POWER CORPORATION LIMITED	CHENAB VALLEY P
CHENNAI METRO RAIL LTD	CMRL
CHENNAI PETROLEUM CORPORATION LIMITED	CPCL
CENTRAL PUBLIC WORKS DEPARTMENT	CPWD
CPWD OF HIGHER EDUCATION	CPWD EDUCATION
CPWD FOR DEFENCE	CPWD FOR DEFENC
CPWD FOR FINANCE	CPWD FOR FINANC
CPWD FOR HEALTH	CPWD FOR HEALTH
CPWD FOR MHA	CPWD FOR MHA
CPWD FOR POWER	CPWD FOR POWER
CPWD FOR RURAL	CPWD FOR RURAL
CPWD FOR TELECOM	CPWD FOR TELECO
CPWD FOR RENEWABLE ENERGY	CPWD R ENERGY
CENTRAL RAILWAYS	CR
COCHIN REFINERY LIMITED	CRL
COCHIN SHIPYARD LTD	CSL
CHENAB VELLEY POWER PROJECTS [P] LIMITED	CVPPPL
DUMMY AGENCY	DA
DEDICATED FREIGHT CORRIDOR CORPORATION OF INDIA LTD	DFCC
DIRECTORATE GENERAL OF CIVIL AVIATION	DGCA
Delhi Jal Board	DJB
Delhi Mumbai Industrial Corridor	DMIC
DMIC FOR DPIIT	DMIC FOR DPIIT
DELHI METRO RAIL CORPORATION	DMRC
DEPARTMENT OF TELECOMMUNICATION	DOT
Department for Promotion of Industry and Internal Trade	DPIIT
DAMODAR VALLEY CORPORATION	DVC
EASTERN COAL FIELDS LIMITED	ECL
EAST COAST RAILWAY	ECOR
EAST CENTRAL RAILWAYS	ECR

AGENCY_NAME	AGENCY_NAME_SHORT
EDCIL(India) Limited	EDCIL
ENNORE PORT LTD.	ENNORE PORT LTD
ENNORE TANK TERMINAL PVT.LTD.	ENNORE TANK
EASTERN RAILWAYS	ER
FERTILISER AND CHEMICAL TRIVANCORE	FACT
FREIGHT OPERATION INFORMATION SYSTEM	FOIS
SETTING UP FILM AND TELEVISION INSTITUTE	FTI
GAS AUTHORITY OF INDIA LIMITED	GAIL
GOA SHIPYARD LIMITED	GSL
HEALTH & FAMILY WELFARE	H&FW
HINDUSTAN AERONAUTICS LTD	HAL
HINDUSTAN COPPER LIMITED	HCL
HALDIA FERTILISER CORPORATION	HFC
HLL Infra Tech Services Limited	HITES
HYDERABAD METRO RAIL LTD	HMRL
HINDUSTAN PETROLEUM CORPORATION LIMITED	HPCL
HPCL Rajasthan Refinery Limited(JV)	HPCLRRL(JV)
HPOIL Gas Pvt. Ltd	HPOIL(JV)
HOSPITAL SERVICES CONSULTANCY CORPORATION LTD	HSCC
HINDUSTAN STEELWORK CONSTRUCTION LIMITED	HSCL
HINDUSTHAN STEELWORKS CONSTRUCTION LIMITED	HSCL
HSCL FOR DONER	HSCL FOR DONER
HSCL FOR RURAL	HSCL FOR RURAL
HSCL FOR WATER	HSCL FOR WATER
INDIAN FARMERS FERTILISER CORPORATION	IFFCO
INDIRA GANDHI CENTRE FOR ATOMIC RESEARCH	IGCAR
INDRADHANUSH GAS GRID LTD	IGGL
India International Convention and Expo Centre	IICC
IICC FOR DPIIT	IICC FOR DPIIT
INDIAN IRON STEEL COMPANY	IISCO
Indian Institute of Technology, Kharagpur	IITKGP
INDIAN OIL CORPORATION LIMITED	IOCL
INDIAN PETRO-CHEMICAL CORPORATION LIMITED	IPCL
Indian Railway Construction Company Limited	IRCON
INDIAN STRATEGIC PETROLEUM RESERVES LTD	ISPRL
INDIAN TELEPHONE INDUSTRY	ITI
Inland Waterways Authority of India	IWAI
INLAND WATER TRANSPORT	IWT
JAWAHAR LAL NEHRU NATIONAL URBAN RENEWAL MISSION	JNNURM
JWAAHARLAL NEHRU PORT TRUST	JNPT
Jharkhand Urban Infrastructure Development Company Ltd	JUIDCO
Kolkata Metropolitan Development Authority	KMDA
KOCHI METRO RAIL CORPORATION LTD	KMRCL
KOLKATA METRO RAIL CORPORATION LIMITED	KOMRCL
KAMARAJAR PORT LIMITED	KPL
KONKAN RAILWAY	KR
Rail Infrastructure Development Company	KRIDE
KOCHI REFINERIES LIMITED	KRL
Kochi Salem Pipeline Private Limited(JV)	KSPPL(JV)
LINE DOUBLING	LD
LUCKNOW METRO RAIL CORPORATION LIMITED	LMRCL
MANGALORE REFINERY AND PETROCHEMICALS LIMITED	MANGALORE REFIN

AGENCY_NAME	AGENCY_NAME_SHORT
MAHANADI COAL FIELDS LIMITED	MCL
MECON LIMITED	MECON LIMITED
AHMEDABAD METRO RAIL	MEGA
MADRAS FERTILISER LIMITED	MFL
Munitions India Limited	MIL
MAHARASTRA METRO RAIL CORPORATION LTD.	MMRC
MUMBAI METRO RAIL CORPORATION LTD	MMRCL
MINISTRY OF WATER RESOURCES	MOWR
Madhya Pradesh Metro Rail Co Limited	MPMRCL
Maharashtra Rail Infrastructure Development Corporation Limited	MRIDC
MANGALORE REFINARY LIMITED	MRL
METROPOLITAN RAPID TRANSPORT PROJECTS	MRTP
Mumbai Railway Vikas Corporation	MRVC
MAHANAGAR TELEPHONE NIGAM LIMITED	MTNL
MUMBAI PORT TRUST	MUMBAI PORT TRU
Armoured Vehicles Nigam Limited	MVNL
MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)	MoRTH
NATIONAL ALUMINUM COMPANY LIMITED (NALCO)	NALCO
NATRIIP IMPLEMENTATION SOCIETY	NATIS
NATIONAL BUILDING CONSTRUCTION CORPORATION LTD	NBCC
NBCC FOR COMMERCE	NBCC FOR COMMER
NBCC FOR HEALTH	NBCC FOR HEALTH
NORTHERN COAL FIELDS LIMITED	NCL
NORTH CENTRAL RAILWAY	NCR
NATIONAL CAPITAL REGION TRANSPORT CORP	NCRTC
NATIONAL CENTRE OF EXCELLENCE	NCoE
NORTH EAST ELECTRIC POWER CORPORATION	NEEPCO
NORTH EAST GAS GRID	NEGG
NORTH EASTERN RAILWAY	NER
National Film Archive of India	NFAI
NUCLEAR FUEL CORPORATION	NFC
NATIONAL FERTILISER LIMITED	NFL
NORTH EAST FRONTIER RAILWAY	NFR
NATIONAL HIGHWAYS AUTHORITY OF INDIA	NHAI
NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.	NHIDCL
NATIONAL HYDRO-ELECTRIC POWER CORPORATION	NHPC
National High Speed Rail Corporation Limited	NHSRCL
NEW LINE	NL
NEYVELI LIGNITE CORPORATION	NLC
NATIONAL MISSION FOR CLEAN GANGA	NMCG
NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)	NMDC
NAGPUR METRO RAIL CORPORATION LTD	NMRCL
NATIONAL PROJECTS CONSTRUCTION CORPORATION LIMITED	NPCC
NUCLEAR POWER CORPORATION OF INDIA LIMITED	NPCIL
NORTHERN RAILWAY	NR
NUMALIGARH REFINERY LIMITED	NRL
SETTING UP OF NEW RAILWAY ZONES	NRZ
NATIONAL THERMAL POWER CORPORATION	NTPC
NORTH WESTERN RAILWAY	NWR
OIL INDIA LIMITED	OIL
OIL & NATURAL GAS CORPORATION LIMITED	ONGC
PATNA METRO RAIL CORPORATION	PATNA METRO RAI

AGENCY_NAME	AGENCY_NAME_SHORT
PAWAN HANS HELICOPTERTERS LTD.	PAWAN HANS HELI
POWER GRID CORPORATION OF INDIA LIMITED	PGCIL
PORT TRUST	PORT TRUST
Polavaram Project Authority	PPA
RASHTRIYA CHEMICAL & FERTILISER LIMITED	RCF
RAILWAY ELECTRIFICATION	RE
RASTRIYA ISPAT NIGAM LIMITED	RINL
RAIL INDIA TECHNICAL AND ECONOMIC SERVICE	MITES
MITES OF HIGHER EDUCATION	MITES OF HIGHER
RAIL VIKAS NIGAM LTD.	RVNL
SIGNALLING & TELECOMMUNICATIONS	S&T
STEEL AUTHORITY OF INDIA LIMITED (SAIL)	SAIL
SINGARENI COLLIERS COMPANY LIMITED	SCCL
SOUTH CENTRAL RAILWAY	SCR
SOUTH-EASTERN COAL FIELDS LIMITED	SECL
SOUTH EAST CENTRAL RAILWAY	SECR
SOUTH EASTERN RAILWAY	SER
SER(GC) GAUGE CONVERSION	SER(GC
SHIPPING CRP. OF INDIA	SHIPP.
SATLUJ JAL VIDYUT NIGAM LIMITED	SJVN
SOUTHERN RAILWAY	SR
SOUTH WESTERN RAILWAY	SWR
Sikkim University	Sikkim Universi
THDC INDIA LIMITED	THDCIL
TUTICORIN PORT TRUST	TUTICORIN
URANIUM CORPORATION OF INDIA LIMITED	UCIL
URBAN DEVELOPMENT	UD
Uttarakhand Pey Jal Nigam	UKJalNigam
Uttar Pradesh Jal Nigam	UPJalNigam
VISAKHAPATNAM PORT TRUST	VPT
Varanasi Smart City	Varanasi Smart
WAPCOS	WAPCOS
WESTERN COAL FIELDS LIMITED	WCL
WEST CENTRAL RAILWAY	WCR
WESTERN RAILWAY	WR
WORKSHOPS & PRODUCTION UNIT	WS&PU



Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
